

THE STATE OF SOUTH CAROLINA
In The Court of Appeals

APPEAL FROM CHARLESTON COUNTY
Court of Common Pleas

Mikell R. Scarborough, Master-In-Equity

Appellate Case No. 2024-000788
Case No.: 2019-CP-10-01108

RECEIVED

Aug 12 2026

SC Court of Appeals

Balfour Beatty Construction, LLC, Appellant,

v.

Library Associates, LLC; and Metropolitan Life Insurance Company, a New York Corporation, Defendants,

And

Library Associates, LLC, Third-Party Plaintiff,

v.

Lithko Contracting, LLC, Guy M. Beaty, Inc., Bernard MMC, LLC, Gulf Stream Construction Company, Inc., Precision Walls, Inc., Palmetto Automatic Sprinkler Company, Inc., Cook & Boardman, LLC, Strong Tower Construction, LLC d/b/a Koch Corporation, Watson Electrical Construction Co., LLC, Trimark Foodcraft, LLC, Pleasant Places, Inc., David Allen Company, Inc., Premier Exteriors, LLC, Warco Construction, Inc., Old North State Masonry, LLC, Tom Rochester & Associates d/b/a Southeastern Architectural Systems, Forton Company, LLC, Low Country Case & Millwork, Inc., Quantum Coatings, LLC, Balfour Beatty Construction Group, Inc., Third-Party Defendants.

Of which Library Associates, LLC is the Respondent.

AMENDED RECORD ON APPEAL - VOLUME 4 OF 20

James Lynn Werner (S.C. Bar No. 6029)
Katon E. Dawson, Jr. (S.C. Bar No. 101167)
1221 Main Street, Suite 1100
Columbia, SC 29201
(803) 255-8000
jimwerner@parkerpoe.com
katondawson@parkerpoe.com

Thomas C. Hildebrand, Jr. (S.C. Bar No. 2501)
Robert C. Byrd (S.C. Bar No. 1069)
850 Morrison Drive, Suite 400
Charleston, SC 29403
(843) 727- 2650
tomhildebrand@parkerpoe.com
bobbybyrd@parkerpoe.com

*Attorneys for Appellant Balfour Beatty
Construction, LLC*

Walter H. Bundy, Jr., Esquire
M. Brent McDonald, Esquire
Bundy McDonald, LLC
1516 Old Trolley Rd 2nd Floor
Summerville, SC 29485-8209
walter@bundymcdonald.com
brent@bundymcdonald.com

and

Jesse Sanchez, Esquire
The Law Office of Jesse Sanchez, LLC
751 Johnnie Dodds Boulevard
Suite 200
Mount Pleasant, SC 29464
jesse@jessesanchezlaw.com

Attorneys for Library Associates, LLC

INDEX

Page(s)

Section 1 - Orders

Volume - 1

Order Granting Balfour Beatty Construction, LLC's Motion to Amend Complaint, filed October 2, 2019.....	R-001
Order to Consolidate C.A. No. 2019-CP-10-2275 and Refer to the Charleston County Master-In Equity, filed November 18, 2019	R-003
Order to Consolidate C.A. No. 2019-CP-10-2868 and Refer to Charleston County Master-In-Equity, filed November 18, 2019.....	R-007
Form 4 Order Granting Library Associates, LLC's Motion for an Affirmative Junction, filed March 17, 2020	R-011
Order Granting Library Associates, LLC's Motion to Enforce the Court Order, filed June 17, 2020.....	R-014
Order Granting Strong Tower Construction, LLC d/b/a Koch Corporation's Motion for Partial Summary Judgment, filed September 9, 2021	R-021
Order Granting Third-Party Defendant Warco Construction, Inc.'s Motion for Partial Summary Judgment, filed September 13, 2021	R-037
Order Granting Watson Electrical Construction Co., LLC's Motion for Partial Summary Judgment, filed September 13, 2021	R-047
Order Regarding Multiple Motions, filed October 26, 2021	R-057
Form 4 Order Judgment Entered in Favor of Premier Exteriors, LLC Against Balfour Beatty Construction, LLC, filed December 22, 2021.....	R-060
Order Granting Premier Exteriors, LLC's Motion for Summary Judgment Against Balfour Beatty Construction, LLC, filed December 22, 2021	R-063
Form 4 Order Judgment in Favor of Library Associates, LLC Against Balfour Beatty Construction, LLC, filed October 6, 2023.....	R-076
Trial Order, filed October 6, 2023	R-079
Order Awarding Attorneys' Fees and Costs, filed April 12, 2024	R-126
Order Awarding Punitive Damages, filed April 12, 2024	R-132

Order Granting and Denying in Part Balfour Beatty Construction, LLC’s Motion to Alter or Amend the Order Awarding Punitive Damages and Election of Remedy, filed April 29, 2024R-144

Form 4 Judgment Order in Favor of Library Associates, LLC Against Balfour Beatty Construction, LLC, filed May 6, 2024.....R-147

Form 4 Order Denying Balfour Beatty Construction, LLC’s Motions to Alter or Amend, filed May 15, 2024R-153

Section 2 - Pleadings

Summons and Complaint, C.A. No. 2019-CP-10-01108, filed March 5, 2019R-156

Library Associates, LLC’s Answer to Plaintiff’s Complaint and Counterclaims, filed May 3, 2019R-182

Amended Answer and Counterclaims of Library Associates, LLC and Third-Party Complaint, filed May 15, 2019R-196

Amended Summons and Complaint, C.A. No. 2019-CP-10-01108, filed October 3, 2019.....R-364

Answer and Counterclaims of Library Associates, LLC to Amended Complaint of Balfour Beatty Construction, LLC and Third-Party Complaint, filed October 17, 2019.....R-385

Second Amended Summons and Complaint, C.A. No. 2019-CP-10-01108, filed October 12, 2020.....R-418

Answer and Counterclaims of Library Associates, LLC to the Second Amended Complaint of Balfour Beatty Construction, LLC and Third-Party Complaint, filed October 20, 2020R-446

Volume - 2

Answer and Counterclaims of Library Associates, LLC to the Second Amended Complaint of Balfour Beatty Construction, LLC and Third-Party Complaint, filed October 20, 2020, cont’dR-501

Section 3 - Transcripts

Excerpts from Trial Transcript of September 13, 2021 to December 3, 2021, to include:

Pages: 1-3; 90-164; 204; 215-284; 385-386; 392; 675-815; 1786-1797; 1843-1892; 1916-2046; 2204-2207; 2231-2233; 2274; 2299-2331; 2553-2554; 2599; 2607-2613; 2615-2662; 2665-2705; 2714-2716; 2759-2761; 2794-2924; 2949-2950; 2968-2971; 3039-3061; 3142-3148; 3154-3155; 3166-3173; 3175-3179; 3194; 3247-3255; 3267-3272; 3817; 3819-3827; 3835-3837; 3839-3853; 3856-3860; 3890-3893; 3901-3902; 3907-3908; 3916-3941; 3955-

3957; 4110-4112; 4120-4121; 4149-4150; 4216-4234; 4248-4251; 4275-4296; 4316; 4340-4341; 4460-4487.R-523

Volume - 3

Excerpts from Trial Transcript of September 13, 2021 to December 3, 2021, to include:

Pages: 1-3; 90-164; 204; 215-284; 385-386; 392; 675-815; 1786-1797; 1843-1892; 1916-2046; 2204-2207; 2231-2233; 2274; 2299-2331; 2553-2554; 2599; 2607-2613; 2615-2662; 2665-2705; 2714-2716; 2759-2761; 2794-2924; 2949-2950; 2968-2971; 3039-3061; 3142-3148; 3154-3155; 3166-3173; 3175-3179; 3194; 3247-3255; 3267-3272; 3817; 3819-3827; 3835-3837; 3839-3853; 3856-3860; 3890-3893; 3901-3902; 3907-3908; 3916-3941; 3955-3957; 4110-4112; 4120-4121; 4149-4150; 4216-4234; 4248-4251; 4275-4296; 4316; 4340-4341; 4460-4487, cont'd.R-1001

Volume - 4

Excerpts from Trial Transcript of September 13, 2021 to December 3, 2021, to include:

Pages: 1-3; 90-164; 204; 215-284; 385-386; 392; 675-815; 1786-1797; 1843-1892; 1916-2046; 2204-2207; 2231-2233; 2274; 2299-2331; 2553-2554; 2599; 2607-2613; 2615-2662; 2665-2705; 2714-2716; 2759-2761; 2794-2924; 2949-2950; 2968-2971; 3039-3061; 3142-3148; 3154-3155; 3166-3173; 3175-3179; 3194; 3247-3255; 3267-3272; 3817; 3819-3827; 3835-3837; 3839-3853; 3856-3860; 3890-3893; 3901-3902; 3907-3908; 3916-3941; 3955-3957; 4110-4112; 4120-4121; 4149-4150; 4216-4234; 4248-4251; 4275-4296; 4316; 4340-4341; 4460-4487, cont'd.R-1501

Transcript of April 2, 2024 Hearing on Balfour Beatty Construction, LLC's
Motion to Alter/Amend Order granting Judgment to Library Associates, LLC,
only pages 1-4, 29-38.....R-1507

Section 4 - Exhibits

Balfour Beatty Construction, LLC's Exhibit 3R-1521
Balfour Beatty Construction, LLC's Exhibit 11R-1534
Balfour Beatty Construction, LLC's Exhibit 12R-1542

Volume - 5

Balfour Beatty Construction, LLC's Exhibit 12, cont'd.....R-2001

Volume - 6

Balfour Beatty Construction, LLC's Exhibit 12, cont'd.....R-2501
Balfour Beatty Construction, LLC's Exhibit 26R-2518
Balfour Beatty Construction, LLC's Exhibit 27, only pages 1, 3-12, 23, 47-49, 53,
55, 67.....R-2520

Balfour Beatty Construction, LLC's Exhibit 42, only pages 1-2, 8.....	R-2538
Balfour Beatty Construction, LLC's Exhibit 46, only pages 1-2, 18.....	R-2541
Balfour Beatty Construction, LLC's Exhibit 56	R-2544
Balfour Beatty Construction, LLC's Exhibit 72	R-2689
Balfour Beatty Construction, LLC's Exhibit 81	R-2691
Balfour Beatty Construction, LLC's Exhibit 83	R-2693
Balfour Beatty Construction, LLC's Exhibit 85	R-2695
Balfour Beatty Construction, LLC's Exhibit 111	R-2699
Balfour Beatty Construction, LLC's Exhibit 138, only pages 1-2	R-2702
Balfour Beatty Construction, LLC's Exhibit 141	R-2704
Balfour Beatty Construction, LLC's Exhibit 143	R-2706
Balfour Beatty Construction, LLC's Exhibit 150	R-2709
Balfour Beatty Construction, LLC's Exhibit 151	R-2715
Balfour Beatty Construction, LLC's Exhibit 154.....	R-2724
Balfour Beatty Construction, LLC's Exhibit 201	R-2735
Balfour Beatty Construction, LLC's Exhibit 202	R-2742
Balfour Beatty Construction, LLC's Exhibit 215	R-2745
Balfour Beatty Construction, LLC's Exhibit 226	R-2774

Volume - 7

Balfour Beatty Construction, LLC's Exhibit 226, cont'd	R-3001
--	--------

Volume - 8

Balfour Beatty Construction, LLC's Exhibit 226, cont'd	R-3501
--	--------

Volume - 9

Balfour Beatty Construction, LLC's Exhibit 226, cont'd	R-4001
Balfour Beatty Construction, LLC's Exhibit 231	R-4352
Balfour Beatty Construction, LLC's Exhibit 255	R-4383
Balfour Beatty Construction, LLC's Exhibit 257	R-4385
Balfour Beatty Construction, LLC's Exhibit 258	R-4389
Balfour Beatty Construction, LLC's Exhibit 261	R-4391
Balfour Beatty Construction, LLC's Exhibit 263, only pages 1-2.....	R-4396
Balfour Beatty Construction, LLC's Exhibit 292	R-4398
Balfour Beatty Construction, LLC's Exhibit 300, only pages 1-2, 9-12	R-4435
Balfour Beatty Construction, LLC's Exhibit 301	R-4441
Balfour Beatty Construction, LLC's Exhibit 303, only pages 1-4, 16-18	R-4490
Balfour Beatty Construction, LLC's Exhibit 304, only pages 1-2, 10.....	R-4497
Balfour Beatty Construction, LLC's Exhibit 305, only pages 1-2, 12-13, 42-43 45, 57-59, 90	R-4500

Volume - 10

Balfour Beatty Construction, LLC's Exhibit 305, only pages 1-2, 12-13, 42-43 45, 57-59, 90, cont'd	R-4501
Balfour Beatty Construction, LLC's Exhibit 312	R-4511
Balfour Beatty Construction, LLC's Exhibit 350	R-4715
Library Associates LLC's Exhibit 3	R-4747
Library Associates LLC's Exhibit 11	R-4966

Volume - 11

Library Associates LLC's Exhibit 11, cont'd	R-5001
---	--------

Volume - 12

Library Associates LLC's Exhibit 11, cont'd	R-5501
Library Associates LLC's Exhibit 12	R-5770

Volume - 13

Library Associates LLC's Exhibit 12, cont'd	R-6000
Library Associates LLC's Exhibit 13	R-6309

Volume - 14

Library Associates LLC's Exhibit 13, cont'd	R-6501
Library Associates LLC's Exhibit 14	R-6849
Library Associates LLC's Exhibit 28	R-6915
Library Associates LLC's Exhibit 35	R-6919

Volume - 15

Library Associates LLC's Exhibit 35, cont'd	R-7001
Library Associates LLC's Exhibit 39	R-7077
Library Associates LLC's Exhibit 44	R-7199
Library Associates LLC's Exhibit 45	R-7206
Library Associates LLC's Exhibit 50	R-7212
Library Associates LLC's Exhibit 89	R-7214
Library Associates LLC's Exhibit 90	R-7351
Library Associates LLC's Exhibit 91	R-7377

Volume - 16

Library Associates LLC's Exhibit 91, cont'd	R-7501
Library Associates LLC's Exhibit 103	R-7523
Library Associates LLC's Exhibit 104	R-7634
Library Associates LLC's Exhibit 105	R-7640
Library Associates LLC's Exhibit 114	R-7643

Library Associates LLC’s Exhibit 141	R-7700
Library Associates LLC’s Exhibit 142	R-7845

Volume - 17

Library Associates LLC’s Exhibit 142, cont’d	R-8001
Library Associates LLC’s Exhibit 143	R-8045
Library Associates LLC’s Exhibit 146B	R-8178
Library Associates LLC’s Exhibit 150	R-8242

Section 5 - Other Documents

Balfour Beatty Construction, LLC’s Notice and Certificate of Mechanic’s Lien, filed January 25, 2019	R-8255
Balfour Beatty Construction, LLC’s Notice and Certificate of Amended Mechanic’s Lien, filed July 23, 2019	R-8261
Proposed Trial Order submitted by Balfour Beatty Construction, LLC, filed May 23, 2023	R-8268
Proposed Trial Order submitted by Library Associates, LLC, filed May 23, 2023	R-8413
Balfour Beatty Construction, LLC’s Motion to Alter/Amend Order Granting Judgment to Library Associates, LLC, filed October 16, 2023	R-8461

Volume - 18

Balfour Beatty Construction, LLC’s Motion to Alter/Amend Order Granting Judgment to Library Associates, LLC, filed October 16, 2023, cont’d	R-8501
Balfour Beatty Construction, LLC’s Motion to Require Library Associates, LLC to Elect a Remedy, filed October 16, 2023	R-8631
Library Associates, LLC’s Petition for Attorneys’ Fees and Costs, filed November 6, 2023.....	R-8633
Balfour Beatty Construction, LLC’s Memorandum in Opposition to Defendant Library Associates, LLC’s Petition for Attorneys’ Fees and Costs, filed March 7, 2024.....	R-8642
Balfour Beatty Construction, LLC’s Memorandum in Support of its Motion to Require Library Associates, LLC to Elect a Remedy, filed March 7, 2024.....	R-8672

Balfour Beatty Construction, LLC’s Memorandum in Support of Motion to Alter/Amend the Order Granting Judgment to Library Associates, LLC, filed March 7, 2024	R-8675
Library Associates, LLC’s Memorandum in Support of its Petition for Attorneys’ Fees and Costs and Pursuant to the Declaratory Judgment Act, Additional Interest Payments, Past and Future, as Direct Costs Incurred and for Prejudgment Interest as Provided by Law; and in Support of Pending Rule 52(B) and 59(E) Motions to Alter or Amend and Make Additional Findings, filed March 7, 2024.....	R-8718
Balfour Beatty Construction, LLC’s Amended Motion to Require Library Associates, LLC to Elect a Remedy, filed March 8, 2024.....	R-8739
Balfour Beatty Construction, LLC Memorandum in Response to Library Associates, LLC’s Memorandum in Support of its Petition for Attorneys’ Fees and Costs and Pursuant to the Declaratory Judgment Act, Additional Interest Payments, Past and Future, as Direct Costs Incurred and for Prejudgment Interest as Provided by Law; and in Support of Pending Rule 52(B) and 59(E) Motions to Alter or Amend and Make Additional Findings, filed March 11, 2024.....	R-8741
Balfour Beatty Construction, LLC’s Motion to Strike Affidavit of Marvin D. Infinger, filed March 11, 2024	R-8754
Library Associates, LLC’s Reply to Balfour Beatty Construction, LLC’s Memorandum in Opposition to its Petition for Attorneys’ Fees and Costs, filed March 11, 2024	R-8760
Revised Affidavit of Marvin D. Infinger, filed March 11, 2024	R-8766
Affidavit of Franklin E. Worrell, filed March 28, 2024	R-8779
Balfour Beatty Construction, LLC’s Motion in Limine Regarding Hearing on Punitive Damages, filed April 1, 2024.....	R-8786
Library Associates, LLC’s Filing of March 13, 2024 Hearing Exhibits, filed April 10, 2024	R-8793

Volume - 19

Library Associates, LLC’s Filing of March 13, 2024 Hearing Exhibits, filed April 10, 2024, cont’d.....	R-9001
--	--------

Volume - 20

Library Associates, LLC’s Filing of March 13, 2024 Hearing Exhibits, filed April 10, 2024, cont’d.....	R-9501
--	--------

Library Associates, LLC’s Supplemental Petition for Attorneys’ Fees and Costs; and in Addition Other Relief Pursuant to Declaratory Judgment Cause of Action, filed April 10, 2024	R-9826
Supplemental Affidavit of Kimberly Bennett Brown, filed April 10, 2024	R-9828
Balfour Beatty Construction, LLC’s Motion to Alter or Amend the Order Awarding Punitive Damages and Election of Remedy Pursuant to Rule 59(E), filed April 22, 2024	R-9864
Library Associates, LLC’s Notice of Election of Remedy, filed May 2, 2024	R-9867
Balfour Beatty Construction, LLC’s Motion to Alter or Amend Pursuant to Rule 59(E), filed May 9, 2024	R-9870
Video Deposition Testimony of George Michael Baumbach, 13:5-14:10 (Timestamp 7:28-8:23); 14:24-15:11 (Timestamp 10:00-10:30); 42:12-45:23 (Timestamp 47:40-52:05); 46:22-47:15 (Timestamp 53:27-54:22) (Placeholder for video file being submitted via Court of Appeal’s OneDrive)	R-9876

1 these damages or is only responsible for some of
2 them. Unless and until he does that, his
3 testimony is just speculation that a
4 theoretical -- well, I see an issue here. I see
5 that the stone mason might have been delayed. I
6 see that Pasco might have done something.

7 But by all the testimony is, that
8 doesn't matter until you can show that it's on
9 the critical path, that's only a theoretical
10 issue that doesn't hold water. And since the
11 only testimony in front of the Court is
12 Mr. Doran's -- where he did say this is the
13 critical path, then I don't think that Library
14 has met its burden of proof to establish that it
15 is entitled to any liquidated damages.

16 Another issue -- I think some of these
17 are affirmative defenses, and -- that we've
18 raised, or all of them are and related to the
19 counter-claim as by Library -- is forfeiture.
20 I'm sure you're -- the Court is familiar with
21 that. The Court abhors a forfeiture. Equity
22 abhors a forfeiture.

23 What the owner would like to argue in
24 this case is that, because Balfour didn't dot --
25 perhaps it didn't dot its I's or cross its T's on

1 some of the claims, that it should not be
2 entitled to any damages for delay, for the year
3 and a half that it -- extra that was out there,
4 for all of the damages it incurred.

5 Basically, we just -- the owner is
6 saying, we just want that -- all of that time and
7 effort and work for free. We just don't want
8 Balfour to have to pay for it.

9 And the case law is that, even in issues
10 where you have a condition precedent, that those
11 can't -- if the case law were black and white, if
12 you have a condition precedent that the -- the
13 other party is just out of court, black and
14 white, then you would have ruled on summary
15 judgment, or we wouldn't be in front of you.

16 It's up to you, as the Master-in-Equity,
17 look at the case, look at the facts and make a
18 decision as to whether we are entitled to the
19 work that we performed. And even if Mr. Bundy
20 says that -- well, you didn't follow the court --
21 the contract exactly, you didn't make a claim for
22 31 days or whatever, the courts have said, we're
23 going to look at principals of equity, and we
24 abhor forfeiture.

25 There have been arguments that,

1 appropriate notice for delays was not made, but I
2 believe that it was. And, again, Your Honor, on
3 these issues, waiver and estoppel and such, the
4 courts have held that actual notice is
5 sufficient. If a party has received actual
6 notice, then exact compliance with contract
7 documents is not necessary.

8 If an owner recognized -- wants a
9 benefit and recognizes that it's got the benefit,
10 it can't then turn back to the contract and say,
11 well, you didn't follow exact the notification
12 provisions, or we're not going to pay you. So I
13 think that the -- there was actual notice, and if
14 you will recall, there was a delay notification
15 log that was issued that had 20 notifications of
16 delay. With each payment application, there was
17 a carve out of claims that were being made by
18 Balfour.

19 And you will recall from the testimony,
20 deposition testimony of Jim Clements -- I asked
21 him this very specifically, I said, in your view,
22 even if Balfour did not dot all the I's and cross
23 all the T's on making the claims, do you
24 recognize that it was making a claim and a
25 continuing claim for delays on this job, and he

1 said yes.

2 They make -- they tried to -- they might
3 not have done so perfectly, but they certainly
4 tried to. Active interference, the case law --
5 construction case law is that, if an owner
6 actively interferes and causes damage, that it
7 has to -- it's liable for the damages it caused
8 here.

9 The owner made a lot of changes and did
10 not, by omission, did a lot of active
11 interference by not making decision and such.
12 And all we're simply asking the Court to do is
13 say, okay, owner, by your changes and your
14 failure to act in the things that you did, we --
15 that constitutes active interference, and you've
16 got to pay the contractor for the work that you
17 performed.

18 The case I would like to cite, Your
19 Honor, regarding waiver of claims for extra work
20 is the -- you cited it in our pretrial brief, I
21 believe. It's Lazer, L-A-Z-E-R, Construction vs.
22 Long, 370 Southeast Second 900 Court of Appeals
23 1988, South Carolina.

24 And the quotation is, where the owner
25 has actual notice of extra work and permits it to

1 proceed without objection. The notice
2 requirements, if any, may be waived. The owner
3 hasn't shown any prejudice from having
4 received -- not having received notice. I think
5 they got actual notice that we were doing the
6 work and had claims for the work that we
7 performed, and just simply didn't pay them.

8 Another issue, Your Honor, is that
9 relating to the notice obligations or notice
10 claim is, the principle of cumulative impact.
11 And I know that the -- that Mr. Query testified
12 that that's commonly known as a death by a
13 thousand cuts. And he said that he didn't think
14 much of it. It's not one that he -- that he
15 recognizes.

16 But I will tell you that the courts do
17 recognize it, and it's where, when there are
18 changes after changes after changes that cause a
19 cascading ripple type of impact, they can be
20 considered a single change that can't be made
21 until the end of the project, and it's called a
22 cumulative impact.

23 And I think that, if you look at all the
24 changes that the owner made, you could very well
25 come to the conclusion that the change after

1 change after change that were testified by Nick
2 Starcevic, Tim Spano, David Simonton, Mr. Doran,
3 they constituted a cumulative impact. And I will
4 refer you on that provision to Santa Fe Engineers
5 vs. United States 818 F Second, 856, 1987. And
6 I've got a brief on that point as well.

7 So, Your Honor, I believe that those are
8 all the grounds that -- let me check with my
9 colleagues. All right. Thank you for your
10 attention, Your Honor. That's it.

11 THE COURT: All right. Thank you.

12 MR. BUNDY: If it pleases the
13 Court.

14 THE COURT: Yes, sir.

15 MR. BUNDY: I would like to talk
16 about something unusual in this case, which is
17 evidence and what's in the record. That's what I
18 would like to talk about. I don't want to talk
19 about what people think happened. If it's not
20 written down in this young lady's book, it didn't
21 happen.

22 THE COURT: I understand that.

23 MR. BUNDY: We can start back -- I
24 will start back with the conspiracy. Recently,
25 as my adversary pointed out, the conspiracy fraud

STATE OF SOUTH CAROLINA
COUNTY OF CHARLESTON

) IN THE COURT OF COMMON PLEAS
) CASE NO. 2019-CP-10-01108

BALFOUR BEATTY CONSTRUCTION, LLC,
Plaintiff,
versus

LIBRARY ASSOCIATES, LLC; AND METROPOLITAN
LIFE INSURANCE COMPANY, A NEW YORK
CORPORATION,
Defendants.

LIBRARY ASSOCIATES, LLC,
Third-Party Plaintiff,

versus

LITHKO CONTRACTING, LLC, GUY M. BEATY, INC.,
BERNARD MMC, LLC, GULF STREAM CONSTRUCTION
COMPANY, INC., PRECISION WALLS, INC.,
PALMETTO AUTOMATIC SPRINKLER COMPANY, INC.,
COOK & BOARDMAN, LLC, STRONG TOWER
CONSTRUCTION, LLC, D/B/A KOCH CORPORATION,
WATSON ELECTRICAL CONSTRUCTION CO., LLC,
TRIMARK FOODCRAFT, LLC, PLEASANT PLACES,
INC., DAVID ALLEN COMPANY, INC., PREMIER
EXTERIORS, LLC, WARCO CONSTRUCTION, INC.,
OLD NORTH STATE MASONRY, LLC, TOM ROCHESTER
& ASSOCIATES D/B/A SOUTHEASTERN ARCHITECTURAL
SYSTEMS, FORTON COMPANY, LLC, LOW COUNTRY
CASE & MILLWORK, INC., QUANTUM COATINGS, LLC,
BALFOUR BEATTY CONSTRUCTION GROUP, INC.,
Third-Party Defendants.

H E A R I N G

BEFORE: JUDGE MIKELL R. SCARBOROUGH
DATE: APRIL 2, 2024
TIME: 2:03 P.M.
LOCATION: CHARLESTON COUNTY COURTHOUSE
100 BROAD STREET, COURTROOM 2A
CHARLESTON, SOUTH CAROLINA 29401
REPORTED BY: ANGELA WATSON, COURT REPORTER

LEGAL EAGLE

Post Office Box 5682
Greenville, South Carolina 29606
864-467-1373 / depos@legaleagleinc.com

1 APPEARANCES:

2

3 THOMAS C. HILDEBRAND, JR., ESQUIRE

4 PARKER POE, ATTORNEYS & COUNSELORS AT LAW

5 850 MORRISON DRIVE, SUITE 400

6 CHARLESTON, SC 29403

7 tomhildebrand@parkerpoe.com

8

9 JAMES WERNER, ESQUIRE

10 PARKER POE, ATTORNEYS & COUNSELORS AT LAW

11 1221 MAIN STREET, SUITE 1100

12 COLUMBIA, SC 29201

13 jimwerner@parkerpoe.com

14

15 WALTER HERNY BUNDY, JR., ESQUIRE

16 BUNDY MCDONALD, LLC

17 1516 OLD TROLLEY ROAD, 2ND FLOOR

18 SUMMERVILLE, SOUTH CAROLINA 29485

19 walter@bundymcdonald.com

20

21 DON RUSSELL TERRY, ESQUIRE

22 WINDLE, TERRY, BIMBO CONSTRUCTION LAW

23 150 MILESTONE WAY, SUITE C

24 GREENVILLE, SOUTH CAROLINA 29615

25 dterry@wtbconstructionlaw.com

1 APPEARANCES CONTINUED:

2

3 JOHN P. LINTON, ESQUIRE

4 DUFFY & YOUNG, LLC

5 96 BROAD STRRET

6 CHARLESTON, SOUTH CAROLINA 29401

7 jllinton@duffyandyoung.com

8

9

10 ALSO PRESENT: MICHAEL BENNITT

11

12

13

14

15

16

17

18

19

20

21

22

23

24

25

INDEX

COLLOQUY BETWEEN JUDGE SCARBOROUGH AND COUNSEL.....	5
TESTIMONY OF MICHAEL BENNITT:	
EXAMINATION BY MR. BUNDY.....	39
EXAMINATION BY MR. WERNER.....	50
EXAMINATION BY THE COURT.....	59
CERTIFICATE OF REPORTER.....	79

EXHIBITS

DEFENDANT'S EXHIBIT 1.....	29
DEFENDANT'S EXHIBIT 2.....	30
DEFENDANT'S EXHIBIT 3.....	30
DEFENDANT'S EXHIBIT 4.....	30
DEFENDANT'S EXHIBIT 5.....	30

(THIS TRANSCRIPT MAY CONTAIN QUOTED MATERIAL. SUCH MATERIAL
IS REPRODUCED AS READ OR QUOTED BY THE SPEAKER.)

1 MR. WERNER: Well, I don't know what he
2 intends to offer, Judge, but, I mean, if Your
3 Honor's going to go forward with it, again, we've
4 made our motion. So we'll respond as they try to
5 put evidence in and we'll make whatever objections
6 are appropriate.

7 THE COURT: Very good. Okay. Thank you,
8 sir. All right, Mr. Bundy. It's your turn, sir.

9 MR. BUNDY: Thank you, Your Honor. If it may
10 please the Court, Your Honor, we might as well go
11 ahead and get into the -- the objection,
12 presumably -- evidence before I put Mr. Bennitt
13 up. Excuse me one second, Judge.

14 THE COURT: Sure.

15 MR. BUNDY: I'm just going to mark them right
16 now, Judge, if that's okay.

17 THE COURT: That will be fine.

18 MR. BUNDY: This will be -- do you want to do
19 them one for ID for the purposes of the punitive
20 damage hearings, and we'll have all these numbers
21 again?

22 THE COURT: That'd be great.

23 MR. BUNDY: All right. One, for
24 identification.

25 (Whereupon, the below-described document was

1 marked as Defendant's Exhibit No. 1.)

2 MR. BUNDY: This will be Defendant's two,
3 Defendant's three, Defendant's four. This will be
4 five.

5 (Whereupon, the below-described documents
6 were marked as Defendant's Exhibit Nos. 2, 3, 4,
7 and 5, respectively.)

8 MR. WERNER: So four bills total that you've
9 marked for identification. Four that you've
10 marked for identification. There are four
11 exhibits you've marked for identification; is that
12 correct?

13 MR. BUNDY: There are five. I just marked
14 one more.

15 MR. WERNER: Oh, okay. Sorry.

16 MR. BUNDY: One through five exhibits, for
17 identification. One through four, I'm going to
18 offer up to the Court without a witness.

19 THE COURT: Okay.

20 MR. BUNDY: These are filed documents in the
21 Federal Register and various -- these are public
22 documents. I think you're good with the
23 exceptions of hearsay rule.

24 THE COURT: All right.

25 MR. BUNDY: Defendant's 1 is entitled,

1 Justice Department Announces Global Resolution of
2 Criminal and Civil Investigations with Privatized
3 Military Housing Contract for defrauding U.S.
4 Military.

5 MR. WERNER: Judge, before they're published
6 up, let me make the objection for the record.

7 THE COURT: All right.

8 MR. WERNER: We would object to the
9 admissibility of any of these documents. They do
10 not, in fact, come under any recognized exception
11 to the hearsay rule in South Carolina. When they
12 have been admitted in federal matters, the federal
13 rule differs -- 803(8) differs in South Carolina
14 from the federal rule. The subsection in the
15 federal rule that has been used by a few federal
16 courts, not all, to allow the admissibility of
17 press releases like this does not exist in the
18 state rule. And, therefore, there is no exception
19 to the hearsay rule in South Carolina, under which
20 these would be used.

21 THE COURT: All right. So, actually, Exhibit
22 Number 1, you object not admissible under the
23 rules of evidence?

24 MR. WERNER: Well, yes. And then, secondly,
25 we also would object, again, as we've moved in --

1 in limine, this does not relate to the party in
2 this case, I guess you want to say the defendant,
3 the Plaintiff, of Balfour Beatty Construction,
4 LLC. You can see, from the face of it, it relates
5 to an entity known as Balfour Beatty Communities,
6 which is not the same. And there's no foundation
7 to suggest that they are the same or have
8 sufficient nexus of money.

9 THE COURT: Okay. You will be heard on that.

10 MR. BUNDY: Well, Your Honor, there are other
11 exceptions of the hearsay rule. You can let
12 things in just that you find their credibility is
13 adequate to give you assistance in arriving at
14 your decision about punitive damage. I think you
15 have broad discretion with regard to the documents
16 themselves. The documents speak for themselves
17 and it is your determination as to whether or not
18 simply these corporations, by having single
19 purpose entities, can go out and just commit fraud
20 willy-nilly and hide behind the corporate shield.
21 It's interesting they, on the one hand, hide
22 behind the corporate shield and yet then use it as
23 a sword to say, well, these are individuals who do
24 all these bad things, not the corporation. Well
25 the corporation is the legal fiction for which

1 they're responsible. They're all interrelated.
2 But, again, this is entirely up to you for your
3 consideration. You may find it to be completely
4 irrelevant. We believe it to be highly relevant
5 within the context of a punitive damage here.

6 THE COURT: Okay. All right. So, in
7 particular, as it relates to this particular
8 document that you have propounded -- I'm looking
9 at this --

10 MR. BUNDY: Yes, sir.

11 THE COURT: -- it's dated December 22 of '21,
12 which was right about the time we were -- finished
13 up this trial in particular what does it -- what
14 does it relate to? Who is this? It says Balfour
15 Beatty Communities.

16 MR. WERNER: This is a False Claim Act
17 settlement and basically what they do is is they
18 were inflating their claim for damages, making
19 false claims for repair work, inflating change
20 orders, and doing that kind of thing. The same
21 thing you do in the hotel's interest.

22 MR. BUNDY: That's not what it says, Judge.
23 That's not what it says.

24 THE COURT: All right. All right. Well, I'm
25 going to allow it for now on the basis that I'm

1 going to look at it and take a look at it and see
2 if we can get it. I think it's admissible. It
3 may not be applicable, but -- or at least it's
4 admissible.

5 MR. BUNDY: Right. And that's really what
6 I'm simply doing, is bringing --

7 THE COURT: Right.

8 MR. BUNDY: -- these things to your
9 attention, for whatever they're worth, okay? But
10 a couple of these things are very informative,
11 particularly the plea agreement, which involved
12 Balfour Beatty Communities, okay. If you look at
13 the one -- once you have a chance to read these, I
14 think you'll understand that there is, in fact, a
15 nexus here.

16 THE COURT: Okay.

17 MR. BUNDY: Thank you, Your Honor. Exhibit 2
18 -- sorry, I didn't know what Exhibit 2 was. There
19 we go, two. Exhibit 2 is entitled to -- entitled
20 Department of Justice. Foreign and U.S.
21 government, nearly \$25 million for inflating
22 claims made to Amtrak, and that's 2005. And that
23 relates to, again, claiming for work that was not
24 done and making claims that aren't true. They
25 were false.

1 MR. WERNER: Same objections, although in
2 this case the additional objection is that there
3 is clearly no temporal relationship, which the law
4 is quite clear, there must be. 2005 and 2019,
5 '20, or '21 do not relate, Judge.

6 THE COURT: Okay.

7 MR. BUNDY: The only other thing I would add,
8 Your Honor, is apparently there's not enough money
9 that you can penalize these people to make them
10 quit.

11 THE COURT: Okay. It's also under the False
12 Claims Act, right?

13 MR. BUNDY: Thank you.

14 THE COURT: That relates to Amtrak?

15 MR. BUNDY: Defendant's Exhibit 3 is an
16 information filed in the United States of America
17 vs. Balfour Beatty Communities.

18 MR. WERNER: Same objections, Your Honor.

19 MR. BUNDY: Exhibit Number 4 is a plea
20 agreement.

21 THE COURT: Is this -- does this relate to
22 the, what was it, Exhibit Number 1?

23 MR. BUNDY: There are two, there's a -- there
24 are two different -- one happened in 2005. It
25 related to all these Air Force communities they

1 were supposed to be servicing, and that was the
2 bigger crime, I guess.

3 THE COURT: Okay.

4 MR. BUNDY: And then the other one was the
5 conspiracy on the Amtrak. And the last one is
6 Exhibit 4, entitled Plea Agreement. And that's
7 the end of these types of documents.

8 MR. WERNER: Same objection, Your Honor.

9 THE COURT: The last two documents are dated
10 the same as the press release, December 21 of '21,
11 correct?

12 MR. BUNDY: I think so.

13 THE COURT: Timing-wise, they're right --

14 MR. BUNDY: Exhibit 2 is Balfour Beatty, LLC.
15 It's the same company.

16 MR. WERNER: And that's not correct, Judge.
17 None of these -- on their face, none of these
18 relate to the same company.

19 THE COURT: All right.

20 MR. BUNDY: All right, Your Honor, that's all
21 I have on that. Those exhibits just speak for
22 themselves. They're worth whatever they're worth.
23 I just want to bring them to your attention.

24 THE COURT: All right. All right. Just one
25 second.

1 MR. BUNDY: If y'all are ready to call a
2 witness -- if you're ready, let me know.

3 THE COURT: Yeah, just one second.

4 MR. BUNDY: Sure.

5 THE COURT: That was what I was gonna ask
6 you. On item number two, I assume you got that in
7 front of you. It talks about a false claim to
8 that case. This is the one that's back from
9 October 2005. It clearly says Balfour Beatty
10 Construction. Is that a separate entity?

11 MR. WERNER: It is, Your Honor. It's not
12 Balfour Beatty Construction, LLC. They're not the
13 same.

14 THE COURT: Okay. A precursor or just
15 totally different company?

16 MR. WERNER: Different companies, Judge, do
17 different things.

18 THE COURT: There's also Balfour Beatty, PLC.
19 Is that the parent corporation?

20 MR. WERNER: That's the British company, I
21 understand.

22 THE COURT: Okay. All right. Okay. And
23 then the other two documents, 3 and 4 -- case
24 number -- I see a case number on item number 4.

25 MR. WERNER: Criminal case number on Exhibit

1 4, 21-CR-742.

2 THE COURT: Correct. Criminal case number.
3 And I believe the other one, looks like 3 maybe as
4 well. And it says it's under seal. This is
5 information and the plea agreement commensurate
6 with the same case.

7 MR. BUNDY: Yes, sir.

8 THE COURT: Right?

9 MR. BUNDY: Yes, sir.

10 THE COURT: And that gets into the same
11 discussion about item number 1. Those are clearly
12 related; are they not?

13 MR. BUNDY: Yes, your honor. I just think
14 they tend to explain each other and it gives you a
15 feel for the underlying people involved in what
16 they were doing, that's all.

17 THE COURT: All right. All right. Well, I'm
18 going to find Exhibits 1, 3, and 4 clearly
19 admissible and relevant. Number 5, I will hold on
20 that for now, okay?

21 MR. BUNDY: All right. Thank you.

22 THE COURT: Just so you're clear. All right.
23 Do you want to call your witness?

24 MR. BUNDY: Yes, sir, Micheal Bennitt.

25 THE COURT: Hi, Mr. Bennitt. Let's go around

Plaintiff Balfour Beatty's Trial Exhibit # 3

RFI #	Subject	RFI Date	Due from A/E	Rcvd from A/E	Days Held	Days Overdue	Status
0001	Pile Design Load	3/24/2015	3/31/2015	3/24/2015	0		Closed
0002	Grease Trap and Vault Support	3/26/2015	4/2/2015	3/26/2015	0		Closed
0003	Termite Treatment Below Water Table	3/26/2015	4/2/2015	3/26/2015	0		Closed
0004	Vapor Barrier and Waterproof Barrier	3/26/2015	4/2/2015	3/30/2015	4		Closed
0005	Stone Connection at Walls	3/26/2015	4/2/2015	3/31/2015	5		Closed
0006	Construction Logistics Plan	3/30/2015	4/6/2015	4/6/2015	7		Closed
0007	Sheet Pile Brace Spacing	3/30/2015	4/6/2015	3/31/2015	1		Closed
0008	Pile Application and Uplift	3/30/2015	4/6/2015	3/31/2015	1		Closed
0009	Guest Room Entry Door Frames	3/30/2015	4/7/2015	4/8/2015	9	1	Closed
0010	Fire Protection Secondary Supply	3/31/2015	4/7/2015	4/6/2015	6		Closed
0011	Concrete Finish Level	4/1/2015	4/8/2015	4/6/2015	5		Closed
0012	Sheet Pile Bracing Deadman Anchors	4/8/2015	4/13/2015	4/9/2015	3		Closed
0013	Grout at Pile Dowels	4/15/2015	4/22/2015	4/15/2015	0		Closed
0014	Test Pile Locations	4/20/2015	4/27/2015	4/21/2015	1		Closed
0015	Rebar at PT Slab to Capping Beam Connection	4/20/2015	4/27/2015	4/21/2015	1		Closed
0016	Sheet Pile Brace Spacing with Dewatering	4/20/2015	4/27/2015	4/23/2015	3		Closed
0017	Sloped Concrete Slabs at Guestroom Showers	4/28/2015	5/5/2015	5/6/2015	8	1	Closed
0018	Waterstop at Slab to Capping Beam Connection	4/28/2015	5/5/2015	4/29/2015	1		Closed
0019	Section at Garage Ramp	4/29/2015	5/6/2015	5/6/2015	7		Closed
0020	Slab Edge at Ground Level	4/29/2015	5/6/2015	5/6/2015	7		Closed
0021	Mirrored Ceiling at Camilla's Lounge	5/6/2015	5/13/2015	9/15/2015	132	125	Closed
0022	Crane Pile Cap and Location	5/11/2015	5/18/2015	5/20/2015	9	2	Closed
0023	Fire Pump Sizing	5/13/2015	5/20/2015	5/14/2015	1		Closed
0024	Unit Shower Curb Floor Detail	5/20/2015	5/27/2015	6/16/2015	27	20	Closed
0025	IBC Code	5/21/2015	5/28/2015	5/28/2015	7		Closed
0026	Pile to Grade Beam Connection	5/28/2015	6/5/2015	6/4/2015	6		Closed
0027	Permanent Transformer Pad	6/3/2015	6/10/2015	6/4/2015	1		Closed
0028	Cold Formed Metal Framing Delegated Design	6/11/2015	6/18/2015	6/18/2015	5		Closed
0029	Permanent Generator	6/11/2015	6/18/2015	6/22/2015	11	4	Closed
0030	Combined Electrical Panels and Transformers	6/11/2015	6/18/2015	6/12/2015	1		Closed
0031	Construction Joint at Grade Beams and Pile Caps	6/12/2015	6/19/2015	6/22/2015	10	3	Closed
0032	Columns 3, 4, 9, and 15	6/12/2015	6/19/2015	6/23/2015	11	4	Closed
0033	Precast Concrete Pile Blow Count	6/19/2015	6/26/2015	6/22/2015	3		Closed
0034	Ramp Slope	6/19/2015	6/26/2015	6/24/2015	5		Closed
0035	Slab Thickness at Drains	6/19/2015	6/26/2015	6/23/2015	4		Closed
0036	Horizontal Construction Joint in Grade Beams and Girders	6/19/2015	6/26/2015	7/1/2015	12	5	Closed
0037	Doors in Curved Walls	6/22/2015	6/29/2015	7/1/2015	9	2	Closed
0038	Footings and Pile Cap Locations	6/22/2015	6/29/2015	6/24/2015	2		Closed
0039	Sheet Pile Bracing Attachment	6/23/2015	6/30/2015	6/24/2015	1		Closed
0040	Dirt Wedge Support at Sheet Piles	7/1/2015	7/8/2015	7/2/2015	1		Closed
0041	Grade Beam Reinforcing at Pile Cap	7/1/2015	7/8/2015	7/2/2015	1		Closed
0042	Placing Boom Blockout	7/1/2015	7/8/2015	7/2/2015	1		Closed
0043	Sheet Pile Bracing Bottom Plate	7/1/2015	7/8/2015	7/2/2015	1		Closed
0044	Concrete Brick to Support Rebar	7/1/2015	7/8/2015	7/2/2015	1		Closed
0045	Supp Instructions 08 Pile Length	7/2/2015	7/9/2015	7/2/2015	0		Closed
0046	Sub Level Architectural and Structural Coordination	7/2/2015	7/9/2015	7/28/2015	26	19	Closed
0047	Underground Plumbing Coordination	7/2/2015	7/9/2015	7/14/2015	12	5	Closed
0048	Grease Trap Sizing	7/2/2015	7/9/2015	7/30/2015	28	21	Closed
0049	Data and Communications Routing	7/2/2015	7/9/2015	8/7/2015	36	29	Closed
0050	Sheet Pile and Underground Electrical Vault Conflict	7/2/2015	7/9/2015	8/4/2015	33	26	Closed
0051	Replacement Piles for #2032 and #2038	7/2/2015	7/9/2015	7/6/2015	4		Closed
0052	Guestroom Separation Wall	7/14/2015	7/21/2015	7/21/2015	7		Closed
0053	Concrete Wall Locations	7/14/2015	7/21/2015	7/22/2015	8	1	Closed
0054	Shaftwall at Elevators 1-4	7/14/2015	7/21/2015	7/21/2015	7		Closed
0055	Section Cuts on Sub Level	7/17/2015	7/24/2015	7/29/2015	12	5	Closed
0056	Elevator 5 Pit Fill	7/17/2015	7/24/2015	7/21/2015	4		Closed
0057	Entry Structural Details	7/17/2015	7/24/2015	7/22/2015	5		Closed
0058	Column and Wall Pours on SOG	7/17/2015	7/24/2015	7/21/2015	4		Closed
0059	54" Pipe Material	7/21/2015	7/28/2015	7/22/2015	1		Closed
0060	Stair 3 Door Sizing on First Floor	7/23/2015	7/30/2015	7/29/2015	6		Closed
0061	Exterior Column Wall Type	7/23/2015	7/30/2015	8/4/2015	12	5	Closed
0062	Folding Door Between Lobby and Bar	7/23/2015	7/30/2015	7/28/2015	5		Closed
0063	Wall Types on First Floor NW	7/23/2015	7/30/2015	7/29/2015	6		Closed
0064	Type G Windows in Locker Rooms	7/23/2015	7/30/2015	8/4/2015	12	5	Closed
0065	Sump Pit for Elevator 6	7/27/2015	8/3/2015	7/28/2015	1		Closed
0066	Sub Level and First Floor Low Voltage	7/28/2015	8/4/2015	8/4/2015	7		Closed
0067	Drains at Level 1 Slab	7/29/2015	8/5/2015	7/30/2015	1		Closed
0068	CMU Exterior Wall Thicknesses	7/29/2015	8/5/2015	7/30/2015	1		Closed
0069	Stair 3 Exterior Wall Thickness	7/29/2015	8/5/2015	7/30/2015	1		Closed
0070	Double Lavatory in the Model Room	7/29/2015	8/5/2015	8/13/2015	15	8	Closed
0071	Generator Emergency Power	7/29/2015	8/5/2015	8/10/2015	12	5	Closed
0072	Grease Waste in Sub Level	7/29/2015	8/5/2015	8/12/2015	14	7	Closed
0073	Pile Locations for SI08	7/30/2015	8/6/2015	7/30/2015	0		Closed
0074	Building Stucco Colors	7/30/2015	8/6/2015	8/25/2015	26	19	Closed
0075	Sheet Piling System with Dewatering	7/30/2015	8/6/2015	7/30/2015	0		Closed
0076	Equipment Weight Limit Near Sheet Pile	7/30/2015	8/19/2015	9/15/2015	47	27	Closed
0077	Pipe Bracing Damage	7/30/2015	8/6/2015	8/3/2015	4		Closed
0078	Sheet Pile Welding	7/30/2015	8/6/2015	8/3/2015	4		Closed
0079	Drain Clarification at Col. 39 (C-F)	8/3/2015	8/10/2015	8/4/2015	1		Closed
0080	Cap Beam at Proposed Angled Sheet Pile Corner	8/4/2015	8/11/2015	8/13/2015	9	2	Closed
0081	Sub Level Pump and Electrical Rooms	8/4/2015	8/20/2015	8/25/2015	21	5	Closed
0082	Dewatering Duration	8/4/2015	8/11/2015	8/7/2015	3		Closed
0083	Finish Hardware Questions	8/5/2015	8/13/2015	9/29/2015	54	47	Closed
0084	Sub-Level Storm Drain	8/10/2015	8/17/2015	8/25/2015	15	8	Closed
0085	Sump Elevations	8/10/2015	8/17/2015	8/13/2015	3		Closed
0086	Floor Slab Elevations	8/10/2015	8/17/2015	8/10/2015	0		Closed
0087	CAD Column Sizing	8/10/2015	8/17/2015	8/13/2015	3		Closed
0088	Capping Beam Durability	8/11/2015	8/18/2015	8/13/2015	2		Closed
0090	Car Lift Clearance	8/11/2015	8/18/2015	8/25/2015	14	7	Closed
0091	Duct in Sub Level Pump Room	8/11/2015	8/18/2015	8/25/2015	14	7	Closed
0092	Duct in Wall on Sub Level	8/11/2015	8/18/2015	8/17/2015	6		Closed
0093	Floor Troughs	8/11/2015	8/18/2015	8/18/2015	7		Closed
0094	Structural Grout to Prime Pump	8/13/2015	8/20/2015	8/13/2015	0		Closed
0095	Exterior Mockup Structural Design	8/17/2015	8/24/2015	8/24/2015	7		Closed
0096	Insulating Storefront Doors	8/17/2015	8/24/2015	8/18/2015	1		Closed
0097	Sheet Pile Embedment Depth	8/17/2015	8/24/2015	8/18/2015	1		Closed
0098	Sheet Pile Corner C Layout	8/18/2015	8/25/2015	8/18/2015	0		Closed

0099	Public Restroom Mirrors	8/18/2015	8/25/2015	8/25/2015	7		Closed
0100	Exterior Mockup Location	8/18/2015	8/25/2015	8/25/2015	7		Closed
0101	Type G Door Fire Rating	8/18/2015	8/25/2015	8/18/2015	0		Closed
0102	Sound Isolation Hanger Location	8/18/2015	8/25/2015	8/18/2015	0		Closed
0103	Hopes Insulated Glass	8/18/2015	8/25/2015	9/28/2015	41	34	Closed
0104	Support for Louvers at the Roof	8/18/2015	8/25/2015	8/25/2015	7		Closed
0105	Fire Protection Secondary Supply Storage	8/18/2015	8/25/2015	11/20/2015	94	87	Closed
0106	Third Floor CAD vs Plumbing Drawing	8/19/2015	8/26/2015	8/31/2015	12	5	Closed
0107	South End Hip Roof Slopes	8/20/2015	8/27/2015	8/24/2015	4		Closed
0108	Grease Waste Clarification	8/20/2015	8/27/2015	8/20/2015	0		Closed
0109	Grease Vent Routing	8/20/2015	8/27/2015	8/20/2015	0		Closed
0110	Scissor Joist Detail	8/20/2015	8/27/2015	8/25/2015	5		Closed
0111	6th Floor Fixture Drain Conflict	9/28/2015	10/5/2015	12/3/2015	66	59	Closed
0112	Step Down at CMU Wall	8/27/2015	8/28/2015	8/28/2015	1		Closed
0113	Sheet Pile Corner D Layout	8/25/2015	9/1/2015	8/25/2015	0		Closed
0114	Model Room Window Clarification	8/25/2015	9/1/2015	8/31/2015	6		Closed
0115	Second Floor Perimeter PTBs	8/25/2015	9/1/2015	8/27/2015	2		Closed
0116	Proposed Fire Pump Room Location	8/26/2015	9/22/2015	10/20/2015	55	48	Closed
0117	Columns C-25 and C-30	8/28/2015	9/22/2015	8/27/2015	1		Closed
0118	Post Tension Slab Embed Depth	8/28/2015	9/22/2015	8/27/2015	1		Closed
0119	Capping Beam on Hudson Street Side	8/28/2015	9/22/2015	8/27/2015	1		Closed
0120	Capping Beam Elevation	8/27/2015	9/3/2015	8/28/2015	1		Closed
0121	Sub-Level Sanitary Waste and Vent Questions	8/27/2015	9/3/2015	9/28/2015	33	26	Closed
0122	Cap Beam Step Down Sketch	8/28/2015	9/4/2015	8/31/2015	3		Closed
0123	Sleeve through Cap Beam and Sheet Pile	9/1/2015	9/8/2015	9/1/2015	0		Closed
0124	Mockup Room Pocket Door Clarification	9/1/2015	9/8/2015	9/1/2015	0		Closed
0125	Sheet Pile Corner A Layout	9/1/2015	9/8/2015	9/1/2015	0		Closed
0126	Capping Beam on Marion Street Side	9/1/2015	9/8/2015	9/1/2015	0		Closed
0127	Capping Beam Concrete PSI	9/1/2015	9/8/2015	9/2/2015	1		Closed
0128	Cast Stone vs Plant Precast	9/2/2015	9/9/2015	9/9/2015	7		Closed
0129	Light at Guestroom Doorway Clarification	9/2/2015	9/9/2015	9/15/2015	13	6	Closed
0130	Pile Cap and Grade Beam Conflict	8/2/2015	9/9/2015	9/3/2015	1		Closed
0131	CMU Building Corner at King and Hutson	9/2/2015	9/9/2015	9/10/2015	8	1	Closed
0133	Revised Sheet Pile Corner A	9/9/2015	9/16/2015	9/10/2015	1		Closed
0134	Sheet Pile and Cap Beam Waterproofing Detail	9/11/2015	9/18/2015	9/15/2015	4		Closed
0135	ID Material Selections	9/11/2015	9/18/2015	10/1/2015	20	13	Closed
0138	Overhead Beam at Garage Door Beam	9/11/2015	9/18/2015	9/15/2015	4		Closed
0137	GG Light Fixtures	9/11/2015	9/18/2015	9/15/2015	4		Closed
0138	Fireman's Phone	9/11/2015	9/18/2015	10/23/2015	42	35	Closed
0139	Dishwater Hot Water	9/11/2015	9/18/2015	11/9/2015	59	52	Closed
0140	Cap Beam Along King Street	9/15/2015	9/22/2015	9/15/2015	0		Closed
0141	Elevator Finishes	9/15/2015	9/22/2015	10/5/2015	20	13	Closed
0142	Third Floor Beams SB-4, SB-5	9/15/2015	9/22/2015	9/16/2015	1		Closed
0143	Exterior Mockup Window Size	9/15/2015	9/22/2015	9/16/2015	1		Closed
0144	MCC RFI 16 - Storm Drain Sizing	9/16/2015	9/23/2015	9/18/2015	2		Closed
0145	MCC RFI 17 Storm Drain Sizing	9/16/2015	9/23/2015	9/23/2015	7		Closed
0147	Electrical Room Egress	9/16/2015	9/23/2015	9/23/2015	7		Closed
0148	Cap Beam to Slab Connection along King	9/16/2015	9/23/2015	9/18/2015	2		Closed
0149	Roof Truss Revisions Clarifications	9/16/2015	9/23/2015	10/23/2015	37	30	Closed
0150	Laundry Area Duct Sizing	9/16/2015	9/23/2015	9/18/2015	2		Closed
0151	Light at Guestroom Doorway Alternative	9/17/2015	9/24/2015	9/29/2015	12	5	Closed
0152	Capping Beam to Column Connection	9/17/2015	9/24/2015	9/18/2015	1		Closed
0153	Capping Beam at ATT Vault Detail	9/21/2015	9/28/2015	9/28/2015	7		Closed
0154	Three Wire Dimming	9/21/2015	9/28/2015	9/23/2015	2		Closed
0155	Steel Pipe in Mechanical Vault	9/22/2015	9/29/2015	10/19/2015	27	20	Closed
0156	Expanded Room Clarifications	9/23/2015	9/30/2015	9/28/2015	5		Closed
0157	Feasible Window Criteria	9/24/2015	10/1/2015	9/28/2015	4		Closed
0158	Beam Verification - 7th & 8th Floors	9/24/2015	10/1/2015	9/28/2015	4		Closed
0159	MOD-1 Dome Questions	9/28/2015	10/5/2015	9/29/2015	1		Closed
0160	Plumbing Fixture Designations	9/28/2015	10/5/2015	10/15/2015	17	10	Closed
0161	PT Beams 1PTB11 & 1PTB9	9/28/2015	10/5/2015	9/29/2015	1		Closed
0162	Elevator Cab Walls	9/29/2015	10/6/2015	9/29/2015	0		Closed
0163	Mechanical Airway Waterproofing	9/30/2015	10/7/2015	10/19/2015	19	12	Closed
0165	Mani Pede Accent Light	9/30/2015	10/7/2015	10/20/2015	20	13	Closed
0166	Manager's Apartment Stair	9/30/2015	10/7/2015	10/5/2015	5		Closed
0167	MOD 1 Lighting Deletions	9/30/2015	10/7/2015	10/20/2015	20	13	Closed
0168	Owner Furnished Light Fixtures	10/1/2015	10/8/2015	12/3/2015	63	56	Closed
0169	Rooftop Gutter Downspouts & Nanawall Drain Connections	10/2/2015	10/9/2015	2/29/2016	150	143	Closed
0170	Pile Cap Braces	10/2/2015	10/9/2015	10/5/2015	3		Closed
0171	Outlets & Boxes Submittal Clarifications	10/5/2015	10/12/2015	11/5/2015	31	24	Closed
0172	MOD-1 Storm Drain Sizes	10/5/2015	10/12/2015	10/19/2015	14	7	Closed
0173	MOD-1 Linear Lights	10/6/2015	10/13/2015	10/19/2015	13	6	Closed
0174	MOD-1 2nd Floor Sconces	10/6/2015	10/13/2015	10/19/2015	13	6	Closed
0175	Underground Storm Piping	10/8/2015	10/15/2015	10/12/2015	4		Closed
0176	Blocking for CMU/Slab Interface	10/8/2015	10/15/2015	10/12/2015	4		Closed
0177	Mechanical Shaft to Vault Pipe	10/9/2015	10/16/2015	10/12/2015	3		Closed
0178	Concrete Pile Embedment Depth	10/12/2015	10/19/2015	10/12/2015	0		Closed
0179	Low Overhead Clearance on Elevators 1-4	10/12/2015	10/19/2015	10/12/2015	0		Closed
0180	Kitchen Layout	10/12/2015	10/19/2015	10/20/2015	8	1	Closed
0181	Shower Pan Slope	10/12/2015	10/19/2015	10/13/2015	1		Closed
0182	P-2 Pile Cap at Angled Capping Beam	10/13/2015	10/20/2015	11/19/2016	98	91	Closed
0183	Kitchen 243 Layout	10/13/2015	10/20/2015	10/13/2015	0		Closed
0185	Elevator Rail Bracket Support	10/13/2015	10/20/2015	12/7/2015	55	48	Closed
0188	Elevator Flush Transom Design	10/19/2015	10/26/2015	10/20/2015	1		Closed
0189	1st Floor PT Shop Drawing Clarifications	10/19/2015	10/26/2015	10/20/2015	1		Closed
0190	Broken Pile Tops	10/20/2015	10/27/2015	10/21/2015	1		Closed
0191	Generator Enclosure	10/20/2015	10/27/2015	10/20/2015	0		Closed
0192	Security Conduit Raceway	10/20/2015	10/27/2015	10/21/2015	1		Closed
0193	Tower Crane Embedment	10/21/2015	10/28/2015	10/21/2015	0		Closed
0194	Beam 2PTB-1 Size and Slab Fold at Exterior Wall	10/21/2015	10/28/2015	10/21/2015	0		Closed
0195	Control Joint Between Column Lines B36-39/C36-39	10/21/2015	10/28/2015	10/21/2015	0		Closed
0196	Hopes Window Mullions	10/21/2015	10/28/2015	10/23/2015	2		Closed
0197	Domestic Water Risers & Branch Lines	10/21/2015	10/28/2015	10/26/2015	5		Closed
0198	Lighting Controls	10/22/2015	10/29/2015	12/1/2015	40	33	Closed
0200	1st Floor Rebar Questions	10/28/2015	11/4/2015	11/10/2015	13	6	Closed
0201	CC2 & CC3 Light Fixtures	10/28/2015	11/4/2015	11/16/2015	19	12	Closed
0202	Area Way Detail Clarification	11/3/2015	11/10/2015	11/3/2015	0		Closed
0203	2nd Floor Post-Tension Questions	11/3/2015	11/10/2015	11/4/2015	1		Closed
0204	Exterior Mockup Storefront Question	11/4/2015	11/11/2015	11/4/2015	0		Closed

0205	Mockup Guestroom Sink	11/4/2015	11/11/2015	11/6/2015	2		Closed
0206	Canilever Walkway Detail Discrepancy	11/5/2015	11/12/2015	12/3/2015	28	21	Closed
0207	Elevator #6 Dimensions	11/5/2015	11/12/2015	11/6/2015	1		Closed
0208	Mock Up Plumbing Fixtures	11/5/2015	11/12/2015	11/5/2015	0		Closed
0209	Miscellaneous Rebar Questions	11/5/2015	11/12/2015	11/16/2015	11	4	Closed
0210	Elevator #5 Slab Dowels	11/5/2015	11/16/2015	11/6/2015	1		Closed
0211	Mechanical Platform and Column C-18	11/6/2015	11/13/2015	11/16/2015	10	3	Closed
0212	In Slab Lighting	11/6/2015	11/13/2015	11/9/2015	3		Closed
0213	Concrete Protection for Waterproofing	11/6/2015	11/13/2015	11/9/2015	3		Closed
0214	Fixed Shutters at Covered Windows	11/9/2015	11/16/2015	6/23/2016	227	220	Closed
0215	Booster Heater Electrical Information	11/9/2015	11/16/2015	11/9/2015	0		Closed
0217	Model Room Vanity Shop Drawings	11/9/2015	11/16/2015	11/10/2015	1		Closed
0218	Model Room Revision 5	11/9/2015	11/16/2015	11/11/2015	2		Closed
0219	Model Room King Bathroom Second Pocket Door	11/10/2015	11/17/2015	11/10/2015	0		Closed
0220	Plumbing Coordination from BIM 11.04.15	11/10/2015	11/17/2015	12/1/2015	21	14	Closed
0221	Pile Cap, Grade Beam, and Grade Girders Dimensions	11/10/2015	11/17/2015	11/11/2015	1		Closed
0222	ST-2 and ST-11 Material Selections	11/11/2015	11/18/2015	12/14/2015	33	26	Closed
0223	Roof Truss Section Cuts	11/13/2015	11/20/2015	12/1/2015	18	11	Closed
0224	Alternate Wall Type C4	11/13/2015	11/20/2015	11/20/2015	7		Closed
0225	Pile Cap Dowel Epoxy	11/13/2015	11/20/2015	11/16/2015	3		Closed
0226	Crane & Mat Foundations Hook Bars	11/13/2015	11/20/2015	11/16/2015	3		Closed
0227	Washer Pad	11/16/2015	11/23/2015	11/23/2015	7		Closed
0228	Shutter Vertical Side Sill Width & Wind Load Capacity	11/17/2015	11/24/2015		1,183	1,176	Open
0229	Drapery Control Switch Locations	11/17/2015	11/24/2015	11/23/2015	6		Closed
0230	Television Mounting Heights	11/17/2015	11/24/2015	11/25/2015	8	1	Closed
0231	Concrete Pile As-built Locations	11/17/2015	11/24/2015	11/19/2015	2		Closed
0232	Makeup Mirror Controls	11/17/2015	11/24/2015	11/20/2015	3		Closed
0233	Waterproofing Concrete Cover in Pile Caps	11/18/2015	11/25/2015	11/18/2015	0		Closed
0234	Concrete Finish under Flooding	11/20/2015	11/27/2015	11/20/2015	0		Closed
0235	Floor Slope to Drains	11/20/2015	11/27/2015	12/1/2015	11	4	Closed
0237	Continuous Top Bar Pthrough Pile Cap	11/23/2015	11/30/2015	11/24/2015	1		Closed
0238	Kitchen Equipment - 1st Floor Freezer	11/24/2015	12/1/2015	12/3/2015	9	2	Closed
0239	Mechanical Platform Door 299B	11/24/2015	12/1/2015	11/30/2015	6		Closed
0240	Model Room Material Selections	11/25/2015	12/2/2015	12/1/2015	6		Closed
0241	RFI-0237 Response Questions	12/1/2015	12/8/2015	12/3/2015	2		Closed
0242	1st Floor Upper Crust Ceiling	12/1/2015	12/8/2015	12/1/2015	0		Closed
0243	Model Room Lift Clothing Rods	12/2/2015	12/9/2015	12/15/2015	13	6	Closed
0244	HFCU Breaker Sizes	12/2/2015	12/9/2015	12/3/2015	1		Closed
0245	Shutter Louvers	12/3/2015	12/10/2015	12/3/2015	0		Closed
0246	LAB Type Fixture Color & Voltage	12/4/2015	12/11/2015	12/15/2015	11	4	Closed
0247	Mechanical Platform Piping	12/7/2015	12/14/2015	12/28/2015	21	14	Closed
0248	12/4 BIM Coordination Meeting Questions	12/7/2015	12/14/2015	12/28/2015	21	14	Closed
0249	Mechanical Platform Storage Tanks	12/7/2015	12/14/2015	12/28/2015	21	14	Closed
0250	4" Sanitary Waste Line	12/7/2015	12/14/2015	12/28/2015	21	14	Closed
0251	2" Waste Line at Elevator 5 Shear Wall	12/7/2015	12/14/2015	12/29/2015	22	15	Closed
0252	2" Waste Line at Stair Tower 6 Shear Wall	12/7/2015	12/14/2015	12/29/2015	22	15	Closed
0253	Canopy Roof Drains	12/7/2015	12/14/2015	12/29/2015	22	15	Closed
0254	Waste Pipe at the Rotunda Ceiling	12/7/2015	12/14/2015	12/29/2015	22	15	Closed
0255	Waste Pipe Missing in Room 115B	12/7/2015	12/14/2015	12/29/2015	22	15	Closed
0256	Storm Drain and Wall Size	12/7/2015	12/14/2015	12/29/2015	22	15	Closed
0257	Level 02 Wall Sizes	12/7/2015	12/14/2015	12/29/2015	22	15	Closed
0258	Waste Pipe Conflict at Level 01 Exterior Wall	12/7/2015	12/14/2015	12/29/2015	22	15	Closed
0259	Barn Door Openings - Mock Up	12/8/2015	12/15/2015	12/14/2015	6		Closed
0260	Tie Behind Vanities	12/8/2015	12/15/2015	12/9/2015	1		Closed
0261	Barn Door Jamb Detail - Mock Up Only	12/8/2015	12/15/2015	12/11/2015	3		Closed
0262	Interior Mockup 8th Floor Window	12/8/2015	12/15/2015	12/10/2015	2		Closed
0263	Guest Corridor Ceiling Panel Soft Cavity	12/8/2015	12/15/2015	1/11/2016	34	27	Closed
0264	Precast Questions	12/9/2015	12/16/2015	1/25/2016	47	40	Closed
0265	Grand Stair Landing Mirrors	12/10/2015	12/17/2015	12/15/2015	5		Closed
0268	Additional Roof Truss Section Cut	12/10/2015	12/17/2015	12/14/2015	4		Closed
0267	Model Room Wood Casing At Windows	12/10/2015	12/17/2015	12/15/2015	5		Closed
0268	Pool Weight Clarification	12/10/2015	12/17/2015	12/11/2015	1		Closed
0269	Lutron Driver & ICO Fixture Compatibility	12/10/2015	12/17/2015	12/15/2015	5		Closed
0270	Amerlux Fixture Cans	12/10/2015	12/17/2015	1/21/2016	42	35	Closed
0271	Storm Pipe Relocation for Mechanical Vault	12/11/2015	12/18/2015	1/8/2016	28	21	Closed
0272	Updated Pile Locations	12/14/2015	12/21/2015	12/15/2015	1		Closed
0273	1st Floor Rain Leader Pipe Size	12/14/2015	12/21/2015	12/15/2015	1		Closed
0274	Canilever Walkway Structural Detail	12/14/2015	12/21/2015	1/7/2016	24	17	Closed
0275	Square Solid Interceptor Substitutes	12/16/2015	12/23/2015	1/6/2016	21	14	Closed
0276	Insulation on Sanitary Above Guest Rooms	12/16/2015	12/23/2015	12/30/2015	14	7	Closed
0277	Tub Location	12/16/2015	12/23/2015	12/28/2015	12	5	Closed
0278	King Suite Model Room Lavatory Faucet	12/17/2015	12/24/2015	1/11/2016	25	18	Closed
0279	Car Lift Adjustment	12/17/2015	12/24/2015	12/29/2015	12	5	Closed
0281	Exposed Pipe in Luggage Room 104B	12/17/2015	12/24/2015	1/29/2016	43	36	Closed
0282	Retail Room 107 Ceiling Height	12/17/2015	12/24/2015	12/29/2015	12	5	Closed
0283	Waste Pipe in Upper Crust 115B Ceiling	12/17/2015	12/24/2015	2/22/2016	67	60	Closed
0284	Beverage Conduit in Private Dining Room 146	12/17/2015	12/24/2015	3/3/2016	77	70	Closed
0285	Storm Drain Sizing	12/17/2015	12/24/2015	1/4/2016	18	11	Closed
0286	Missing Riser Locations	12/17/2015	12/24/2015	1/4/2016	18	11	Closed
0287	4" Storm Drain	12/17/2015	12/24/2015	1/4/2016	18	11	Closed
0288	Drop Panel Conflict	12/17/2015	12/24/2015	12/28/2015	11	4	Closed
0289	Shower Pan Thickness	12/17/2015	12/24/2015	1/20/2016	34	27	Closed
0290	Roof Drain Conflict with Beam	12/17/2015	12/24/2015	12/28/2015	11	4	Closed
0291	Storm Riser Furring	12/17/2015	12/24/2015	1/4/2016	18	11	Closed
0292	Shower Drain Conflict	12/17/2015	12/24/2015	12/28/2015	11	4	Closed
0293	Room 503 Ceiling Elevation	12/17/2015	12/24/2015	1/8/2016	22	15	Closed
0294	Wall Furring on 6th Floor for Storm Riser	12/17/2015	12/24/2015	6/15/2016	181	174	Closed
0295	Stair 3 500A Ceiling Elevation	12/17/2015	12/24/2015	1/8/2016	22	15	Closed
0296	Room 505 Ceiling Elevation	12/17/2015	12/24/2015	1/8/2016	22	15	Closed
0297	Room 507 Ceiling Elevation	12/18/2015	12/25/2015	1/8/2016	21	14	Closed
0298	Room 513 Plumbing Conflict	12/18/2015	12/25/2015	6/15/2016	180	173	Closed
0299	Missing Floor Sink - 6th Floor	12/18/2015	12/25/2015	12/28/2015	10	3	Closed
0300	Room 601 - Wall Furring Behind Lave	12/18/2015	12/25/2015	6/15/2016	180	173	Closed
0301	Room 531 Ceiling/635 Tub Location	12/18/2015	12/25/2015	6/15/2016	180	173	Closed
0302	Room 543 Ceiling Elevation	12/18/2015	12/25/2015	6/15/2016	180	173	Closed
0303	5th Floor Ceiling Conflict	12/18/2015	12/25/2015	6/15/2016	180	173	Closed
0304	Stair 4 Ceiling Conflicts	12/18/2015	12/25/2015	6/15/2016	180	173	Closed
0305	Sub Level Parking Slope to Drains	12/22/2015	12/29/2015	12/22/2015	0		Closed
0306	Guestroom Closet Light Fixture	12/22/2015	12/29/2015	12/22/2015	0		Closed

0307	Parking Ramp Thickness	12/28/2015	1/4/2016	12/30/2015	2		Closed
0308	1st Level Ceiling Grease Waste Conflict with Structure	12/29/2015	1/5/2016	1/11/2016	13	6	Closed
0309	Guestroom Closet Door Switch	12/30/2015	1/6/2016	1/12/2016	13	6	Closed
0310	Model Room Vanity-Deck Mounted Faucet	1/4/2016	1/11/2016	1/4/2016	0		Closed
0311	Model Room Closet Door Size	1/4/2016	1/11/2016	1/6/2016	2		Closed
0312	Lighting Fixture Voltage Confirmation	1/4/2016	1/11/2016	1/26/2016	22	15	Closed
0313	1st Floor Upper Crust Slot Diffuser	1/5/2016	1/12/2016	2/22/2016	48	41	Closed
0314	Exterior Door and Ceiling Height Issue at Vestibule 117	1/5/2016	1/12/2016	2/29/2016	55	48	Closed
0316	MF-3 Elevation and GB/GG Termination	1/5/2016	1/13/2016	1/12/2016	6		Closed
0317	Condensate Line for VFCU-27	1/7/2016	1/14/2016	1/20/2016	13	6	Closed
0318	Sump Pit Elevation	1/11/2016	1/18/2016	3/23/2016	72	65	Closed
0319	Schluter Profiles From Submittal	1/11/2016	1/18/2016	1/19/2016	8	1	Closed
0320	Slab/Bearing Dimensions	1/11/2016	1/18/2016	1/14/2016	3		Closed
0321	Gas Riser Diagram	1/12/2016	1/19/2016	1/19/2016	7		Closed
0322	Model Room Shower Door Side Height	1/13/2016	1/20/2016	1/15/2016	2		Closed
0323	Paint Colors	1/13/2016	1/20/2016	9/30/2016	261	254	Closed
0324	Chilled Water Schematics	1/13/2016	1/20/2016	1/20/2016	7		Closed
0325	Pipe In Foyer Ceiling	1/13/2016	1/20/2016	1/20/2016	7		Closed
0326	Trap Primers for Sub-Level Floor Drains	1/14/2016	1/21/2016	1/15/2016	1		Closed
0327	Sleeves in Beams	1/14/2016	1/21/2016	1/26/2016	12	5	Closed
0328	Elevator 6 Rebar Embedment	1/14/2016	1/21/2016	1/14/2016	0		Closed
0329	P-8 Pile Repairs	1/14/2016	1/21/2016	1/14/2016	0		Closed
0330	P-9, P-3, & CB-1 Pile As-Built Locations	1/14/2016	1/21/2016	1/15/2016	1		Closed
0331	Doors 101A, 101B, & 101C Rough Openings	1/15/2016	1/22/2016	1/26/2016	11	4	Closed
0332	GB-3B #1 Rebar	1/18/2016	1/25/2016	1/18/2016	0		Closed
0333	Mosaic Tile Above Stock	1/18/2016	1/25/2016	3/17/2016	59	52	Closed
0334	Domestic Water Line In Foyer	1/18/2016	1/25/2016	1/19/2016	1		Closed
0335	Section Cut in King Bathroom Mockup	1/19/2016	1/26/2016	1/20/2016	1		Closed
0336	Dome Ceiling Diameter	1/19/2016	1/26/2016	2/3/2016	15	8	Closed
0337	P-2, P-3, and P-8 Pile As-Built	1/20/2016	1/27/2016	1/20/2016	0		Closed
0338	Mechanical Platform Equipment & Piping	1/20/2016	1/27/2016	2/3/2016	14	7	Closed
0339	ID-003 Missing P-47	1/20/2016	1/27/2016	3/17/2016	57	50	Closed
0340	MOD3 Gas Pipe Questions	1/21/2016	1/28/2016	3/1/2016	40	33	Closed
0342	Domestic Water Sizing	1/21/2016	1/28/2016	2/3/2016	13	6	Closed
0343	Column C-3 in Pile Cap P-2	1/21/2016	1/28/2016	1/27/2016	8		Closed
0344	Stair 3 and 4 Finishes	1/25/2016	2/1/2016	1/25/2016	0		Closed
0345	GG-7 & GB-2 Intersection	1/26/2016	2/2/2016	1/27/2016	1		Closed
0346	Large Missile Glazing	1/27/2016	2/3/2016	1/30/2016	3		Closed
0347	Model Room Entry Vestibule/Guestroom Transition	1/27/2016	2/3/2016	2/1/2016	5		Closed
0348	Underground Plumbing Piping Soil Compaction	1/27/2016	2/3/2016	5/2/2016	96	89	Closed
0349	Sections 5 & 6 Pile As-Built	1/28/2016	2/4/2016	2/1/2016	4		Closed
0350	Parking Drain Relocation Confirmation	2/1/2016	2/8/2016	2/1/2016	0		Closed
0351	Model Room Shower Doors	2/1/2016	2/8/2016	2/2/2016	1		Closed
0352	Section 5 Grade Beams & Pile Caps	2/1/2016	2/8/2016	2/1/2016	0		Closed
0353	Mosaic in Double Queen Model Room	2/4/2016	2/11/2016	2/4/2016	0		Closed
0354	Model Room Mirror Above Vanity	2/4/2016	2/11/2016	2/16/2016	12	5	Closed
0355	East Wall 1st Floor Beam Above Ramp	2/4/2016	2/11/2016	2/11/2016	7		Closed
0356	Model Room Door Threshold	2/5/2016	2/12/2016	2/9/2016	4		Closed
0357	Guestroom WC Ventilation	2/8/2016	2/15/2016	3/21/2016	42	35	Closed
0358	Flat Roof at Elevators	2/8/2016	2/15/2016	2/9/2016	1		Closed
0359	Mockup Roof Dimensions	2/8/2016	2/15/2016	2/15/2016	7		Closed
0360	Grade Beam at Southeast Corner of Elevator 6	2/8/2016	2/16/2016	2/9/2016	0		Closed
0361	MF-3 Pile As-Built	2/9/2016	2/16/2016	2/9/2016	0		Closed
0362	Pool Deck Jet Cover	2/9/2016	2/16/2016	2/11/2016	2		Closed
0363	Front Desk Power/Data Boxes and Knock Out Sizing	2/9/2016	2/16/2016	2/11/2016	2		Closed
0364	Lighting Control Panel Locations	2/10/2016	2/17/2016	2/29/2016	19	12	Closed
0365	Lights and Diffusers in Restrooms 119 & 121	2/10/2016	2/17/2016	2/11/2016	1		Closed
0366	PVC Jacketed MC Cable & ENT Conduit	2/10/2016	2/17/2016	2/11/2016	1		Closed
0367	Owner Furnished Light Fixture Mounting and Supporting	2/10/2016	2/17/2016	3/28/2016	47	40	Closed
0368	Suspended Elevator Pit Construction Joint	2/10/2016	2/17/2016	2/11/2016	1		Closed
0369	Sublevel Door Access Controls	2/15/2016	2/22/2016	3/14/2016	28	21	Closed
0370	Mockup Tub Filler Location	2/15/2016	2/22/2016	2/22/2016	7		Closed
0371	Mockup Tub Filler Bracing	2/15/2016	2/22/2016	3/7/2016	21	14	Closed
0372	Guardrails at 3rd Floor Balcony	2/15/2016	2/22/2016	2/15/2016	0		Closed
0373	Exterior Egress Lighting	2/15/2016	2/22/2016	3/28/2016	42	35	Closed
0374	Mirrors in Model Room Corridor	2/16/2016	2/23/2016	2/16/2016	0		Closed
0375	King Model Room Vanity Height to Electrical Outlet	2/16/2016	2/23/2016	2/18/2016	2		Closed
0376	King Model Room Night Stand Location	2/16/2016	2/23/2016	2/18/2016	2		Closed
0377	Model King Vanity Top Fit	2/16/2016	2/23/2016	2/18/2016	2		Closed
0378	Model room king bookcase and drapery conflict	2/16/2016	2/23/2016	3/7/2016	20	13	Closed
0379	Model room furniture notched around base	2/16/2016	2/23/2016	2/18/2016	2		Closed
0380	Model room wood base	2/16/2016	2/23/2016	2/18/2016	2		Closed
0381	Model Corridor Entry Door	2/16/2016	2/23/2016	2/19/2016	3		Closed
0382	Condensate Pump for VFCUs	2/17/2016	2/24/2016	2/29/2016	12	5	Closed
0383	Parking Ramp & Car Lift Conflict	2/18/2016	2/25/2016	2/18/2016	0		Closed
0384	Chilled Water Pump Housekeeping Pads	2/20/2016	2/27/2016	2/29/2016	9	2	Closed
0385	Irons in Sublevel	2/20/2016	2/27/2016	2/23/2016	3		Closed
0386	ACT in Luggage Room 104B	2/20/2016	2/27/2016	2/29/2016	9	2	Closed
0387	Model room solid surface conflicts	2/22/2016	2/29/2016	3/2/2016	9	2	Closed
0388	Tub Locations	2/23/2016	3/1/2016	2/23/2016	0		Closed
0389	Xypex Waterproofing Locations	2/24/2016	3/2/2016	2/24/2016	0		Closed
0390	Model Room Wall Panels at King Bath	2/25/2016	3/3/2016	3/10/2016	14	7	Closed
0391	Section 7 Pile As-Built	3/2/2016	3/9/2016	3/8/2016	6		Closed
0392	AV & Security Questions	3/2/2016	3/9/2016	3/19/2016	17	10	Closed
0393	Capping Beam and Column Conflict	3/4/2016	3/11/2016	3/4/2016	0		Closed
0394	Drip Screed at Window Heads	3/4/2016	3/11/2016	6/16/2016	104	97	Closed
0395	Lath at Stucco over CMU	3/4/2016	3/11/2016	3/7/2016	3		Closed
0396	Hot Water Schematic	3/8/2016	3/15/2016	3/10/2016	2		Closed
0397	Maximum Allowable Live Point Loads	3/8/2016	3/15/2016	3/9/2016	1		Closed
0398	Elevator Stirrups	3/9/2016	3/16/2016	3/9/2016	0		Closed
0399	Elevators 1-4 Sump Pit	3/9/2016	3/16/2016	3/10/2016	1		Closed
0400	Exterior Mockup Opening Enlargement	3/11/2016	3/18/2016	3/11/2016	0		Closed
0401	Column C-3 at Column Lines J & 24	3/11/2016	3/18/2016	3/14/2016	3		Closed
0402	Pile 2286 Repair	3/14/2016	3/21/2016	3/16/2016	2		Closed
0403	QQ Window Muntin Detail	3/14/2016	3/21/2016	3/25/2016	11	4	Closed
0404	Section 8 Pile As-Built	3/15/2016	3/22/2016	3/15/2016	0		Closed
0405	Truss Coordination Conference Follow Up	3/15/2016	3/22/2016	5/4/2016	50	43	Closed
0406	Sublevel Column Steel Questions	3/15/2016	3/22/2016	3/16/2016	1		Closed
0407	First Floor Elevated Slab - Floor Sink Slab Penetrations	3/16/2016	3/23/2016	3/17/2016	1		Closed

0408	Elevator 1-4 Drain String	3/16/2016	3/23/2016	3/17/2016	1		Closed
0409	Bedroom Gable End Piece	3/16/2016	3/23/2016	3/30/2016	14	7	Closed
0410	3rd Floor Additional Carolina Lantens	3/17/2016	3/24/2016	6/23/2016	88	91	Closed
0411	Lower Level Overhead Paint	3/18/2016	3/25/2016	4/1/2016	14	7	Closed
0413	Post Tensioned Slab Penetrations at CL B20 and B26	3/21/2016	3/28/2016	3/28/2016	7	0	Closed
0414	Graham Window Sill Flashing	5/23/2016	3/29/2016	6/1/2016	9	64	Closed
0415	Low Voltage Networking Requirements	3/22/2016	3/29/2016	3/23/2016	1		Closed
0418	Pool Chemical Room Light Fixture	3/22/2016	3/29/2016	3/22/2016	0		Closed
0417	MOD 4 Panel RA Relocation	3/22/2016	3/29/2016	5/11/2016	50	43	Closed
0418	Northeast Section Pile As-Built	3/24/2016	3/31/2016	3/25/2016	1		Closed
0419	Geofoam In Elevator Pit #5	3/24/2016	3/31/2016	3/28/2016	4		Closed
0420	Lighting Fixtures LN4, LN5, and LN6	3/28/2016	4/4/2016	4/12/2016	15	8	Closed
0421	1st Floor Slab at Angled Capping Beam	3/28/2016	4/4/2016	3/30/2016	2		Closed
0422	Exterior Mock Up Lantern Location	3/29/2016	4/5/2016	3/28/2016	0		Closed
0423	1st Floor Slab Edge	4/1/2016	4/8/2016	4/1/2016	0		Closed
0424	Slab Edge At South Wall	4/4/2016	4/11/2016	4/4/2016	0		Closed
0425	Sub-Level Ramp Wall	4/7/2016	4/14/2016	4/12/2016	5		Closed
0426	DC-04 Mounting Clarification	4/8/2016	4/15/2016	4/12/2016	4		Closed
0428	1st Floor PT Letter - West Slab	4/11/2016	4/18/2016	4/11/2016	0		Closed
0429	Dewatering System Shutoff	4/11/2016	4/18/2016	4/12/2016	1		Closed
0430	Acoustical & Fire Caulk Color	4/12/2016	4/19/2016	4/22/2016	10	3	Closed
0431	Stud Gauge and Spacing	4/13/2016	4/20/2016	6/20/2016	68	61	Closed
0433	Resilient Channel In Lieu of CRC	4/14/2016	4/21/2016	6/24/2016	71	64	Closed
0434	Plumbing Sleeve in 1st Floor PT Slab Beam	4/14/2016	4/21/2016	4/15/2016	1		Closed
0435	A304 Tub Drain Location	4/14/2016	4/21/2016	4/14/2016	0		Closed
0436	Guest Room Closet Wall Sizes	4/14/2016	4/21/2016	5/19/2016	35	28	Closed
0437	Elevator Vestibule Doorway	4/14/2016	4/21/2016	4/15/2016	1		Closed
0438	Reception Desk South Floor Box	4/15/2016	4/22/2016	4/18/2016	3		Closed
0440	3rd Floor Beams and Opening Sizes	4/18/2016	4/25/2016	4/22/2016	4		Closed
0441	Rebar Lap at 1st Floor Openings	4/18/2016	4/25/2016	4/18/2016	0		Closed
0442	3rd Floor Grill Size	4/18/2016	4/25/2016	4/19/2016	1		Closed
0443	Lobby Floor Box Conflict with Crane Blockout	4/19/2016	4/26/2016	4/21/2016	2		Closed
0444	Second Floor Shaft Locations for stair 3 and 4	4/20/2016	4/27/2016	4/21/2016	1		Closed
0445	Crane Opening Rebar Development	4/20/2016	4/27/2016	4/20/2016	0		Closed
0446	Column Projection into slabs and beams	4/20/2016	4/27/2016	4/20/2016	0		Closed
0447	Stressing Duration Variation	4/20/2016	4/27/2016	4/22/2016	2		Closed
0448	Third Floor Concrete Reinforcement Clarifications	4/21/2016	4/28/2016	5/8/2016	15	8	Closed
0449	Interior wall requirements for mounting stone	4/22/2016	4/29/2016	7/21/2016	80	63	Closed
0450	Concrete embeds for owner provided lights	4/22/2016	4/29/2016	6/30/2016	69	62	Closed
0451	Plumbing Manifold Type	4/22/2016	4/29/2016	8/26/2016	126	119	Closed
0452	Ridge Detail for Ballroom Roof	4/22/2016	4/29/2016	4/27/2016	5		Closed
0453	Shear Wall Opening Along Column Line R	4/25/2016	5/2/2016	4/26/2016	1		Closed
0455	Wing Wall at Column N5	4/27/2016	5/4/2016	4/29/2016	2		Closed
0456	1st Floor Pour 2 Post Tension Elongations	4/27/2016	5/4/2016	5/4/2016	7		Closed
0457	Column A1 Relation to 2PTB-4	4/29/2016	5/6/2016	4/29/2016	0		Closed
0458	Cable Bus Penetration at DT66	4/29/2016	5/6/2016	4/29/2016	0		Closed
0460	DT Cables 65 and 70 at South East Shear Wall	5/2/2016	5/9/2016	5/3/2016	1		Closed
0461	Control Joints in Gypsum Walls and Ceilings	5/2/2016	5/9/2016	6/23/2016	52	45	Closed
0462	2PTB-2 and 2PTB-3 Relationship to Edge of Slab	5/4/2016	5/11/2016	5/4/2016	0		Closed
0463	Linon Storage 300H and TL1300J Ceiling Elevation	5/4/2016	5/11/2016	5/4/2016	0		Closed
0464	Banquet Kitchen Floor Sinks Below Column Line I	5/5/2016	5/12/2016	5/5/2016	0		Closed
0465	Response to SAME Discrepancies 18 and 23	5/5/2016	5/12/2016	5/5/2016	0		Closed
0466	6" Storm Drain Conflicts at Column N30	5/5/2016	5/12/2016	5/6/2016	1		Closed
0467	ACC-1 and ACC-2 Locations	5/6/2016	5/13/2016	5/18/2016	12	5	Closed
0468	ACC and Generator Pad Elevation	5/6/2016	5/13/2016	6/3/2016	28	21	Closed
0469	Level Two Pour One Tendon Elongations	5/6/2016	5/13/2016	5/12/2016	6		Closed
0470	8" Sewer Manhole in Hutson Street	5/6/2016	5/13/2016	5/16/2016	10	3	Closed
0471	Door 129 at Stair 6	5/9/2016	5/16/2016	5/12/2016	3		Closed
0473	Exterior Chilled Water Pipe Support Type	5/10/2016	5/17/2016	5/18/2016	8	1	Closed
0474	Wall Type C4 at Guest Floor Corridor Walls	5/10/2016	5/17/2016	5/11/2016	1		Closed
0475	S103 SB-5 and Shear Wall Penetration	5/11/2016	5/18/2016	5/18/2016	7		Closed
0476	Concrete Capping Beam Temporary Braces	5/11/2016	5/18/2016	5/11/2016	0		Closed
0477	C-4 Column In Shear Wall at Stair 3	5/11/2016	5/18/2016	5/18/2016	5		Closed
0478	Crown Moulding Size in Guest Room Entry Way	5/11/2016	5/18/2016	5/21/2016	10	3	Closed
0479	Third Floor Closet Wall Increase for Mechanical	5/11/2016	5/18/2016	5/13/2016	2		Closed
0480	Shared Condensate Riser at HFCU	5/12/2016	5/19/2016	5/18/2016	6		Closed
0481	Natural Gas Run Outs	5/12/2016	5/19/2016	6/1/2016	20	13	Closed
0482	Banquet Kitchen MEP Coordination with PT Slab	5/13/2016	5/20/2016	5/13/2016	0		Closed
0483	Third Floor Guest Room Entry Way Ceiling Height	5/13/2016	5/20/2016	5/13/2016	0		Closed
0484	Ninth Floor Chilled Water Distribution	5/13/2016	5/20/2016	6/20/2016	38	31	Closed
0485	Shear Wall at Stairway 8 Edge of Slab	5/13/2016	5/20/2016	5/16/2016	3		Closed
0486	Electrical Conduit at J34 Drop Down Panel	5/16/2016	5/23/2016	5/16/2016	0		Closed
0487	1st Floor East Pour Tendon 40 A	5/16/2016	5/23/2016	9/13/2016	120	113	Closed
0488	Chilled Water Pump Discharge	5/16/2016	5/23/2016	5/17/2016	1		Closed
0489	C-3 Columns in Stairwell 6 Shearwall	5/17/2016	5/24/2016	5/17/2016	0		Closed
0490	W1 Shearwall at Second Floor End Verticals	5/17/2016	5/24/2016	5/17/2016	0		Closed
0491	Elevator Shaft Wall End Verticals	5/18/2016	5/25/2016	5/18/2016	0		Closed
0492	Chilled Water Sleeves in 42 x 19 Beam	5/18/2016	5/25/2016	5/18/2016	0		Closed
0493	Bronze Frenestration and Exit Door Shop Drawings Submittal Clarification	5/19/2016	5/26/2016	5/19/2016	0		Closed
0494	Alternate Aircraft Details Per Mockup Review	5/19/2016	5/26/2016	5/19/2016	0		Closed
0495	Cast Stone Veneer Masonary Color	5/20/2016	5/27/2016	6/24/2016	35	28	Closed
0497	East 1.484/12 Rafter Framing	5/20/2016	5/27/2016	5/23/2016	3		Closed
0498	Northwest Terrace Ceiling Heights	5/20/2016	5/27/2016	6/27/2016	38	31	Closed
0499	Third Floor Post Tensioned Cable Profiles and Layout	5/20/2016	5/27/2016	5/20/2016	0		Closed
0500	Area Drain Reinforcing in 48 x 14 1/4 Beam	5/21/2016	5/28/2016	5/23/2016	2		Closed
0501	Typical Guestroom Vanity Faucet	5/23/2016	5/30/2016	6/21/2016	29	22	Closed
0502	Column C-9 Floor Termination	5/23/2016	5/30/2016	5/24/2016	1		Closed
0503	Hurricane Rating on Louvers	5/24/2016	5/31/2016	5/26/2016	2		Closed
0504	Second Floor Ballroom Lighting Locations	5/24/2016	5/31/2016	6/9/2016	16	9	Closed
0505	Back to Back VFCU Chilled Water Routing	5/24/2016	5/31/2016	6/9/2016	16	9	Closed
0506	Guestroom A307 Ceiling Height	5/24/2016	5/31/2016	5/24/2016	0		Closed
0507	Third Floor Bath Tub Selection	5/24/2016	5/31/2016	5/25/2016	1		Closed
0508	Distributed antenna System	5/24/2016	5/31/2016	5/28/2016	2		Closed
0509	Guest Room 348 Domestic Water Riser Access	5/24/2016	5/31/2016	5/25/2016	1		Closed
0510	Heater Gas Line and Lantern Location	5/24/2016	5/31/2016	5/26/2016	2		Closed
0511	First Floor Pour Two PT Bundles 22 and 23	5/25/2016	6/1/2016	7/26/2016	62	55	Closed
0512	First Floor Pour Two PT Bundle 32	5/25/2016	6/1/2016	6/1/2016	7		Closed
0513	Level Two Pour Two Tendon Elongations	5/25/2016	6/1/2016	5/28/2016	1		Closed
0514	Level Two R/A Opening	5/25/2016	6/1/2016	6/8/2016	14	7	Closed

0515	Second Floor Ceiling Heights	5/25/2016	6/1/2016	6/1/2016	7		Closed
0516	Third Floor Edge of Slab	5/25/2016	6/1/2016	5/31/2016	6		Closed
0517	Guestroom 348 Shower Drain Conflict	5/25/2016	6/1/2016	5/26/2016	1		Closed
0518	ADA Bathtub Rough Opening	5/25/2016	6/1/2016	5/26/2016	1		Closed
0519	Sub Level Piping Core Drilling	5/26/2016	6/2/2016	6/24/2016	29	22	Closed
0520	Sublevel Communication Conduit Routing	5/27/2016	6/3/2016	6/16/2016	20	13	Closed
0521	3rd Floor Slab ENT Plan	5/27/2016	6/3/2016	6/6/2016	10	3	Closed
0522	Updated A122 Drawings	5/31/2016	6/7/2016	6/6/2016	6		Closed
0523	3rd Floor Slab Edge Affecting PT Length	5/31/2016	6/7/2016	5/31/2016	0		Closed
0524	PT-59 and PT-60 Placement	5/31/2016	6/7/2016	6/1/2016	1		Closed
0525	Conduit Routing to JS Fixtures	6/3/2016	6/10/2016	6/3/2016	0		Closed
0526	Retaining Wall Foundation at East Atrium Type	6/3/2016	6/10/2016	6/7/2016	4		Closed
0527	Retaining Wall Foundation at East Atrium Location	6/3/2016	6/10/2016	6/7/2016	4		Closed
0528	3rd to 4th Floor Column Splice Height	6/6/2016	6/13/2016	6/7/2016	1		Closed
0529	Primary and Secondary Chiller Pump VFD's	6/6/2016	6/13/2016	6/20/2016	14	7	Closed
0530	Third Floor West Pour Stressing Report	6/9/2016	6/16/2016	6/14/2016	5		Closed
0531	Third Floor Terrace Lantern Junction Box Elevation	6/10/2016	6/17/2016	6/10/2016	0		Closed
0532	Room 341 Bathroom Layout	6/10/2016	6/17/2016	6/10/2016	0		Closed
0533	Locker Room Shower Bench	6/10/2016	6/17/2016	6/20/2016	10	3	Closed
0534	Second Floor Rotunda Quarrycast	6/10/2016	6/17/2016	6/14/2016	4		Closed
0535	Concierge Level Stone Tops and Bookcases	6/13/2016	6/20/2016	6/14/2016	1		Closed
0536	Rooftop Shower Schluter	6/20/2016	6/20/2016	6/20/2016	0		Closed
0537	Patioserie Stone Dimensions	6/13/2016	6/20/2016	6/20/2016	7		Closed
0538	3rd Floor Post Tensioned Banded Tendon 18	6/13/2016	6/20/2016	6/13/2016	0		Closed
0539	Column Termination at Slab Edge	6/13/2016	6/20/2016	6/13/2016	0		Closed
0540	Rooftop Fireplace Gas Rough-Ins	6/14/2016	6/21/2016	6/22/2016	8	1	Closed
0541	Junction Box in Column S35	6/15/2016	6/22/2016	6/24/2016	9	2	Closed
0542	Typical Guestroom Exhaust Fan Location	6/15/2016	6/22/2016	6/16/2016	1		Closed
0543	4th Floor Slab ENT Plan	6/16/2016	6/23/2016	6/24/2016	8	1	Closed
0544	3rd Floor Pour 2 Stressing Report	6/17/2016	6/24/2016	6/23/2016	6		Closed
0545	Revised Chilled Water Layout Resolutions	6/17/2016	6/24/2016	6/17/2016	0		Closed
0547	9th Floor Drop Heads Studrail Length	6/22/2016	6/29/2016	6/22/2016	0		Closed
0549	Third Floor Overhead HFCU Rotation	6/27/2016	7/4/2016	6/27/2016	0		Closed
0550	Bronze Fenestration V/E	6/28/2016	7/5/2016	6/16/2016	49	42	Closed
0551	Fourth Floor West Pour Stress Report	6/29/2016	7/6/2016	6/29/2016	0		Closed
0552	KEF-5 Exhaust Duct	6/30/2016	7/7/2016	6/30/2016	0		Closed
0553	Levels 5 Thru 8 Back to Back VFCU's	6/30/2016	7/7/2016	7/7/2016	7		Closed
0554	5th Floor Slab Edge Beam	6/30/2016	7/7/2016	6/30/2016	0		Closed
0555	Slab Reinforcing at Blockout South of W3	6/30/2016	7/7/2016	7/1/2016	1		Closed
0556	4th Floor HFCU Air Discharge	6/30/2016	7/7/2016	7/1/2016	1		Closed
0557	4th Floor Chilled Water and Condensate Routing and Sizing	7/1/2016	7/8/2016	7/1/2016	0		Closed
0558	Porcelain Tile 14 Size	7/1/2016	7/8/2016	7/1/2016	0		Closed
0559	Rooftop Pool Stair Tile	7/5/2016	7/12/2016	7/11/2016	6		Closed
0560	Concierge Suite Perimeter Tile	7/6/2016	7/13/2016	7/12/2016	6		Closed
0561	Concierge Lounge Buffet Stone Countertop	7/6/2016	7/13/2016	8/1/2016	26	19	Closed
0562	Concierge Bathroom Adjacent Sink Wall Finish	7/11/2016	7/18/2016	7/12/2016	1		Closed
0563	PTB-05 Location Clarification	7/11/2016	7/18/2016	7/19/2016	8	1	Closed
0564	Inspection Holes at CMU Walls	7/12/2016	7/19/2016	7/14/2016	2		Closed
0565	18 x 18 Louver at West Elevation	7/15/2016	7/19/2016	7/15/2016	0		Closed
0566	Southwest Chilled Water Risers	7/13/2016	7/20/2016	7/13/2016	0		Closed
0567	Northwest Chilled Water Risers	7/13/2016	7/20/2016	7/13/2016	0		Closed
0568	Post Installed Masonry Dowels Embedment Depth	8/26/2016	7/21/2016	8/26/2016	0	36	Closed
0569	Sublevel Electrical Room Topping Slab Reinforcement	7/14/2016	7/21/2016	7/15/2016	1		Closed
0570	Electrical Room Floor Finish	7/18/2016	7/25/2016	7/19/2016	1		Closed
0571	Hi-LO Pool Drinking Fountain Rough In	7/18/2016	7/25/2016	7/19/2016	1		Closed
0572	Fire Damper Size at Stairwell 4 Landing	7/19/2016	7/26/2016	7/19/2016	0		Closed
0573	Concierge Lounge Domestic Water Routing	7/19/2016	7/26/2016	7/26/2016	7		Closed
0574	Level Five West Stressing Report	7/19/2016	7/26/2016	7/19/2016	0		Closed
0575	Masonry Bond Beam Grouting at Expansion Anchors	7/20/2016	7/27/2016	7/20/2016	0		Closed
0576	Masonry Rebar Through Elevated Slabs	7/20/2016	7/27/2016	7/21/2016	1		Closed
0577	Room 502 Storm and Overflow Drain Line Offset	7/20/2016	7/27/2016	7/22/2016	2		Closed
0578	Vertical Pipe Routing Through Concierge Lounge	7/20/2016	7/27/2016	7/26/2016	6		Closed
0579	Sixth Floor Elevated Slab Layout	7/21/2016	7/28/2016	7/21/2016	0		Closed
0580	Riser C18 Chilled Water Distribution	7/22/2016	7/29/2016	7/26/2016	4		Closed
0581	Shower Drain at S34 Studrail Conflict	7/22/2016	7/29/2016	7/22/2016	0		Closed
0582	Studrails at Shower Beds	7/22/2016	7/29/2016	7/25/2016	3		Closed
0583	North Side of Building Closet Wall Increase	7/28/2016	8/2/2016	7/27/2016	1		Closed
0584	Southeast Corner HVAC and DW Risers at Stair 4	7/26/2016	8/2/2016	8/9/2016	14	7	Closed
0585	Riser C8 Piping at Room 515	7/26/2016	8/2/2016	8/1/2016	6		Closed
0586	Chilled Water Sleeves at 6PTB-2	7/28/2016	8/2/2016		931	924	Internal Review
0587	Room 601, 701, 801 Wall Thickness Increase	7/28/2016	8/2/2016	7/26/2016	0		Closed
0588	Condensate Water Riser C15	7/28/2016	8/2/2016	7/27/2016	1		Closed
0589	Level Four East Pour Stressing Report	7/27/2016	8/3/2016	7/27/2016	0		Closed
0590	Level Five East Stressing Report	7/27/2016	8/3/2016	7/28/2016	1		Closed
0591	Ballroom Joist Length Discrepancy	7/27/2016	8/3/2016	7/27/2016	0		Closed
0592	Door 127 Masonry Opening	7/27/2016	8/3/2016	7/27/2016	0		Closed
0593	Stair 1 & 2 Treads	7/27/2016	8/3/2016	7/27/2016	0		Closed
0594	Room 611 Toilet Wall	7/27/2016	8/3/2016	7/28/2016	1		Closed
0595	Guestroom Type E7 at Room 639 and 739	7/29/2016	8/4/2016	8/6/2016	11	4	Closed
0596	Sixth Floor Shower Drain Layout	7/28/2016	8/4/2016	7/28/2016	0		Closed
0597	MOD 5 Mechanical Equipment Electrical Requirements	7/28/2016	8/4/2016	8/1/2016	4		Closed
0598	Stair 1 & 2 Structural Support	7/28/2016	8/4/2016	8/4/2016	7		Closed
0599	CMU Control Joints @ Concrete Columns	7/29/2016	8/5/2016	8/3/2016	5		Closed
0600	Discrepancy 32 - C16 Column Not Tested	7/29/2016	8/5/2016	7/29/2016	0		Closed
0601	Ulen 500H Ceiling Height	7/29/2016	8/5/2016	7/29/2016	0		Closed
0602	Room 531 Overhead MEP Routing	7/29/2016	8/5/2016		928	921	Internal Review
0603	Room 501 Overhead MEP Routing	7/29/2016	8/5/2016	8/1/2016	3		Closed
0604	Room 635, 735, 835 Closet Wall Thickness	8/1/2016	8/8/2016	8/1/2016	0		Closed
0605	LU Light Fixture Beam Angle	8/2/2016	8/9/2016	8/24/2016	22	15	Closed
0606	Transformer Pad Layout	8/2/2016	8/9/2016	8/3/2016	1		Closed
0607	East Elevation Retaining Wall Light	8/2/2016	8/9/2016	8/3/2016	1		Closed
0608	Under Slab CMU Over Bond Beam	8/2/2016	8/9/2016	8/11/2016	9	2	Closed
0609	7 5/8" x 29 3/8" Concrete Beam Connection	8/3/2016	8/10/2016	8/4/2016	1		Closed
0610	Keyway Size RFI-0019	8/3/2016	8/10/2016	8/4/2016	1		Closed
0612	Mechanical Louver Color Selection	8/3/2016	8/10/2016	8/4/2016	1		Closed
0613	Manager's Apartment Shower and Toilet Doors	8/4/2016	8/11/2016	8/5/2016	1		Closed
0614	Stair 1&2 Connection Level 1	8/4/2016	8/11/2016	8/4/2016	0		Closed
0615	Marquis Canopy HSS 8x6 Spacing	8/5/2016	8/12/2016	8/5/2016	1		Closed
0616	5th Floor Ceiling Adjustments	8/5/2016	8/12/2016	8/19/2016	14	7	Closed

0617	DW and CW Riser at Rooms 635, 735, 835	8/8/2016	8/15/2016	8/8/2016	0		Closed
0618	Room 531 Entry Corridor Wing Wall	8/8/2016	8/15/2016	8/8/2016	0		Closed
0619	Chilled Water Riser C16 at Managers Apartment	8/8/2016	8/15/2016	8/9/2016	1		Closed
0620	Managers Apartment Domestic Water Routing	8/8/2016	8/15/2016	8/9/2016	1		Closed
0621	Level 06 Area Drains Installation Details	8/9/2016	8/16/2016	8/12/2016	3		Closed
0622	Door 115B3 Clarification	8/9/2016	8/16/2016	8/19/2016	10	3	Closed
0623	6th Floor West Pour Conflicts	8/15/2016	8/17/2016	8/15/2016	0		Closed
0624	Guestroom Entry Light	8/10/2016	8/17/2016	8/10/2016	0		Closed
0625	Guest Bathroom Lighting over Tubs	8/10/2016	8/17/2016	8/10/2016	0		Closed
0626	Carolina Lantern Mounting Bracket	8/10/2016	8/17/2016		916	909	Open
0627	Zaneen Fixtures	8/10/2016	8/17/2016	8/12/2016	2		Closed
0628	MOD 6 VFCUs in Managers Apt	8/10/2016	8/17/2016	8/15/2016	5		Closed
0629	Managers Apt Recessed Cans	8/10/2016	8/17/2016	9/21/2016	42	35	Closed
0630	Low Lift Grout Vibrating Procedure	8/15/2016	8/22/2016	8/15/2016	0		Closed
0631	CMU Bond Beam @ Floors 3 and Up	8/15/2016	8/22/2016	8/22/2016	7		Closed
0632	Decorative Gilt Relation to Crown Moulding	8/15/2016	8/22/2016	8/15/2016	0		Closed
0633	Submittal Comments from the MOD 5 Door Hardware Schedule	8/16/2016	8/23/2016	8/19/2016	3		Closed
0634	6th Floor Column B20 Sleeve Conflict	8/16/2016	8/23/2016	8/18/2016	2		Closed
0635	Storm Sleeve Conflict with Existing Utilities	8/16/2016	8/23/2016	8/16/2016	0		Closed
0636	Ballroom Structure Wall Type	8/16/2016	8/23/2016	8/16/2016	0		Closed
0637	Storm Drain Offset at Room 635	8/16/2016	8/23/2016	9/12/2016	27	20	Closed
0638	Managers Apartment Bath Tub	8/16/2016	8/23/2016	8/17/2016	1		Closed
0639	Sublevel Masonry Wall Bond Beam Location	8/17/2016	8/24/2016	8/17/2016	0		Closed
0640	Managers Apartment Natural Gas Stub Out	8/17/2016	8/24/2016	8/18/2016	1		Closed
0642	1st Floor Return Air Opening FSD	8/18/2016	8/25/2016	8/24/2016	6		Closed
0643	6th Floor Overhead Sleeve at J35	8/22/2016	8/29/2016	8/23/2016	1		Closed
0644	6th Floor Overhead Sleeve at Column M35	8/22/2016	8/29/2016	8/23/2016	1		Closed
0645	Guestroom 848 Tub Layout	8/22/2016	8/29/2016	8/23/2016	1		Closed
0646	Elevation Dimensions for Exterior Electrical Rough In	8/22/2016	8/29/2016	9/12/2016	21	14	Closed
0647	Managers Apartment Column M38 Furnout	8/22/2016	8/29/2016	8/22/2016	0		Closed
0648	Stair 3 and 4 Opening Relationship to SB-1	8/22/2016	8/29/2016	8/22/2016	0		Closed
0649	Carpet Seaming Diagrams	8/22/2016	8/29/2016	1/20/2017	151	144	Closed
0650	Hopes Doors Hardware Clarification	8/23/2016	8/30/2016	8/23/2016	0		Closed
0651	Aluminum Corbice Clarification	8/23/2016	8/30/2016	8/24/2016	1		Closed
0652	Stair 9 Level 6 Embeds	8/24/2016	8/31/2016	8/27/2016	3		Closed
0653	Ninth Floor Slab Step Dimensions	8/24/2016	8/31/2016	8/29/2016	5		Closed
0654	Studral Conflict 6th Floor Column H38	8/25/2016	9/1/2016	8/28/2016	1		Closed
0655	Masonry Rebar Sleeve Conflict with PT Anchorage	8/26/2016	9/2/2016	8/29/2016	3		Closed
0656	Mechanical Louvers to Match Exterior Substrate	8/26/2016	9/2/2016	8/28/2016	0		Closed
0657	Mechanical Block Out at 6th Floor Stair Four	8/26/2016	9/2/2016	8/28/2016	0		Closed
0659	Elevator Lobby Vaulted Ceiling Height	8/26/2016	9/2/2016	9/12/2016	17	10	Closed
0660	Valet Room Ceiling Height	8/26/2016	9/2/2016	10/31/2016	66	59	Closed
0662	Stud Rails in RCB J38 and N38	8/29/2016	9/5/2016	8/29/2016	0		Closed
0663	Stair 1 and 2 Tread Reinforcing	8/29/2016	9/5/2016	8/29/2016	0		Closed
0664	Arches @ Level 2 South Elevation	8/30/2016	9/5/2016	8/30/2016	0		Closed
0665	6th Floor Slab Reinforcing Steel Clashing with Block Outs	8/30/2016	9/5/2016	8/30/2016	0		Closed
0666	6th Floor West Stressing Report	8/30/2016	9/5/2016	8/30/2016	0		Closed
0667	6th Floor Terrace Door Size	8/31/2016	9/7/2016	8/31/2016	0		Closed
0668	SP-4 Electrical Requirements	8/31/2016	9/7/2016	9/1/2016	1		Closed
0669	Equipment Yard Masonry Wall Height	9/8/2016	9/8/2016	9/9/2016	1	1	Closed
0670	Mockup Base Transition Details	9/2/2016	9/9/2016	9/8/2016	6		Closed
0671	Make Up Air Unit Submittal Comments	9/2/2016	9/9/2016	9/26/2016	24	17	Closed
0672	HFCU Color Selection	9/2/2016	9/9/2016	9/7/2016	5		Closed
0673	Masonry Rebar Thru Level 5 and 8 Precast Band	9/8/2016	9/9/2016	9/15/2016	7	6	Closed
0675	Make Up Air Unit Digital Scroll Compressor	9/8/2016	9/13/2016	9/23/2016	17	10	Closed
0676	Secondary Pool Rules Location	9/6/2016	9/13/2016	9/6/2016	0		Closed
0677	Level Six East Stressing Report	9/6/2016	9/13/2016	9/7/2016	1		Closed
0678	South Wall Elevation Floors 1-3	9/6/2016	9/13/2016	9/21/2016	15	8	Closed
0679	Seventh Floor West Sleeve Layout	9/7/2016	9/14/2016	9/7/2016	0		Closed
0680	Level 3 Terrace Wall Details	9/13/2016	9/15/2016	9/19/2016	6	4	Closed
0681	Riser C3 Eighth Floor HFCU-3 Condensate Size	9/8/2016	9/15/2016	9/8/2016	0		Closed
0682	Condensate Pumps Added in BIM Process	9/8/2016	9/15/2016	9/9/2016	1		Closed
0683	Pool Deck Drinking Fountain Valve Access	9/8/2016	9/15/2016	9/8/2016	0		Closed
0684	Pool Equipment Room Hub Drain	9/8/2016	9/15/2016	9/29/2016	21	14	Closed
0685	Double Queen Guestroom Low Voltage Layout	9/8/2016	9/15/2016	9/8/2016	1		Closed
0686	Guestroom Terrace Door Transition	9/9/2016	9/16/2016	9/9/2016	0		Closed
0687	CMU Placement After Dead Load Deflections	9/9/2016	9/16/2016	9/9/2016	0		Closed
0688	7th Floor Q6 Studral Conflict	9/12/2016	9/19/2016	9/12/2016	0		Closed
0689	7th Floor Column L16 Studral Conflict	9/12/2016	9/19/2016	9/12/2016	0		Closed
0690	7th Floor Column D6 Studral Conflict	9/12/2016	9/19/2016	9/12/2016	0		Closed
0692	Equipment Yard Retaining Wall Light Fixtures	9/12/2016	9/19/2016	9/21/2016	9	2	Closed
0693	7th Floor West Blockout for MOD 7	9/12/2016	9/19/2016	9/13/2016	1		Closed
0694	VFCU-26 Condensate	9/13/2016	9/20/2016	9/13/2016	0		Closed
0695	Studral Conflict with Masonry Sleeves Column's C6 and L6	9/13/2016	9/20/2016	9/13/2016	0		Closed
0696	Roof Top Bar Beverage Conduit Sleeve	9/13/2016	9/20/2016	9/19/2016	6		Closed
0697	Level 06 Ceiling Vent Routing	9/13/2016	9/20/2016	9/15/2016	2		Closed
0698	Level 09 Storm Drain Routing	9/14/2016	9/21/2016	9/29/2016	15	8	Closed
0699	Domestic Water Risers Water Hammer Arrestors	9/14/2016	9/21/2016	10/6/2016	22	15	Closed
0700	Level 09 Additional Venting	9/14/2016	9/21/2016	9/29/2016	15	8	Closed
0701	Domestic Hot Water Risers to Seventh Floor Return	9/14/2016	9/21/2016	9/19/2016	5		Closed
0702	Cameleon's Entry Doors	9/14/2016	9/21/2016	9/21/2016	7		Closed
0703	Flashing At Level 3 Guestroom Fixed Doors	9/14/2016	9/21/2016	10/12/2016	28	21	Closed
0704	Third Floor CMU Window Headers and Bond Beam	9/16/2016	9/23/2016	9/16/2016	0		Closed
0705	Terrace Divider Wall Clarification	9/19/2016	9/26/2016	9/20/2016	1		Closed
0706	7th Floor LP Sleeve at C38	9/21/2016	9/28/2016		874	867	Internal Review
0707	Managers Apartment MA Panel Relocation	9/21/2016	9/28/2016	9/21/2016	0		Closed
0708	7th Floor West Slab Stressing Report	9/22/2016	9/29/2016	9/22/2016	0		Closed
0709	MA Panel Sleeves in RCB 9	9/22/2016	9/29/2016	9/22/2016	0		Closed
0710	Wall Type Change @ Mech. Room 235	9/22/2016	9/29/2016	9/27/2016	5		Closed
0711	Room 508, 540, and 542 Ceiling Height	9/23/2016	9/30/2016	9/23/2016	0		Closed
0712	Straight Railing Top Cap	9/23/2016	9/30/2016	9/23/2016	0		Closed
0713	Level 06 West Partial Stressing Report	9/26/2016	10/3/2016	9/26/2016	0		Closed
0714	Room 744 Entry Way South Wall	9/26/2016	10/3/2016	9/26/2016	0		Closed
0715	Eyebrow Balcony Bracket Material Thickness	9/26/2016	10/3/2016	9/28/2016	0		Closed
0716	3rd Floor Terrace Drain Elevations	9/27/2016	10/4/2016		868	861	Internal Review
0717	North Shearwall at Eighth Floor Elevator Lobby	9/28/2016	10/5/2016	9/28/2016	0		Closed
0718	ST-4 Review Comments	9/28/2016	10/5/2016	9/30/2016	2		Closed
0719	6th Floor Tendons 1p and 1q Stressing Report	9/30/2016	10/7/2016	10/10/2016	10	3	Closed
0723	Level 09 NFH Water Feed	10/3/2016	10/10/2016	10/4/2016	1		Closed

0724	Eighth Floor Overhead Storm Drain Lines CL F	10/9/2016	10/10/2016	10/19/2016	16	9	Closed
0725	Ninth Floor Cantilevered Walkway	10/13/2016	10/26/2016	10/14/2016	1		Closed
0726	Canopy Bracket Finish	10/7/2016	10/14/2016	10/12/2016	5		Closed
0727	Managers Apartment Lighting Product Data	10/7/2016	10/14/2016	4/13/2017	188	181	Closed
0728	Sublevel Exhaust Duct Connection to 54" Airshaft	10/10/2016	10/17/2016	10/24/2016	14	7	Closed
0729	Stair Six Stand Pipe Location	10/10/2016	10/17/2016	10/11/2016	1		Closed
0730	Elevator Equipment Room 800M FCU Type	10/11/2016	10/18/2016	10/11/2016	0		Closed
0731	Gutter Drain Pipe Routing	10/11/2016	10/18/2016	10/20/2016	9	2	Closed
0733	Eighth Floor West Stressing Report	10/12/2016	10/19/2016	10/12/2016	0		Closed
0734	Missing Rebar Sleeves @ L4 Slab	10/13/2016	10/20/2016	10/17/2016	4		Closed
0735	Level Two South Wall Arch Reinforcement	10/14/2016	10/21/2016	10/14/2016	0		Closed
0736	7th Floor Overhead HWR Routing	10/14/2016	10/21/2016	10/24/2016	10	3	Closed
0737	P-40 Color Selection	10/14/2016	10/21/2016	10/14/2016	0		Closed
0738	Pool Deck Slab Revision	10/15/2016	10/22/2016	10/18/2016	3		Closed
0739	8th Floor Overhead Open Waste and Vent Coordination	10/17/2016	10/24/2016	10/24/2016	7		Closed
0740	8th Floor Overhead Open Storm Drain Coordination	10/17/2016	10/24/2016	10/24/2016	7		Closed
0741	8th Floor Open Beverage Conduit Coordination	10/17/2016	10/24/2016	10/20/2016	3		Closed
0742	8th Floor Overhead Domestic Water Coordination	10/17/2016	10/24/2016	10/24/2016	7		Closed
0743	9th Floor Edge of Slab Detail	10/24/2016	10/31/2016	10/25/2016	1		Closed
0744	ACC-1 and ACC-2 Feeder Size	10/24/2016	10/31/2016	10/28/2016	4		Closed
0745	SI 26 SAR Change	10/25/2016	11/1/2016	11/1/2016	7		Closed
0746	Eighth Floor East Pour Stressing Report	10/25/2016	11/1/2016	10/25/2016	0		Closed
0748	Booster Heater Feeder Size	10/27/2016	11/3/2016	10/28/2016	1		Closed
0749	Retal Zone Sprinkler Drain	10/28/2016	11/4/2016	10/28/2016	0		Closed
0750	Guestroom 340 Terrace Drain	10/28/2016	11/4/2016	10/28/2016	0		Closed
0751	East Sidewalk ADA Compliance	10/29/2016	11/5/2016	10/31/2016	2		Closed
0753	Gutter Drain Penetration at C6	10/31/2016	11/7/2016	10/31/2016	0		Closed
0754	Custom Grilles Under Grand Stairs	10/31/2016	11/7/2016	10/31/2016	0		Closed
0755	SI 32 Panel BHS Feed to 3HS	10/31/2016	11/7/2016	11/3/2016	3		Closed
0756	Missing Sleeves L4 Col. V-9	11/1/2016	11/8/2016	11/2/2016	1		Closed
0757	Pool Deck Height	11/1/2016	11/8/2016	11/1/2016	0		Closed
0758	Elevator 3-4 8th Floor Rough Opening	11/1/2016	11/8/2016	11/23/2016	22	15	Closed
0759	Second Floor Elevator 3-4 Misplaced Embed	11/2/2016	11/9/2016	11/8/2016	6		Closed
0760	Merkrete Vertical Transition Details	11/3/2016	11/10/2016	11/9/2016	6		Closed
0761	S109 Stair and Slab Reinforcing Shift	11/3/2016	11/10/2016	11/3/2016	0		Closed
0762	OFCL Light Fixtures DW-06 and DW-23	11/3/2016	11/10/2016	11/17/2016	14	7	Closed
0763	Circular Ornamental Grille Galvanized Coating	11/3/2016	11/10/2016	11/4/2016	1		Closed
0764	Cameo Lounge North Hornstrobe	11/4/2016	11/11/2016	11/18/2016	14	7	Closed
0765	Private Dining Ductwork Routing	11/5/2016	11/12/2016	11/5/2016	0		Closed
0766	Revised Rooftop Bar Layout	11/5/2016	11/12/2016	11/7/2016	2		Closed
0767	Level 09 Statewide Dish Location	11/7/2016	11/14/2016	11/8/2016	1		Closed
0768	CMU size Change @ Stair 384	11/9/2016	11/16/2016	11/9/2016	0		Closed
0769	Access Panel @ Shafts by Stair 384	11/18/2016	11/25/2016	12/1/2016	13	6	Closed
0770	Merkrete Metal Flashing Dimensions	11/18/2016	11/25/2016	12/14/2016	26	19	Closed
0771	9th Floor West Sleeve Layout	11/11/2016	11/18/2016	11/11/2016	0		Closed
0772	Ninth Floor Roof Drain Elevations	11/14/2016	11/21/2016	11/15/2016	1		Closed
0773	Elevator 1-2 S5x18.4 Embed	11/14/2016	11/21/2016	11/15/2016	1		Closed
0774	FRP Column Paint & Caulk	11/15/2016	11/22/2016	11/21/2016	6		Closed
0775	9th Floor Column L16 Studrail	11/15/2016	11/22/2016	11/15/2016	0		Closed
0776	Roof Drains in Built Up TPO Roof	11/16/2016	11/23/2016	11/16/2016	0		Closed
0777	Pump Room B30 North Wall	11/16/2016	11/23/2016	11/18/2016	2		Closed
0778	Pre-Function 207 Soffit Heights	11/16/2016	11/23/2016	1/23/2017	68	61	Closed
0779	Upper Dining 247 Ceiling Pocket Dimensions	11/16/2016	11/23/2016	11/18/2016	2		Closed
0781	9th Floor Column H17 Studrails	11/17/2016	11/24/2016	11/18/2016	1		Closed
0782	Tendon RDT-4 Profile High Point	11/18/2016	11/25/2016	11/18/2016	0		Closed
0783	Pool Deck Sleeve Offset for Structural Framing	11/18/2016	11/25/2016	11/18/2016	0		Closed
0784	9th Floor Low Voltage ENT Plan	11/18/2016	11/25/2016	11/18/2016	0		Closed
0785	Guestroom Floors Finished Ceiling Height	11/21/2016	11/28/2016	11/22/2017	52	45	Closed
0786	Cameo Lounge Fire Rating	11/22/2016	11/29/2016	11/22/2016	0		Closed
0787	Banquet Kitchen UDS Power Feed	11/22/2016	11/29/2016	12/14/2016	22	15	Closed
0789	Private Dining Lighting Revisions	11/22/2016	11/29/2016	11/28/2016	6		Closed
0791	Level 09 West Stressing Report	11/28/2016	12/5/2016	11/28/2016	0		Closed
0792	Guestroom Floors Fire Alarm Cable	11/28/2016	12/5/2016	12/5/2016	7	0	Closed
0793	Level One Elevator Sill Angle Conflict	11/28/2016	12/5/2016	11/28/2016	0		Closed
0794	Elevator 5 Holst Beam Embeds	11/30/2016	12/7/2016	11/30/2016	0		Closed
0795	Kitchen Equipment Wall Finish	12/1/2016	12/8/2016	11/22/2017	42	35	Closed
0796	Man-Pedi 215 Sink Type	12/1/2016	12/8/2016	12/5/2016	4		Closed
0797	Dishwasher Exhaust Fan Assembly	12/1/2016	12/8/2016	12/9/2016	8	1	Closed
0798	Level 9 East Stressing Report	12/2/2016	12/9/2016	12/5/2016	3		Closed
0799	Ceiling Mounted Light Fixture Locations	12/3/2016	12/10/2016	11/7/2017	45	38	Closed
0800	Level 3-8 Corridor Casing Conflict	12/5/2016	12/12/2016	11/8/2017	44	37	Closed
0801	221B and 222B ADA Shower Fixture Orientation	12/5/2016	12/12/2016	12/20/2016	15	8	Closed
0802	Level 6 CMU Slab Connection	12/6/2016	12/13/2016	12/12/2016	8		Closed
0803	L2 Sprinkler Beam Penetration	12/6/2016	12/13/2016	12/9/2016	3		Closed
0805	Dome Rotunda Soffit Dimensions	12/6/2016	12/13/2016	12/7/2016	1		Closed
0806	Kitchen Hood Ceiling Height	12/7/2016	12/14/2016	3/27/2017	110	103	Closed
0807	Mechanical Pad Overpour Cut Back	12/9/2016	12/16/2016	12/13/2016	4		Closed
0808	Fire Smoke Damper Circulating	12/10/2016	12/17/2016	12/16/2016	6		Closed
0809	EE2 Light Pole Fixture Orientation	12/12/2016	12/19/2016	12/7/2017	46	39	Closed
0811	Guestroom HFCU Duct Routing Coordination	12/13/2016	12/20/2016	12/16/2016	3		Closed
0812	Private Dining DC-30	12/13/2016	12/20/2016	11/22/2017	30	23	Closed
0813	L5 Precast Band Anchoring @ Shearwalls	12/14/2016	12/21/2016	11/2/2017	29	22	Closed
0814	Roof Kitchen Hood Exhaust Direction	12/15/2016	12/22/2016	12/16/2018	1		Closed
0815	Cabana Column Framing	12/15/2016	12/22/2016	12/15/2016	0		Closed
0816	Ballroom Two and Three Operable Wall Support	12/16/2016	12/23/2016	12/18/2016	0		Closed
0817	Exterior Masonry/Stucco Control Joints	12/16/2016	12/23/2016	11/1/2017	28	19	Closed
0818	Guestroom Air Volume Dampers	12/16/2016	12/23/2016	12/16/2016	0		Closed
0819	Marquis Framing Corner Support	12/16/2016	12/23/2016	11/3/2017	28	21	Closed
0820	Board Room Ceiling Feature	12/18/2016	12/26/2016	12/19/2016	0		Closed
0821	Roof Truss Channel Attachments	12/19/2016	12/26/2016	12/19/2016	0		Closed
0822	Elevator 6 Holst Beam Embeds	12/19/2016	12/26/2016	12/19/2016	0		Closed
0823	Level 3 Fire Alarm Ceiling Conflict	12/20/2016	12/27/2016	1/25/2017	36	29	Closed
0824	Stair 4 Level 4 Drop Beam Conflict	12/22/2016	12/29/2016	1/3/2017	12	5	Closed
0825	Level 2 Fire Sprinkler Ceiling Conflict	12/22/2016	12/29/2016	1/1/2017	20	13	Closed
0826	Fire Damper Clarification	12/22/2016	12/29/2016	12/28/2016	6		Closed
0827	Won Door Dimension Conflict	12/22/2016	12/29/2016	1/5/2017	14	7	Closed
0828	HFCU Column / Crown Conflict	12/22/2016	12/29/2016	12/22/2016	0		Closed
0829	Vanity GRM-210-A Coordination	12/22/2016	12/29/2016	12/29/2016	7		Closed
0831	Roof Top Bar and Lobby Tile Selection	12/27/2016	1/3/2017	5/9/2017	133	126	Closed

0832	ADA Shower Head and Tub Valve Orientation	12/28/2016	1/4/2017	1/27/2017	30	23	Closed
0833	BAR Comment L3 Terrace Guardrail	12/28/2016	1/5/2017		775	768	Open
0834	#2 BAR Comment: Precast Mortar and Caulk	12/28/2016	1/5/2017		775	768	Open
0835	#4 BAR Comment: Exterior Brackets	12/28/2016	1/5/2017		775	768	Open
0836	#5 BAR Comment: Marquis Canopy	12/28/2016	1/5/2017	3/20/2017	81	74	Closed
0837	#7 BAR Comment: Rope Weeps	12/28/2016	1/5/2017	1/23/2017	25	18	Closed
0838	#8 BAR Comment: Shutters and Hardware	12/28/2016	1/5/2017		775	768	Open
0839	#9 BAR Comment: Aluminum Cornice Joints	12/28/2016	1/5/2017		775	768	Open
0840	BAR Comment: L3 Trellis	12/28/2016	1/5/2017	1/27/2017	29	22	Closed
0841	MOD 7 RA Panel Wall Shift	12/28/2016	1/5/2017	1/27/2017	29	22	Closed
0843	Elevator 1-4 Embeds for Columns	1/3/2017	1/10/2017	1/4/2017	1		Closed
0845	Lights in Mens Locker Room	1/3/2017	1/10/2017	1/4/2017	1		Closed
0846	Type R Window L5 North	1/3/2017	1/10/2017	1/4/2017	1		Closed
0847	Stair 3 Floor Finish	1/3/2017	1/10/2017	5/16/2017	133	128	Closed
0848	Stair Four Landing Connection	1/4/2017	1/11/2017	1/4/2017	0		Closed
0849	Precast SAs @ South Courtyard Elevation	1/4/2017	1/11/2017	1/11/2017	7		Closed
0850	Level 7 Precast Slab Elevations	1/4/2017	1/11/2017	1/4/2017	0		Closed
0851	Operable Panel Door Trim	1/5/2017	1/12/2017	1/25/2017	20	13	Closed
0852	Fire Extinguisher Cabinet at door 104B	1/6/2017	1/13/2017	1/13/2017	7		Closed
0853	Water Heater 240 Pipe Penetrations	1/7/2017	1/14/2017	1/7/2017	0		Closed
0854	4 Inch SD at Vestibule 200 Column D27	1/7/2017	1/14/2017	1/7/2017	0		Closed
0855	5th Floor Slab Connection Revision	1/10/2017	1/17/2017	1/11/2017	1		Closed
0856	CMU At Elevated Pool Deck	1/11/2017	1/18/2017	1/13/2017	2		Closed
0857	Room Type A16 Barn Door Conflict	1/11/2017	1/18/2017	3/29/2017	77	70	Closed
0858	Second Floor Projector Locations	1/11/2017	1/18/2017	1/27/2017	16	9	Closed
0859	VAV 1-1 and 2-1 Electrical Requirements	1/11/2017	1/18/2017	1/12/2017	1		Closed
0860	Level Two Men and Womens Restroom Ceiling Height	1/12/2017	1/19/2017	1/12/2017	0		Closed
0861	Elevator 1-4 Lobby Return Grille	1/13/2017	1/20/2017	2/14/2017	32	25	Closed
0862	Steel Grate @ Ventilation Shaft	1/13/2017	1/20/2017	1/13/2017	0		Closed
0863	Level 2 Precast Angle Anchoring	1/16/2017	1/23/2017	1/17/2017	1		Closed
0864	Pool Deck Edge of Slab Relationship to Masonry	1/16/2017	1/23/2017	1/16/2017	0		Closed
0865	Third Floor Fixed Door Header Repair Detail	1/16/2017	1/23/2017	1/17/2017	1		Closed
0866	Guestroom Shower Hand Wand and Slide Bar Locations	1/19/2017	1/26/2017	1/19/2017	0		Closed
0867	Low Masonry Grout Compressive Strength Repair	1/19/2017	1/26/2017	1/19/2017	0		Closed
0868	Shower Niche Confirmation	1/19/2017	1/26/2017	2/3/2017	15	8	Closed
0869	Sprinkler Conflict SW Entry Level 2	1/20/2017	1/27/2017	3/11/2017	50	43	Closed
0870	Pool Deck Framing Layout	1/25/2017	2/1/2017	1/27/2017	2		Closed
0871	New Mockup Storefront Precast Dimensions	1/26/2017	2/2/2017	3/23/2017	58	49	Closed
0872	Guestroom Bathtub Domestic Pipe Size	1/27/2017	2/3/2017	2/7/2017	11	4	Closed
0874	Guest Room Shower Toe Rest	1/28/2017	2/4/2017	2/10/2017	13	6	Closed
0875	Roof Stud Wall Anchor Bolts	1/30/2017	2/5/2017	1/31/2017	1		Closed
0876	Section Detail at South Elevation Piers	2/1/2017	2/8/2017	2/27/2017	26	19	Closed
0877	Stair 4 Connection at Level 5	2/2/2017	2/9/2017		740	733	Internal Review
0878	Guestroom C3 Electrical Bathroom Conflicts	2/2/2017	2/9/2017	3/6/2017	32	25	Closed
0879	Spa Light Cove Ceiling Height	2/2/2017	2/9/2017	3/3/2017	29	22	Closed
0880	Pool Fountain Housing Drain Lines	2/6/2017	2/13/2017	2/6/2017	0		Closed
0881	Roof Cornice Gutter Connection to Downspout	2/6/2017	2/15/2017	2/10/2017	2		Closed
0882	Crane Opening Hanging Form Size	2/8/2017	2/15/2017	2/10/2017	2		Closed
0883	2PTB-6 at Dining Room Soffit	2/13/2017	2/20/2017	4/20/2017	66	59	Closed
0884	Plaster Ceiling Detail	2/14/2017	2/21/2017	3/10/2017	24	17	Closed
0885	Guestroom Shower Waterproofing and Curb Detail	2/14/2017	2/21/2017	3/24/2017	38	31	Closed
0886	Missing Drain Sleeves L5 (Col. 38)	2/15/2017	2/22/2017	3/12/2017	25	18	Closed
0887	LAV 3 Different Spec	2/15/2017	2/22/2017	7/19/2017	154	147	Closed
0889	Luggage Room Air Supply	2/16/2017	2/23/2017	2/16/2017	0		Closed
0890	Roof Detail @ Parapet Returns	2/16/2017	2/23/2017	4/28/2017	71	64	Closed
0891	Smoke Screen Steel Channel Installation Detail	2/16/2017	2/23/2017	2/27/2017	11	4	Closed
0892	Lighting Control Station Column A26	2/16/2017	2/23/2017	4/12/2017	55	48	Closed
0893	Mechanical Control Panel Locations	2/16/2017	2/23/2017	5/7/2017	80	73	Closed
0894	Lightning Protection Mast Location and Connection	2/17/2017	2/24/2017	2/20/2017	3		Closed
0895	Ninth Floor Damper Classification	2/20/2017	2/27/2017	3/13/2017	21	14	Closed
0896	Precast @ South Elevation Storefront Doors	2/22/2017	3/1/2017	6/19/2017	117	110	Closed
0899	Attic Space Walk Way Routing and Access	2/24/2017	3/3/2017	2/24/2017	0		Closed
0900	Public Area Thermostats	2/24/2017	3/3/2017	3/10/2017	14	7	Closed
0901	SD-1 Plenum @ Spa Retail Wall Change	2/24/2017	3/3/2017	2/27/2017	3		Closed
0902	8th Floor CMU to 9th Floor Slab Connection	2/27/2017	3/6/2017	3/6/2017	7		Closed
0903	Exterior Terrace Tile Grout	2/27/2017	3/6/2017	3/10/2017	11	4	Closed
0904	SI 38 Added Transformer	2/27/2017	3/6/2017	6/5/2017	98	91	Closed
0905	SI 38 MSB2 GFCI	2/28/2017	3/7/2017	2/28/2017	0		Closed
0906	SI 34 Elevator Lobby Horn Strobe Location	2/28/2017	3/7/2017	3/21/2017	21	14	Closed
0907	Server 145 Discreet Diffuser	3/4/2017	3/11/2017	3/6/2017	2		Closed
0908	Spa Retail Ceiling Lighting	3/6/2017	3/15/2017	3/6/2017	0		Closed
0909	SI 32 - SPS Location	3/9/2017	3/16/2017	3/20/2017	11	4	Closed
0910	First Floor PT Tendon Repair Stressing Report	3/9/2017	3/16/2017	3/9/2017	0		Closed
0911	Second Floor PT Tendon Repair Stressing Results	3/9/2017	3/16/2017	3/9/2017	0		Closed
0912	Foyer Storefront Rough Openings	3/9/2017	3/16/2017	3/31/2017	22	15	Closed
0913	Restroom 223 Baby Changing Station	3/9/2017	3/16/2017	4/20/2017	42	35	Closed
0914	Lower Level Concrete Painting Color	3/10/2017	3/17/2017	3/24/2017	14	7	Closed
0915	Ballroom RCP Conflict With Ducts	3/10/2017	3/17/2017	5/5/2017	56	49	Closed
0917	Stair 3&4 Pressurization Duct Grille Heights	3/15/2017	3/22/2017	3/15/2017	0		Closed
0918	Level 1 Spa/Retail Duct and Lighting Conflict	3/15/2017	3/22/2017	3/27/2017	12	5	Closed
0919	Guestroom Switch Alignment	3/15/2017	3/22/2017	4/10/2017	26	19	Closed
0920	Stucco to PVC Roofing Detail	3/21/2017	3/28/2017	4/28/2017	38	31	Closed
0921	Insulation Type Under Pool Deck Slab	3/21/2017	3/28/2017	3/27/2017	6		Closed
0922	Room D1 Sprinkler Conflict	3/21/2017	3/28/2017	5/4/2017	44	37	Closed
0923	Cabana Column Wall Type	3/22/2017	3/29/2017	3/24/2017	2		Closed
0924	Terrace Tile Base Height	3/22/2017	3/29/2017	3/22/2017	0		Closed
0926	Room Type C3 Closet	3/27/2017	4/3/2017	4/6/2017	10	3	Closed
0927	Ballroom Vaulted Ceiling MEP Chaseway	3/27/2017	4/3/2017	6/6/2017	71	64	Closed
0928	Ballroom Ext Sign Mounting Location	3/27/2017	4/3/2017	4/7/2017	11	4	Closed
0929	L2 1 Lights at Foyer 101	3/27/2017	4/3/2017	3/30/2017	3		Closed
0930	Etched Glass at Foyer 101 and Stair 4	3/27/2017	4/3/2017	3/31/2017	4		Closed
0931	Ballroom Ceiling High Can Lights	3/28/2017	4/4/2017	5/15/2017	48	41	Closed
0932	GR 737 & 739 HFCU Shift	3/30/2017	4/6/2017	4/17/2017	18	11	Closed
0933	Elevator 1-4 Roof Parapet Cap Detail	3/30/2017	4/6/2017	4/11/2017	12	5	Closed
0934	DW-01 Light Fixture at Foyer	3/30/2017	4/6/2017	4/13/2017	14	7	Closed
0935	Fitness Room Ceiling Type	3/31/2017	4/7/2017	4/6/2017	6		Closed
0936	Entry Foyer Grille Type	4/3/2017	4/10/2017	4/28/2017	25	18	Closed
0937	Room 415 Closet Grille/Crown Conflict	4/3/2017	4/10/2017	4/10/2017	7		Closed
0938	Room 640 Beam/IVAC Coordination	4/3/2017	4/10/2017	4/17/2017	14	7	Closed

0939	Master Guestroom On Off Switch	4/3/2017	4/10/2017	4/5/2017	2		Closed
0940	Room C4 Pocket Door Conflict	4/3/2017	4/10/2017	5/4/2017	31	24	Closed
0941	C3 Thermostat Locations	4/4/2017	4/11/2017	4/5/2017	1		Closed
0942	Restroom Vestibule 225V Fire Rating	4/10/2017	4/17/2017	4/10/2017	0		Closed
0943	Managers Apartment Thermostats	4/10/2017	4/17/2017	5/19/2017	39	32	Closed
0944	Expanded Suite Type F VFCU Power	4/10/2017	4/17/2017	4/17/2017	7		Closed
0945	RFI 0861 Follow Up - L3 Elec Room	4/10/2017	4/17/2017	4/24/2017	14	7	Closed
0946	Concierge Lounge TV Box	4/10/2017	4/17/2017	4/10/2017	0		Closed
0947	Guestroom Thermostat Programming and Set Points	4/13/2017	4/20/2017	5/4/2017	21	14	Closed
0948	Private Dining Wainscot	4/13/2017	4/20/2017	4/14/2017	1		Closed
0949	Flat Tile Floors	4/17/2017	4/24/2017	4/21/2017	4		Closed
0950	Chair Rail Size	4/19/2017	4/26/2017	5/11/2017	22	15	Closed
0951	1st Floor Spa Retail Casework Paint Color	4/24/2017	5/1/2017	4/27/2017	3		Closed
0952	Mechanical Control Panel Power Provisions	4/26/2017	5/3/2017	5/3/2017	7		Closed
0953	Level 3 Guestroom Juliet Base	4/26/2017	5/3/2017	5/17/2017	21	14	Closed
0954	Second Floor Dome Light Layout	4/27/2017	5/4/2017	4/28/2017	1		Closed
0955	First Floor Employee Restroom Wetwalls	4/27/2017	5/4/2017	4/28/2017	1		Closed
0956	Exterior Carolina Lantern Circuits	4/27/2017	5/4/2017	5/4/2017	7		Closed
0957	EIFS Color L3 East Elevation	4/28/2017	5/5/2017	5/15/2017	17	10	Closed
0958	Expanded Guest Suite VFCU Thermostat	4/28/2017	5/5/2017	4/29/2017	1		Closed
0960	Final Fixture Schedules	5/3/2017	5/10/2017	6/31/2017	120	113	Closed
0961	Guestroom Closet Light Fixture	5/7/2017	5/14/2017	5/8/2017	1		Closed
0962	Carolina Lantern Accessory Location	5/7/2017	5/14/2017	5/24/2017	17	10	Closed
0963	Rooftop Bar LN Fixture	5/9/2017	5/16/2017	5/9/2017	0		Closed
0964	Guest Bathroom Type 6 Tub Faucet Orientation	5/10/2017	5/17/2017	5/15/2017	5		Closed
0965	SI39 Electrical Coordination with Furniture	5/10/2017	5/17/2017	6/23/2017	44	37	Closed
0967	First Floor Dome Rotunda Light Layout	5/15/2017	5/22/2017	5/15/2017	0		Closed
0968	Plumbing above Elevator Equipment - 800M	5/16/2017	5/23/2017	5/16/2017	0		Closed
0970	Lobby LD Diner Mounting Location	5/17/2017	5/24/2017	5/19/2017	2		Closed
0971	Guestroom A16 Shower Niche	5/17/2017	5/24/2017	5/24/2017	7		Closed
0972	Guestroom C1 Closet Access	5/18/2017	5/25/2017	6/15/2017	28	21	Closed
0973	Guestroom 415 VFCU Duct Routing	5/18/2017	5/25/2017	5/31/2017	13	6	Closed
0975	Level 4 Corridor HFCU Conflict	5/26/2017	6/2/2017	6/23/2017	28	21	Closed
0976	Upper Dining Soffit Heights	5/30/2017	6/6/2017	6/13/2017	14	7	Closed
0977	Room 304 - Barn Door Conflict	5/31/2017	6/7/2017	6/7/2017	7		Closed
0978	Guestroom Decorative Access Panel Size Change	5/31/2017	6/7/2017	5/31/2017	0		Closed
0979	Guestroom D1 Cased Opening Height	5/31/2017	6/7/2017	6/20/2017	20	13	Closed
0980	Third Floor Terrace In Swing Doors Hardware	6/1/2017	6/8/2017	6/23/2017	22	15	Closed
0981	Guest Bathroom Ceiling Light Layout	6/1/2017	6/8/2017	6/7/2017	6		Closed
0982	Guestroom 531 Drop Beam Conflict	6/4/2017	6/11/2017	6/7/2017	3		Closed
0983	Guestroom A16 Sprinkler Conflict At Window	6/4/2017	6/11/2017	6/28/2017	25	18	Closed
0984	Patisserie Wall Section 1X Primed Poplar	6/5/2017	6/12/2017	6/5/2017	0		Closed
0985	Elevator 06 Smoke Relief	6/5/2017	6/12/2017	6/6/2017	1		Closed
0986	Guestroom D1 Entry Closet Confirmation	6/7/2017	6/14/2017	6/15/2017	8	1	Closed
0988	SI 39 - Concierge Alcove Revision	6/8/2017	6/15/2017	6/13/2017	5		Closed
0989	Room 348 - Grill conflict with soffit	6/13/2017	6/20/2017	6/13/2017	0		Closed
0990	Room 535 - Bedroom Sprinkler	6/13/2017	6/20/2017	6/28/2017	15	8	Closed
0991	ADA Bathroom Control Valve Locations	6/13/2017	6/20/2017	6/13/2017	0		Closed
0992	Water Closet Room Ceiling Height	6/13/2017	6/20/2017		609	602	Internal Review
0993	SI 47 Spa Retail Desk	6/13/2017	6/20/2017	6/23/2017	10	3	Closed
0994	3rd Floor Portal Heights	6/14/2017	6/21/2017	6/16/2017	2		Closed
0995	Window Blank Off Panel in Shower Areas	6/15/2017	6/22/2017	7/17/2017	32	25	Closed
0996	Guestroom Floor BOH&Corridor Ductwork/Ceiling Conflicts	6/16/2017	6/23/2017	7/14/2017	28	21	Closed
0997	Pool Deck Piers - Clarification	6/16/2017	6/23/2017	6/16/2017	0		Closed
0998	Spray Fireproofing in Bathroom - Confirming	6/16/2017	6/23/2017	6/16/2017	0		Closed
1000	Rooftop Terrace Electrical Switches - Alternate	6/20/2017	6/27/2017	6/28/2017	8	1	Closed
1001	Room 342 - Indicator Bell Relocation	6/20/2017	6/27/2017	6/20/2017	0		Closed
1002	Man/Pedi PT-21 Tile Layout	6/20/2017	6/27/2017	6/23/2017	3		Closed
1003	Elevator Bump Out Design	6/21/2017	6/28/2017	7/6/2017	15	8	Closed
1004	Guestroom 315, 415, 515 Furniture Conflict	6/22/2017	6/29/2017	7/28/2017	36	29	Closed
1005	Guestroom 606 and 706 Condensate Line Conflict	6/22/2017	6/29/2017		600	593	Internal Review
1006	Condensate Pump Electrical Requirements	6/23/2017	6/30/2017	7/5/2017	12	5	Closed
1007	Light Conflict with HFCU units in Guestroom 503, 507, 513, 537	6/23/2017	6/30/2017	6/26/2017	3		Closed
1008	RTWRW and RTERW Threshold Conflict	6/28/2017	7/3/2017	7/17/2017	21	14	Closed
1009	Bar 148 Bar Location Coordination	6/28/2017	7/3/2017	6/30/2017	4		Closed
1010	Ballroom Roof - Ridge Vent Conflict	6/28/2017	7/5/2017	6/28/2017	0		Closed
1011	Patisserie West Door Millwork Details	7/5/2017	7/12/2017	7/5/2017	0		Closed
1012	Camellias Lounge Back Bar Countertop Edge	7/5/2017	7/12/2017	7/20/2017	15	8	Closed
1013	#2 BAR Comment: Sealant Joint and Caulk Color	7/5/2017	7/12/2017		587	580	Open
1014	#3 BAR Comment: Column Shaft Overhang	7/5/2017	7/12/2017		587	580	Open
1017	#12 BAR Comment: Lantern Sizes	7/5/2017	7/12/2017		587	580	Open
1018	Precast Detail over Garage Entry	7/6/2017	7/13/2017	7/10/2017	4		Closed
1019	Stone Countertop Remarks in the Patisserie	7/6/2017	7/13/2017	7/26/2017	20	13	Closed
1020	Stone Countertop Remarks in the Bridal Suite	7/6/2017	7/13/2017	7/11/2017	5		Closed
1021	Stone Countertop Remarks in Mens/Womens Restroom	7/6/2017	7/13/2017	7/24/2017	18	11	Closed
1022	Stone Countertop Remarks at the Concierge Lounge Fireplace	7/6/2017	7/13/2017	7/24/2017	18	11	Closed
1023	Wine Cooler Condensing Unit Mounting	7/7/2017	7/14/2017	7/12/2017	5		Closed
1024	Wine Cooler Supply and Return Air Grilles	7/7/2017	7/14/2017	7/28/2017	21	14	Closed
1025	Fire Damper in room 533	7/10/2017	7/17/2017	7/10/2017	0		Closed
1026	Retaining Wall - Confirmation	7/10/2017	7/17/2017	7/14/2017	4		Closed
1028	Level 9 Electrical Coordination	7/12/2017	7/19/2017	9/3/2017	53	46	Closed
1029	Retaining Wall at the Chiller Yard	7/12/2017	7/19/2017	7/24/2017	12	5	Closed
1030	Lower Level CMU Paint Color	7/13/2017	7/20/2017	7/14/2017	1		Closed
1031	Call Buttons & Position Indicator for Elevator Bump Out (L1 & 2)	7/14/2017	7/21/2017	7/28/2017	14	7	Closed
1032	3rd Floor Terrace Drain Against CMU	7/17/2017	7/24/2017	7/17/2017	0		Closed
1033	Control Valves Above Bar 148	7/18/2017	7/25/2017	7/20/2017	2		Closed
1034	9th Floor Fire Rated Ductwork - Stair 4	7/19/2017	7/26/2017	7/24/2017	5		Closed
1035	East Atrium Hardscape Material	7/19/2017	7/26/2017	8/2/2017	14	7	Closed
1036	Patisserie Doorway & Electrical Relocation	7/26/2017	7/27/2017	7/28/2017	2	1	Closed
1037	Stucco Color Clarification	7/26/2017	7/27/2017	8/1/2017	12	5	Closed
1038	6th Floor Terrace Roof North Ends	7/24/2017	7/31/2017	8/3/2017	10	3	Closed
1039	RT18 and RT20 Bathroom Doors/Ceiling Conflict	7/24/2017	7/31/2017	7/28/2017	4		Closed
1040	Ballroom Four Lighting Revisions	7/24/2017	7/31/2017	7/25/2017	1		Closed
1042	Ballroom Column H34 Drywall Wrap	7/24/2017	7/31/2017	7/25/2017	1		Closed
1043	Elevator 5 Sump Drain Location	7/24/2017	7/31/2017	8/2/2017	9	2	Closed
1044	Guestroom Common Door Threshold	7/24/2017	7/31/2017	7/31/2017	7		Closed
1045	WD-10 in Managers Suite Spec	7/25/2017	8/1/2017	7/26/2017	1		Closed
1046	ADA Tub Niches	7/25/2017	8/1/2017	7/31/2017	6		Closed
1047	Guestroom Crown and Air Grille Conflicts	7/25/2017	8/1/2017	8/4/2017	10	3	Closed

1048	Jamb Switch in Guestroom Approval	7/25/2017	8/1/2017	8/4/2017	10	3	Closed
1049	Level 2 Kitchen - Device Locations	7/26/2017	8/2/2017	8/9/2017	14	7	Closed
1050	Level 3 Terrace Divider Wall Follow Up	7/26/2017	8/2/2017	8/29/2017	34	27	Closed
1051	Guestroom 603 TV and VFCU Conflict	7/26/2017	8/2/2017	8/4/2017	9	2	Closed
1052	Level 6 Eyebrow Roof Soffit Orientation	7/26/2017	8/2/2017	8/3/2017	8	1	Closed
1053	Chilled Water Conflicts in Closet Ceilings	7/26/2017	8/2/2017	8/4/2017	9	2	Closed
1054	Guestroom 533 Conflicts	7/26/2017	8/2/2017	7/31/2017	5		Closed
1055	Guestroom 402 and 502 Light in Shower Conflict	7/26/2017	8/2/2017	7/31/2017	5		Closed
1056	Tub Valve Orientation	7/26/2017	8/2/2017	8/2/2017	7		Closed
1057	Conderge Lounge Ceiling Heights	7/27/2017	8/3/2017	8/28/2017	32	25	Closed
1058	Room 619S Light Layout	7/27/2017	8/3/2017	8/10/2017	14	7	Closed
1061	Guestroom 501 and 601 Light Conflicts	7/27/2017	8/3/2017	8/11/2017	15	8	Closed
1062	Guestroom 640 Soffit Issue	7/27/2017	8/3/2017	8/10/2017	14	7	Closed
1063	Operable Wall at PTB Soffit Framing	7/29/2017	8/5/2017	7/31/2017	2		Closed
1064	Guestroom Vertical Fan Coil Units	7/29/2017	8/5/2017	7/31/2017	2		Closed
1065	Formglass Trim Over Curved Diffuser	8/1/2017	8/8/2017	8/7/2017	6		Closed
1066	Marquis Tension Bar Diameter	8/1/2017	8/8/2017	8/3/2017	2		Closed
1067	Trench Drain by Transformer	8/2/2017	8/9/2017	8/10/2017	8	1	Closed
1068	Pipe Stub Ups for Future at Third Floor Terrace	8/3/2017	8/10/2017	8/11/2017	8	1	Closed
1069	Elevator 06 Smoke Seal Offset	8/7/2017	8/14/2017	8/7/2017	0		Closed
1070	Guestroom 510 Soffit Issue	8/7/2017	8/14/2017	8/15/2017	8	1	Closed
1071	Boardroom Access Panel conflict with Soffit	8/7/2017	8/14/2017	8/15/2017	8	1	Closed
1073	Ballroom One Diffusers Tie-In to Soffit Trim	8/8/2017	8/15/2017	8/22/2017	14	7	Closed
1074	Conderge Lounge Linear Diffuser	8/9/2017	8/16/2017	8/8/2017	0		Closed
1075	Elevator Life Safety Panel Location	8/9/2017	8/16/2017	8/9/2017	0		Closed
1077	Downspout Locations at Nanawalls	8/10/2017	8/17/2017	9/12/2017	33	26	Closed
1078	Guestroom 515 Vanity Coordination	8/11/2017	8/18/2017	9/21/2017	41	34	Closed
1079	Elevator 1-2 Smoke Relief Damper Sawcut	8/11/2017	8/18/2017	8/18/2017	7	0	Closed
1080	Liquor Shelf Riser Laminate Type	8/14/2017	8/21/2017	8/7/2017	24	17	Closed
1081	Elevators 1-5 Card Reader Location	8/15/2017	8/22/2017	9/26/2017	42	35	Closed
1082	Conderge Lounge HFCU and Bookcase Conflict	8/17/2017	8/24/2017	8/18/2017	1		Closed
1083	Guestroom 639 Shower Wall	8/18/2017	8/25/2017	8/29/2017	11	4	Closed
1084	9th Floor Public Area Lights	8/18/2017	8/25/2017	8/31/2017	13	6	Closed
1085	Guestroom 639 Ceiling and Soffit Height	8/22/2017	8/29/2017	9/5/2017	14	7	Closed
1088	Section Cut for Door Type "R"	8/23/2017	8/30/2017	8/28/2017	5		Closed
1089	Guestroom 302 Shower Crown	8/23/2017	8/30/2017	9/7/2017	15	8	Closed
1090	Elevator 5 Alcove Ceiling Height	8/23/2017	8/30/2017	9/5/2017	13	6	Closed
1091	Level 1 Precast Window Surrounds	8/28/2017	9/2/2017	9/12/2017	17	10	Closed
1092	CMU Patch At Buckshot Support	8/28/2017	9/2/2017	8/28/2017	2		Closed
1093	Guestroom 603 TV Wall Conflict	8/28/2017	9/4/2017	9/14/2017	17	10	Closed
1094	SI 39 Floor Box Relocation	8/29/2017	9/5/2017	9/5/2017	7		Closed
1095	Conderge Lounge HVAC Grille Relocation	8/29/2017	9/5/2017	8/29/2017	0		Closed
1096	Level 8 Low Voltage Riser Routing	8/30/2017	9/5/2017	9/5/2017	6		Closed
1097	Stucco Re-Coat Confirmation	8/30/2017	9/5/2017	8/31/2017	1		Closed
1098	Camillas Lounge Bar Wall Construction	8/30/2017	9/6/2017	10/23/2017	54	47	Closed
1099	Guestroom 533 Closet Light Fixture Location	8/30/2017	9/6/2017	9/5/2017	6		Closed
1100	Rooftop Bar Community Table Floor Box Location	8/30/2017	9/6/2017	9/5/2017	6		Closed
1101	741 Managers Apartment Supply Grille Location	8/31/2017	9/7/2017	9/5/2017	5		Closed
1102	Guestroom 701 Soffit and HFCU Conflict	8/31/2017	9/7/2017	9/5/2017	5		Closed
1103	Service Entry Gates and Rails - Color	9/1/2017	9/8/2017	9/8/2017	7		Closed
1104	9th Floor Air Device Location	9/1/2017	9/8/2017	9/22/2017	21	14	Closed
1105	Rm Type F2 Missing Outlet	9/5/2017	9/12/2017	9/5/2017	0		Closed
1106	SF-01 Paint Substitution	9/5/2017	9/12/2017	9/7/2017	2		Closed
1108	Caulk Color Change at Water Chestnut Stucco Control Joints	9/6/2017	9/13/2017	9/6/2017	0		Closed
1109	Location for TV Low Voltage in Patiserie	9/7/2017	9/14/2017	9/12/2017	5		Closed
1111	DC-29 Driver Location	9/12/2017	9/19/2017	10/5/2017	23	16	Closed
1112	DC 37 Location and Driver Coordination	9/12/2017	9/19/2017	9/15/2017	3		Closed
1113	6th Floor Managers Apartment Can Lights	9/13/2017	9/20/2017	9/15/2017	2		Closed
1114	Camillas Lounge Return Air Grill	9/14/2017	9/21/2017	9/14/2017	0		Closed
1115	Rooftop East Vent Stack	9/14/2017	9/21/2017	9/15/2017	1		Closed
1116	Knox Box Submittal Comments	9/18/2017	9/25/2017	10/5/2017	17	10	Closed
1117	Grand Stair Guardrail PT Color	9/18/2017	9/25/2017	10/5/2017	17	10	Closed
1118	639/739/839 Vanity Outlet	9/19/2017	9/26/2017	12/8/2017	80	73	Closed
1119	Mgr. Apt. Level 6 Bathroom Ceiling Height	9/19/2017	9/26/2017	9/25/2017	8		Closed
1120	Guestroom 703 Sprinkler Location	9/22/2017	9/29/2017	9/22/2017	0		Closed
1121	Room 719 and 819 Supply Duct	9/22/2017	9/29/2017	10/5/2017	13	6	Closed
1122	SI 52 Missing Paint Finishes	9/25/2017	10/2/2017	10/9/2017	14	7	Closed
1123	Conderge Lounge Fireplace Framing	9/26/2017	10/3/2017	12/8/2017	73	66	Closed
1124	Boardroom Return Air Grille	9/28/2017	10/5/2017	10/25/2017	27	20	Closed
1125	Stair 7 and 8 Finish Materials	9/28/2017	10/5/2017	10/17/2017	19	12	Closed
1126	Bar RT10 Center Coffey Light Layout	9/29/2017	10/6/2017	10/4/2017	5		Closed
1127	First and Second Floor Kitchen Ice Maker CHW Feed	10/2/2017	10/9/2017	10/3/2017	1		Closed
1128	linen/Storage Ceiling Heights	10/3/2017	10/10/2017	10/9/2017	8		Closed
1129	GRM 240 Furniture Installation	10/3/2017	10/10/2017	10/6/2017	3		Closed
1130	Guestroom Thermostat Heights	10/9/2017	10/16/2017	11/2/2017	24	17	Closed
1131	P-3 Color Selection	10/10/2017	10/17/2017	10/12/2017	2		Closed
1132	P-01 Finish Selection	10/10/2017	10/17/2017	10/12/2017	2		Internal Review
1134	Stained Doors - Finish	10/12/2017	10/19/2017	11/13/2017	32	25	Closed
1135	Camillas Lounge Bar Top Size	10/12/2017	10/19/2017	10/23/2017	11	4	Closed
1136	Guestroom 533 Ceiling Height at Tub	10/12/2017	10/19/2017	12/7/2017	56	49	Closed
1137	Stair 04 L5-B Lighting	10/13/2017	10/20/2017	10/13/2017	0		Closed
1138	TV Panel FFE Modifications	10/13/2017	10/20/2017	11/2/2017	20	13	Closed
1139	MAU Roof Hydrant Type and Location	10/16/2017	10/23/2017	10/26/2017	10	3	Closed
1141	Marquis Sign Electrical Requirements	10/18/2017	10/25/2017	10/19/2017	1		Closed
1142	Guestroom 347,447,547 Vanity Depth	10/18/2017	10/25/2017	11/2/2017	15	8	Closed
1143	Level 6 Terrace Bracket Layout	10/19/2017	10/26/2017	11/2/2017	14	7	Closed
1144	Room 323 Soffit Layout	10/19/2017	10/26/2017	11/9/2017	21	14	Closed
1146	Ceiling Diffuser Size at Roof Pantry	11/2/2017	11/1/2017	11/9/2017	7	8	Closed
1147	Molding Around DW-19 in Ballroom	10/25/2017	11/1/2017	10/26/2017	1		Closed
1148	9th Floor Ceiling Air Device Fire Dampers	10/25/2017	11/1/2017	10/27/2017	2		Closed
1150	Dome Rotunda Ceiling Paint Color	10/30/2017	11/6/2017	11/9/2017	10	3	Closed
1151	Dish Washer Exhaust Fan Power Requirements	11/1/2017	11/8/2017	11/4/2017	3		Closed
1152	Camillas Lounge GFRG Palm Finish	11/1/2017	11/8/2017	12/11/2017	40	33	Closed
1154	Kitchen Step Down Gas Regulator Location	11/6/2017	11/13/2017		463	456	Internal Review
1155	Guestroom 639 Donut Dimensions	11/7/2017	11/14/2017		462	455	Internal Review
1157	Wheel Chair Lift Tile Size	11/8/2017	11/15/2017	11/8/2017	0		Closed
1158	Ballroom Ceiling Drywall Between Crown Paint	11/9/2017	11/16/2017	11/13/2017	4		Closed
1159	Guestroom Entry Door Paint Transition	11/9/2017	11/16/2017	11/14/2017	5		Closed
1160	Pool Storage RT16 Floor Drain	11/10/2017	11/17/2017	11/10/2017	0		Closed

1161	ADA Bathroom (Type 3) Wall Finish	11/15/2017	11/22/2017	11/16/2017	1		Closed
1162	Guestroom 839 Column Addition	11/15/2017	11/22/2017	11/28/2017	13	6	Closed
1163	Room 136 MDF Ceiling	11/15/2017	11/22/2017	11/15/2017	0		Closed
1164	Guestroom 839 Duct Relocation	11/17/2017	11/24/2017	11/17/2017	0		Closed
1165	Laundry Washer Trough Drain	11/20/2017	11/27/2017		449	442	Closed
1166	Rooftop Pantry Kitchen Hood Height	11/20/2017	11/27/2017	12/13/2017	23	16	Closed
1168	Marquee Canopy Structural Modification	12/4/2017	12/11/2017	12/7/2017	3		Closed
1170	Inspection DN#58 Resolution	12/5/2017	12/12/2017	1/11/2018	37	30	Closed
1171	Lighting Storage Room Cooling Requirements	12/5/2017	12/12/2017	12/13/2017	8	1	Closed
1172	Elevator 1-4 Guestroom Floor Trim	12/6/2017	12/13/2017	12/19/2017	13	6	Closed
1173	Elevator 6 Position Indicator	12/6/2017	12/13/2017	12/8/2017	2		Closed
1175	Site Light Layout	12/8/2017	12/15/2017	1/23/2018	46	39	Closed
1177	Added Crown at Ballroom Vaulted Ceiling	12/12/2017	12/19/2017	12/14/2017	2		Closed
1178	Stucco Color @ Garage and Screen Wall	12/13/2017	12/20/2017	1/11/2018	29	22	Closed
1179	Exterior Atrium Center Sidewall Sprinkler Head	12/13/2017	12/20/2017		426	419	Internal Review
1180	Guestroom 610/644 TV Panel Conflict	12/14/2017	12/21/2017	12/14/2017	0		Closed
1181	Marquee Canopy Scaffolding	12/18/2017	12/26/2017	12/19/2017	0		Closed
1182	SPF 1 & SPF 2 Outlet Orientation	12/22/2017	12/29/2017	12/22/2017	0		Closed
1183	ADA Guestroom Shower Glass Panel	1/2/2018	1/9/2018	3/19/2018	78	69	Closed
1184	Booster Heater Warewasher Single Point Connection	1/16/2018	1/23/2018	3/16/2018	59	52	Closed
1185	Guestroom Shower Escutcheon Caulk	1/17/2018	1/24/2018	1/23/2018	6		Closed
1186	Rm Type D2 Vanity Conflict	1/18/2018	1/25/2018	2/1/2018	14	7	Closed
1187	Master Light Switch Font	1/19/2018	1/26/2018	2/1/2018	13	6	Closed
1188	Spa Retail Stone Selection	1/23/2018	1/30/2018	2/6/2018	14	7	Closed
1189	Concierge Alcove Desk Stone Top Selection	1/24/2018	1/31/2018	2/6/2018	13	6	Closed
1190	Camellias Lounge Back Bar Refrigerator Leg Kit	1/31/2018	2/7/2018	2/8/2018	8	1	Closed
1192	Pool Heater Air Intake and Exhaust Routing	2/5/2018	2/12/2018	3/27/2018	50	43	Closed
1193	IDF X001 Fire Rating	2/6/2018	2/13/2018	2/7/2018	1		Closed
1195	Entry Foyer Hopes Doors Transom	2/12/2018	2/19/2018	2/13/2018	1		Closed
1196	Fitness Room Linear Light Fixture End Condition	2/12/2018	2/19/2018		365	358	Internal Review
1197	Spa Retail Vestibule Discreet HVAC	2/13/2018	2/20/2018	2/14/2018	1		Closed
1198	Room Type F4 and F3 Trim Detail	2/14/2018	2/21/2018	3/1/2018	15	8	Closed
1199	Level 3 Corridor Exit Sign Conflict	2/22/2018	3/1/2018	3/1/2018	7		Closed
1201	Suite Carpet Orientation	3/7/2018	3/14/2018	3/8/2018	1		Closed
1202	CCD 004 - TV Wall Dimensions	3/23/2018	3/30/2018	3/30/2018	7		Closed
1204	Main Entryway Stucco Color	3/28/2018	4/4/2018	4/4/2018	7		Closed
1205	Patisserie Wainscot Finish	4/25/2018	5/2/2018	4/25/2018	0		Closed
1207	Garage Door Controller Location	5/8/2018	5/15/2018		280	273	Closed
1209	CCD-08 Managers Apartment Master Bath Clarifications	6/1/2018	6/8/2018		256	249	Internal Review
1210	Manager Apartment Kitchen Phone	6/5/2018	6/12/2018	6/8/2018	3		Closed
1211	Barn Door Guide	6/8/2018	6/15/2018	6/11/2018	3		Closed
1212	Concierge Toilet Lav Type	6/27/2018	7/4/2018	7/5/2018	8	1	Closed
1213	Patisserie Fire Extinguisher Cabinet Location	7/9/2018	7/16/2018		218	211	Open
1215	Fitness Room Sidefight	8/2/2018	8/9/2018	8/8/2018	6		Closed
1216	Spa Fire Extinguisher Cabinet	8/13/2018	8/20/2018		183	176	Open
1217	Concierge Buffet Outlets	8/23/2018	8/30/2018		173	166	Closed
1222	Manager's Apt Kitchen Sink, KS-2	10/2/2018	10/5/2018	10/2/2018	0		Closed
1223	CCD 039 - Wine Cooler Clarifications	11/28/2018	12/5/2018	12/5/2018	7		Closed
1224	Elevator Inspection Requirements	12/3/2018	12/10/2018		71	64	Open

Report Total:
1,136

TOTAL
439

Plaintiff Balfour Beatty's Trial Exhibit # 11

PLAINTIFF'S
EXHIBIT 28
Brown
8-5-20 TB

Exhibit XX The Hotel at Marion Square - Balfour Beatty Construction Master Request for Change Order Log

RCO	Description	Date of Most Recent Submission	Pending	Submitted	Approved	Rejected	Executed Date	OCO	Comments
1	Rebar at PT Slab to Capping Beam Connection	9/1/2015			\$ 5,291.99		9/17/2015	1	
2	Increased Bracing Size and cap beam					\$ 11,595.00		Void See CCO 001	
3	Busport Pricing	1/26/2016			\$ 21,647.07		3/31/2016	2	
4	Added Piles and Pile Cap Column J-23				\$ 9,289.94		9/17/2015	1	
5	FFE Warehousing Scope Addition				\$ 106,944.20		9/17/2015	1	
6	Stucco Limestone Finish Upgrade				\$ 154,383.76		9/17/2015	1	
7	Bentonite Geotextile Waterproofing Foundation Shop Drawings	12/11/2015			\$ 12,288.10		3/31/2016	2	
8	Chester Horizon Gutter System				\$ 23,066.40		9/17/2015	1	
9	Kitchen Equipment Scope Addition	2/17/2016			\$ 1,032,612.25		4/4/2016	3	
10	Epoxy Flooring In Lieu of Quarry Tile-NOTE VE ITEM IN GMP				\$ (20,010.09)		9/17/2015	1	
11	Change size of Switchboard LSP from 1600A to 2000A	10/1/2015			\$ 20,436.27		3/31/2016	2	
12	Factory Primed Guestroom Entrance Doors				\$ 9,314.63		9/17/2015	1	
13	Revise LV Point of Entry per Actual Services Provided - Void					0		Not Executed	
14	Revise structural drawings to delete 4 columns in the ballroom	10/29/2015			\$ 4,947.25		2/24/2016	3	
15	Added Concrete and Rebar at Capping Beam Penetrations-RFI-084 RFI 0123	10/12/2015			\$ 5,826.46		11/12/2015	2	
16	Finish Hardware Questions Response to RFI 0083					\$ 32,470.05		Assa Abloy Change	
17	Sheet Pile Joint Waterproofing Detail	2/24/2016			\$ 7,496.58		4/30/2016	4	
18	Shower Door Revisions from Submittal Response	2/15/2017			\$ 27,757.27		1/12/2018	9	
19	Shower Door Handle Revision				\$ 50,698.89		2/3/2017	7	
20	MOD 1 Underground Plumbing	3/21/2016			\$ 62,069.57		4/4/2016	3	
21	Tube Mullion Change					\$ 32,030.84			
22	Graham Window	12/17/2015			\$ 183,519.38		7/21/2016	5	
23	Electrical Revisions in Model Room-SI 21	1/15/2016			\$ 3,523.91		5/17/2017	7	
24	Mockup Graham Windows					\$ 14,936.55			
25	Added Millwork Trim Per Model Room Revision Set Dated 2015-10-16, Millwork TV Cabinets, Deleting Trim-SI 21				\$ 4,064.63		6/14/2017	7	
26	Added Barn Door at King Guestroom Mockup	3/7/2017			\$ 3,717.21		3/8/2017	7	
27	100 year storm delay (20 days)			\$ 124,089.10				3	
28	Pool Tile Edge ILO paver Edge				\$ 2,935.72		8/10/2016	5	
29	Guest Room Closet Light Fixtures					\$ 43,753.52			
30	Adding Glass Mosaic Tile to All Queen Guestbaths					\$ 322,014.22			
31	Mockup Glass Tile Mosaic	3/23/2016			\$ 9,732.97		2/3/2017	7	
32	Waterstop at Pile Caps				\$ 23,933.36		3/31/2016	2	
33	Drawing Modification SI 19	7/28/2016			\$ 4,704.65		8/10/2016	5	
34	October, November, and December 2015 Rain Days - Rejected								
35	Elevator 1-4 Entrance Finish Revision				\$ 145,423.14		2/7/2017	6	
36	Watson MOD 1 Drawing Revisions	2/4/2016			\$ (31,965.00)		2/3/2017	6	
37	Cook and Boardman MOD 1 Drawing Revisions					\$ 352.14			
38	Model Room Barn Door Installation				\$ 1,383.99		5/17/2017	7	
39	Utility Design Changes	12/29/2016			\$ 61,424.59		2/21/2017	6	

40	54" Steel Casing Revision				\$ 6,002.17		4/30/2016	4	
41	1000 Year Storm Repair Cost					\$ 124,089.00			
42	Manager's Suite Stair					\$ 42,725.00			
43	Request to Adjust Start Date And Add 20 Days due to 100 Yr Flood								
44	Added valves and access panels for gas line to lanterns					\$ 6,815.00			
45	MOD 1 Drywall Revisions	9/8/2016			\$ 19,540.37		9/14/2016	6	
46	Mechanical Areaway Waterproofing					\$ 345.04			
47	Cap Beam Core Drilling Penetration				\$ 5,241.40		6/15/2016	5	
48	Watson MOD 2 and MOD 4 Drawing Revisions	9/9/2016			\$ 74,419.55		9/14/2016	6	
49	Merit Painting MOD 1 Drawing Revisions	6/5/2018			\$ 9,413.56		7/12/2018	16	
50	Engineering for Acrylic Pool Cover				\$ 8,020.82		7/14/2016	5	
51	Arcylic Pool Cover				\$ 81,099.35		11/20/2016	6	
52	MOD 1 interior glazing revisions	1/13/2017			\$ 2,046.75		2/21/2017	6	
53	Demo Allowance Reconciliation	5/23/2016			\$ (22,490.00)		6/15/2016	5	
54	GMP Allowance Reduction					\$ (200,000.00)			
55	Supplemental Instructions #27 - Slab Fold				\$ 10,311.14		5/3/2017	7	
56	Manufacturer's 20 Year Watertight Warranty on Copper Roof					\$ 27,103.02			
57	Merit Painting MOD 2 Drawing Revisions				\$ 780.37		7/12/2018	16	
58	MOD 2 Drywall Only Revisions-Split Out MEP	4/13/2017			\$ 8,200.10		5/17/2017	7	
59	MOD 1 Plumbing and HVAC Revisions - VOID								
60	REMOVED - MOD 1-3 Submitted together								
61	MOD 4 Revisions (Drywall)	5/23/2017			\$ 26,747.58		6/14/2017	7	
62	RFI-0149, RFI-0405 Roof Truss Revisions	2/1/2017			\$ 19,012.14		5/3/2017	7	
63	Concealed Sprinkler Heads in Guestrooms and Corridors					\$ 22,136.00			
64	Waterproofing buckstrips around windows				\$ 42,237.44		3/8/2017	7	
65	Lotusan Stucco Finish Coat					\$ 56,433.00			
66	NanaWall design change				\$ 11,940.53		8/16/2016	5	
67	SI #25 Drawing Revisions	4/19/2017			\$ 14,713.00		5/17/2017	7	
68	Spring Hinges in lieu of Door Closers on Guestroom Entrances	7/5/2016			\$ (11,517.28)		8/10/2016	5	
69	Guestroom Entry Door Concealed Closers	7/5/2016				\$ 148,301.00			
70	Changes to doors and frames per submittal comments	7/17/2017			\$ 40,623.38		9/6/2017	7	
71	Change to fully welded pocket door frames	7/5/2016				\$ 123,045.00			
72	Guestroom Decorative Grilles	2/21/2017			\$ 86,207.99		5/3/2017	7	
73	Graham Window Louvers	7/31/2017			\$ 17,230.60		9/8/2017	7	
74	Third Floor Terrace Carolina Lanterns	12/12/2016				\$ 20,812.00			
75	Interior Mock Up Tile Revisions			\$ 5,989.93					
76	Demo Column Per RFI 0502	7/7/2016				\$ 12,277.00			
77	Lower Gas Line on Hutson (SCEG)	7/29/2016			\$ 2,565.62		7/29/2016	5	
78	Interior SF08 Allowance Reconciliation	6/7/2017			\$ 257,069.72		6/14/2017	7	
79	Storm Relocation on Hutson, Add Pump - Submitted in MOD 7					\$ 35,000.00			
80	MOD 5 Plumbing Revisions - Void - Submitted with 103								
81	Allowance Reconciliation - Arriscraft Columns and Pedastals in Lobby Area				\$ (109,637.00)		8/16/2017	5	
82	Allowance Reconciliation - Custom Doors on L1 & L2 - Void								
83	RFI-449 Interior Wall Requirements for Mounting Stone					\$ 4,198.00			
84	New Mock Up for BAR	7/24/2017			\$ 123,333.18		8/2/2017	8	
85	RFI 0019 and 425 Garage Ramp Wall Revisions	11/10/2016			\$ 7,213.49		2/21/2017	6	
86	RFI 0714 Room 744 Entry Way South Wall Revisions - VOID								
87	RFI-0738 Pool Deck Revision	11/30/2016			\$ 8,729.59		2/21/2017	6	

88	Lithko Change Orders	3/11/2019	\$ 56,414.30				
89	GRG Ceiling Wells at Mock Up - Void - Combine with 111						
90	Sublevel Sheet Pile Painting Upgrade	1/25/2017		\$ 6,133.57	5/17/2017	7	
91	Private Dining Revisions	2/10/2017		\$ 5,191.30	5/17/2017	7	
92	Grout Behind Precast Base per RJK Report	2/2/2017		\$ 12,348.41	5/17/2017	7	
93	RFI 0745 - SI 26 SAR Change	2/21/2017		\$ 8,332.30	5/3/2017	7	
94	Dishwater Booster Heater Revision	2/7/2017		\$ 22,572.96	5/3/2017	7	
95	Capstone Flashing at L6 and L9	2/13/2017		\$ 20,829.86	2/21/2017	6	
96	Plumbing MODs 1-3 (HVAC Excluded)	2/15/2017		\$ 105,789.00	6/14/2017	7	
97	SI 36 - ID Room Revisions	6/16/2017		\$ 50,924.99	8/2/2017	7	
98	MOD 4 Piping Revisions	2/21/2017		\$ 31,380.00	6/14/2017	7	
99	RFI 473 - Exterior Chilled Water Piping Supports	3/6/2017		\$ 15,507.96	5/17/2017	7	
100	MOD 5 - Electrical	11/17/2017		\$ 14,725.70	11/30/2017	9	
101	MOD 5 - Drywall, Painting	4/24/2017		\$ 22,118.58	6/14/2017	7	
102	MOD 2 and 4 Ductwork Revisions - VOID - RCO 137						
103	MOD 5 Mechanical Revisions	12/16/2017	\$ 290,257.00				
104	MOD 6 - Drawing Revisions	8/31/2017		\$ 41,305.90	8/31/2017	8	
106	Void						
107	MOD 7 - Drawing Revisions	9/27/2017		\$ 88,965.61	10/19/2017	8	
108	Void						
109	Void						
110	PASCO Thru MOD 8						
111	Ceiling Wells in Guestroom Bath-MOD 8	6/12/2017		\$ 135,710.00	7/13/2017	8	
112	Carolina Lantern - Revised Bracket	5/8/2017		\$ 14,292.44	1/12/2018	9	
113	UDS Second Floor Feeder	9/16/2017		\$ 12,653.00	9/21/2017	8	
114	Blank Panel at Covered Windows	4/17/2017		\$ 9,829.00	5/3/2017	7	
115	Elevator 4 - Rear Entry Gunderlin Finish	4/17/2017			\$ 21,037.33		
116	Symmóns Plumbing Fixtures	6/1/2017		\$ 154,230.73	6/14/2017	7	
117	SI 38 - Secondary Feed to MSB2 Electrical Only	7/7/2017		\$ 161,933.00	7/13/2017	7	
118	RFI 451 Added Valves at Guestrooms	6/6/2017	\$ 18,521.08				
119	Lighting Fixture Finish Revisions	5/16/2017		\$ 10,401.00	7/13/2017	7	
120	SI 39 Patisserie Revisions	5/23/2017		\$ 4,636.00	6/11/2017	7	
121	SI 39 - Spa Retail Revisions	7/12/2017		\$ 7,771.00	7/13/2017	7	
122	Structural Delay Claim	11/17/2017	\$ 1,057,057.00				
123	SI 39 - Dining and Private Dining Revision	6/26/2017			\$ 7,761.00		
124	Spa Retail Case and Millwork Revisions	7/12/2017		\$ 2,514.24	7/13/2017	7	
125	Spa Case and Millwork Revisions	8/11/2017		\$ 46,918.00	8/31/2017	8	
126	MOD 2 - Glass Revisions	6/2/2017		\$ 6,933.55	11/30/2017	9	
127	Supplemental Instruction 23	9/21/2017		\$ 61,150.00	9/21/2017	8	
128	SI 39 - Guestroom C3 Light Fixtures	6/5/2017		\$ 3,297.00	7/13/2017	7	
129	RFI 0927 - Ballroom Vaulted Ceiling MEP Chaseway	6/6/2017		\$ 3,864.67	1/25/2018	9	
130	Managers Apartment Revisions				3446		
131	Supplemental Instruction 44				19733		
132	SI 39 - Lobby	6/9/2017			8101		
133	Revised Pocket Door Hardware	6/14/2017		\$ 2,146.09	7/13/2017	7	
134	RFI 0974 Guestroom 315 and 415 Soffit Height	6/15/2017		\$ 1,552.87		16	
135	SI 39 - Stair 4	6/16/2017		\$ 21,136.75	8/2/2017	8	
136	SI 39 - Reception	7/20/2017			1932		

137	MOD 2 and 4 Ductwork Revisions	6/22/2017		\$ 36,510.00		9/21/2017	8
138	Supplemental Instruction 32	10/17/2017		\$ 71,152.63		10/19/2017	8
139	RFI 991 - ADA Control Valve Location	6/26/2017		\$ 3,325.16		7/13/2017	7
140	Common Area Plumbing Fixture (Balance)	1/8/2018		\$ 48,106.34		5/10/2018	12
141	SI 46 Millwork Revisions	9/13/2017		\$ 2,338.36		9/6/2018	22
142	Hotel Millwork Revisions	8/1/2017		\$ 212,932.19		8/1/2017	8
143	Change in Door Frame at Patisserie	6/28/2017		\$ 629.30		1/25/2018	9
144	Add Low Voltage Sleeves on Floors 1 and 2	6/29/2017		\$ 4,190.00		3/8/2017	10
145	Domestic Hot Water Riser Offsets	6/30/2017		\$ 16,926.00		8/31/2017	8
146	MOD 8 Drawing Revisions	10/31/2017		\$ 32,767.00		11/30/2017	9
147	RFI 0682 and 1006 Added Condensate Pumps	7/7/2017		\$ 4,756.00		8/31/2017	8
148	SI 39 - Boardroom and Vestibule	7/20/2017			\$ 1,752.00		
149	SI 40R1	8/1/2017		\$ 71,341.33		8/21/2017	8
150	Delete Car Lift for Storm Pump	7/14/2017		\$ (7,558.00)		10/19/2017	8
151	RFI 0968 Plumbing Drain Pan	1/23/2018		\$ 2,178.73		3/8/2018	10
152	RFI 0936 - Entry Foyer Grill Type	7/20/2017			\$ 1,082.85		
153	Guestroom Tub Accessory Reconciliation	8/10/2017		\$ (14,478.00)		8/31/2017	8
154	Louver Credit to RCO 073	7/29/2017			\$ (649.00)		
155	Break Metal Window Panels at Foyer	7/31/2017		\$ 1,081.00		8/31/2017	8
156	SF-01 Allowance				\$ 250,000.00		
157	RFI 1063 - Operable Wall Soffit	10/2/2017		\$ 6,552.96		10/17/2017	8
158	RFI 0922 Add Bulkhead in 435	8/14/2017		\$ 1,021.00		1/25/2018	9
159	FFE Expanded Scope	8/21/2017	\$ 242,633.00				
160	SI 54 Managers Apartment Ceilings	11/7/2017		\$ 5,352.13		11/30/2017	9
161	Offsite Mock Up Drywall and Plumbing Reconciliation	8/26/2017	\$ 17,376.00				
162	RFI 1070 - Guestroom 510 Soffit Issue	8/28/2017		\$ 983.00		1/25/2018	9
163	RFI 0953 Juliet Balcony Door Base	8/30/2017		\$ 1,867.00		2/22/2018	10
164	Guestroom Window Casing	12/16/2017		\$ 102,614.00		1/12/2018	9
165	SI 48 Additional Spa Shower	9/26/2017		\$ 21,851.22		10/19/2017	8
166	RFI 996 - Revise Ductwork Due to Corridor Crown	11/13/2017			9546.44		
167	ADA Guestroom Bathroom Floor Tile Revisions	9/14/2017		\$ 3,681.00		2/22/2018	10
168	RFI 0915 - Ballroom RCP Conflict with Ductwork	9/14/2017		\$ 8,734.00		2/22/2018	10
169	MOD 6, 7 and SI 42 Electrical Revisions	10/5/2017		\$ 67,635.88		11/30/2017	9
170	Barn Doors - Doors, Hardware, and Installation	10/9/2017		\$ 258,025.97		10/19/2017	8
171	Private Dining Millwork Revisions - Paint Grade	9/26/2017			\$ 10,182.72		
171.1	Private Dining Millwork Revisions - Mozambique	9/26/2017		\$ 17,009.37		11/30/2017	9
172	SI 39 Stair 04 Millwork Revisions	9/26/2017		\$ 30,733.53		10/19/2017	22
173	Sixth Floor Parapet Stucco Band Color Change	9/26/2017		\$ 5,545.89		10/17/2017	8
174	Furr Out Fitness Room West Wall	9/28/2017		\$ 3,258.65		43128	9
175	Fire Damper in Room 533	11/28/2017		\$ 2,699.70		43069	9
176	Concierge Lounge Case and Millwork Revisions	10/9/2017		\$ 18,335.69		43112	9
177	SI 54 Managers Apartment Millwork	10/9/2017			12448		
178	Delivery and Storage for DC-67	10/10/2017	\$ 2,245.84				
179	Boardroom Vestibule 209 Alcove Revisions	10/13/2017		\$ 3,267.04		43042	9
180	Patisserie Casework Revisions	10/17/2017		\$ 8,083.72		43112	9
181	Lower Soffits in Concierge Alcove	10/27/2017		\$ 2,378.98		43069	9
182	Custom Entry Doors - Partial Allowance Reconciliation	8/3/2018		\$ 16,340.26			16
182.2	Custom Entry Doors	6/18/2018		\$ 109,400.48		43293	16

183	Guestroom Window Valences	11/6/2017		\$ 47,619.53		42747	9	
184	Hurricane Irma Prep and Recovery		\$ 57,467.82					
185	RFI 1121 - Add Soffit in Room 719	11/8/2017		\$ 1,624.08		42760	9	
186	Won Door Submittal Revisions	11/9/2017		\$ (7,900.00)		43069	9	
187	Stair 03 and 04 Black Metal Panels	11/30/2017			7563.69			
188	Added Crown at Rotunda for Wall Covering	11/13/2017		\$ 1,464.71		43112	9	
189	Added FRP at Concierge Kitchen	12/7/2017		\$ 2,653.68		43125	9	
190	RFI 1160 - Provide Floor Drain at Pool Storage Room	11/15/2017		\$ 2,629.06		43125	9	
191	Pile Integrity Testing Credit	11/16/2017		\$ (14,432.40)		43069	9	
192	SI 57 Managers Apartment Kitchen Rough In	11/17/2017			16685			
193	Balance of SI 36	1/19/2018		\$ 95,638.19			10	
194	Linen Storage Room Soffits	1/11/2018			\$ 5,687.00			
195	Remobilization for DC-04 Mounting	11/28/2017		\$ 4,036.62		12/31/2017	9	
196	REI Additional Inspections	11/29/2017		\$ (3,180.00)		11/30/2017	9	
197	RFI 1127 - First Floor Ice Maker Chilled Water Feed	12/7/2017			\$ 4,472.49			
198	Remobilization for DC-18 Mounting	12/18/2017			\$ 16,431.00			
199	Patisserie Stone and Tile Revisions	3/7/2018		\$ 1,605.21		43202	10	
200	South Patio Revision	12/19/2017			\$ 680,535.00			
201	Remove Crown for Full Height TV Cabinets	1/11/2018		\$ (10,973.00)		2/22/2018	10	
202	SI 53 Electrical Pricing	12/11/2017		\$ 1,850.66		1/12/2018	9	
203	Camellia's Lounge Bar Wall Construction	1/11/2018		\$ 3,274.38			9	
204	Back of House Casework Submittals	1/29/2018		\$ 30,337.55		5/10/2018	12	
205	Revised Canopy Support Brackets	1/18/2017			\$ 4,040.00			
206	Elevator Lobby Stone and Tile Revision	1/20/2018		\$ 2,058.16		2/22/2018	10	
207	Lobby Reception Desk Stand By Power	12/18/2017		\$ 557.83		1/12/2018	9	
208	Remove and Reinstall DC-14	12/18/2017			\$ 10,255.08			
209	Rooftop Bar Communal Table							
210	SI 54 Tile Revisions - Entry Foyer	1/5/2018		\$ 6,799.34		2/22/2018	10	
211	Added Stainless Shelf at Kitchen				\$ 2,058.16			
212	Use Robert Thomas for Decorative Brackets	1/11/2018	\$ 6,937.00	\$ 21,253.00		11/1/2018	22	Owner Struck costs owed to Contractor, balance of RCO shown in PENDING column
213	Custom Sprinkler Heads	1/12/2018			\$ 13,972.00			
214	SI 59 - Add Wood Flooring Only	1/12/2018		\$ 41,570.88		1/25/2018	9	
215	Lutron Lighting Control Revision	8/15/2018	\$ 14,937.63					
216	Blank							
217	Camellias Lounge Bar - Pink Marble Changes Only	1/20/2018		\$ 7,340.25		2/22/2018	10	
218	Tint Windows at Dining	1/22/2018		\$ 1,445.14		1/25/2018	9	
219	Guestroom Tile Revision - GMP to SI 54	1/22/2018		\$ 52,555.74		7/12/2018	16	
220	Level 09 Attic Access	1/31/2018		\$ (57,153.71)		2/22/2018	9	
221	Additional Tinting on Hopes Windows		\$ 846.12					
223	RFI 1093 - Guestroom 603 TV Wall Conflict		\$ 3,304.78					
224	SI 37 - Credit Plumbing Fixtures	2/16/2018		\$ (4,353.58)		2/22/2018	10	
225	Upper Dining MOD 1-8 Millwork Revisions	2/19/2018		\$ 9,461.42		7/12/2018	16	
226	Cabana Casework Revisions	2/19/2018		\$ 1,386.09		3/8/2018	10	
227	Warehousing - Mirrors	4/9/2018	\$ 9,169.01					
228	Spa Retail Countertop Revision	3/2/2018		\$ 8,836.53		4/12/2018	10	
229	Lobby and Bar GMP to SI 54	3/3/2018		\$ 1,796.04		4/12/2018	10	

230	Rooftop Bar Countertop Revisions	3/23/2018			\$ 24,643.94		4/12/2018	10	
231	Ninth Floor Tile Revisions	3/7/2018			\$ 6,029.28		5/10/2018	12	
232	Spa Countertop Revision GMP to SI 54	3/17/2018			\$ 2,027.75		4/12/2018	10	
233	Provide Backlit Panels at Mani Pedi	3/20/2018				\$ 13,846.78			
234	RFI-1200 - Added Quarry Cast at Front Entry	3/22/2018			\$ 21,433.93		4/12/2018	10	
235	BBC								
236	Exterior Shutter Upgrades	4/16/2018		in CCD					
237	BBC								
238	South Patio Blue Stone Revision	5/4/2018			\$ 14,341.80		5/10/2018	12	
239									
240	Temp Doors at Ballroom	5/31/2018				\$ 54,669.91			
241	RFI 1118 - GFCI Outlet at Vanity	6/5/2018			\$ 2,967.81		7/12/2018	16	
242	Relocate Smoke Detectors for Barn Door Header	6/7/2018			\$ 10,657.19		7/12/2018	16	
243	Misc Stucco Changes		\$ 3,100.00						
244	OFCI DC-41 Fixture Credit	6/29/2018		\$ (1,090.21)					
245	CCD 009 Casework Pricing	7/23/2018				\$ 82,344.44			
246	Supplemental Instruction 067	8/17/2018		\$ 31,157.12	\$ 2,185.72			22	Owner Struck costs owed to Contractor, balance of RCO shown in PENDING column
247	Credit Managers Apartment Base Contract	7/26/2018				\$ (59,175.75)			
248	BBC								
249	SI #10 Ballroom Wall Change	8/10/2018		\$ 5,129.09					
250	MOD 7 Terrace Door Change	8/13/2018		\$ 1,462.80	\$ 20,477.28			22	Owner Struck costs owed to Contractor, balance of RCO shown in PENDING column
251	Dining Room MOD 1-8 Millwork Change Order	8/31/2018		\$ 22,305.58					
252	Revised SCEG Site Lighting	8/14/2018		\$ -	\$ 20,909.43		11/16/2018	22	
253	Add Crown at Dome Rotunda	8/14/2018		\$ 10,055.16					
254	Decorative Screening Allowance Reconciliation	8/21/2018		\$ 41,082.30					
255	Add Trim to Conceal Pocket Door Header	8/31/2018		\$ 11,789.32					
256	2nd Floor Added Soffits	8/21/2018		\$ -	\$ 1,386.48		11/16/2018	22	
257	Add Triangle Panel Molding	8/21/2018		\$ -	\$ 1,479.76		11/19/2018	22	
258	Additional Mock Up Revisions	3/29/2019		\$ 65,782.09					
259	Hudson Street Storm Repair	8/30/2018		\$ 12,921.40	\$ 20,477.28		9/6/2018	22	Owner Struck costs owed to Contractor, balance of RCO shown in PENDING column
260	ASI 52 Added Wallcovering	3/7/2019		\$ 5,586.12					
261	Allowance Reconciliation - Accordion Doors	11/15/2018		\$ 71,723.42					
262	RFI 1004 TV Wall Revisions	8/31/2018		\$ 15,635.00					
263	Mirrored Barn Door Paint and Prep	8/31/2018		\$ -	\$ 8,338.41		11/19/2018	22	
264	RFI 1180 Sprinkler Heads in TV Walls	8/31/2018		\$ 14,930.21					
265	Ballroom Can Light Trim Rings	9/4/2018		\$ -	\$ 1,080.14		11/19/2018	22	
266	Additional Framing and Sheetrock	9/7/2018		\$ 2,203.74					
267	Rooftop Bar MOD 1-8 Millwork	9/7/2018		\$ 7,922.44					
268	Allowance Reconciliation - MT-03 & MT-04	9/26/2018		\$ 51,979.21					
269	Elevator Reconciliation					\$ 9,133.29			
270	Framing and Drywall Change Orders - Precision Walls	3/12/2019		\$ 49,885.72					
271	Painting and Wallcovering Change Orders - Quantum	3/12/2019		\$ 41,394.11					

272	Ornamental Metal Change Orders - Tate	3/7/2019		\$ 19,286.37				
273	Tile Change Orders - David Allen			\$ 110,810.29				
274	Salamander Punch List			\$ 30,537.68				
275	Guestroom Vanity Rework	4/12/2019		\$ 67,384.91				
276	Case and Millwork Change Orders - LCCM	3/13/2019		\$ 78,632.10				
277	Structural Steel Change Orders - MSI	3/13/2019		\$ 138,304.56				
278	Hope's Type Q Windows Flashing Revisions - SI 10	3/29/2019		\$ 8,511.80				
279	Construction Change Directive - Jan and March			\$ 228,211.20				
280								
			Pending	Submitted	Approved	Rejected		
	Totals		\$ 3,100.00	\$ 3,050,779.14	\$ 5,382,417.24	\$ 2,089,322.81		
	*HIGHLIGHTED ROWS DENOTE EXECUTED BUT IN PROTEST BY CONTRACTOR							

Plaintiff Balfour Beatty's
Trial Exhibit # 12
(part 1 of 11)

Balfour vs. Library Assoc.

Amended Lien

Submitted RCOs

Property of:

Parker Poe Adams & Bernstein
200 Meeting St., Suite 301
Charleston, SC 29401
843-727-2650



Tab No. 27

Balfour Beatty Construction

January 13, 2016

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 027
1000 Year Storm Delay & Recovery Cost

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 027 in the amount of One hundred twenty-four thousand eighty-nine (\$124,089.19) to provide additional work in accordance with the following qualifications:

Provide all material, labor, equipment and supervision necessary to complete all work with returning the jobsite to pre-storm conditions, including but not limited to pumping, import dry fill, export muck, rebuild dirt wedge, ramp and well point roads. This exercise was a six week process but based on the days needed to get back to the scope of work starting prior to the storm, we are requesting the schedule be extended 20 calendar days for delay from October 1st through October 20th 2015.

This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Tim Spano
Sr. Project Manager

cc: Jim Clements
Jennifer Faulkinberry
Marty Wall
Brandon Denney
Jeff Sandeen

RCO # 027 - File

Balfour Beatty
Construction**Hotel at Marion Square**

Request for Change Order # 027- 1000 Year Storm

The additional work for the **1000 Year Storm** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.30160500.35	6 Inch Diesel Pump	\$2,383.15
2	400.50200000.40	1000 Year Storm	\$115,969.21

Total Items \$118,352.36

Total Markups \$5,736.83

RCO Total \$124,089.19

The total Cost to perform the work as described above is an ADD of One hundred twenty-four thousand eighty-nine (\$124,089.19).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 027

Tab No. 75

Balfour Beatty

Construction

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 075
Interior Mockup Tile Revisions

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 075 in the amount of Five thousand nine hundred eighty-nine (\$5,989.93) to provide additional work in accordance with the following qualifications:

Provide all material, labor, equipment, and supervision to complete all work associated with completing the stone and tile work in the interior mockup per the revisions to the mockup drawings.

This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,

Nick Starcevic
Project Manager

cc:

RCO # 075 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 075— Interior Mockup Tile Revisions

The additional work for the **Interior Mockup Tile Revisions** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50932000.40	Interior Mockup Tile Revisions	\$5,713.00

Total Items	\$5,713.00
Total Markups	\$276.93
RCO Total	\$5,989.93

The total Cost to perform the work as described above is an ADD of Five thousand nine hundred eighty-nine (\$5,989.93).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 075

Tab No. 88

Balfour Beatty Construction

March 7, 2019

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 088R1
Concrete Change Orders - Lithko

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 088 in the amount of Fifty-six thousand four hundred fourteen (\$56,414.30) to provide additional work in accordance with the following qualifications:

This change order includes structural cost items that have not been reconciled. Supporting documentation is attached.

- 3-PTB4 Steel
- Extra Labor & Materials to Make 1st Floor Slab Pour
- Extra Labor & Materials to Make 2nd Floor Slab Pour per Design/BIM
- COR 48 - L&M per RFI-0466
- COR 59 - L&M per RFI 0482 & 0492
- COR 50 - RFI 0434 Rework and Materials for 1PTB-8
- COR 56 - RFI-0634 Stud Rail at Column B20
- COR 57 - RFI-0648 Stair 3 & 4 Dimension Change
- COR 58 - RFI-0655 Hairpins at PT Heads to Allow for Masonry Sleeves
- COR 59 - RFI-0663 Stair 1 & 2 Nose Resteel
- COR 60 - Stair Formwork
- COR 61 Sleeve Protection for Floors 7-9 (this is due to the clearances between PT and sleeves being shrunk)
- COR 63 Rework for added VFCUs on the 6th floor

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Balfour Beatty Construction

Nick Starcevic
Project Manager

cc:
Jennifer Faulkinberry
Jim Clements
David Simonton
Tim Spano

RCO # 088R1 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 088R1 – Concrete Change Orders - Lithko

The additional work for the **Concrete Change Orders - Lithko** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50300001.40	RFI 0466	\$407.39
2	400.50300001.40	L&M For Last Minutes Changes on L2	\$3,902.24
3	400.50300001.40	3PTB-4 Steel Changes	\$3,203.61
4	400.50300001.40	L1 Slab BIM Changes	\$2,708.25
5	400.50300001.40	RFI 0655 Hairpins at PT Heads to Allow for Masonry Sleeves	\$3,810.00
6	400.50300001.40	Sleeve Protection for L7-9 (clearances for PT)	\$7,127.43
7	400.50300001.40	Rework for added VFCUs on L6	\$1,552.50
8	400.50300001.40	RFI-0482 & 0492 L&M	\$1,620.19
9	400.50300001.40	RFI-0434 Rework and Material for 1PTB-8	\$1,456.99
10	400.50300001.40	RFI 0634 Added Stud Rail and Rebar at B20	\$783.04
11	400.50300001.40	RFI 0648 Stair 3 & 4 Dimension Changes	\$1,854.91
12	400.50300001.40	Stair Formwork	\$17,383.83
13	400.50300001.40	RFI 0663 Stair 1 & 2 Nore Resteel	\$7,410.66

Total Items \$53,221.04

Total Markups \$3,193.26

RCO Total \$56,414.30

The total Cost to perform the work as described above is an ADD of Fifty-six thousand four hundred fourteen (\$56,414.30).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____

Kim Brown, Library Associates, LLC

RCO# 088R1

[illegible]



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO25
Change Order Date: 4/26/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: REINFORCEMENT ADDED TO BEAM 3PTB-4
ON DETAILER RETURNED SHOP
DRAWINGS

Description of Changes:

REINFORCEMENT ADDED TO BEAM 3PTB-4 ON DETAILER RETURNED SHOP DRAWINGS

Amount of this Change Order (excluding taxes) \$ 1,702.65

It is mutually agreed that for such change the contract price is changed by \$ 1,702.65 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____
Salesman - Catherine McDowell

Date: _____

Date: _____

[illegible]

PROJECT TITLE: Mario's Square
PROJECT NO. _____

DATE PERFORMED: 4.4.16
DATE OF REPORT: _____

Description of Work	Labor		Hours	Hourly Rate	Extended Amount
Fix all the Chimney and Gabled	1) 1 foreman	Reg.	4 hrs		
Cables were they had penetrations		O.T.			
on steel close to any columns.	2) 5 foremen	Reg.	4 hrs		
We had relocated cables the		O.T.			
So we had cables thru the columns	3)	Reg.			
but keeping a minimum of 2		O.T.			
inches clearance to any penetrations.	4)	Reg.			
		O.T.			
	5)	Reg.			
		O.T.			
	6)	Reg.			
		O.T.			
	7)	Reg.			
		O.T.			
	8)	Reg.			
		O.T.			
	9)	Reg.			
		O.T.			
	10)	Reg.			
		O.T.			
TOTAL					

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Plowton Square
PROJECT NO. _____

DATE PERFORMED: 4/9/18
DATE OF REPORT: _____

Description of Work	labor		Hours	Hourly Rate	Extended Amount
We had to accept the Bundle # 75	11	Reinforcing	Reg.	12.00	
#76 of Uniform cables for the			O.T.		
openings that they puted inside the	2)		Reg.		
plaster #6.			O.T.		
	3)		Reg.		
			O.T.		
	4)		Reg.		
			O.T.		
	5)		Reg.		
			O.T.		
	6)		Reg.		
			O.T.		
	7)		Reg.		
			O.T.		
	8)		Reg.		
			O.T.		
	9)		Reg.		
			O.T.		
	10)		Reg.		
			O.T.		
TOTAL					

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Religion Square
PROJECT NO. _____

DATE PERFORMED: 4.19.24
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
Revised cable #23, 24, 27, 28 & 29	1) 2 roadbuilders	Reg. 2hr ea		
edge form on south end has to be		O.T.		
removed to the north after we had 2)		Reg.		
all cables and head installed. W. had		O.T.		
to take cables out of the heads and 3)		Reg.		
cut the plastic sheathing again. Also		O.T.		
the plastic put a glue right in 4)		Reg.		
front of the heads we had to drill		O.T.		
over holes to the form work and 5)		Reg.		
relocated some heads.		O.T.		
	6)	Reg.		
		O.T.		
	7)	Reg.		
		O.T.		
	8)	Reg.		
		O.T.		
	9)	Reg.		
		O.T.		
	10)	Reg.		
		O.T.		
TOTAL				

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Pavilion Square
PROJECT NO. _____

DATE PERFORMED: 4-19-16
DATE OF REPORT: _____

Description of Work	labor		Hours	Hourly Rate	Extended Amount
Bundle #30 Uniform has to be replaced	2	Reg.	1hr ea		
cause the pulled a big block out		O.T.			
right in front the cable heads next	2	Reg.			
to column at H-39 line.		O.T.			
	3	Reg.			
		O.T.			
	4	Reg.			
		O.T.			
	5	Reg.			
		O.T.			
	6	Reg.			
		O.T.			
	7	Reg.			
		O.T.			
	8	Reg.			
		O.T.			
	9	Reg.			
		O.T.			
	10	Reg.			
		O.T.			
TOTAL					

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Merion Square
PROJECT NO. _____

DATE PERFORMED: 4.20.16
DATE OF REPORT _____

Description of Work	labor		Hours	Hourly Rate	Extended Amount
Bundled #32 Uniform has to be swept around that opening that was put in next to column on D-23 has after we had all cables down. We had to move rebar in top & bottom at same column.	1) 2 Rod busting	Reg.	1 1/2		
	2)	Reg.			
	3)	Reg.			
	4)	Reg.			
	5)	O.T.			
		Reg.			
	6)	O.T.			
		Reg.			
	7)	O.T.			
		Reg.			
	8)	O.T.			
		Reg.			
	9)	O.T.			
		Reg.			
	10)	O.T.			
TOTAL					

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Mission Statement
PROJECT NO. _____

DATE PERFORMED: 4.20.16
DATE OF REPORT: _____

Description of Work	Labor	Reg.	O.T.	Hours	Hourly Rate	Extended Amount
We had to move water and relocated some cable heads at	1) 2 R. Johnsons	Reg.	1 1/2 hrs.			
Bentley #25 & 26 North end	2)	Reg.				
They put a 13.5 sleeve in front of the anchor after we had all	3)	Reg.				
over water cables and heads Done.	4)	Reg.				
	5)	Reg.				
	6)	Reg.				
	7)	Reg.				
	8)	Reg.				
	9)	Reg.				
	10)	Reg.				
		O.T.				
TOTAL						

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Mannon Square
PROJECT NO. _____

DATE PERFORMED: 4.20.16
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
Bundled #31, 32, 33, 34 Bundled cables	1) 3 Leadwires	Reg. 3		
We had to cut them cables 1055		O.T. 3 hrs ea.		
and swept them around the big	2)	Reg.		
Plus cut that were installed		O.T.		
after we had all our work done.	3)	Reg.		
Also then cables the hold us		O.T.		
up to put in the Top of Bottom	4)	Reg.		
steel next to the elevator		O.T.		
We end of up working late in	5)	Reg.		
order to make that pour and		O.T.		
pour concrete next Day.	6)	Reg.		
		O.T.		
	7)	Reg.		
		O.T.		
		Reg.		
	8)	Reg.		
		O.T.		
		Reg.		
	9)	Reg.		
		O.T.		
		Reg.		
	10)	Reg.		
		O.T.		
TOTAL				

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

[illegible]



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO28
Change Order Date: 5/17/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: MEP PENETRATIONS FOR 2ND FLOOR

Description of Changes:

EXTRA STEEL FOR MEP PENETRATIONS FOR 2ND FLOOR, EAST HALF

COR #44 = \$1,450

COR #48 = \$ 50

COR #49 = \$ 469

Amount of this Change Order (excluding taxes) \$ 1,969.00

It is mutually agreed that for such change the contract price is changed by \$ 1,969.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____

Salesman - Catherine McDowell

Date: _____

5/18/16

Date: _____

DAILY WORK ORDER REPORT

PROJECT TITLE: Murison Square
PROJECT NO. _____DATE PERFORMED: 5.18.16
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
1.- We had to take cables out of the column at 36 line and sweep them around the sleeves that they put in (about 34 east of same column) after all our work on these were done.	11 Foreman 2 Rodbusters Reg. 24.5 each. O.T.			
2.- We had to cut lose all the cables at Bendle #36 and 37 and get them swept around the two 14 inches sleeves that the plumbers installed in front of the cable heads. Right about 34 line.	31 Foreman 2 Rodbusters Reg. 24.5 each. O.T.			
3.- Bendle #40, 41 and 42. We had to take them cable out of column at J-30 line 800 they get another two sleeves in. Just east of that same column. Also we had to pull top and Bottom Bars same.	101 Reg. O.T.			
The below agree to all above stated conditions: Column Decays those cable Bar's moved out of the column.				
General Contractor Representative				
Subcontractor Representative				
TOTAL				

DAILY WORK ORDER REPORT

PROJECT TITLE: Mechan Square
PROJECT NO. _____DATE PERFORMED: 5.11.16
DATE OF REPORT: _____

Description of Work	Labor	Reg.	O.T.	Hours	Hourly Rate	Extended Amount
We had to set rebar at the	1) Foreman	Reg.		4		
Mechanical Platform below 2nd		O.T.				
Floor so the Plumber can	2) Rod Buster	Reg.		4		
get all their sewer and Borms		O.T.				
15"	3)	Reg.				
Then we had to get all the		O.T.				
rebar ground hand opairs by	4)	Reg.				
The typical slt opairs detail.		O.T.				
	5)	Reg.				
		O.T.				
	6)	Reg.				
		O.T.				
	7)	Reg.				
		O.T.				
	8)	Reg.				
		O.T.				
	9)	Reg.				
		O.T.				
	10)	Reg.				
		O.T.				
TOTAL						

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

R - 1568



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO28
Change Order Date: 5/17/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: MEP PENETRATIONS FOR 2ND FLOOR

Description of Changes:

EXTRA STEEL FOR MEP PENETRATIONS FOR 2ND FLOOR, EAST HALF

COR #44 = \$1,450

COR #48 = \$ 50

COR #49 = \$ 469

Amount of this Change Order (excluding taxes) \$ 1,969.00

It is mutually agreed that for such change the contract price is changed by \$ 1,969.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: 

Signature: _____
Salesman - Catherine McDowell

Date: 5/18/16

Date: _____

PROJECT TITLE: Majorion Spore
PROJECT NO. _____

DATE PERFORMED: 5.18.16
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
1. We had to take cables out of the column at 36 line and wrap them around the sleeves that they putted in (about 3ft east of same column) after all our work on these came done.	1) Foreman 2 Rodbusters 2) Foreman 2 Rodbusters 3) Foreman 2 Rodbusters 4) _____ 5) _____ 6) _____ 7) _____	Reg. 2hrs each. Reg. 2hrs each. Reg. 2hrs each. O.T. O.T. Reg. Reg.		
2. We had to cut all the add/ins at Bundle #36 and 37 and get them wrapped around the two 14 inches sleeves that the plumbers installed in front of the cable heads. Right about 34 line.	5) _____ 6) _____ 7) _____	Reg. Reg. Reg.		
3. Bundle #40, 41 and 42.	8) _____ 9) _____ 10) _____	Reg. Reg. Reg.		
We had to take them cable out of column at J-30 line 800 they get another two sleeves in J-30 east of that same column. Also we had to pull top and bottom bars same. Both moved out of the column.				
The below agree to all above stated conditions: Column Bascas phase cable				
Both moved out of the column.				
TOTAL				

General Contractor Representative _____

Subcontractor Representative _____

[illegible]



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO28
Change Order Date: 5/17/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: MEP PENETRATIONS FOR 2ND FLOOR

Description of Changes:

EXTRA STEEL FOR MEP PENETRATIONS FOR 2ND FLOOR, EAST HALF

COR #44 = \$1,450

COR #48 = \$ 50


COR #49 = \$ 469

Amount of this Change Order (excluding taxes) \$ 1,969.00

It is mutually agreed that for such change the contract price is changed by \$ 1,969.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: 

Signature: _____

Salesman - Catherine McDowell

Date: 5/18/16

Date: _____

PROJECT TITLE: Marion Square
PROJECT NO. _____

DATE PERFORMED: 5.18.16
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
We had to make and add	1) 8 Rodbusters	Reg. 2 1/2 hrs	Reg. 22.40	
Bands and Horizontal Bars for all		O.T.		
the Vertical Punctations at the	2)	Reg.		
Primer for Beams.		O.T.		
We had to put 3 Bands and 3 #5	3)	Reg.		
straight Bars on other sides of		O.T.		
the 3c slabs.	4)	Reg.		
By typical Vertical Punctation		O.T.		
Detail.	5)	Reg.		
		O.T.		
	6)	Reg.		
		O.T.		
	7)	Reg.		
		O.T.		
	8)	Reg.		
		O.T.		
	9)	Reg.		
		O.T.		
	10)	Reg.		
		O.T.		
TOTAL				

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

Job: Document			Marion Square COR #50 RFL-0434 Rework and Materials										TO BE COMPLETED BY CONTRACTOR										TO BE COMPLETED BY				
A	B	C	D	E	H	H	H	H	I	J	K	M	M	M	N	M	Q										
	Item No.	Description	Quantity	Unit of measure	Hours Per Unit	Labor Rate	Labor (L)	Material (M)	Equip. (E)	Sub Contract (\$)	Total L +M +E +S	Raw Unit cost	Type Of Change	Comments	Status												
		Extra Reinforcing Steel Rodbuster Labor OT	1 LS 8 HR		1.00	67.50	\$540.00	\$670.00						Steel around sleeves 1PTB-B Rework or steel and PT in 1PTB-B @ OT Rates													
													</														



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO23
Change Order Date: 4/18/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: RFI-434 - ADD. STIRRUPS & 5' BARS

Description of Changes:

RFI-434 - ADD. STIRRUPS & 5' BARS

Amount of this Change Order (excluding taxes) \$ 315.00

It is mutually agreed that for such change the contract price is changed by \$ 315.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____

Salesman - Catherine McDowell

Date: _____

Date: _____



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO24
Change Order Date: 4/19/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: RFI-434 T&B SLEEVE TIES & #5 6' LONG

Description of Changes:


RFI-434 T&B SLEEVE TIES & #5 6' LONG
REMAINDER OF BARS AND EXPEDITE FEE FROM RAPID REBAR

Amount of this Change Order (excluding taxes) \$ 355.00

It is mutually agreed that for such change the contract price is changed by \$ 355.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: 
Timothy Quinn

Signature: _____
Salesman - Catherine McDowell

Date: 4/20/16

Date: _____

PROJECT TITLE: Mission Square
PROJECT NO. _____

DATE PERFORMED: 4.20.16
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
We had to move rebar and HDD	1) 2 rebar busters	Reg.		
Bands on Band Sides, Above and		O.T. 4 hr ea		
Under the slabs on Beam 11TB-8	2)	Reg. 8		
We had to make all the Bands.		O.T.		
	3)	Reg.		
(We had to HDD that steel they		O.T.		
change that because the cables	4)	Reg.		
in the Beam being to close to		O.T.		
them slabs.	5)	Reg.		
		O.T.		
	6)	Reg.		
		O.T.		
	7)	Reg.		
		O.T.		
	8)	Reg.		
		O.T.		
	9)	Reg.		
		O.T.		
	10)	Reg.		
		O.T.		
TOTAL				

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

[illegible]



Tendon Systems, LLC

7340 McGinnis Ferry Road
Suite 100
Suwanee GA 30024
678 835-1100

Change Order

Order#: 3

Order Date: 08/24/2016

To: Lithko Contracting, Inc.
1810 Orr Industrial Court
Charlotte NC 28213

Project: Marion Square Hotel
404 King Street
Charleston SC 29403

Job No.: 150303

Client PO #:

The contractor agrees to perform and the owner agrees to pay for the following changes to this contract.

Plans Attached ☐

Submitted By: 134 Boris Miller

Submitted To: Timothy Quinn

Specifications Attached ☐

Description of Work	Amount
6th Floor Add'l Material	1,515.28

Notes

Add'l Material:

120 Studs x \$1.85 = \$222.00

1032 LF of tendons x \$0.77 = \$794.64

16 Fixed anchors x \$5.69 = \$91.04

200 grease caps x \$0.75 = \$150.00

Shipping = \$257.60 / 2 = \$128.80

Negative changes will lower the overall contract price requiring no additional payment by owner.

Requested Amount of Change

1,515.28

The original Contract Sum was	245,800.00
Net change by previous Change Orders	0.00
The Contract Sum prior to this Change Order	245,800.00
The Contract Sum will be changed by this Change Order	1,515.28
The new Contract Sum including this Change Order will be	247,315.28
The Contract Time will be changed by	0 Days

Owner: _____ Date: _____

Contractor: _____ Date: _____

R - 1579

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108



**SUBCONTRACT
CHANGE
ORDER**

Subcontract Change Order Number: 4
Contractor: Lithko Contracting Inc.
Subcontractor: East Coast Rebar, Inc.
Project: Hotel at Marion Square
Date of Original Subcontract: June 17, 2015

Pursuant to and subject to the terms and conditions of the above referenced Subcontract, Subcontractor is directed to make the following changes in the work:

C/O #	Item Description	Approved Amount
04	Rodbusters 76 hrs Moving rebar and PT cables in slam pour #2 on level 2 for mechanical openings and pipe sleeves	45.00/hour \$3,420.00
TOTAL THIS CHANGE ORDER		\$3,420.00

Except as specifically set forth hereinabove, Subcontractor waives any and all other claims it may have arising out of or related to the above referenced changes to the Subcontract. Retention of this Change Order for ten (10) days or commencement of the work or shipment of materials set forth herein shall constitute acceptance of this Change Order.

EAST COAST REBAR, INC.
PO Box 351
Rutherfordton, NC 28139
P: 828-287-4287 F: 828-287-9268

Original Subcontract:	\$ 380,234.00
Previous Change Orders:	\$ 12,465.00
Subcontract Sum Prior to this C/O	\$ 392,699.00
Value This Change Order	\$3,420.00
Revised Subcontract Amount	\$ 396,119.00

By: Larry Greene
Name: Larry Greene
Title: President
Date: 5/19/2016

Lithko Contracting Inc.
PO Box 270
Monroe, Ohio 45050

ACCEPTED - The above prices and specifications of this change order are satisfactory and are hereby accepted. All work to be performed under same terms and conditions as specified in original contract unless before or herein modified.

Name: _____
Title: _____
Date: _____

PROJECT TITLE: Marion Square
PROJECT NO. _____

DATE PERFORMED: 11/11/2011
DATE OF REPORT: 11/11/2011

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
Level 6 West				
4 men 3 hrs ea. changing uniform cables bundle 90-94	1)	Reg.	12	
		O.T.		
	2)	Reg.		
		O.T.		
4 men 3 hrs Relocating cables around sleeves + block outs added after cables were installed	3)	Reg.	12	
		O.T.		
	4)	Reg.		
		O.T.		
3 men 2 hrs adding rebars and hangers around sleeves + blockouts added	5)	Reg.	6	
		O.T.		
	6)	Reg.		
		O.T.	6	
3 men 2 hrs Repairing cables + steel rails for RF1 # D634 opening added @ cd	7)	Reg.		
B-20		O.T.		
	8)	Reg.		
		O.T.		
	9)	Reg.		
		O.T.		
	10)	Reg.		
		O.T.		
TOTAL				36

The below agree to all above stated conditions:

The below agree to all above stated conditions:

General Contractor Representative

[illegible]



SUBCONTRACT CHANGE ORDER

Subcontract Change Order Number: 4

Contractor: Lithko Contracting Inc.

Subcontractor: East Coast Rebar, Inc.

Project: Hotel at Marion Square

Date of Original Subcontract: June 17, 2015

Pursuant to and subject to the terms and conditions of the above referenced Subcontract, Subcontractor is directed to make the following changes in the work:

C/O #	Item Description	Approved Amount
04	Rodbusters 76 hrs Moving rebar and PT cables in slam pour #2 on level 2 for mechanical openings and pipe sleeves	45.00/hour \$3,420.00
TOTAL THIS CHANGE ORDER		\$3,420.00

Except as specifically set forth hereinabove, Subcontractor waives any and all other claims it may have arising out of or related to the above referenced changes to the Subcontract. Retention of this Change Order for ten (10) days or commencement of the work or shipment of materials set forth herein shall constitute acceptance of this Change Order.

EAST COAST REBAR, INC.
PO Box 351
Rutherfordton, NC 28139
P: 828-287-4287 F: 828-287-9268

Original Subcontract:	\$ 380,234.00
Previous Change Orders:	\$ 12,465.00
Subcontract Sum Prior to this C/O	\$ 392,699.00
Value This Change Order	\$3,420.00
Revised Subcontract Amount	\$ 396,119.00

By:	<u>Larry Greene</u>
Name:	<u>Larry Greene</u>
Title:	<u>President</u>
Date:	<u>5/19/2016</u>

Lithko Contracting Inc.
PO Box 270
Monroe, Ohio 45050

ACCEPTED - The above prices and specifications of this change order are satisfactory and are hereby accepted. All work to be performed under same terms and conditions as specified in original contract unless before or herein modified.

Name: _____
Title: _____
Date _____



Tendon Systems, LLC

7340 McGinnis Ferry Road
Suite 100
Suwanee GA 30024
678 835-1100

Change Order

Order#: 3

Order Date: 08/24/2016

To: Lithko Contracting, Inc.
1810 Orr Industrial Court
Charlotte NC 28213

Project: Marion Square Hotel
404 King Street
Charleston SC 29403

Job No.: 150303

Client PO #:

The contractor agrees to perform and the owner agrees to pay for the following changes to this contract.

Plans Attached ☐

Submitted By: 134 Boris Miller

Submitted To: Timothy Quinn

Specifications Attached ☐

Description of Work	Amount
6th Floor Add'l Material	1,515.28

Notes

Add'l Material:

120 Studs x \$1.85 = \$222.00

1032 LF of tendons x \$0.77 = \$794.64

16 Fixed anchors x \$5.69 = \$91.04

200 grease caps x \$0.75 = \$150.00

Shipping = \$257.60 /2 = \$128.80

Negative changes will lower the overall contract price requiring no additional payment by owner.

Requested Amount of Change

1,515.28

The original Contract Sum was	245,800.00
Net change by previous Change Orders	0.00
The Contract Sum prior to this Change Order	245,800.00
The Contract Sum will be changed by this Change Order	1,515.28
The new Contract Sum including this Change Order will be	247,315.28
The Contract Time will be changed by	0 Days

Owner: _____

Date: _____

Contractor: _____

Date: _____

R - 1584

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

PROJECT TITLE: Marion Square
PROJECT NO. _____

DATE PERFORMED: _____
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
Level 6 West				
4 men 3 hrs ea. changing uniform cables bundle 90-94	1)	Reg. 12		
	2)	O.T.		
		Reg.		
		O.T.		
4 men 3 hrs relocating cables around sleeves & block outs added after cables were installed	3)	Reg. 12		
		O.T.		
	4)	Reg.		
		O.T.		
3 men 2 hrs adding rebars and harpins around sleeves & blockouts added	5)	Reg. 6		
		O.T.		
	6)	Reg.		
3 men 2 hrs repairing cables + stud rails for RF1 # D634 opening added @ col B-20	7)	O.T. 6		
		Reg.		
		O.T.		
	8)	Reg.		
		O.T.		
	9)	Reg.		
		O.T.		
	10)	Reg.		
		O.T.		
TOTAL		36		

The below agree to all above stated conditions:

The below agree to all above stated conditions:

General Contractor Representative

[illegible]



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO34
Change Order Date: 8/29/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: Add Hairpins

Description of Changes:

ADD HAIRPINS REQUIRED PER RFI-- 0655

Amount of this Change Order (excluding taxes) \$ **1,397.25**

It is mutually agreed that for such change the contract price is changed by \$ **1,397.25**, terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____
Salesman - Catherine McDowell

Date: _____

Date: _____



**SUBCONTRACT
CHANGE
ORDER**

Subcontract Change Order Number: 4
Contractor: Lithko Contracting Inc.
Subcontractor: East Coast Rebar, Inc.
Project: Hotel at Marion Square
Date of Original Subcontract: June 17, 2015

Pursuant to and subject to the terms and conditions of the above referenced Subcontract, Subcontractor is directed to make the following changes in the work:

C/O #	Item Description	Approved Amount
04	Rodbusters 76 hrs Moving rebar and PT cables in slam pour #2 on level 2 for mechanical openings and pipe sleeves	45.00/hour \$3,420.00
TOTAL THIS CHANGE ORDER		\$3,420.00

Except as specifically set forth hereinabove, Subcontractor waives any and all other claims it may have arising out of or related to the above referenced changes to the Subcontract. Retention of this Change Order for ten (10) days or commencement of the work or shipment of materials set forth herein shall constitute acceptance of this Change Order.

EAST COAST REBAR, INC.
PO Box 351
Rutherfordton, NC 28139
P: 828-287-4287 F: 828-287-9268

Original Subcontract:	\$ 380,234.00
Previous Change Orders:	\$ 12,465.00
Subcontract Sum Prior to this C/O	\$ 392,699.00
Value This Change Order	\$3,420.00
Revised Subcontract Amount	\$ 396,119.00

By: Larry Greene
Name: Larry Greene
Title: President
Date: 5/19/2016

Lithko Contracting Inc.
PO Box 270
Monroe, Ohio 45050

ACCEPTED - The above prices and specifications of this change order are satisfactory and are hereby accepted. All work to be performed under same terms and conditions as specified in original contract unless before or herein modified.

Name: _____
Title: _____
Date: _____

PROJECT TITLE: Mazon Spence
PROJECT NO. _____

DATE PERFORMED: _____
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extend
Level 6 East	1)	8	Reg.	
2 men 4 hrs adding rebar & haupms	2)		O.T.	
around openings & sleeves added after			Reg.	
cables were in place	3)	12	O.T.	
8/29			Reg.	
4 men 3 hrs relocating PT & rebar	4)		O.T.	
for sleeves & openings			Reg.	
8/30	5)	8	O.T.	
4 men 2 hrs relocating PT, rebar			Reg.	
and stud rails for added sleeves &	6)		O.T.	
block outs			Reg.	
3 men 2 hrs relocating cables	7)	6	O.T.	
RFI 0655			Reg.	
3 men 2 hrs fixing banded & uniform	8)	6	O.T.	
between line 23 & 26 lines A+B	9)		Reg.	
			O.T.	
	10)		Reg.	
			O.T.	
TOTAL		40		

The below agree to all above stated conditions:

General Contractor Representative _____

Job: Marion Square
Document: COR 89 RF-H0683 Stair 1 & 2 Nose Resteel

COR 59 RH-0663 Stair 1 & 2 Nose Restlet															
Document		TO BE COMPLETED BY CONTRACTOR													
A	B	C	D	E	H	H	H	H	J	K	M	M	M	N	Q
	Item No.	Description	Quantity	Unit of measure	Hours Per Unit	Labor Rate	Labor (L)	Material (M)	Equip. (E)	Sub Contract (\$)	Total L *M *E *S	Raw Unit cost	Type Of Change	Comments	Status
		Additional Steel	1 LS					\$300.00							
		Labor to wet set all steel	2 HR			36.00	\$72.00								
		Forms			Days	Daily rate									
		10k 4x2'	12 day		8.00	7.83		\$761.14							
		10k 6' braces	12.0 day		8.00	1.64		\$157.71							
		10k baseplate	16 day		8.00	1.36		\$173.71							
		10k screw jack	24 day		8.00	2.86		\$548.57							
		300 prop	2 day		8.00	6.00		\$96.00							
		350 prop	4 day		8.00	7.14		\$228.57							
		450 prop	11 day		8.00	11.11		\$977.43							
		4-way U-Head	6 day		8.00	1.82		\$67.43							
		Bracing clamp	24 day		8.00	0.71		\$137.14							
		2.90m beam	75 day		8.00	3.07		\$1,842.86							
		3.30m beam	8 day		8.00	3.54		\$226.29							
		16"-I" beam	8 day		8.00	5.25		\$336.00							
							72.00	5872.86	0.00	0.00					
		Sales Tax	8.5%					495.19	0.00	0.00					
		Subtotal					72.00	6372.05	0.00	0.00					
		Mark-Up	15%				10.80	955.87	0.00	0.00					
		Subtotal					82.80	7327.86	0.00	0.00					
		General Liability Insurance						0.00	0.00	0.00					
		Charleston Bus. License					0.00	0.00	0.00	0.00					
		Total					\$82.80	\$7,327.86	\$0.00	\$0.00					
		TOTAL REQUEST THIS PAGE								\$7,410.66					



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO36
Change Order Date: 9/1/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: Additional Material

Description of Changes:

RFI - 0655: ADD. #3 BARS AROUND ELECTRICAL BOXES AT STAIR TREADS

Amount of this Change Order (excluding taxes) \$ 300.00

It is mutually agreed that for such change the contract price is changed by \$ 300.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____
Salesman - Catherine McDowell

Date: _____

Date: _____

Attachment to Invoice**Rental****No.:412663564**

Date: 06/30/2016

Page: 20 / 26

Ship To:Marion Square
LITHKO CONTRACTING, INC.
404 King StreetDoka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045T (770) 862-7914
F (770) 862-5238
usa@doka.com
www.dokausa.com**doka**Job Site 412006077 Marion Square- Shoring & Reshore
Start of Rental 10/10/2013

Beginning Inventory per	06/01/2016	2,248,334.00				
Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price Unit Value
183045000	Dokamatic insertion beam 2.45m		200.00	EA	61.00	EA
189701000	Doka beam H20 top P 1.80m		474.00	EA	55.00	EA
189702000	Doka beam H20 top P 2.45m		866.00	EA	76.00	EA
189702000	Doka beam H20 top P 2.45m		400.00	EA	76.00	EA
189704000	Doka beam H20 top P 2.90m		30.00	EA	86.00	EA
189705000	Doka beam H20 top P 3.30m		213.00	EA	99.00	EA
189706000	Doka beam H20 top P 3.60m		12.00	EA	110.00	EA
189707000	Doka beam H20 top P 3.90m		16.00	EA	117.00	EA
189712000	Doka beam H20 top P 16'-0"		88.00	EA	147.00	EA
189712000	Doka beam H20 top P 16'-0"		30.00	EA	147.00	EA
189713000	Doka beam H20 top P 11'-6"		20.00	EA	107.00	EA
189836000	Doka beam H20 eco P 2.45m		9.00	EA	76.00	EA
581603000	Multi-purpose walling WS10 Top50 6'-0"		1.00	EA	289.00	EA
581616000	Multi-purpose walling WS10 Top50 7'-0"		52.00	EA	337.00	EA
581626000	Dokamatic S table 9'-0"x18'-0"		7.00	EA	4,633.00	EA
581626000	Dokamatic S table 9'-0"x18'-0"		43.00	EA	4,633.00	EA
581627000	Dokamatic S table 9'-0"x12'-0"		17.00	EA	3,159.00	EA
581627000	Dokamatic S table 9'-0"x12'-0"		18.00	EA	3,159.00	EA
581628000	Dokamatic S table 7'-0"x18'-0"		20.00	EA	4,001.00	EA

Amount/USD

281.04

600.54

1,516.12

700.28

59.43

485.76

30.41

43.12

230.27

101.59

49.30

15.76

6.66

403.68

747.07

4,589.16

1,237.00

1,309.86

1,843.32

Transfer/USD

14,250.46

Wire Transfer Ref: Bank of America

Account: 0031127115

ABA Code:

001200009

Attachment to Invoice
Rental

No.:412663564

Date: 06/30/2016

Page: 21 / 26

Ship To:

Marion Square
LITKO CONTRACTING, INC.
404 King StreetDoka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045T (770) 962-7914
F (770) 962-5238
usa@doka.com
www.dokausa.com**doka**Job Site 412006077 Marion Square-Shoring & Reshore
Start of Rental 10/10/2013

Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price Unit Value	Days	Rental Rate	Amount/USD
Transfer/USD									
581628000	Dokamatic S table 7'-0"x18'-0"		28.00	EA	4,001.00	EA	112,028.00	28 + 2	2,580.65
581629000	Dokamatic S table 7'-0"x12'-0"		31.00	EA	2,938.00	EA	91,078.00	28 + 2	2,028.04
581629000	Dokamatic S table 7'-0"x12'-0"		8.00	EA	2,938.00	EA	23,504.00	28 + 2	541.43
582528000	Spring locked connecting pin 16mm		30.00	EA	9.00	EA	270.00	28 + 2	8.22
583011000	Doka multi-rip transport box 1.20x0.80m		10.00	EA	558.00	EA	5,580.00	28 + 2	128.52
583012000	Doka skeleton transport box 1.70x0.80m		12.00	EA	1,042.00	EA	12,504.00	28 + 2	288.04
583016000	Doka stacking pallet 1.20x0.80m		1.00	EA	329.00	EA	329.00	28 + 2	7.58
585700000	10k crossbrace 3/4"x4W		544.00	EA	46.00	EA	25,024.00	28 + 2	576.45
585701000	10k crossbrace 3/4"x5W		210.00	EA	46.00	EA	9,660.00	28 + 2	222.53
585702000	10k crossbrace 3/4"x6W		62.00	EA	46.00	EA	2,852.00	28 + 2	65.70
585707000	10k frame 2Wx4'-0"		8.00	EA	222.00	EA	1,776.00	28 + 2	40.91
585707000	10k frame 2Wx4'-0"		8.00	EA	222.00	EA	1,776.00	28 + 2	40.91
585712000	10k Frame 4Wx4'-0"		168.00	EA	249.00	EA	41,832.00	28 + 2	963.63
585713000	10k Frame 4Wx5'-0"		104.00	EA	260.00	EA	27,040.00	28 + 2	622.89
585713000	10k Frame 4Wx5'-0"		200.00	EA	260.00	EA	52,000.00	28 + 2	1,197.86
585714000	10k Frame 4Wx6'-0"		185.00	EA	300.00	EA	55,500.00	28 + 2	1,279.48
585715000	10k Universal connector		958.00	EA	15.00	EA	14,370.00	28 + 2	331.02
585716000	10k Rivet		1,950.00	EA	4.70	EA	9,165.00	28 + 2	211.13
585717000	10k Hitch pin		1,350.00	EA	4.70	EA	9,165.00	28 + 2	211.12

Transfer/USD 25,863.57

Wire Transfer Det. Bank of America

Account 0031121715

ABA Code

00730003

Attachment to Invoice

Rental

No.:412663564

Date: 06/30/2016

Page: 22 / 26

Ship To:

Marion Square
LITHKO CONTRACTING, INC.
404 King Street

Doka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045

T (770) 962-7914
F (770) 962-5238
usa@doka.com
www.dokausa.com

doka

Job Site 412006077 Marion Square- Shoring & Reshore
Start of Rental 10/10/2013

Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price Unit Value	Days	Rental Rate	Amount/USD	
Transfer/USD 25,663.57										
585721000	10k Screw jack 35"		884.00	EA	80.00	EA	70,720.00	28 + 2	2.150% / 28 days	1,629.09
585722000	10k Screw jack baseplate		442.00	EA	38.00	EA	16,796.00	28 + 2	2.150% / 28 days	386.91
586018000	Lashing strap 5.00m		40.00	EA	77.00	EA	3,080.00	28 + 2	2.150% / 28 days	70.95
586097000	Plastic mallet 4kg		4.00	EA	173.00	EA	692.00	28 + 2	2.150% / 28 days	15.94
Transfer/USD 16,806.00										
586151000	Doka sticking pulk 1.55x0.85m		81.00	EA	363.00	EA	29,403.00	28 + 2	2.150% / 28 days	677.31
586155000	Removable folding tripod		88.00	EA	153.00	EA	13,464.00	28 + 2	2.150% / 28 days	310.16
586155500	Removable folding tripod top		50.00	EA	153.00	EA	7,650.00	28 + 2	2.150% / 28 days	176.22
586174000	Lowering head H20		176.00	EA	62.00	EA	11,036.00	28 + 2	2.150% / 28 days	254.23
586179000	Supporting head H20 DF		123.00	EA	22.00	EA	2,706.00	28 + 2	2.150% / 28 days	62.33
586195000	Bracing clamp B		150.00	EA	20.00	EA	3,000.00	28 + 2	2.150% / 28 days	69.11
586214000	Dokamatic swivel head 40		724.00	EA	252.00	EA	182,448.00	28 + 2	2.150% / 28 days	4,202.82
586215000	Dokamatic strut connection		30.00	EA	64.00	EA	1,920.00	28 + 2	2.150% / 28 days	44.23
586231000	Dokamatic lifting strap 13.00m		2.00	EA	653.00	EA	1,306.00	28 + 2	2.150% / 28 days	30.08
741000266	10k U-head 8"x9"		442.00	EA	51.00	EA	22,542.00	28 + 2	2.150% / 28 days	519.28
741001221	Dokamatic WS-10 table 9'-0"x18'-0"		2.00	EA	4,949.00	EA	9,898.00	28 + 2	2.150% / 28 days	226.01
741001222	Dokamatic WS-10 table 9'-0"x12'-0"		6.00	EA	3,370.00	EA	20,220.00	28 + 2	2.150% / 28 days	465.78
741001224	Dokamatic WS-10 table 7'-0"x12'-0"		1.00	EA	3,106.00	EA	3,106.00	28 + 2	2.150% / 28 days	71.55
Total Square Feet: 21.199										
Actively during the Month										

Transfer/USD

51,792.02

Wire Transfer Cost: Bank of America

Account ID: 1001101011

ABA Code:

601100000

Job: Document:			TO BE COMPLETED BY CONTRACTOR										TO BE COMPLETED BY N			
A	B	C	D	E	H	H	H	H	I	J	K	M	M	M	Q	
	Item No.	Description	Quantity	Unit of measure	Hours Per Unit	Labor Rate	Labor (L)	Material (M)		Equip. (E)	Sub Contract (\$)	Total L+M+E+S	Raw Unit cost	Type Of Change	Status	
		Forms			Days	Daily rate										
	10k 4"x2"		12 day		20	7.93		\$1,992.86							Stairs were ready to pour 8/10/16 but then we	
	10k 6" braces		12.0 day		20	1.64		\$394.29							were put on hold because the electrical boxes	
	10k baseplate		16 day		20	1.36		\$434.29							had not been approved and released for delivery	
	10k screw jack		24 day		20	2.86		\$1,371.43							in time. Boxes arrived and install began 8/25/16	
	300 prop		2 day		20	6.00		\$240.00							with them being completed before	
	350 prop		4 day		20	7.14		\$571.43							for us to pour 8/30/16. On 8/28/16 RF-10663	
	450 prop		11 day		20	11.11		\$2,443.57							was generated delaying the pour an additional	
	4-way U-Head		6 day		20	1.82		\$218.57							8 days. 8/10/16-8/30/16 = 20 day delay	
	Bracing clamp		24 day		20	0.71		\$342.86								
	2.90m beam		75 day		20	3.07		\$4,807.14								
	3.30m beam		8 day		20	3.54		\$565.71								
	16'-0" beam		8 day		20	5.25		\$840.00								
							0.00	13932.14		0.00	0.00					
		Sales Tax	8.5%					1184.23		0.00	0.00					
		Subtotal					0.00	15116.38		0.00	0.00					
		Mark Up	15%				0.00	2287.46		0.00	0.00					
		Subtotal					0.00	17383.83		0.00	0.00					
		General Liability Insurance						0.00		0.00	0.00					
		Charleston Bus. License					0.00	0.00		0.00	0.00					
		Total					\$0.00	\$17,383.83		\$0.00	\$0.00					
		TOTAL REQUEST THIS PAGE								\$17,383.83						

Attachment to Invoice

Rental

No.:412663564

Date: 06/30/2016

Page: 20 / 26

Ship To:

Marion Square
LITRHO CONTRACTING, INC.
404 King StreetDoka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045T (770) 962-7914
F (770) 962-5238
usa@doka.com
www.dokausa.com**doka**Job Site 41206077 Marion Square- Shoring & Reshore
Start of Rental 10/10/2013

Beginning Inventory per		06/01/2016	2,248,334.00							
Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price Unit Value	Days	Rental Rate	Amount/USD	
183045000	Dokamatic insertion beam 2.45m		200.00	EA	61.00	EA	12,200.00	28 + 2	2,150% / 28 days	281.04
189701000	Doka beam H20 top P 1.80m		474.00	EA	55.00	EA	26,070.00	28 + 2	2,150% / 28 days	600.54
189702000	Doka beam H20 top P 2.45m		866.00	EA	76.00	EA	65,816.00	28 + 2	2,150% / 28 days	1,516.12
189702000	Doka beam H20 top P 2.45m		400.00	EA	76.00	EA	30,400.00	28 + 2	2,150% / 28 days	700.28
189704000	Doka beam H20 top P 2.90m		30.00	EA	86.00	EA	2,580.00	28 + 2	2,150% / 28 days	59.43
189705000	Doka beam H20 top P 3.30m		213.00	EA	99.00	EA	21,087.00	28 + 2	2,150% / 28 days	485.76
189706000	Doka beam H20 top P 3.80m		12.00	EA	110.00	EA	1,320.00	28 + 2	2,150% / 28 days	30.41
189707000	Doka beam H20 top P 3.90m		16.00	EA	117.00	EA	1,872.00	28 + 2	2,150% / 28 days	43.12
189712000	Doka beam H20 top P 16'-0"		68.00	EA	147.00	EA	9,996.00	28 + 2	2,150% / 28 days	230.27
189712000	Doka beam H20 top P 16'-0"		30.00	EA	147.00	EA	4,410.00	28 + 2	2,150% / 28 days	101.59
189713000	Doka beam H20 top P 11'-6"		20.00	EA	107.00	EA	2,140.00	28 + 2	2,150% / 28 days	49.30
189936000	Doka beam H20 eco P 2.45m		9.00	EA	76.00	EA	684.00	28 + 2	2,150% / 28 days	15.76
581603000	Multi-purpose walling WS10 Top50 6'-0"		1.00	EA	289.00	EA	289.00	28 + 2	2,150% / 28 days	6.66
581616000	Multi-purpose walling WS10 Top50 7'-0"		52.00	EA	337.00	EA	17,524.00	28 + 2	2,150% / 28 days	403.68
581626000	Dokamatic S table 9'-0"x18'-0"		7.00	EA	4,633.00	EA	32,431.00	28 + 2	2,150% / 28 days	747.07
581626000	Dokamatic S table 9'-0"x18'-0"		43.00	EA	4,633.00	EA	199,219.00	28 + 2	2,150% / 28 days	4,589.16
581627000	Dokamatic S table 9'-0"x12'-0"		17.00	EA	3,159.00	EA	53,703.00	28 + 2	2,150% / 28 days	1,237.09
581627000	Dokamatic S table 9'-0"x12'-0"		18.00	EA	3,159.00	EA	56,862.00	28 + 2	2,150% / 28 days	1,309.86
581628000	Dokamatic S table 7'-0"x18'-0"		20.00	EA	4,001.00	EA	80,020.00	28 + 2	2,150% / 28 days	1,843.32

Transfer/USD 14,250.46

Wire Transfer Ref: Bank of America

Account: 003121115

ABA Code:

001200009

Attachment to Invoice**Rental****No.: 412663564**

Date: 06/30/2016

Page: 21 / 26

Ship To:

Marion Square
LITHKO CONTRACTING, INC.
404 King Street

Doka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045

T (770) 962-7914
F (770) 962-5238
usa@doka.com
www.dokausa.com

doka

Job Site 412005077 Marion Square- Shoring & Reshore
Start of Rental 10/10/2013

Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price	Unit Value	Days	Rental Rate	Amount/USD
Transfer/USD										
581628000	Dokamatic S table 7'-0"x18'-0"		28.00	EA	4,001.00	EA	112,028.00	28 + 2	2.150% / 28 days	2,580.65
581629000	Dokamatic S table 7'-0"x12'-0"		31.00	EA	2,938.00	EA	91,078.00	28 + 2	2.150% / 28 days	2,098.04
581629000	Dokamatic S table 7'-0"x12'-0"		8.00	EA	2,938.00	EA	23,504.00	28 + 2	2.150% / 28 days	541.43
582528000	Spring locked connecting pin 16mm		30.00	EA	9.00	EA	270.00	28 + 2	2.150% / 28 days	6.22
583011000	Doka multi-rip transport box 1.20x0.80m		10.00	EA	558.00	EA	5,580.00	28 + 2	2.150% / 28 days	128.52
583012000	Doka skelaton transport box 1.70x0.80m		12.00	EA	1,042.00	EA	12,504.00	28 + 2	2.150% / 28 days	288.04
583016000	Doka stacking pallet 1.20x0.80m		1.00	EA	329.00	EA	329.00	28 + 2	2.150% / 28 days	7.58
585700000	10k crossbrace 3/4"x4W		544.00	EA	46.00	EA	25,024.00	28 + 2	2.150% / 28 days	576.45
585701000	10k crossbrace 3/4"x5W		210.00	EA	46.00	EA	9,660.00	28 + 2	2.150% / 28 days	222.53
585702000	10k crossbrace 3/4"x6W		62.00	EA	46.00	EA	2,852.00	28 + 2	2.150% / 28 days	65.70
585707000	10k frame 2W"x4'-0"		8.00	EA	222.00	EA	1,776.00	28 + 2	2.150% / 28 days	40.91
585712000	10k frame 4W"x4'-0"		168.00	EA	249.00	EA	41,832.00	28 + 2	2.150% / 28 days	963.63
585713000	10k frame 4W"x5'-0"		104.00	EA	260.00	EA	27,040.00	28 + 2	2.150% / 28 days	622.89
585714000	10k frame 4W"x6'-0"		200.00	EA	260.00	EA	52,000.00	28 + 2	2.150% / 28 days	1,197.86
585715000	10k Universal connector		185.00	EA	300.00	EA	55,500.00	28 + 2	2.150% / 28 days	1,278.48
585716000	10k Rivet		958.00	EA	15.00	EA	14,370.00	28 + 2	2.150% / 28 days	331.02
585717000	10k Hitch pin		1,950.00	EA	4.70	EA	9,165.00	28 + 2	2.150% / 28 days	211.13
Transfer/USD										25,663.57

Wire Transfer Ref: 06-06-2016

Account 0231121716

ABA Code

(09) 200003

Attachment to Invoice

Rental

No.: 412663564

Date: 06/30/2016

Page: 22 / 26

Ship To:

Marion Square
LITHKO CONTRACTING, INC.
404 King Street

Doka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045

T (770) 962-7914
F (770) 962-5238
usa@doka.com
www.dokausa.com



Job Site 41206077 Marion Square- Shoring & Reshore
Start of Rental 10/10/2013

Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price Unit Value	Days	Rental Rate	Amount/USD
Transfer/USD									25,663.57
585721000	10k Screw Jack 38"		884.00	EA	80.00	EA	70,720.00	28 + 2	2,150% / 28 days
585722000	10k Screw Jack baseplate		442.00	EA	38.00	EA	16,796.00	28 + 2	2,150% / 28 days
586018000	Lashing strap 5.00m		40.00	EA	77.00	EA	3,090.00	28 + 2	2,150% / 28 days
586097000	Plastic mallet 4kg		4.00	EA	173.00	EA	692.00	28 + 2	2,150% / 28 days
586100000	586100000 Floor prop Euxor 30 top 450		23.00	EA	311.00	EA	7,153.00	28 + 2	2,150% / 28 days
586151000	Doka stacking pulley 1.55x0.85m		81.00	EA	303.00	EA	24,543.00	28 + 2	2,150% / 28 days
586155000	Removable folding tripod		88.00	EA	153.00	EA	13,464.00	28 + 2	2,150% / 28 days
586155500	Removable folding tripod top		50.00	EA	153.00	EA	7,650.00	28 + 2	2,150% / 28 days
586174000	Lowering head H20		178.00	EA	62.00	EA	11,036.00	28 + 2	2,150% / 28 days
586178000	Supporting head H20 DF		123.00	EA	22.00	EA	2,706.00	28 + 2	2,150% / 28 days
586195000	Bracing clamp B		150.00	EA	20.00	EA	3,000.00	28 + 2	2,150% / 28 days
586214000	Dokamatic swivel head 40		724.00	EA	252.00	EA	182,448.00	28 + 2	2,150% / 28 days
586215000	Dokamatic strut connection		30.00	EA	64.00	EA	1,920.00	28 + 2	2,150% / 28 days
586231000	Dokamatic lifting strap 13.00m		2.00	EA	653.00	EA	1,306.00	28 + 2	2,150% / 28 days
741000266	10k U-head 8"x8"		442.00	EA	51.00	EA	22,562.00	28 + 2	2,150% / 28 days
741001221	Dokamatic WS-10 table 9'-0"x18'-0"		2.00	EA	4,949.00	EA	9,898.00	28 + 2	2,150% / 28 days
741001222	Dokamatic WS-10 table 9'-0"x12'-0"		6.00	EA	3,370.00	EA	20,220.00	28 + 2	2,150% / 28 days
741001224	Dokamatic WS-10 table 7'-0"x12'-0"		1.00	EA	3,106.00	EA	3,106.00	28 + 2	2,150% / 28 days
Total Square Feet: 21,199									71,555.57
Activity during the Month									

Transfer/USD 51,792.02

Wire Transfer/Cheq. Bank of America

Account 0011-017116

404 Corp

09/23/2021

[illegible]



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO35
Change Order Date: 8/29/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: ADDITIONAL 1000 #5 5'-0"

Description of Changes:

ADDITIONAL 1000 #5 5'-0" LONG REQUIRED FOR TENDONS, AT PIPE PENETRATIONS

Amount of this Change Order (excluding taxes) \$ 2,972.55

It is mutually agreed that for such change the contract price is changed by \$ 2,972.55 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____

Salesman - Catherine McDowell

Date: _____

Date: _____

[illegible]

DAILY WORK ORDER REPORT

PROJECT TITLE: Marlin Square
PROJECT NO. _____

DATE PERFORMED: _____
DATE OF REPORT: _____

Description of Work		Labor	
1)	Level 6 West	Reg.	12
2)	4 men 3 hrs ea. changing uniform cables bundle 90-94	O.T.	
3)	4 men 3 hrs relocating cables around sleeves & block outs added after cables were installed	Reg.	12
4)		O.T.	
5)	3 men 2 hrs adding rebar and hangers around sleeves & blockouts added	Reg.	6
6)		O.T.	
7)	3 men 2 hrs repairing cables & stud rails for RF1 # 0634 opening added @ col B-20	Reg.	6
8)		O.T.	
9)		Reg.	
10)		O.T.	
TOTAL		Reg.	36
		O.T.	

The below agree to all above stated conditions:

General Contractor Representative

PROJECT TITLE: Marion Spence
PROJECT NO. _____

DATE PERFORMED: _____
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extens
Level 6 East	1)	Reg.	8	
2 men 4 hrs adding rebar & hangers		O.T.		
around openings & sleeves added after	2)	Reg.		
cables were in place		O.T.		
8/29	3)	Reg.	12	
4 men 3 hrs relocating PT & rebar		O.T.		
for sleeves & openings	4)	Reg.		
8/30		O.T.		
4 men 2 hrs relocating PT, rebar	5)	Reg.	8	
and stud rails for added sleeves &		O.T.		
block outs	6)	Reg.		
		O.T.		
3 men 2 hrs relocating cables	7)	Reg.	6	
RFI 0655		O.T.		
	8)	Reg.		
3 men 2 hrs fixing banded & uniform		O.T.	6	
between line 23 & 26 lines A+B	9)	Reg.		
		O.T.		
	10)	Reg.		
		O.T.		
TOTAL			40	

The below agree to all above stated conditions:

General Contractor Representative

[illegible]



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO25
Change Order Date: 4/26/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc.
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: REINFORCEMENT ADDED TO BEAM 3PTB-4
ON DETAILER RETURNED SHOP
DRAWINGS

Description of Changes:

REINFORCEMENT ADDED TO BEAM 3PTB-4 ON DETAILER RETURNED SHOP DRAWINGS

Amount of this Change Order (**excluding taxes**) \$ 1,702.65

It is mutually agreed that for such change the contract price is changed by \$ **1,702.65**, terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____
Salesman - Catherine McDowell

Date: _____

Date: _____

Job Document	Manion Square Extra Materials and Labor to Coordinate with Electrical and MEP to make 1st Floor Slab Pour							
	A	B	C	D	E	H	H	H
			Description	Quantity	Unit of measure	Hours Per Unit	Labor Rate	Labor (L)
								H
								I
								J
								K
							Total L +M +E +S	M
							Raw Unit cost	N
							Type Of Change	Q
							Comments	Status
			Rework Rodbuster Forman Labor	4 HR		60.00	\$240.00	
			Rework Rodbuster Labor	29 HR		45.00	\$1,305.00	
			Rework Rodbuster Labor OT	12 HR		67.50	\$810.00	
			Sales Tax	8.5%			2355.00	0.00
			Subtotal				2355.00	0.00
			Mark Up	15%			353.25	0.00
			Subtotal				2708.25	0.00
			General Liability Insurance				0.00	0.00
			Charleston Bus. License				0.00	0.00
			Total				\$2,708.25	\$0.00
			TOTAL REQUEST THIS PAGE				\$2,708.25	

DAILY WORK ORDER REPORT

PROJECT TITLE: Mission Square
PROJECT NO. _____DATE PERFORMED 4.4.16
DATE OF REPORT: _____

Description of Work	Labor	Reg.	Hours	Hourly Rate	Extended Amount
Fix all the Uniform and Banded	1) 1 foreman	O.T.	4 hrs		
Cables were they had production	2) 5 foreman	Reg.	4 hrs		
we had relocated cables from		O.T.			
so we had cables thru the columns	3)	Reg.			
but keeping a minimum of 2		O.T.			
inches clearance to any production.	4)	Reg.			
		O.T.			
	5)	Reg.			
		O.T.			
	6)	Reg.			
		O.T.			
	7)	Reg.			
		O.T.			
	8)	Reg.			
		O.T.			
	9)	Reg.			
		O.T.			
	10)	Reg.			
		O.T.			
TOTAL					

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Refinishing Square
PROJECT NO. _____

DATE PERFORMED: 4/19/18
DATE OF REPORT: _____

Description of Work	Labor	Reg.	Hours	Hourly Rate	Extended Amount
We had to unspool the Bundle #75	1) Redbusher	Reg.	1 hr. ea.		
#76 of Uniform cables for 4th		O.T.			
openings had they pulled inside the	2)	Reg.			
feeder #6.		O.T.			
	3)	Reg.			
		O.T.			
	4)	Reg.			
		O.T.			
	5)	Reg.			
		O.T.			
	6)	Reg.			
		O.T.			
	7)	Reg.			
		O.T.			
	8)	Reg.			
		O.T.			
	9)	Reg.			
		O.T.			
	10)	Reg.			
		O.T.			
TOTAL					

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Median Square
PROJECT NO. _____

DATE PERFORMED: 4.17.16
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
Rebar cable #23, 24, 27, 28 & 29	1) 2 rebarbers	Reg. 2 hrs ea		
edge form on south end has to be		O.T.		
removed to the north after we had 2)		Reg.		
all cables and steel installed. We had		O.T.		
to turn cables out at the heads and 3)		Reg.		
cut the plastic sheeting again. Also		O.T.		
The plastic put a shoe right in	4)	Reg.		
front of the heads we had to drill		O.T.		
more holes to the form work and	5)	Reg.		
relocated some heads.		O.T.		
	6)	Reg.		
		O.T.		
	7)	Reg.		
		O.T.		
	8)	Reg.		
		O.T.		
	9)	Reg.		
		O.T.		
	10)	Reg.		
		O.T.		
TOTAL				

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Polivision Service
PROJECT NO. _____

DATE PERFORMED: 4-19-16
DATE OF REPORT: _____

Description of Work	Labor	Reg.	O.T.	Hours	Hourly Rate	Extended Amount
Bundle #70 Uniform has to be replaced 2 Rod bushes		Reg.	O.T.	1 hr 00		
cause the pulled a big block out		Reg.	O.T.			
right in front the cable heads next	21	Reg.	O.T.			
to column at H-39 line.		O.T.				
	31	Reg.	O.T.			
		Reg.	O.T.			
	41	Reg.	O.T.			
		O.T.				
	51	Reg.	O.T.			
		O.T.				
	61	Reg.	O.T.			
		O.T.				
	71	Reg.	O.T.			
		O.T.				
	81	Reg.	O.T.			
		O.T.				
	91	Reg.	O.T.			
		O.T.				
	101	Reg.	O.T.			
		O.T.				
TOTAL						

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Merion Square
PROJECT NO: _____

DATE PERFORMED: 4.20.16
DATE OF REPORT: _____

Description of Work	Labor	Reg.	O.T.	Hours	Hourly Rate	Extended Amount
Bundled #12 Uniform has to be	1) 2 Rod busters	Reg.	O.T.	1 hr ea		
except need that opening that		O.T.				
was put in next to column on	2)	Reg.	O.T.			
D-23 line after we had all cables		O.T.				
Done. We had to move rebar on	3)	Reg.	O.T.			
top & bottom at same column.	4)	Reg.	O.T.			
		O.T.				
	5)	Reg.	O.T.			
		O.T.				
	6)	Reg.	O.T.			
		O.T.				
	7)	Reg.	O.T.			
		O.T.				
	8)	Reg.	O.T.			
		O.T.				
	9)	Reg.	O.T.			
		O.T.				
	10)	Reg.	O.T.			
		O.T.				
TOTAL						

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

PROJECT TITLE: Proton Skate
PROJECT NO. _____

DATE PERFORMED: 4.20.16
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
We had to move rebar and relocated some cable heads at Bundle #25 & 26 North end. They noted a B.S. sleeve in front of the anchor after we had all over relax cables and heads done.	1) 2 R.O.B.-T.C.C.	Reg.		
		O.T.	1 1/2 hrs.	
	2)	Reg.		
		O.T.		
	3)	Reg.		
		O.T.		
	4)	Reg.		
		O.T.		
	5)	Reg.		
		O.T.		
	6)	Reg.		
		O.T.		
	7)	Reg.		
		O.T.		
	8)	Reg.		
		O.T.		
	9)	Reg.		
		O.T.		
	10)	Reg.		
		O.T.		
TOTAL				

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

DAILY WORK ORDER REPORT

PROJECT TITLE: Mansion Square
PROJECT NO. _____DATE PERFORMED: 4.20.16
DATE OF REPORT: _____

Description of Work	Labor	Reg.	O.T.	Hours	Hourly Rate	Extended Amount
Bundle # 31, 32, 33, 34 Banded cables	1) 3 Laborers	Reg.	3	3 hrs ea.		
We had to cut these cables loose	2)	Reg.				
and swept them around the big		O.T.				
floor our that were installed	3)	Reg.				
after we had all our work done		O.T.				
the 7 men cables we hold us	4)	Reg.				
up to put in the top & bottom		O.T.				
steel next to the elevator.	5)	Reg.				
We end of yr working late in		O.T.				
order to move this pour and	6)	Reg.				
pour concrete next Day.		O.T.				
	7)	Reg.				
		O.T.				
	8)	Reg.				
		O.T.				
	9)	Reg.				
		O.T.				
	10)	Reg.				
		O.T.				
TOTAL						

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

[illegible]



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO28
Change Order Date: 5/17/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: MEP PENETRATIONS FOR 2ND FLOOR

Description of Changes:

EXTRA STEEL FOR MEP PENETRATIONS FOR 2ND FLOOR, EAST HALF

COR #44 = \$1,450

COR #48 = \$ 50

COR #49 = \$ 469

Amount of this Change Order (excluding taxes) \$ 1,969.00

It is mutually agreed that for such change the contract price is changed by \$ 1,969.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: 

Signature: _____
Salesman - Catherine McDowell

Date: 5/18/16

Date: _____

DAILY WORK ORDER REPORT

PROJECT TITLE: Mansion Square
PROJECT NO. DATE PERFORMED: 5.18.16
DATE OF REPORT:

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
1. We had to take cables out of the column at 36 line and sweep them around the sleeves that they put in (About 3ft east of same column) after all our work on these were done.	11 Foreman 2 Rodbusters 31 Foreman 2 Rodbusters 41	Reg. 2hrs each. Reg. 2hrs each. Reg.		
2. We had to cut all the cables at Bundle #36 and 37 and get them swept around the two 14 inches sleeves that the plumbers installed in front of the cable heads. Right about 34 line.	51 61 71	Reg. Reg. Reg.		
3. Bundle #40, 41 and 42. We had to take them cable out of column at J-30 line 800 they get another two sleeves in. Just west of that same column. Also we had to pull top and bottom bars same.	81 91 101	Reg. Reg. Reg.		
The below agree to all above stated conditions: Column Brackets those cable Br's moved out of the column.				
General Contractor Representative				
Subcontractor Representative				
TOTAL				

DAILY WORK ORDER REPORT

PROJECT TITLE: Deletion Square
PROJECT NO. _____DATE PERFORMED: 5.11.16
DATE OF REPORT: _____

Description of Work	Labor		Hours	Hourly Rate	Extended Amount
We had to cut rebar at the	1) Foreman	Reg.	4		
Mechanical Platform below end		O.T.			
floor so the plumbers can	2) Rod Buster	Reg.	4		
get all their sleeves and bolts		O.T.			
in.	3)	Reg.			
Then we had to get all the		O.T.			
rebar ground thru openings by	4)	Reg.			
the typical slot opening detail.		O.T.			
	5)	Reg.			
		O.T.			
	6)	Reg.			
		O.T.			
	7)	Reg.			
		O.T.			
	8)	Reg.			
		O.T.			
	9)	Reg.			
		O.T.			
	10)	Reg.			
		O.T.			
TOTAL					

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

TO BE COMPLETED BY CONTRACTOR															TO BE COMPLETED BY				
A	B	C	D	E	H	H	H	H	I	J	K	M	M	N	Q				
	Item No.	Description	Quantity	Unit of measure	Hours Per Unit	Labor Rate	Labor (L)	Material (M)		Equip (E)	Sub Contract (\$)	Total L +M +E +S	Raw (ml cost	Comments	Status				
		Extra Reinforcing Steel	1 LS					\$50.00						#5 bar					
		Rework Rodbuster Forman Labor	2 HR		1.00	60.00	\$120.00							see attached description					
		Rework Rodbuster Labor	4 HR		1.00	45.00	\$180.00							see attached description					



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO28
Change Order Date: 5/17/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: MEP PENETRATIONS FOR 2ND FLOOR

Description of Changes:

EXTRA STEEL FOR MEP PENETRATIONS FOR 2ND FLOOR, EAST HALF

COR #44 = \$1,450

COR #48 = \$ 50

COR #49 = \$ 469

Amount of this Change Order (excluding taxes) \$ 1,969.00

It is mutually agreed that for such change the contract price is changed by \$ 1,969.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____

Salesman - Catherine McDowell

Date: _____

5/18/16

Date: _____

PROJECT TITLE: Marian Spence
PROJECT NO. _____

DATE PERFORMED: 5.18.16
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
1. We had to take cables out of the column at J-36 line and wrap them around the sleeves that they put in (about 3ft east of same column) after all our work on these same Poles.	1) Foreman 2 Rodbusters 2) Foreman 2 Rodbusters 3) Foreman 2 Rodbusters 4) _____ 5) _____ 6) _____ 7) _____	Reg. 2 hrs each. Reg. 2 hrs each. Reg. 2 hrs each. O.T. O.T. Reg. Reg.		
2. We had to extend (use all the cables at Bendle #36 and 37 and get them wrapped around the two 14 inches sleeves that the plumbers installed in front of the cable heads. Right about 34 line.	5) _____ 6) _____ 7) _____	Reg. Reg. Reg.		
3. Bundle #40, 41 and 42.	8) _____	Reg.		
We had to take them cable out of column at J-30 line. They got another two sleeves in. Just west of that same column.	9) _____ 10) _____	Reg. Reg.		
Also we had to add top and bottom Bars same.	O.T.			
The below agree to all above stated conditions: Cabling because these cable Br's moved out of the column.				
TOTAL				

General Contractor Representative _____
Subcontractor Representative _____

[illegible]



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO28
Change Order Date: 5/17/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: MEP PENETRATIONS FOR 2ND FLOOR

Description of Changes:

EXTRA STEEL FOR MEP PENETRATIONS FOR 2ND FLOOR, EAST HALF

COR #44 = \$1,450

COR #48 = \$ 50


COR #49 = \$ 469

Amount of this Change Order (excluding taxes) \$ 1,969.00

It is mutually agreed that for such change the contract price is changed by \$ 1,969.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: 

Signature: _____

Salesman - Catherine McDowell

Date: 5/18/16

Date: _____

PROJECT TITLE: Marion Square
 PROJECT NO. _____

DATE PERFORMED: 5.18.16
 DATE OF REPORT: _____

Description of Work	Labor	Reg.	O.T.	Hours	Hourly Rate	Extended Amount
We had to make and add	1) 8 Rodbusters	Reg.	O.T.	2 1/2 hrs	per hr.	
Bands and Horizontal Bars for all		O.T.				
the Vertical Punctations at the	2)	Reg.				
Perimeter Beams.		O.T.				
We had to put 3 Bands and 3 #5	3)	Reg.				
straight Bars on other sides of		O.T.				
those slabs.	4)	Reg.				
It typical Vertical Punctations		O.T.				
Detail.	5)	Reg.				
		O.T.				
	6)	Reg.				
		O.T.				
	7)	Reg.				
		O.T.				
	8)	Reg.				
		O.T.				
	9)	Reg.				
		O.T.				
	10)	Reg.				
		O.T.				
TOTAL						

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

Job: Document															Marion Square COR #50 RFL-034 Rework and Materials																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
A			B			C			D			E			H			H			H			I			J			K			M			M			N			Q																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
			Item No.			Description			Quantity			Unit of measure			Hours Per Unit			Labor Rate			Labor (L)			Material (M)			Equip. (E)			Sub Contract (\$)			Total L +M +E +S			Raw Unit cost			Type Of Change			Comments			Status																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
						Extra Reinforcing Steel			1 LS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															</		



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO23
Change Order Date: 4/18/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: RFI-434 - ADD. STIRRUPS & 5' BARS

Description of Changes:

RFI-434 - ADD. STIRRUPS & 5' BARS

Amount of this Change Order (excluding taxes) \$ 315.00

It is mutually agreed that for such change the contract price is changed by \$ 315.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____

Salesman - Catherine McDowell

Date: _____

Date: _____



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO24
Change Order Date: 4/19/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: RFI-434 T&B SLEEVE TIES & #5 6' LONG

Description of Changes:

RFI-434 T&B SLEEVE TIES & #5 6' LONG
REMAINDER OF BARS AND EXPEDITE FEE FROM RAPID REBAR

Amount of this Change Order (excluding taxes) \$ 355.00

It is mutually agreed that for such change the contract price is changed by \$ 355.00 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Timothy Quinn

Signature: _____

Salesman - Catherine McDowell

Date: _____

4/20/16

Date: _____

PROJECT TITLE: refining square
PROJECT NO. _____

DATE PERFORMED: 4-20-16
DATE OF REPORT: _____

Description of Work	Labor	Reg.	O.T.	Hours	Hourly Rate	Extended Amount
We had to move rebar and add	1) 2 rebar benders	Reg.				
Bands on both sides, above and		O.T.	4 hr ea			
Under the slabs on beam 1PTB-8	2)	Reg.				
We had to make all the Bands.		O.T.				
	3)	Reg.				
(We had to add that steel they		O.T.				
change that because the cables	4)	Reg.				
in the beam been to close to		O.T.				
them steel.	5)	Reg.				
		O.T.				
	6)	Reg.				
		O.T.				
	7)	Reg.				
		O.T.				
	8)	Reg.				
		O.T.				
	9)	Reg.				
		O.T.				
	10)	Reg.				
		O.T.				
TOTAL						

The below agree to all above stated conditions:

General Contractor Representative _____

Subcontractor Representative _____

Job: Marion Square Document: COR 55 RP-H0834 Added Stud Rails & Rebar at B20		TO BE COMPLETED BY CONTRACTOR										TO BE COMPLETED BY			
A	B	C	D	E	H	H	H	H	I	J	K	M	M	N	Q
	Item No.	Description	Quantity	Unit of measure	Hours Per Unit	Labor Rate	Labor (L)	Material (M)		Equip. (E)	Sub Contract (\$)	Total L +M +E +S	Raw Unit cost	Comments	Status
	1	Additional Stud Rails	120 stud	LS	1.85			\$222.00			\$128.80			See attached \$128.80 in shipping	
	2	Additional Reinforcing Steel	1 LS		38.00			\$38.00						See attached	
		Rodbuster Labor	2 HR		3.00	45.00	\$270.00								



Tendon Systems, LLC

7340 McGinnis Ferry Road
Suite 100
Suwanee GA 30024
678 835-1100

Change Order

Order#: 3

Order Date: 08/24/2016

To: Lithko Contracting, Inc.
1810 Orr Industrial Court
Charlotte NC 28213

Project: Marion Square Hotel
404 King Street
Charleston SC 29403

Job No.: 150303

Client PO #:

The contractor agrees to perform and the owner agrees to pay for the following changes to this contract.

Plans Attached ☐

Submitted By: 134 Boris Miller

Submitted To: Timothy Quinn

Specifications Attached ☐

Description of Work	Amount
6th Floor Add'l Material	1,515.28

Notes

Add'l Material:

120 Studs x \$1.85 = \$222.00

1032 LF of tendons x \$0.77 = \$794.64

16 Fixed anchors x \$5.69 = \$91.04

200 grease caps x \$0.75 = \$150.00

Shipping = \$257.60 / 2 = \$128.80

Negative changes will lower the overall contract price requiring no additional payment by owner.

Requested Amount of Change

1,515.28

The original Contract Sum was	245,800.00
Net change by previous Change Orders	0.00
The Contract Sum prior to this Change Order	245,800.00
The Contract Sum will be changed by this Change Order	1,515.28
The new Contract Sum including this Change Order will be	247,315.28
The Contract Time will be changed by	0 Days

Owner: _____ Date: _____

Contractor: _____ Date: _____



**SUBCONTRACT
CHANGE
ORDER**

Subcontract Change Order Number: 4
Contractor: Lithko Contracting Inc.
Subcontractor: East Coast Rebar, Inc.
Project: Hotel at Marion Square
Date of Original Subcontract: June 17, 2015

Pursuant to and subject to the terms and conditions of the above referenced Subcontract, Subcontractor is directed to make the following changes in the work:

C/O #	Item Description	Approved Amount
04	Rodbusters 76 hrs Moving rebar and PT cables in slam pour #2 on level 2 for mechanical openings and pipe sleeves	45.00/hour \$3,420.00
TOTAL THIS CHANGE ORDER		\$3,420.00

Except as specifically set forth hereinabove, Subcontractor waives any and all other claims it may have arising out of or related to the above referenced changes to the Subcontract. Retention of this Change Order for ten (10) days or commencement of the work or shipment of materials set forth herein shall constitute acceptance of this Change Order.

EAST COAST REBAR, INC.
PO Box 351
Rutherfordton, NC 28139
P: 828-287-4287 F: 828-287-9268

Original Subcontract:	\$ 380,234.00
Previous Change Orders:	\$ 12,465.00
Subcontract Sum Prior to this C/O	\$ 392,699.00
Value This Change Order	\$3,420.00
Revised Subcontract Amount	\$ 396,119.00

By: Larry Greene
Name: Larry Greene
Title: President
Date: 5/19/2016

Lithko Contracting Inc.
PO Box 270
Monroe, Ohio 45050

ACCEPTED - The above prices and specifications of this change order are satisfactory and are hereby accepted. All work to be performed under same terms and conditions as specified in original contract unless before or herein modified.

Name: _____
Title: _____
Date: _____

DAILY WORK ORDER REPORT

PROJECT TITLE: Marina Square
PROJECT NO. _____

DATE PERFORMED: _____
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended Amount
Level 6 West				
4 men 3 hrs ea. changing uniform	1)	Reg. 12		
cables bundle 90-94	2)	O.T.		
		Reg.		
		O.T.		
4 men 3 hrs Relocating cables around	3)	Reg. 12		
sleeves + block outs added after cables		O.T.		
were installed	4)	Reg.		
		O.T.		
3 men 2 hrs adding rebar and harpins	5)	Reg. 6		
around sleeves + blockouts added		O.T.		
	6)	Reg.		
3 men 2 hrs Repairing cables + stud rails		O.T. 6		
for RFI # 0634 opening added @ col	7)	Reg.		
B-20		O.T.		
	8)	Reg.		
		O.T.		
	9)	Reg.		
		O.T.		
	10)	Reg.		
		O.T.		
TOTAL				36

The below agree to all above stated conditions:

General Contractor Representative

Job Document			Manor Square COR RFL0648 Stair 3 & 4 Dimension Change													
TO BE COMPLETED BY CONTRACTOR										TO BE COMPLETED BY						
A	B	C	D	E	H	H	H	H	I	J	K	M	M	M	N	Q
	Item No.	Description	Quantity	Unit of measure	Hours Per Unit	Labor Rate	Labor (L)	Material (M)		Equip. (E)	Sub Contract (\$)	Total L+M+E+S	Raw Unit cost	Type Of Change	Comments	Status
	2	New Tendons Rodbuster Labor	8 LS 3 HR		4.00	45.00	\$640.00	\$885.98			\$128.80				see attached \$128.80 in shipping see attached	
											</					



**SUBCONTRACT
CHANGE
ORDER**

Subcontract Change Order Number: 4
Contractor: Lithko Contracting Inc.
Subcontractor: East Coast Rebar, Inc.
Project: Hotel at Marion Square
Date of Original Subcontract: June 17, 2015

Pursuant to and subject to the terms and conditions of the above referenced Subcontract, Subcontractor is directed to make the following changes in the work:

C/O #	Item Description	Approved Amount
04	Rodbusters 76 hrs Moving rebar and PT cables in slam pour #2 on level 2 for mechanical openings and pipe sleeves	45.00/hour \$3,420.00
TOTAL THIS CHANGE ORDER		\$3,420.00

Except as specifically set forth hereinabove, Subcontractor waives any and all other claims it may have arising out of or related to the above referenced changes to the Subcontract. Retention of this Change Order for ten (10) days or commencement of the work or shipment of materials set forth herein shall constitute acceptance of this Change Order.

EAST COAST REBAR, INC.
PO Box 351
Rutherfordton, NC 28139
P: 828-287-4287 F: 828-287-9268

Original Subcontract:	\$ 380,234.00
Previous Change Orders:	\$ 12,465.00
Subcontract Sum Prior to this C/O	\$ 392,699.00
Value This Change Order	\$3,420.00
Revised Subcontract Amount	\$ 396,119.00

By: Larry Greene
Name: Larry Greene
Title: President
Date: 5/19/2016

Lithko Contracting Inc.
PO Box 270
Monroe, Ohio 45050

ACCEPTED - The above prices and specifications of this change order are satisfactory and are hereby accepted. All work to be performed under same terms and conditions as specified in original contract unless before or herein modified.

Name: _____
Title: _____
Date: _____



Tendon Systems, LLC

7340 McGinnis Ferry Road
Suite 100
Suwanee GA 30024
678 835-1100

Change Order

Order#: 3

Order Date: 08/24/2016

To: Lithko Contracting, Inc.
1810 Orr Industrial Court
Charlotte NC 28213

Project: Marion Square Hotel
404 King Street
Charleston SC 29403

Job No.: 150303

Client PO #:

The contractor agrees to perform and the owner agrees to pay for the following changes to this contract.

Plans Attached ☐

Submitted By: 134 Boris Miller

Submitted To: Timothy Quinn

Specifications Attached ☐

Description of Work	Amount
6th Floor Add'l Material	1,515.28

Notes

Add'l Material:

120 Studs x \$1.85 = \$222.00

1032 LF of tendons x \$0.77 = \$794.64

16 Fixed anchors x \$5.69 = \$91.04

200 grease caps x \$0.75 = \$150.00

Shipping = \$257.60 /2 = \$128.80

Negative changes will lower the overall contract price requiring no additional payment by owner.

Requested Amount of Change

1,515.28

The original Contract Sum was	245,800.00
Net change by previous Change Orders	0.00
The Contract Sum prior to this Change Order	245,800.00
The Contract Sum will be changed by this Change Order	1,515.28
The new Contract Sum including this Change Order will be	247,315.28
The Contract Time will be changed by	0 Days

Owner: _____ Date: _____

Contractor: _____ Date: _____

**Plaintiff Balfour Beatty's
Trial Exhibit # 12**
(part 2 of 11)

DAILY WORK ORDER REPORT

PROJECT TITLE: Marion Square
PROJECT NO. _____


DATE PERFORMED: _____
DATE OF REPORT: _____

Description of Work		Labor	
1)	Level 6 West	Reg.	12
2)	4 men 3 hrs ea. changing uniform cables bundle 90-94	O.T.	
3)	4 men 3 hrs Relocating cables around sleeves & block outs added after cables were installed	Reg.	
4)		O.T.	12
5)	3 men 2 hrs adding rebar and harpins around sleeves & blockouts added	Reg.	6
6)		O.T.	
7)	3 men 2 hrs Repairing cables & stud rails for RFI # 0634 opening added @ col B-20	Reg.	6
8)		O.T.	
9)		Reg.	
10)		O.T.	
TOTAL		Reg.	36
		O.T.	

The below agree to all above stated conditions:

General Contractor Representative _____

[illegible]



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO34
Change Order Date: 8/29/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: Add Hairpins

Description of Changes:

ADD HAIRPINS REQUIRED PER RFI - 0655

Amount of this Change Order (excluding taxes) \$ 1,397.25

It is mutually agreed that for such change the contract price is changed by \$ 1,397.25 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____
Salesman - Catherine McDowell

Date: _____

Date: _____



**SUBCONTRACT
CHANGE
ORDER**

Subcontract Change Order Number: 4
Contractor: Lithko Contracting Inc.
Subcontractor: East Coast Rebar, Inc.
Project: Hotel at Marion Square
Date of Original Subcontract: June 17, 2015

Pursuant to and subject to the terms and conditions of the above referenced Subcontract, Subcontractor is directed to make the following changes in the work:

C/O #	Item Description	Approved Amount
04	Rodbusters 76 hrs Moving rebar and PT cables in slam pour #2 on level 2 for mechanical openings and pipe sleeves	45.00/hour \$3,420.00
TOTAL THIS CHANGE ORDER		\$3,420.00

Except as specifically set forth hereinabove, Subcontractor waives any and all other claims it may have arising out of or related to the above referenced changes to the Subcontract. Retention of this Change Order for ten (10) days or commencement of the work or shipment of materials set forth herein shall constitute acceptance of this Change Order.

EAST COAST REBAR, INC.
PO Box 351
Rutherfordton, NC 28139
P: 828-287-4287 F: 828-287-9268

Original Subcontract:	\$ 380,234.00
Previous Change Orders:	\$ 12,465.00
Subcontract Sum Prior to this C/O	\$ 392,699.00
Value This Change Order	\$3,420.00
Revised Subcontract Amount	\$ 396,119.00

By: Larry Greene
Name: Larry Greene
Title: President
Date: 5/19/2016

Lithko Contracting Inc.
PO Box 270
Monroe, Ohio 45050

ACCEPTED - The above prices and specifications of this change order are satisfactory and are hereby accepted. All work to be performed under same terms and conditions as specified in original contract unless before or herein modified.

Name: _____
Title: _____
Date: _____

PROJECT TITLE: Mazon Square
PROJECT NO. _____

DATE PERFORMED: _____
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extend
1) Level 6 East		8	Reg.	
2 men 4 hrs adding rebar & hairpins around openings & sleeves added after cables were in place			O.T.	
3) 8/29			Reg.	
4 men 3 hrs relocating PT & rebar for sleeves & openings		12	O.T.	
4) 8/30			Reg.	
4 men 2 hrs relocating PT, rebar and stud rails for added sleeves & block outs		8	O.T.	
5) 3 men 2 hrs relocating cables			Reg.	
6) RFI 0655		6	O.T.	
7) 3 men 2 hrs fixing banded & uniform between line 23 & 26 lines A+B			Reg.	
8) 9)		6	O.T.	
10) 10)			Reg.	
			O.T.	
TOTAL		40		

The below agree to all above stated conditions:

General Contractor Representative _____

Job Document		Marion Square COR 59 RFI-0663 Slab 1 & 2 Nose Resteel										TO BE COMPLETED BY CONTRACTOR					TO BE COMPLETED BY				
A	B	C	D	E	H	H	H	H	H	J	K	M	M	M	N	Q					
	Item No	Description	Quantity	Unit of measure	Hours Per Unit	Labor Rate	Labor (L)	Material (M)	Equip. (E)	Sub Contract (\$)	Total L +M +E+S	Raw Unit cost	Type Of Change	Comments	Status						
		Additional Steel	1 LS																		
		Labor to wet set all steel	2 HR		36.00		\$72.00	\$300.00													
		Forms			Days	Daily rate															
		10k 4x2'	12 day	8.00	7.93			\$761.14													
		10k 6' braces	12.0 day	8.00	1.64			\$157.71													
		10k baseplate	16 day	8.00	1.36			\$173.71													
		10k screw jack	24 day	8.00	2.86			\$648.57													
		300 prop	2 day	8.00	6.00			\$96.00													
		350 prop	4 day	8.00	7.14			\$228.57													
		450 prop	11 day	8.00	11.11			\$977.43													
		4-way U-Head	6 day	8.00	1.82			\$67.43													
		Bracing clamp	24 day	8.00	0.71			\$137.14													
		2.90m beam	75 day	8.00	3.07			\$1842.86													
		3.30m beam	8 day	8.00	3.54			\$226.28													
		18'-0" beam	8 day	8.00	5.25			\$336.00													
		Sales Tax	8.5%				72.00	5872.86	0.00	0.00											
		Subtotal					72.00	499.19	0.00	0.00											
		Mark Up	15%				10.80	6372.05	0.00	0.00											
		Subtotal					82.80	7327.86	0.00	0.00											
		General Liability Insurance						0.00	0.00	0.00											
		Charleston Bus. License					0.00	0.00	0.00	0.00											
		Total					\$82.80	\$7,327.86	\$0.00	\$0.00											
		TOTAL REQUEST THIS PAGE								\$7,410.66											



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO36
Change Order Date: 9/1/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: Additional Material

Description of Changes:

RFI - 0655: ADD. #3 BARS AROUND ELECTRICAL BOXES AT STAIR TREADS

Amount of this Change Order (**excluding taxes**) \$ **300.00**

It is mutually agreed that for such change the contract price is changed by \$ **300.00**, terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____
Salesman - Catherine McDowell

Date: _____

Date: _____

Attachment to Invoice

Rental

No.:412663564

Date: 06/30/2016

Page: 20 / 26

Ship To:

Marion Square
LITHKO CONTRACTING, INC.
404 King StreetDoka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045T (770) 962-7914
F (770) 962-5238
usa@doka.com
www.dokausa.com**doka**Job Site 412006077 Marion Square- Shoring & Reshore
Start of Rental 10/10/2013

Beginning Inventory per			06/01/2016		2,248,334.00						
Item No.	Item Description	End/Begin	Rent	Qty	Unit	Price/USD	Price	Unit Value	Days	Rental Rate	Amount/USD
183045000	Dokamatic insertion beam 2.45m			200.00	EA	61.00	EA	12,200.00	28 + 2	2.150% / 28 days	281.04
188701000	Doka beam H20 top P 1.80m			474.00	EA	55.00	EA	26,070.00	28 + 2	2.150% / 28 days	600.54
188702000	Doka beam H20 top P 2.45m			866.00	EA	76.00	EA	65,816.00	28 + 2	2.150% / 28 days	1,516.12
189702000	Doka beam H20 top P 2.45m			400.00	EA	76.00	EA	30,400.00	28 + 2	2.150% / 28 days	700.28
189704000	Doka beam H20 top P 2.90m			30.00	EA	86.00	EA	2,580.00	28 + 2	2.150% / 28 days	59.43
189705000	Doka beam H20 top P 3.30m			213.00	EA	99.00	EA	21,087.00	28 + 2	2.150% / 28 days	485.76
189706000	Doka beam H20 top P 3.60m			12.00	EA	110.00	EA	1,320.00	28 + 2	2.150% / 28 days	30.41
188707000	Doka beam H20 top P 3.90m			16.00	EA	117.00	EA	1,872.00	28 + 2	2.150% / 28 days	43.12
188712000	Doka beam H20 top P 16'-0"			68.00	EA	147.00	EA	9,996.00	28 + 2	2.150% / 28 days	230.27
188712000	Doka beam H20 top P 16'-0"			30.00	EA	147.00	EA	4,410.00	28 + 2	2.150% / 28 days	101.59
189713000	Doka beam H20 top P 11'-6"			20.00	EA	107.00	EA	2,140.00	28 + 2	2.150% / 28 days	49.30
189936000	Doka beam H20 eco P 2.45m			9.00	EA	76.00	EA	684.00	28 + 2	2.150% / 28 days	15.76
581603000	Multi-purpose walling WS10 Top50 6'-0"			1.00	EA	289.00	EA	289.00	28 + 2	2.150% / 28 days	6.66
581616000	Multi-purpose walling WS10 Top50 7'-0"			52.00	EA	337.00	EA	17,524.00	28 + 2	2.150% / 28 days	403.68
581626000	Dokamatic S table 9'-0"x18'-0"			7.00	EA	4,633.00	EA	32,431.00	28 + 2	2.150% / 28 days	747.07
581626000	Dokamatic S table 9'-0"x18'-0"			43.00	EA	4,633.00	EA	199,219.00	28 + 2	2.150% / 28 days	4,589.16
581627000	Dokamatic S table 9'-0"x12'-0"			17.00	EA	3,159.00	EA	53,703.00	28 + 2	2.150% / 28 days	1,237.00
581627000	Dokamatic S table 9'-0"x12'-0"			18.00	EA	3,159.00	EA	56,862.00	28 + 2	2.150% / 28 days	1,309.86
581628000	Dokamatic S table 7'-0"x18'-0"			20.00	EA	4,001.00	EA	80,020.00	28 + 2	2.150% / 28 days	1,843.32

Transfer/USD 14,250.46

Wire Transfer Ref: Bank of America

Account: 003121715

ABA Code:

(61000009)

R - 1644

Attachment to Invoice**Rental****No.:412663564****Date:** 06/30/2016**Page:** 21 / 26**Ship To:**

Marion Square
LITHKO CONTRACTING, INC.
 404 King Street

Doka USA, Ltd.
 105A Boulderbrook Circle
 Lawrenceville, GA 30045

T (770) 962-7914
F (770) 962-5238
 usa@doka.com
 www.dokausa.com

doka

Job Site 412006077 Marion Square- Shoring & Reshore
Start of Rental 10/10/2013

Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price	Unit Value	Days	Rental Rate	Amount/USD
581628000	Dokamatic S table 7'-0"x18'-0"		28.00	EA	4,001.00	EA	112,028.00	28 + 2	2.150% / 28 days	2,580.65
581629000	Dokamatic S table 7'-0"x12'-0"		31.00	EA	2,938.00	EA	91,078.00	28 + 2	2.150% / 28 days	2,098.04
581629000	Dokamatic S table 7'-0"x12'-0"		8.00	EA	2,938.00	EA	23,504.00	28 + 2	2.150% / 28 days	541.43
582528000	Spring locked connecting pin 16mm		30.00	EA	9.00	EA	270.00	28 + 2	2.150% / 28 days	6.22
583011000	Doka multi-trip transport box 1,20x0.80m		10.00	EA	558.00	EA	5,580.00	28 + 2	2.150% / 28 days	128.52
583012000	Doka skeleton transport box 1,70x0.80m		12.00	EA	1,042.00	EA	12,504.00	28 + 2	2.150% / 28 days	288.04
583016000	Doka stacking pallet 1,20x0.80m		1.00	EA	329.00	EA	329.00	28 + 2	2.150% / 28 days	7.58
585700000	10k crossbrace 3/4"x4"V		544.00	EA	46.00	EA	25,024.00	28 + 2	2.150% / 28 days	576.45
585701000	10k crossbrace 3/4"x5"V		210.00	EA	46.00	EA	9,660.00	28 + 2	2.150% / 28 days	222.53
585702000	10k crossbrace 3/4"x6"V		62.00	EA	46.00	EA	2,852.00	28 + 2	2.150% / 28 days	65.70
585707000	10k frame 2V"x4'-0"		8.00	EA	222.00	EA	1,776.00	28 + 2	2.150% / 28 days	40.91
585707000	10k frame 2V"x4'-0"		8.00	EA	222.00	EA	1,776.00	28 + 2	2.150% / 28 days	40.91
585712000	10k frame 4W"x4'-0"		168.00	EA	249.00	EA	41,832.00	28 + 2	2.150% / 28 days	963.63
585713000	10k frame 4W"x5'-0"		104.00	EA	260.00	EA	27,040.00	28 + 2	2.150% / 28 days	622.89
585713000	10k frame 4W"x5'-0"		200.00	EA	260.00	EA	52,000.00	28 + 2	2.150% / 28 days	1,197.85
585714000	10k frame 4W"x6'-0"		185.00	EA	300.00	EA	55,500.00	28 + 2	2.150% / 28 days	1,279.48
585715000	10k Universal connector		958.00	EA	15.00	EA	14,370.00	28 + 2	2.150% / 28 days	331.02
585716000	10k Rivet		1,950.00	EA	4.70	EA	9,165.00	28 + 2	2.150% / 28 days	211.13
585717000	10k Hitch pin		1,950.00	EA	4.70	EA	9,165.00	28 + 2	2.150% / 28 days	211.12

Transfer/USD 25,863.57

WFO Transfer Del. Date of Arrival

Account: 0231121716

ASA Code:

02/200003

Attachment to Invoice

Rental

No.: 412663564

Date: 06/30/2016

Page: 22 / 26

Ship To:

Marion Square
LITHKO CONTRACTING, INC.
404 King Street

Doka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045

T (770) 962-7914
F (770) 962-5238
usa@doka.com
www.dokausa.com

doka

Job Site 412006077 Marion Square- Shoring & Reeshore
Start of Rental 10/10/2013

Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price Unit Value	Days	Rental Rate	Amount/USD
585721000	10k Screw Jack 36"		884.00	EA	80.00	EA	28 + 2	2.150% / 28 days	1,629.09
585722000	10k Screw Jack baseplate		442.00	EA	38.00	EA	28 + 2	2.150% / 28 days	386.91
586018000	Laeshing strap 5.00m		40.00	EA	77.00	EA	28 + 2	2.150% / 28 days	70.95
586097000	Plastic mallet 4kg		4.00	EA	173.00	EA	28 + 2	2.150% / 28 days	15.94
586119400	Doka floor prop Euxec 30 top 450		23.100	EA	911.00	EA	28 + 2	2.150% / 28 days	6,914.45
586151000	Doka sticking pallet 1.55x0.85m		81.00	EA	363.00	EA	28 + 2	2.150% / 28 days	677.31
586155000	Removable folding tripod		88.00	EA	153.00	EA	28 + 2	2.150% / 28 days	310.16
586155900	Removable folding tripod top		50.00	EA	153.00	EA	28 + 2	2.150% / 28 days	176.22
586174000	Lowering head H20		178.00	EA	62.00	EA	28 + 2	2.150% / 28 days	254.23
586179000	Supporting head H20 DF		123.00	EA	22.00	EA	28 + 2	2.150% / 28 days	62.33
586195000	Bracing clamp B		150.00	EA	20.00	EA	28 + 2	2.150% / 28 days	69.11
586214000	Dokamatic swivel head 40		724.00	EA	252.00	EA	28 + 2	2.150% / 28 days	4,202.82
586215000	Dokamatic strut connection		30.00	EA	64.00	EA	28 + 2	2.150% / 28 days	44.23
586231000	Dokamatic lifting strap 13.00m		2.00	EA	653.00	EA	28 + 2	2.150% / 28 days	30.08
741000266	10k U-head B-x3"		442.00	EA	51.00	EA	28 + 2	2.150% / 28 days	519.28
741001221	Dokamatic WS-10 table 9'-0"x18'-0"		2.00	EA	4,949.00	EA	28 + 2	2.150% / 28 days	228.01
741001222	Dokamatic WS-10 table 9'-0"x12'-0"		6.00	EA	3,370.00	EA	28 + 2	2.150% / 28 days	465.78
741001224	Dokamatic WS-10 table 7'-0"x12'-0"		1.00	EA	3,106.00	EA	28 + 2	2.150% / 28 days	71.55
Total Square Feet:			21.199						
Activity during the Month									

Transfer/USD 51,792.02

We Transfer Cert. Bank of America

Account ID: 121715

404 Cont.

07/25/2017

Job: Marion Square
Document: COR Stair Framework

TO BE COMPLETED BY CONTRACTOR															TO BE COMPLETED BY			
A	B	C	D	E	H	H	H	H	I	J	K	M	M	N	Q			
	Item No.	Description	Quantity	Unit of measure	Hours Per Unit	Labor Rate	Labor (L)	Material (M)	Equip. (E)	Sub Contract (\$)	Total L +M +E +S	Raw Unit cost	Type Of Change	Comments	Status			
		Forms			Days	Daily rate												
		10x 4x2'	12 day		20	7.93		\$1,902.86						Stairs were ready to pour 8/10/16 but then we				
		10x 6' braces	12.0 day		20	1.64		\$394.28						were put on hold because the electrical boxes				
		10x baseplate	16 day		20	1.36		\$434.28						had not been approved and released for delivery				
		10x screw jack	24 day		20	2.86		\$1,371.43						in time. Boxes arrived and install began 8/25/16				
		300 drop	2 day		20	6.00		\$240.00						with them being completed in time				
		350 drop	4 day		20	7.14		\$571.43						for us to pour 8/30/16. On 8/28/16 RFI-0663				
		450 drop	11 day		20	11.11		\$2,443.57						was generated delaying the pour an additional				
		4-way U-Head	6 day		20	1.82		\$218.57						8 days 8/10/16-8/30/16 = 20 day delay				
		Bracing clamp	24 day		20	0.71		\$342.86										
		2.90m beam	75 day		20	3.07		\$4,607.14										
		3.30m beam	8 day		20	3.54		\$565.71										
		16'-0" beam	8 day		20	5.25		\$840.00										
		Sales Tax	8.5%				0.00	13932.14	0.00	0.00								
		Subtotal					0.00	1184.23	0.00	0.00								
		Mark-Up	15%				0.00	15116.38	0.00	0.00								
								2267.46	0.00	0.00								
		Subtotal					0.00	17383.83	0.00	0.00								
		General Liability Insurance						0.00	0.00	0.00								
		Charleston Bus. License					0.00	0.00	0.00	0.00								
		Total					\$0.00	\$17,383.83	\$0.00	\$0.00								
		TOTAL REQUEST THIS PAGE								\$17,383.83								

Attachment to Invoice

Rental

No.:412663564

Date: 06/30/2016

Page: 20 / 26

Ship To:

Marion Square
LITTKO CONTRACTING, INC.
404 King Street

Doka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045

T (770) 962-7914
F (770) 962-5238
usa@doka.com
www.dokausa.com



Job Site 412006077 Marion Square- Shoring & Reshore
Start of Rental 10/10/2013

Beginning Inventory per			06/01/2016		2,248,334.00					
Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price	Unit Value	Days	Rental Rate	Amount/USD
183045000	Dokamatic Insertion beam 2.45m		200.00	EA	61.00	EA	12,200.00	28 + 2	2.150% / 28 days	281.04
189701000	Doka beam H20 top P 1.80m		474.00	EA	55.00	EA	26,070.00	28 + 2	2.150% / 28 days	600.54
189702000	Doka beam H20 top P 2.45m		866.00	EA	76.00	EA	65,816.00	28 + 2	2.150% / 28 days	1,516.12
189702000	Doka beam H20 top P 2.45m		400.00	EA	76.00	EA	30,400.00	28 + 2	2.150% / 28 days	700.28
189704000	Doka beam H20 top P 2.90m		30.00	EA	86.00	EA	2,580.00	28 + 2	2.150% / 28 days	59.43
189705000	Doka beam H20 top P 3.30m		213.00	EA	99.00	EA	21,087.00	28 + 2	2.150% / 28 days	485.76
189706000	Doka beam H20 top P 3.80m		12.00	EA	110.00	EA	1,320.00	28 + 2	2.150% / 28 days	30.41
189707000	Doka beam H20 top P 3.80m		16.00	EA	117.00	EA	1,872.00	28 + 2	2.150% / 28 days	43.12
189712000	Doka beam H20 top P 16'-0"		68.00	EA	147.00	EA	9,996.00	28 + 2	2.150% / 28 days	230.27
189712000	Doka beam H20 top P 16'-0"		30.00	EA	147.00	EA	4,410.00	28 + 2	2.150% / 28 days	101.59
189713000	Doka beam H20 top P 11'-6"		20.00	EA	107.00	EA	2,140.00	28 + 2	2.150% / 28 days	49.30
189936000	Doka beam H20 eco P 2.45m		9.00	EA	76.00	EA	684.00	28 + 2	2.150% / 28 days	15.76
581803000	Multi-purpose walling WS10 Top50 6'-0"		1.00	EA	289.00	EA	289.00	28 + 2	2.150% / 28 days	6.66
581816000	Multi-purpose walling WS10 Top50 7'-0"		52.00	EA	337.00	EA	17,524.00	28 + 2	2.150% / 28 days	403.68
581826000	Dokamatic S table 9'-0"x18'-0"		7.00	EA	4,633.00	EA	32,431.00	28 + 2	2.150% / 28 days	747.07
581826000	Dokamatic S table 9'-0"x18'-0"		43.00	EA	4,633.00	EA	199,219.00	28 + 2	2.150% / 28 days	4,589.16
581827000	Dokamatic S table 9'-0"x12'-0"		17.00	EA	3,159.00	EA	53,703.00	28 + 2	2.150% / 28 days	1,237.00
581827000	Dokamatic S table 9'-0"x12'-0"		18.00	EA	3,159.00	EA	56,862.00	28 + 2	2.150% / 28 days	1,309.86
581828000	Dokamatic S table 7'-0"x18'-0"		20.00	EA	4,001.00	EA	80,020.00	28 + 2	2.150% / 28 days	1,843.32

Transfer USD

14,250.46

Wire Transfer Ref: Bank of America

Account: 003127715

ABA Code:

001200009

R - 1648

Attachment to Invoice

Rental

No.:412663564

Date: 06/30/2016

Page: 21 / 26

SHIP To:

Marion Square
LITHKO CONTRACTING, INC.
404 King StreetDoka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045T (770) 962-7914
F (770) 962-5238
usa@doka.com
www.dokausa.com**doka**Job Site 412006077 Marion Square- Shoring & Restore
Start of Rental 10/10/2013

Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price Unit Value	Days	Rental Rate	Amount/USD
					Transfer/USD				14,250.46
581628000	Dokumalle S table 7'-0"x18'-0"		28.00	EA	4,001.00	EA	28 + 2	2,150% / 28 days	2,580.65
581629000	Dokumalle S table 7'-0"x12'-0"		31.00	EA	2,938.00	EA	28 + 2	2,150% / 28 days	2,098.04
581629000	Dokumalle S table 7'-0"x12'-0"		8.00	EA	2,938.00	EA	28 + 2	2,150% / 28 days	541.43
582528000	Spring locked connecting pin 16mm		30.00	EA	9.00	EA	28 + 2	2,150% / 28 days	6.22
583011000	Doka multi-rip transport box 1.20x0.80m		10.00	EA	558.00	EA	28 + 2	2,150% / 28 days	128.52
583012000	Doka skeleton transport box 1.70x0.80m		12.00	EA	1,042.00	EA	28 + 2	2,150% / 28 days	288.04
583016000	Doka stacking pallet 1.20x0.80m		1.00	EA	329.00	EA	28 + 2	2,150% / 28 days	7.58
585700000	10k crossbrace 3/4"x4W		544.00	EA	46.00	EA	28 + 2	2,150% / 28 days	576.45
585701000	10k crossbrace 3/4"x5W		210.00	EA	46.00	EA	28 + 2	2,150% / 28 days	222.53
585702000	10k crossbrace 3/4"x6W		62.00	EA	46.00	EA	28 + 2	2,150% / 28 days	65.70
585707000	10k frame 2W"x4'-0"		8.00	EA	222.00	EA	28 + 2	2,150% / 28 days	40.91
585707000	10k frame 2W"x4'-0"		8.00	EA	222.00	EA	28 + 2	2,150% / 28 days	40.91
585712000	10k Frame 4W"x4'-0"		168.00	EA	249.00	EA	28 + 2	2,150% / 28 days	963.63
585713000	10k Frame 4W"x5'-0"		104.00	EA	260.00	EA	28 + 2	2,150% / 28 days	622.89
585713000	10k Frame 4W"x5'-0"		200.00	EA	260.00	EA	28 + 2	2,150% / 28 days	1,197.86
585714000	10k Frame 4W"x5'-0"		185.00	EA	300.00	EA	28 + 2	2,150% / 28 days	1,278.48
585715000	10k Universal connector		958.00	EA	15.00	EA	28 + 2	2,150% / 28 days	331.02
585716000	10k Rivet		1,950.00	EA	4.70	EA	28 + 2	2,150% / 28 days	211.13
585717000	10k Hitch pin		1,950.00	EA	4.70	EA	28 + 2	2,150% / 28 days	211.12

Transfer/USD 25,063.57

Wire Transfer Det. Bank of America

Account 023121716

ABA Code:

(07-20003)

Attachment to Invoice

Rental

No.:412663564

Date: 06/30/2016

Page: 22 / 26

Ship To:

Marion Square
LITHKO CONTRACTING, INC.
404 King Street

Doka USA, Ltd.
105A Boulderbrook Circle
Lawrenceville, GA 30045

T (770) 362-7914
F (770) 362-5238
usa@doka.com
www.dokausa.com

doka

Job Site 412006077 Marion Square- Shoring & Restore
Start of Rental 10/10/2013

Item No.	Item Description	End/Begin Rent	Qty	Unit	Price/USD	Price Unit Value	Days	Rental Rate	Amount/USD
585721000	10k Screw Jack 35"		884.00	EA	80.00	EA	28 + 2	2.150% / 28 days	1,629.09
585722000	10k Screw Jack Baseplate		442.00	EA	38.00	EA	28 + 2	2.150% / 28 days	386.91
585018000	Lashing strap 5.00m		40.00	EA	77.00	EA	28 + 2	2.150% / 28 days	70.95
585097000	Plastic mallet 4kg		4.00	EA	173.00	EA	28 + 2	2.150% / 28 days	15.94
585119400	Doka floor prop Eures 30 top 450		2,361.00	EA	6.00	EA	28 + 2	2.150% / 28 days	16,914.45
585151000	Doka sticking pallet 1.55x0.85m		81.00	EA	363.00	EA	28 + 2	2.150% / 28 days	677.31
585155000	Removable folding tripod		88.00	EA	153.00	EA	28 + 2	2.150% / 28 days	310.16
585155500	Removable folding tripod top		50.00	EA	153.00	EA	28 + 2	2.150% / 28 days	176.22
585174000	Lowering head H20		178.00	EA	62.00	EA	28 + 2	2.150% / 28 days	254.23
585179000	Supporting head H20 DF		123.00	EA	22.00	EA	28 + 2	2.150% / 28 days	62.33
585195000	Bracing clamp B		150.00	EA	20.00	EA	28 + 2	2.150% / 28 days	69.11
585214000	Dokamatic swivel head 40		724.00	EA	252.00	EA	28 + 2	2.150% / 28 days	4,202.82
585215000	Dokamatic strut connection		30.00	EA	64.00	EA	28 + 2	2.150% / 28 days	44.23
585231000	Dokamatic lifting strap 13.00m		2.00	EA	653.00	EA	28 + 2	2.150% / 28 days	30.08
741000266	10k U-head 8"x8"		442.00	EA	51.00	EA	28 + 2	2.150% / 28 days	519.28
741001221	Dokamatic WS-10 table 9'-0"x18'-0"		2.00	EA	4,949.00	EA	28 + 2	2.150% / 28 days	228.01
741001222	Dokamatic WS-10 table 9'-0"x12'-0"		6.00	EA	3,370.00	EA	28 + 2	2.150% / 28 days	465.78
741001224	Dokamatic WS-10 table 7'-0"x12'-0"		1.00	EA	3,106.00	EA	28 + 2	2.150% / 28 days	71.55
Total Square Feet: 21,199									
Activity during the Month									

Transfer/USD 51,792.02

Wire Transfer/USD, State of Georgia

Account 0011-21711

doka Corp.

0011-21711

R - 1651



CMC Rebar Carolinas - Columbia
2105 South Beltline Blvd
Columbia, SC 29201
Phone (803) 227-7823
Fax (803) 254-4581

CMC Change Order #: CO35
Change Order Date: 8/29/16

CHANGE ORDER REQUEST

Customer: Lithko Contracting Inc
5353 Hamilton-Middletown Rd
Hamilton, OH 45011-2407

Project: Hotel at Marion Square

CMC Job #: 1522100345

Subject: ADDITIONAL 1000 #5 5'-0"

Description of Changes:

ADDITIONAL 1000 #5 5'-0" LONG REQUIRED FOR TENDONS, AT PIPE PENETRATIONS

Amount of this Change Order (excluding taxes) \$ 2,972.55

It is mutually agreed that for such change the contract price is changed by \$ 2,972.55 , terms of payment are net 30 days. No retainage of funds will be allowed. If you have any questions regarding our Change Order, immediately contact the below signed to schedule a meeting to discuss it.

Lithko Contracting Inc

CMC Rebar

Signature: _____

Signature: _____

Salesman - Catherine McDowell

Date: _____

Date: _____

[illegible]



PROJECT FILE: Martin Square
PROJECT NO: _____

DATE PERFORMED:

DATE OF REPORT:

Description of Work	Estimate
Level 6 West	
4 men 3 hrs ea. changing uniform cables bundle 90-94	Reg. 12 O.T.
4 men 3 hrs Relocating cables around sleeves + block outs added after cables were installed	Reg. 12 O.T.
3 men 2 hrs adding rebars and harpins around sleeves + blockouts added	Reg. 6 O.T.
3 men 2 hrs Repairing cables + stud rails for RFI # 0634 opening added @ CD / B-20	Reg. 6 O.T.
	Reg. O.T.
	Reg. O.T.
	Reg. O.T.
	Reg. O.T.
	Reg. O.T.
	Reg. O.T.
TOTAL	36

The below agree to all above stated conditions:

The below agree to all above stated conditions:

General Contractor Representative

PROJECT TITLE: Mazon Spence
PROJECT NO. _____

DATE PERFORMED: _____
DATE OF REPORT: _____

Description of Work	Labor	Hours	Hourly Rate	Extended
Level 6 East		8		
2 men 4 hrs adding rebar & haupins	1)	Reg.		
around openings & sleeves added after	2)	O.T.		
cables were in place		Reg.		
8/29	3)	O.T.		
4 men 3 hrs relocating PT + rebar		Reg.		
for sleeves + openings	4)	O.T.		
8/30		Reg.		
4 men 2 hrs relocating PT, rebar	5)	O.T.		
and stud rails for added sleeves +		Reg.		
block outs	6)	O.T.		
3 men 2 hrs relocating cables	7)	Reg.		
RFI 0655	8)	O.T.		
3 men 2 hrs fixing banded & uniform		Reg.		
between line 23 + 26 lines A+B	9)	O.T.		
		Reg.		
	10)	O.T.		
TOTAL				40

The below agree to all above stated conditions:

General Contractor Representative _____

Tab No. 103

Balfour Beatty Construction

December 16, 2017

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 103R1
MOD 5 - Mechanical Revisions

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 103R1 in the amount of Two hundred ninety thousand two hundred fifty-seven (\$290,257.91) to provide additional work in accordance with the following qualifications:

Change order cost includes added scope from mechanical and plumbing revisions per modification five. This cost specifically includes:

- Drawing M103
 - 12x6 duct and 22x6 SAR for VFCU-14 in guestroom C3. (third floor)
 - Relocated VFCU-15, VFCU-8 and associated ductwork and grilles due to modification of IDF and electrical room.
 - Added fire dampers to ductwork for VFCU-8.
 - Added fire dampers to supply and return ductwork for HFCU-7.
- M103A
 - Relocated VFCU-15, VFCU-8, and associated chilled water lines.
- M104
 - Provide 12x6 duct and 22x6 SAR for VFCU-14 in guestroom C3 (fourth floor)
 - Relocated VFCU-17, VFCU-9 and associated ductwork and grilles due to modification of IDF and electrical room.
 - Added fire dampers to ductwork for VFCU-9.
 - Added fire dampers to supply and return ductwork for HFCU-8.
- M104A
 - Relocated VFCU-17, VFCU-9, and associated chilled water lines.
 - *Revised chilled water distribution from two five inch pipes to four smaller pipes to achieve maximum allowable ceiling height.*
- M105
 - Provided 12x6 duct and 22x6 SAR for VFCU-14 in guestroom C3
 - Relocated VFCU-19, VFCU-10, and associated ductwork and grilles due to modification of IDF and electrical room.
 - Added fire dampers to ductwork for VFCU-10.
 - Added fire dampers to supply and return ductwork for HFCU-9.
- M105A
 - Relocated VFCU-19, VFCU-10, and associated chilled water lines.
 - Updated chilled water lines and riser at guestrooms B10 (519), B3 (521), and B9 (517).

- Relocated chilled water riser at guestroom A18 (503)
- M106
 - Removed VFCU-3~7 from Concierge room and added HFCU-26, HFCU-27, and associated ductwork and grilles.
 - Added VFCU-33, and relocated VFCU-11, associated ductwork, and grilles due to modification/addition of IDF and electrical room.
 - Added fire dampers to ductwork for VFCU-11.
 - Relocated VFCU-14 in guestroom E1.
 - Relocated EF-42 and associated ductwork to relocated restroom and relocated HFCU-10 due to relocation of restroom.
 - Added (5) fire dampers and (2) access panels for HFCU-10 ductwork.
- M106A
 - Added VFCU-33 and relocated VFCU-11 and relocated associated chilled water lines.
 - Added HFCU-26, HFCU-27, and updated chilled water lines and risers.
 - Relocated VFCU-14, and associated chilled water lines.
- M107
 - Relocated VFCU-22, VFCU-12, and associated ductwork and grilles due to modification of IDF and electrical room.
 - Added fire dampers to ductwork for VFCU-12.
 - Added fire dampers to supply and return ductwork for HFCU-11.
 - Relocated VFCU-15 in guestroom E1.
- M107A
 - Relocated VFCU-22, VFCU-12, and associated chilled water lines.
 - Relocated VFCU-14 and associated chilled water lines.
- M108A
 - Relocated VFCU-24, VFCU-13, and associated chilled water lines.
 - Relocated VFCU-14 and associated chilled water lines.
- M409
 - Relocated VFCU-24 and VFCU-13 and associated ductwork and grilles due to modification of IDF and electrical room.
 - Added fire dampers to ductwork for VFCU-12
 - Added 8x3 exhaust ductwork for EF-42.
 - Added fire damper to supply and return ductwork for HFCU-12.
- M410
 - Relocated VFCU-14 in guestroom E1.
- M411
 - Relocated 8x3 exhaust ductwork and 12x12 louver for EF-42.
- M501
 - Added HFCU-26 and HFCU-27 to detail 6/M501 and updated condensate and chilled water line sizes.
- M501A
 - Added VFCU-33 to detail 9/M501A and updated condensate and chilled water line sizes.
- M602
 - Removed VFCU-3~7 from chilled water fan coil unit schedule.
 - Added HFCU-26, HFCU-27, and VFCU-33 to chilled water fan coil unit schedule.
- P100
 - Deleted natural gas pipe to lanterns.
- P103

- Deleted 3" sanitary from relocated bathroom on sixth floor.
- Revised domestic water piping at Linen/Storage 300H and added pipe size information to Toilet 300J.
- P104
 - Deleted 3" sanitary from relocated bathroom on sixth floor.
- P105
 - Deleted 3" sanitary from relocated bathroom on sixth floor.
 - Deleted natural gas piping to lanterns and added natural gas to fireplace at Manager's Apartment.
 - Showed offset for 4" rain leader over guestroom 519.
- P106
 - Deleted sanitary piping from relocated bathroom on sixth floor. Added natural gas stub out for fireplace at Manager's Apartment.
- P107
 - Deleted vent from relocated bathroom on sixth floor.
 - Added natural gas stub out for fireplace at Manager's Apartment.
- P108
 - Deleted vent from relocated bathroom on sixth floor.
 - Deleted natural gas pipe for fireplace at Terrace Bar.
 - Showed water piping up to TMV-3.
 - Showed water piping up to foot rinse.
 - Revised water piping at linen Storage 800H.
- P109
 - Showed natural gas stub out for fireplace.
 - Provided tempered water for ST-3.
 - Provided TMV-3 for ST-3.
 - Provided water for pool drinking fountain and added drainage and air admittance valve.
 - Provided hose bib in Pool Equipment room RT16.
 - Provided water for foot rinse at east entrance to pool deck.
 - Provided NFHW at east entrance to pool deck.
 - Provided hot & cold water to Men RT18 and Women RT20 bathrooms.
- P503
 - Deleted gas lanterns.
 - Added gas to Manager's Apartment.
 - Added gas for rooftop terrace bar fireplace.
 - Revised gas flows and pipe sizes for deleted/added gas equipment.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Balfour Beatty Construction

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Alec Dooley
Assistant Project Manager

cc:

Marty Wall
Melissa Pense
Jim Clements
Jennifer Faulkinberry
Taylor Walker
Nick Starcevic
Tim Spano
David Stanton

RCO # 103R1 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 103R1– MOD 5 - Mechanical Revisions

The additional work for the **MOD 5 - Mechanical Revisions** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.51500000.40	MOD 5 - Mechanical Revisions	\$276,838.84

Total Items	\$276,838.84
Total Markups	\$13,419.07
RCO Total	\$290,257.91

The total Cost to perform the work as described above is an ADD of Two hundred ninety thousand two hundred fifty-seven (\$290,257.91).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 103R1



Mechanical

November 16, 2017

Balfour Beatty Construction
306 Meeting Street
Suite 300
Charleston, SC 29401

Re: Hotel Marion Square – MOD 5 Plan Review

Dear Nick:

Based upon our last meeting to review MOD 5, our estimating department verified their take off. What was discovered on drawing M104A was that on the loops that were added overall capacity was an issue and upsized from 3" to 4" during the coordination process. In one run of piping our estimator took off the 4" as an add, but did not deduct the 3" that was replaced by the 4" it added.

Attached is a revised proposal to reflect this correction. All other drawings related to this change have been verified and remain unchanged. Also included is this proposal is a consolidated take off by drawing. We would like to apologize for any inconvenience this may have caused. Please review and advise should you have any questions.

Sincerely,

Paul Amend
Bernhard MCC
Accounting Manager

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

Proposed Change Summary

Project: The Hotel at Marion Square
Location: Charleston, SC

Date: 11/16/17

BMCC Job # 8350248
BMCC PCO # 36 REV BC_3

Description: MOD 5 Revised

Labor Breakdown:

<u>Std Hrs</u>	<u>Prem Hrs</u>		<u>Std Rate</u>	<u>Prem Rate</u>	
122.6	0.0	Project Manager / Purchasing	\$80.00	\$120.00	\$9,808.00
270.4	0.0	Superintendent / Fab Coordinator	\$75.00	\$112.50	\$20,280.00
394.7	0.0	Foreman (Working)	\$51.00	\$76.50	\$20,129.70
798.6	0.0	Journeyman / Expediter	\$44.00	\$66.00	\$35,138.40
0.0	0.0	Start-up Technician	\$88.00	\$132.00	\$0.00
200.0	0.0	BIM Coordinator	\$70.00	\$105.00	\$14,000.00
112.0	0.0	Detailer - Fabrication	\$53.00	\$79.50	\$5,936.00
499.9	0.0	Laborer	\$25.00	\$37.50	\$12,497.50
60.0	0.0	Quality Control	\$64.50	\$96.75	\$3,870.00
12.0	0.0	Safety Manager	\$64.50	\$96.75	\$774.00
72.0	0.0	Estimator	\$51.00	\$76.50	\$3,672.00
					Subtotal \$126,105.60

Travel/Lodging/Parking Per-Diem for out-of-town field employees calculated \$15,503.67

Subtotal \$0.00
Subtotal \$15,503.67

Overhead & Profit: **15.0%** \$21,241.39

Subtotal Labor \$162,850.66

Material Breakdown	Item Description	Cost	Tax	Net
Pipe, Valve, Fittings, etc	CHWS&R, Plumbing Piping, Fittings	\$36,096.61	\$3,068.21	\$39,164.82
Equipment	HFCU's, Fixtures, Valves	\$6,177.66	\$525.10	\$6,702.76
Permits & Business License Expense	City of Charleston Fees Structure	\$1,225.00	\$0.00	\$1,225.00
Seismic	Chapman	\$395.00	\$33.58	\$428.58
				Subtotal \$47,521.16

State Sales Tax Rate: **8.50%**

Overhead & Profit: **15.0%** \$7,128.17

Subtotal Material & Equipment \$54,649.33

Subcontractor Breakdown	Scope Description	Cost		Total
Sheet metal	Knight & Wilson	\$26,463.00		\$26,463.00
Insulation (Piping & Sheetmetal)	3	\$23,000.00		\$23,000.00
Temperature Controls	Trane	\$816.00		\$816.00
Core Drilling	Nat Gas - 3 Fireplaces	\$1,320.00		\$1,320.00
				Subtotal \$51,599.00

Overhead & Profit: **15.0%** \$7,739.85

Subtotal Subcontractor Costs \$59,338.85

Total Cost \$276,838.84

Schedule Comments: Twenty Two (22) days of schedule extension are necessary as a result of this scope change, however we reserve the right to re-examine that impact at a later date and request appropriate time/cost compensation should the cumulative effect with other scope modifications warrant. No cost associated with the schedule extension is included in this proposal. It is assumed that incorporation of schedule modifications into the Master Schedule will be made and issued, at which point we will address any associated cost at that time.



October 25, 2017

Balfour Beatty Construction
 306 Meeting Street
 Suite 300
 Charleston, SC 29401

Re: Hotel Marion Square – MOD 5

The following itemization of changes reflect the Narrative accompanying MOD-5 issued by WLA May 13, 2016 and supplemented by additional notes by Bernhard MCC pertaining to the observed changes to the drawings.

MECHANICAL DRAWINGS:

- A. DRAWING M103 – 3RD FLOOR MECHANICAL PLAN
 - 1. Provided 12x6 duct and 22x6 SAR for VFCU-14 in guestroom C3.
 - 2. Relocated VFCU-15, VFCU-8, and associated ductwork, and grilles due to modification of IDF and electrical room.
 - 3. Added fire dampers to ductwork for VFCU-8.
 - 4. Added fire dampers to supply and return ductwork for HFCU-7
 - 5. Pricing for associated changes included in Knight & Wilson Proposal
- B. DRAWING M103A - 3RD FLOOR MECHANICAL CHILLED WATER PLAN
 - 1. Relocated VFCU-15, VFCU-8, and associated chilled water lines.
 - 2. No cost impact
- C. DRAWING M104 - 4TH FLOOR MECHANICAL PLAN
 - 1. Provided 12x6 duct and 22x6 SAR for VFCU-14 in guestroom C3.
 - 2. Relocated VFCU-17, VFCU-9, and associated ductwork, and grilles due to modification of IDF and electrical room.
 - 3. Added fire dampers to ductwork for VFCU-9.
 - 4. Added fire dampers to supply and return ductwork for HFCU-8.
 - 5. Ductwork for VFFU-14 for Guestroom C3 provided in Knight & Wilson Proposal
 - 6. Fire dampers for VFU and HFCU-8 included in Knight & Wilson Proposal.



- D. DRAWING M104A - 4TH FLOOR MECHANICAL CHILLED WATER PLAN
1. Relocated VFCU-17, VFCU-9, and associated chilled water lines.
 2. Narrative states VFCU's 9 & 17 are relocated, but no cost impact.
 3. Considerable change in pipe footage not noted in Narrative, but shown on drawing.
 4. Original M104A shows 5" and 4" Chilled Water supplying FCU's.
 5. MOD-5 drawing shows 5" Chilled Water pipe coming off the risers, then Two 3" loops throughout the floor serving the guestrooms.
 6. Coordination of this floor was underway, when MOD-5 came about and BMCC Detailer, Ryan Shepard, had to redraw and explain in meetings with BBC, Engineer and Owner's Representative why piping on original drawing would not work.
 7. This resulted re-drawing the piping on this floor with one 3" loop changing to 4".
 8. Shop Drawings were completed and released BMCC fabrication, however due to the additional piping and material needed BMCC incurred additional delivery charges for an additional load of fabrication.
- E. DRAWING M105 - 5TH FLOOR MECHANICAL PLAN
1. Provided 12x6 duct and 22x5 SAR for VFCU-14 in guestroom C3.
 2. Relocated VFCU-19, VFCU-10, and associated ductwork, and grilles due to modification of IDF and electrical room.
 3. Added fire dampers to ductwork for VFCU-10.
 4. Added fire dampers to supply and return ductwork for HFCU-9.
 5. Ductwork and changes to noted FCU's included in Knight & Wilson Proposal.
- F. DRAWING M105A - 5TH FLOOR MECHANICAL CHILLED WATER PLAN
1. Relocated VFCU-19, VFCU-10, and associated chilled water lines.
 2. Updated chilled water lines and riser at guestrooms B10 (519), B3 (521), and B9 (517).
 3. Relocated chilled water riser at guestroom A18 (503).
 4. Slight Changes to Chilled Water riser and VFCU-19 and VFCU-10 relocation included in pricing.
- G. DRAWING M106 - 6TH FLOOR MECHANICAL PLAN
1. Removed VFCU-3-7 from the Concierge room, and added HFCU-26, HFCU-27, and associated ductwork and grilles
 2. Added VFCU-33, and relocated VFCU-11, associated ductwork, and grilles due to modification/addition of IDF and electrical room.
 3. Added fire dampers to ductwork for VFCU-11.
 4. Relocated VFCU-14 in guestroom E1.



5. Relocated EF-42 and associated ductwork to relocated restroom, and relocated HFCU-10 due to relocation of restroom.
 6. Added (5) fire dampers and (2) access panels for HFCU-10 ductwork.
 7. Ductwork, dampers, access panels and changes to EF-42 included in Knight & Wilson Proposal.
 8. Credit for Five VFCU's (VFCU 3, 4, 5, 6 and 7).
 9. Add HFCU's 26 and 27 and VFCU-33 and associated piping.
- H. DRAWING M106A - 6TH FLOOR MECHANICAL CHILLED WATER PLAN
1. Added VFCU-33, relocated VFCU-11, and relocated associated chilled water lines.
 2. Added HFCU-26, HFCU-27, and updated chilled water lines and risers.
 3. Relocated VFCU-14, and associated chilled water lines
 4. Add HFCU's 26 and 27 and VFCU-33 and associated piping.
 5. Relocating of VFCU-11 and-14 no cost impact.
- I. DRAWING M107 - 7TH FLOOR MECHANICAL PLAN
1. Relocated VFCU-22, VFCU-12, and associated ductwork and grilles due to modification of IDF and electrical room.
 2. Added fire dampers to ductwork for VFCU-12.
 3. Added fire dampers to supply and return ductwork for HFCU-11.
 4. Relocated VFCU-15 in guestroom E1.
 5. Ductwork, dampers and grilles included in Knight & Wilson Proposal.
 6. Relocation of VFCU-15 No cost impact.
- J. DRAWING M107A - 7TH FLOOR MECHANICAL CHILLED WATER PLAN
1. Relocated VFCU-22, VFCU-12, and associated chilled water lines.
 2. Relocated VFCU-14, and associated chilled water lines.
 3. No cost impact related to relocating VFCU's.
- K. DRAWING M108A - 8TH FLOOR MECHANICAL CHILLED WATER PLAN
1. Relocated VFCU-24, VFCU-13, and associated chilled water lines.
 2. Relocated VFCU-14, and associated chilled water lines.
 3. No cost impact related to relocating VFCU's.
- L. DRAWING M409 - 8TH FLOOR MECHANICAL EXPANDED PLAN
1. Relocated VFCU-24, VFCU-13, and associated ductwork and grilles due to modification of IDF and electrical room.
 2. Added fire dampers to ductwork for VFCU-13.
 3. Added 8x3 exhaust ductwork for EF-42.
 4. Added fire damper to supply and return ductwork for HFCU-12.
 5. Ductwork, dampers and grilles included in Knight & Wilson Proposal.



- M. DRAWING M410 - 8TH FLOOR MECHANICAL EXPANDED PLAN
 - 1. Relocated VFCU-14 in guestroom E1.
 - 2. No cost impact related to relocating VFCU's.
- N. DRAWING M411 - ROOF TERRACE MECHANICAL EXPANDED PLAN
 - 1. Relocated 8x3 exhaust ductwork and 12x12 louver for EF-42.
 - 2. Ductwork included in Knight & Wilson Proposal.
- O. DRAWING M501 - MECHANICAL CONDENSATE & CHILLED WATER RISERS
 - 1. Added HFCU-26 and HFCU-27 to detail 6/M501 and updated condensate and chilled water lines sizes.
 - 2. Piping and duct changes captured on M106A (Item H above).
- P. DRAWING M501A - MECHANICAL CONDENSATE & CHILLED WATER RISERS
 - 1. Added VFCU-33 to detail 9/M501A and updated condensate and chilled water line sizes.
 - 2. Piping and duct changes captured on M106A (Item H above).
- Q. DRAWING M602 - MECHANICAL SCHEDULES
 - 1. Removed VFCU-3-7 from chilled water fan coil unit schedule.
 - 2. Added HFCU-26, HFCU-27, and VFCU-33 to chilled water fan coil unit schedule.
 - 3. Piping and duct changes captured on M106A (Item H above).

PLUMBING DRAWINGS

- A. DRAWING P100 - SUB-LEVEL PARKING PLUMBING PLAN
 - 1. Deleted natural gas pipe to lanterns.
 - 2. No additional changes noted.
- B. Drawing P103 – 3RD FLOOR PLUMBING PLAN
 - 1. Deleted 3" Sanitary from relocated bathroom on sixth floor.
 - 2. Revised domestic water piping at Linen/Storage 300H and adding pipe size information to Toilet 300J.
 - 3. Removed 3" sanitary.
 - 4. Replaced with 6" as revised during BIM Process.
 - 5. Rerouted 4" Domestic Cold Water Line.
 - 6. Offset 6" Domestic Hot Water.



- C. DRAWING P104 - 4TH FLOOR PLUMBING PLAN
 - 1. Deleted 3" sanitary from relocated bathroom on sixth floor.
 - 2. Removed 3" sanitary.
 - 3. Replaced with 6" as revised during BIM Process.

- D. DRAWING P105 - 5TH FLOOR PLUMBING PLAN
 - 1. Deleted 3" sanitary from relocated bathroom on sixth floor.
 - 2. Deleted natural gas piping to lanterns and added natural gas to fireplace at Manager's Apartment.
 - 3. Showed offset for 4" rain leader over guestroom 519.
 - 4. Included deduct and add for natural gas.
 - 5. Removed 3" sanitary.
 - 6. Replaced with 6" as revised during BIM Process.
 - 7. Offset of roof leader B10 / 519.

- E. DRAWING P106 - 6TH FLOOR PLUMBING PLAN
 - 1. Deleted sanitary piping from relocated bathroom on sixth floor.
Added natural gas stub out for fireplace at Manager's Apartment.
 - 2. Revised kitchen equipment layout for Concierge Dining/Food Prep.
 - 3. Showed offset for 4" rain leader over Concierge Dining.
 - 4. Added DWV piping and domestic hot & cold water piping for relocated bathroom.
 - 5. Bathroom and concierge changes included in pricing.

- F. DRAWING P107 - 7TH FLOOR PLUMBING PLAN
 - 1. Deleted vent from relocated bathroom on sixth floor.
 - 2. Added natural gas stub out for fireplace at Manager's Apartment.
 - 3. Added stub up for fireplace, deleted vent.

- G. DRAWING P108 - 8TH FLOOR PLUMBING PLAN
 - 1. Deleted vent from relocated bathroom on sixth floor.
 - 2. Added natural gas pipe for fireplace at Terrace Bar.
 - 3. Showed water piping up to TMV-3.
 - 4. Showed water piping up to foot rinse.
 - 5. Revised water piping at Linen Storage 800H.
 - 6. Included gas piping, included domestic water piping changes with foot bath and mixing valve.

- H. DRAWING P109 - ROOF TERRACE
 - 1. Showed natural gas stub out for fireplace.
 - 2. Provided tempered water for ST-3.
 - 3. Provided TMV-3 for ST-3.



4. Provided water for pool drinking fountain and added drainage and air admittance valve.
5. Provided hose bibb in Pool Equipment RT16.
6. Provided water for foot rinse at east entrance to pool deck.
7. Provided NFWH at east entrance to pool deck.
8. Provided hot & cold water distribution to Men RT18 & Women RT20 bathrooms.
9. Natural gas piping, domestic water piping for shower change, drinking fountain, roof hydrant, added bathroom and mixing valve included in pricing.

I. DRAWING P402A - EXPANDED FIRST FLOOR PLUMBING
PLAN - WASTE AND VENT

1. Added backwater valve in 10" storm drain at NW corner of building.
2. Included in pricing.

J. DRAWING P503 - GAS RISER

1. Deleted gas lanterns.
2. Added gas to Manager's Apartment.
3. Added gas for rooftop terrace bar fireplace.
4. Revised gas flows and pipe sizes for deleted/added gas equipment.
5. Natural gas changes incorporated in above plumbing drawings as noted.

OTHER		Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext	Fid Ext
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	SCH 40 BMT T&C-150#	BLK T&C PIPE - W/HGR	1/2"	150		'	101.68	13.6
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	SCH 40 BMT T&C-150#	BLK T&C PIPE- NO HGR	1/2"	81		'	54.75	7.3
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	SCH 40 BMT T&C-150#	90 ELBOW - 110I	1/2"	17		ea	16.87	11.4
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	SCH 40 BMT T&C-150#	TEE - 110S	1/2"	5		ea	6.02	4.4
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	SCH 40 BMT T&C-150#	T&C JOINTS	1/2"	54		ea	0.57	0.0
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	SCH 40 BMT T&C-150#	PIPE CUT	1/2"	33		ea	0.00	3.8
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	INSULATION - NO PRICE	NON INSULATED SYSTEM	1/2"	230		ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	INSULATION - NO PRICE	SURFACE AREA-P.C.	Unized	115		ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	HANGERS, RC, etc.	ALUM. BANDS-LBS.	Unized	0		ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	HANGERS, RC, etc.	CLIPS #B3100 MINSL.	1/2"	28		ea	15.67	7.5
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	28		ea	40.00	15.1
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P100 - P100	HANGERS, RC, etc.	INSERT	3/8"	28		ea	105.32	15.4
							P100 Add		0.00	0.0
							P100 Deduct		-340.89	-78.7
							P100 Total		-340.89	-78.7

OTHER	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext	Fid Ext
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	COPPER L HARD 95/5	JOINT	2"	23	ea	1.12	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	COP VIC L HARD-W/HR	4"	115	+	3,224.03	26.9
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	COP VIC L HARD-W/HR	6"	12	+	768.60	4.4
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	90 ELBOW - 610	6"	9	ea	1,266.84	19.5
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	90 ELBOW - 610	6"	5	ea	2,871.09	18.1
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	TEE - 620	4"	4	ea	776.25	10.8
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	TEE - 620	6"	3	ea	1,790.03	13.3
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	RED TEE GRVXGRV - 625	4"x2"	3	ea	680.00	6.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	CONC RED GRVXGRV 650	4"x3"	3	ea	267.03	4.2
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	CONC RED GRVXGRV 650	6"x4"	5	ea	1,628.06	14.2
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	JOINT	3"	3	ea	1.35	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	JOINT	4"	46	ea	33.40	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	COUPLING - 606	6"	22	ea	27.88	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	COUPLING - 606	3"	2	ea	57.50	0.3
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	COUPLING - 606	6"	46	ea	1,729.60	6.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	COUPLING - 606	6"	21	ea	1,782.85	4.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	COUPLING - 606	2"	23	ea	45.54	0.2
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	PIPE CUT	4"	16	ea	0.00	6.9
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	GROOVED COPPER	PIPE CUT	6"	2	ea	0.00	0.8
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	FLOOR/WALL SLEEVES	FLOOR 18 GA SM	4"	2	ea	13.03	1.5
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	5"	15	ea	51.69	5.7
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	7"	2	ea	17.16	0.9
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	5"	15	ea	145.56	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	HANGERS, RC, etc.	ZOGA. GALV SHIELD B3151	1/2"	15	ea	38.63	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	HANGERS, RC, etc.	HANGER ACCESSORIES	5/8"	2	ea	11.94	1.6
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	HANGERS, RC, etc.	HANGER ACCESSORIES	1/2"	15	ea	47.04	9.8
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	HANGERS, RC, etc.	INSERT	1/2"	15	ea	60.19	9.4
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 005: P103 - P103	HANGERS, RC, etc.	INSERT	5/8"	2	ea	9.26	2.4
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	COPPER L HARD 95/5	JOINT	2"	3	ea	1.58	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	COP VIC L HARD-W/HR	3"	58	+	924.76	9.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	COP VIC L HARD-W/HR	4"	40	+	1,069.54	8.4
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	90 ELBOW - 610	3"	3	ea	195.71	4.8
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	90 ELBOW - 610	3"	3	ea	450.28	6.5
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	TEE - 620	3"	1	ea	111.59	2.4
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	TEE - 620	4"	1	ea	245.25	3.2
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	RED TEE GRVXGRV - 625	3"x2"	2	ea	287.92	4.2
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	CONC RED GRVXGRV 650	3"x2"	1	ea	61.80	1.3
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	CONC RED GRVXGRV 650	4"x3"	2	ea	253.10	3.7
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	JOINT	3"	22	ea	12.08	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	JOINT	4"	15	ea	10.29	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	COUPLING - 606	3"	21	ea	504.13	2.2
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	COUPLING - 606	4"	15	ea	522.55	1.7
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	COUPLING - 606	2"	3	ea	64.75	0.3
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	PIPE CUT	3"	8	ea	0.00	2.5
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	GROOVED COPPER	PIPE CUT	4"	6	ea	0.00	2.2
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	FLOOR/WALL SLEEVES	FLOOR 18 GA SM	4"	1	ea	6.18	0.7
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	INSULATION - NO PRICE	1/2 THK PIPE COVER	3"	58	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	INSULATION - NO PRICE	1/2 THK PIPE COVER	4"	40	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	INSULATION - NO PRICE	SURFACE AREA-P.C.	Unsize	128	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	INSULATION - NO PRICE	ALUM. BANDS-LBS.	Unsize	0	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	4"	8	ea	18.76	2.6
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	5"	6	ea	18.85	1.9
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	4"	8	ea	67.54	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	5"	6	ea	53.06	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	8	ea	11.66	4.4
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	HANGERS, RC, etc.	HANGER ACCESSORIES	1/2"	6	ea	17.15	3.4
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	HANGERS, RC, etc.	INSERT	3/8"	8	ea	30.72	4.5
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	HANGERS, RC, etc.	INSERT	1/2"	6	ea	21.94	3.2
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	SCH 40-PVC-DWV CHARL	PCVDWY SOLID PIP-NO	3"	17	+	26.65	1.6
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	SCH 40-PVC-DWV CHARL	COUPLING - 100	3"	3	ea	0.75	0.2
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	SCH 40-PVC-DWV CHARL	PVC JOINTS	3"	1	ea	0.19	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	SCH 40-PVC-DWV CHARL	PVC PIPE CUT	3"	2	ea	0.00	0.6
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	INSULATION - NO PRICE	NON INSULATED SYSTEM	3"	17	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	INSULATION - NO PRICE	SURFACE AREA-P.C.	Unsize	21	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	INSULATION - NO PRICE	ALUM. BANDS-LBS.	Unsize	0	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 001: P103 - P103	HANGERS, RC, etc.	R-C BK STL PLAIN 3373	3"	1	ea	8.76	0.4
P103 Add 17,345.62 166.9									
P103 Deduct -4,997.52 -75.9									
P103 Total 12,348.10 91.0									

OTHER	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext	Fid Ext
OTHER 001: DEDUCT - DEDUCT Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 002: P104 - P104	SCH 40-PVC-DWV CHARL	PVC DWV SOLID PIP-NO	3"	17	'	26.65	1.6
OTHER 001: DEDUCT - DEDUCT Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 002: P104 - P104	SCH 40-PVC-DWV CHARL	COUPLING - 100	3"	0	ea	0.75	0.2
OTHER 001: DEDUCT - DEDUCT Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 002: P104 - P104	SCH 40-PVC-DWV CHARL	PVC JOINTS	3"	1	ea	0.19	0.0
OTHER 001: DEDUCT - DEDUCT Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 002: P104 - P104	SCH 40-PVC-DWV CHARL	PVC PIPE CUT	3"	2	ea	0.00	0.6
OTHER 001: DEDUCT - DEDUCT Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 002: P104 - P104	INSULATION-NO PRICE	NON INSULATED SYSTEM	3"	17	ca	0.00	0.0
OTHER 001: DEDUCT - DEDUCT Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 002: P104 - P104	INSULATION-NO PRICE	SURFACE AREA-P.C.	Unsize	21	ca	0.00	0.0
OTHER 001: DEDUCT - DEDUCT Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 002: P104 - P104	INSULATION-NO PRICE	ALUM. BANDS-LBS.	Unsize	0	ca	0.00	0.0
OTHER 001: DEDUCT - DEDUCT Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 002: P104 - P104	HANGERS, RC, etc.	R-C BK STL PLAIN 3373	3"	1	ca	8.76	0.4
								0.00	0.0
					P104 Add			-36.35	-2.8
					P104 Deduct			-36.35	-2.8
					P104 Total				

OTHER	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext	Est Ext
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	SCH 40 BMT T&C-150#	BLK T&C PIPE - W/HGR	1/2"	328		235.16	33.5
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	SCH 40 BMT T&C-150#	BLK T&C PIPE- NO HGR	1/2"	17		12.37	1.8
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	SCH 40 BMT T&C-150#	90 ELBOW - 1101	1/2"	15		15.43	11.1
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	SCH 40 BMT T&C-150#	T&C JOINTS	1/2"	2	ea	3.17	2.5
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	SCH 40 BMT T&C-150#	P&C PIPE CUT	1/2"	48	ea	0.53	0.0
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	SCH 40 BMT T&C-150#	P&C PIPE CUT	1/2"	49	ea	0.00	6.5
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	HANGERS, RC, etc.	CLEVIS #B3100 MIN/SL	1/2"	60	ea	35.83	18.3
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	60	ea	91.44	36.7
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	HANGERS, RC, etc.	INSERT	3/8"	60	ea	129.39	37.5
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 008: P105 - P105	THREADED VALVES	MIL PLUG VL SCREWED	1/2"	12		26.45	1.3
OTHER 001: ADD - ADD	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 008: P105 - P105	SCH 40-PVC-DWV CHAIR	PVC DWY SOLID PIP W/H	4"	1	ea	12.54	1.4
OTHER 001: ADD - ADD	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 008: P105 - P105	SCH 40-PVC-DWV CHAIR	L.S. 1/4 BEND - 304	4"	1	ea	9.83	1.4
OTHER 001: ADD - ADD	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 008: P105 - P105	SCH 40-PVC-DWV CHAIR	1/4 BEND - 300	4"	0	ea	0.93	0.3
OTHER 001: ADD - ADD	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 008: P105 - P105	SCH 40-PVC-DWV CHAIR	COUPLING - 100	4"	6	ea	1.27	0.0
OTHER 001: ADD - ADD	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 008: P105 - P105	SCH 40-PVC-DWV CHAIR	PVC JOINTS	4"	2	ea	0.00	0.6
OTHER 001: ADD - ADD	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 008: P105 - P105	SCH 40-PVC-DWV CHAIR	PVC PIPE CUT	4"	3	ea	8.49	1.3
OTHER 001: ADD - ADD	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 008: P105 - P105	HANGERS, RC, etc.	CLEVIS #B3100 MIN/SL	3/8"	3	ea	3.28	2.1
OTHER 001: ADD - ADD	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 008: P105 - P105	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	3	ea	13.89	2.2
OTHER 001: ADD - ADD	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 008: P105 - P105	HANGERS, RC, etc.	INSERT	3/8"	3	ea	406.68	54.4
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	SCH 40 BMT T&C-150#	BLK T&C PIPE - W/HGR	1/2"	598		35.99	24.4
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	SCH 40 BMT T&C-150#	90 ELBOW - 1101	1/2"	37		18.05	13.3
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	SCH 40 BMT T&C-150#	T&C JOINTS	1/2"	14	ea	1.34	0.0
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	SCH 40 BMT T&C-150#	P&C PIPE CUT	1/2"	129	ea	0.00	10.0
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	SCH 40 BMT T&C-150#	P&C PIPE CUT	1/2"	85	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	INSULATION - NO PRICE	NON INSULATED SYSTEM	1/2"	598	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	INSULATION - NO PRICE	SURFACE AREA-P.C.	Unized	299	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	INSULATION - NO PRICE	ALUM. BANDS-LBS.	Unized	1	ea	62.04	29.8
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	HANGERS, RC, etc.	CLEVIS #B3100 MIN/SL	1/2"	109	ea	158.33	59.7
OTHER 001: DEDUCT - DEDUCT	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 003: P105 - P105	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	109	ea	416.89	61.1
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 003: P105 - P105	SCH 40-PVC-DWV CHAIR	PVC DWY SOLID PIP-NO	3"	17		26.65	1.6
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 003: P105 - P105	SCH 40-PVC-DWV CHAIR	COUPLING - 100	3"	0	ea	0.75	0.2
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 003: P105 - P105	SCH 40-PVC-DWV CHAIR	PVC JOINTS	3"	1	ea	0.19	0.0
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 003: P105 - P105	SCH 40-PVC-DWV CHAIR	PVC PIPE CUT	3"	2	ea	0.00	0.6
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 003: P105 - P105	INSULATION - NO PRICE	NON INSULATED SYSTEM	3"	17	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 003: P105 - P105	INSULATION - NO PRICE	SURFACE AREA-P.C.	Unized	21	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 003: P105 - P105	INSULATION - NO PRICE	ALUM. BANDS-LBS.	Unized	0	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 003: P105 - P105	HANGERS, RC, etc.	R-CBK STD PLAIN 3375	3"	1	ea	8.76	0.4
							</		

OTHER		Section		PAGE		Category		Item Desc		Size	Qty	UOM	Mat Ext	Fid Ext
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		L-HARD TUBE - WHGR		1/2"	81		102.11	7.1
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		L-HARD TUBE - WHGR		3/4"	46		93.70	4.0
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		L-HARD TUBE - WHGR		1"	12		34.14	1.2
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		L-HARD TUBE - NO HGR		1/2"	12		14.58	1.0
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		L-HARD TUBE - NO HGR		1"	12		34.14	1.2
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		90 ELBOW CAC - 107C		1/2"	28	ea	10.20	16.1
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		90 ELBOW CAC - 107C		3/4"	2	ea	1.91	1.8
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		90 ELBOW CAC - 107C		1"	1	ea	2.33	1.1
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		COUPLING - 100		1/2"	3	ea	0.79	1.7
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		COUPLING - 100		3/4"	1	ea	0.81	1.1
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		COUPLING - 100		1"	1	ea	0.79	0.7
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		RED TEE BRANCH- 111		1" x1/2"	2	ea	10.84	2.6
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		CAPS - 117		1/2"	5	ea	1.24	1.5
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		CAPS - 117		1"	1	ea	1.37	0.6
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		JOINT		1/2"	68	ea	7.46	0.0
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		JOINT		3/4"	7	ea	1.29	0.0
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		JOINT		1"	10	ea	2.28	0.0
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		RPE CUT		1/2"	13	ea	0.00	1.7
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		RPE CUT		3/4"	7	ea	0.00	1.2
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		COPPER L HARD 95/5		PIPE CUT		1"	3	ea	0.00	0.7
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		SPECIALTIES - #1		STAX FIX		NO SIZE	5	spec	15.18	1.3
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		HANGERS, RC, etc.		CLEVIS #B3100 INSUL		1-1/2"	15	ea	12.39	4.6
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		HANGERS, RC, etc.		CLEVIS #B3100 INSUL		1-3/4"	9	ea	9.30	2.8
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		HANGERS, RC, etc.		CLEVIS #B3100 INSUL		2"	2	ea	2.32	0.7
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		HANGERS, RC, etc.		22GA. GALV SHIELD B3151		1-1/2"	15	ea	81.74	0.0
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		HANGERS, RC, etc.		22GA. GALV SHIELD B3151		1-3/4"	9	ea	50.30	0.0
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		HANGERS, RC, etc.		22GA. GALV SHIELD B3151		2"	2	ea	12.58	0.0
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		HANGERS, RC, etc.		HANGER ACCESSORIES		3/8"	26	ea	40.45	16.2
OTHER 001: ADD - ADD		Section 005: DW A/G - DOMESTIC WTR (L COPPER)		PAGE 010: P106 - P106		HANGERS, RC, etc.		INSERT		3/8"	26	ea	106.49	16.6
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		SCH 40 BMT T&C-150#		BLK T&C PIPE - WHGR		1/2"	122	ca	87.47	12.5
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		SCH 40 BMT T&C-150#		BLK T&C PIPE - NO HGR		1/2"	12	ca	8.26	1.2
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		SCH 40 BMT T&C-150#		90 ELBOW - 1101		1/2"	2	ca	2.37	1.7
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		SCH 40 BMT T&C-150#		NIPPLES		1/2"	9	ca	79.36	0.7
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		SCH 40 BMT T&C-150#		T&C JOINTS		1/2"	37	ca	0.40	0.0
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		SCH 40 BMT T&C-150#		RPE CUT		1/2"	19	ca	0.00	2.5
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		UNIONS/DIELECTRIC U		150# BLK-UNION #463		1/2"	2	ca	10.50	2.3
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		HANGERS, RC, etc.		CLEVIS #B3100 N/NSL		1/2"	23	ca	13.78	7.1
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		HANGERS, RC, etc.		R-C BK STL PLAIN 3373		1/2"	1	ca	5.28	0.5
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		HANGERS, RC, etc.		HANGER ACCESSORIES		3/8"	23	ca	35.17	14.1
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		HANGERS, RC, etc.		INSERT		3/8"	23	ca	92.60	14.4
OTHER 001: ADD - ADD		Section 008: NG A/G - NATURAL GAS (STEEL)		PAGE 010: P106 - P106		THREADED VALVES		MIL PLUG V1 SCREWED		1/2"	2	ca	258.77	1.9
OTHER 001: ADD - ADD		Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		PVC/DWV SOLID PIP W/H		4"	12	ca	26.45	1.3
OTHER 001: ADD - ADD		Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		L.S. 1/4 BEND - 304		4"	1	ca	12.54	1.4
OTHER 001: ADD - ADD		Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		1/4 BEND - 300		4"	1	ca	9.83	1.4
OTHER 001: ADD - ADD		Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		COUPLING - 100		4"	0	ca	0.93	0.3
OTHER 001: ADD - ADD		Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		PVC JOINTS		4"	6	ca	1.27	0.0
OTHER 001: ADD - ADD		Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 010: P106 - P106		HANGERS, RC, etc.		CLEVIS #B3100 N/NSL		4"	2	ca	0.00	0.6
OTHER 001: ADD - ADD		Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 010: P106 - P106		HANGERS, RC, etc.		CLEVIS #B3100 N/NSL		4"	3	ca	8.49	1.3
OTHER 001: ADD - ADD		Section 010: SD A/G - STORM DRAIN (SCH40 PVC)		PAGE 010: P106 - P106		HANGERS, RC, etc.		INSERT		3/8"	3	ca	5.28	2.1
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		COPPER DWV		MALE ADPT- 5804&304		1-1/2"	1	ca	7.04	0.7
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		COPPER DWV		JOINT		1-1/2"	2	ca	0.84	0.0
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		PVC/DWV SOLID PIP W/H		2"	92	ca	74.52	8.1
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		PVC/DWV SOLID PIP W/H		4"	35	ca	79.35	4.0
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		PVC/DWV SOLID PIP-NO		2"	35	ca	22.95	3.0
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		L.S. 1/4 BEND - 304		2"	5	ca	11.13	1.8
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		1/4 BEND - 300		2"	3	ca	5.08	1.4
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		1/8 BEND - 321		2"	5	ca	9.83	1.4
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		1/8 BEND - 321		4"	1	ca	6.05	1.7
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		COUPLING - 100		2"	3	ca	7.83	1.3
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		COUPLING - 100		4"	1	ca	1.68	1.1
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		COUPLING - 100		2"	1	ca	2.81	0.9
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		RED SAN TEE - 400		2"	1	ca	2.86	0.6
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		RED SAN TEE - 400		4"	1	ca	13.35	2.0
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		RED SAN TEE - 401		2" x1-1/2"	1	ca	2.52	0.6
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		WYE - 600		2"	1	ca	3.48	0.6
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		COMBINATION - 501		2"	3	ca	15.07	1.9
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		COMBINATION - 501		4"	1	ca	24.77	2.0
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		REDUCER - 102		4" x2"	1	ca	7.18	0.5
OTHER 001: ADD - ADD		Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)		PAGE 010: P106 - P106		SCH 40-PVC-DWV CHARL		P-TRAP - 706X		2"	5	ca	20.10	2.6

OTHER	Section	PAGE	Category	Item Desc.	Size	Qty	UOM	Mat Ext	Pid Ext
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	SCH 40-PVC-DWV CHARL	CLOSET FLANGE- 812	4"	1	ea	13.59	1.9
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	SCH 40-PVC-DWV CHARL	PVC JOINTS	1-1/2"	1	ea	0.09	0.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	SCH 40-PVC-DWV CHARL	PVC JOINTS	2"	62	ea	6.83	0.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	SCH 40-PVC-DWV CHARL	PVC JOINTS	4"	16	ea	3.54	0.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	SCH 40-PVC-DWV CHARL	PVC PIPE CUT	2"	18	ea	0.00	4.3
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	SCH 40-PVC-DWV CHARL	PVC PIPE CUT	4"	5	ea	0.00	1.7
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	SPECIALTIES - #1	DESANCO - #301-7	1-1/2"	1	ea	10.33	0.2
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	SPECIALTIES - #1	JOINTS-SOLDER	1-1/2"	1	ea	0.41	0.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	HANGERS, RC, etc.	CLEVIS #B3100 NINSL	2"	28	ea	27.50	8.5
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	HANGERS, RC, etc.	CLEVIS #B3100 NINSL	4"	10	ea	25.45	3.8
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 010: P106 - P106	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	38	ea	58.03	23.3
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 004: P106 - P106	HANGERS, RC, etc.	INSERT	3/8"	38	ea	152.79	23.8
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	PVC DWV SOLID PIP-NO	3"	17	ea	26.65	1.6
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	COUPLING - 100	3"	0	ea	0.75	0.2
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	PVC JOINTS	3"	1	ea	0.19	0.0
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	PVC PIPE CUT	3"	2	ea	0.00	0.6
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 004: P106 - P106	INSULATION - NO PRICE	NON INSULATED SYSTEM	3"	17	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 004: P106 - P106	INSULATION - NO PRICE	SURFACE AREA-P.C.	Unsize	21	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 010: SD A/G - STORM DRAIN (SCH40 PVC)	PAGE 004: P106 - P106	INSULATION - NO PRICE	ALUM. BANDS-LBS.	Unsize	0	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	HANGERS, RC, etc.	R-CBK STL PLAIN 3373	3"	1	ea	8.76	0.4
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	PVC DWV SOLID PIP W/H	2"	81	ea	61.80	6.3
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	L.S. 1/4 BEND - 304	2"	1	ea	2.64	0.4
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	1/8 BEND - 321	2"	3	ea	4.31	1.2
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	COUPLING - 100	2"	2	ea	1.01	0.6
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	WYE - 600	2"	5	ea	13.21	2.3
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	P-TRAP- 706X	2"	6	ea	23.82	2.8
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	PVC JOINTS	2"	39	ea	4.08	0.0
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	SCH 40-PVC-DWV CHARL	PVC PIPE CUT	2"	11	ea	0.00	2.4
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	INSULATION - NO PRICE	NON INSULATED SYSTEM	2"	81	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	INSULATION - NO PRICE	SURFACE AREA-P.C.	Unsize	74	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	INSULATION - NO PRICE	ALUM. BANDS-LBS.	Unsize	0	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	HANGERS, RC, etc.	CLEVIS #B3100 NINSL	2"	23	ea	22.04	6.3
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	23	ea	33.33	12.6
OTHER 001: DEDUCT - DEDUCT	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 004: P106 - P106	HANGERS, RC, etc.	INSERT	3/8"	23	ea	87.77	12.9
							P106 Add	1,945.77	260.2
							P106 Deduct	-290.35	-58.5
							P106 Total	1,655.41	201.7

[illegible]

OTHER	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext	Est Ext
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	L-HARD TUBE - W/HGR	1/2"	23	'	29.18	2.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	L-HARD TUBE - W/HGR	3/4"	12	'	23.43	
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	L-HARD TUBE - W/HGR	1-1/2"	46	'	250.77	5.4
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	L-HARD TUBE - W/HGR	2"	46	'	404.36	6.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	90 ELBOW CXC - 10TC	1/2"	5	ea	1.70	2.7
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	90 ELBOW CXC - 10TC	3/4"	2	ea	1.91	1.8
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	90 ELBOW CXC - 10TC	1-1/2"	2	ea	10.90	2.5
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	COUPLING - 100	2"	2	ea	19.87	2.9
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	COUPLING - 100	1/2"	1	ea	0.20	0.4
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	COUPLING - 100	3/4"	0	ea	0.20	0.3
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	COUPLING - 100	1-1/2"	1	ea	3.71	1.5
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	COUPLING - 100	2"	2	ea	6.20	1.8
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	TEE - 111	1-1/2"	2	ea	22.53	3.7
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	TEE - 111	2"	2	ea	35.13	4.2
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	RED TEE BRANCH- 111	1-1/4" x3/4"	1	ea	7.90	1.5
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	RED TEE BRANCH- 111	1-1/2" x3/4"	1	ea	13.27	1.7
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	RED TEE BRANCH- 111	2" x3/4"	1	ea	8.37	1.5
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	JOINT	1/2"	10	ea	1.14	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	JOINT	3/4"	9	ea	1.73	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	JOINT	1-1/4"	2	ea	0.68	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	JOINT	1-1/2"	16	ea	5.84	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	JOINT	1-1/2"	2	ea	7.80	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	PIPE CUT	1/2"	3	ea	0.00	0.4
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	PIPE CUT	3/4"	2	ea	0.00	0.3
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	PIPE CUT	1-1/2"	7	ea	0.00	1.7
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	COPPER L HARD 955	PIPE CUT	2"	7	ea	0.00	1.9
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	SPECIALTIES - #1	24"x24" ACCESS PANEL	NO SIZE	1	spec	83.95	0.1
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	1-1/2"	5	ea	3.62	1.4
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	1-3/4"	2	ea	2.32	0.7
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	2-1/2"	7	ea	11.34	2.3
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	3"	7	ea	14.09	2.4
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	1-1/2"	5	ea	25.15	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	2ZGA. GALV SHIELD B3151	1-3/4"	2	ea	12.58	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	2ZGA. GALV SHIELD B3151	2-1/2"	7	ea	49.76	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	2ZGA. GALV SHIELD B3151	3"	7	ea	49.76	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	21	ea	81.65	12.7
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	HANGERS, RC, etc.	INSERT	3/8"	21	ea	33.34	13.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	SWEAT VALVES	S38570 BALL N/INSUL	1/2"	1	ea	12.14	0.7
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	SWEAT VALVES	JOINTS-SOLDER	1/2"	2	ea	0.23	0.0
OTHER 001: ADD - ADD	Section 005: DW AG - DOMESTIC WTR (L COPPER)	PAGE 006: P108 - P108	SCH 40 BMT T&C-150#	BLK T&C PIPE - W/HGR	1/2"	69	'	49.51	7.1
OTHER 001: ADD - ADD	Section 008: NG AG - NATURAL GAS (STEEL)	PAGE 006: P108 - P108	SCH 40 BMT T&C-150#	BLK T&C PIPE- NO HOR	1/2"	12	'	8.26	1.2
OTHER 001: ADD - ADD	Section 008: NG AG - NATURAL GAS (STEEL)	PAGE 006: P108 - P108	SCH 40 BMT T&C-150#	90 ELBOW - 1101	1/2"	5	ea	4.75	3.4
OTHER 001: ADD - ADD	Section 008: NG AG - NATURAL GAS (STEEL)	PAGE 006: P108 - P108	SCH 40 BMT T&C-150#	TEE - 1105	1/2"	1	ea	1.59	1.2
OTHER 001: ADD - ADD	Section 008: NG AG - NATURAL GAS (STEEL)	PAGE 006: P108 - P108	SCH 40 BMT T&C-150#	T&C JOINTS	1/2"	16	ea	0.17	0.0
OTHER 001: ADD - ADD	Section 008: NG AG - NATURAL GAS (STEEL)	PAGE 006: P108 - P108	SCH 40 BMT T&C-150#	PIPE CUT	1/2"	11	ea	0.00	1.5
OTHER 001: ADD - ADD	Section 008: NG AG - NATURAL GAS (STEEL)	PAGE 006: P108 - P108	HANGERS, RC, etc.	CLEVIS #B3100 N/INSUL	1/2"	13	ea	7.58	3.9
OTHER 001: ADD - ADD	Section 008: NG AG - NATURAL GAS (STEEL)	PAGE 006: P108 - P108	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	13	ea	19.94	7.8
OTHER 001: ADD - ADD	Section 008: NG AG - NATURAL GAS (STEEL)	PAGE 006: P108 - P108	HANGERS, RC, etc.	INSERT	3/8"	13	ea	50.93	7.9
OTHER 001: DEDUCT - DEDUCT	Section 016: SD AG - STORM DRAIN (SCH40 PVC)	PAGE 006: P108 - P108	SCH 40-PVC-DWV CHARL	PVC DWV SOLID FIT-NO	3"	17	'	26.65	1.6
OTHER 001: DEDUCT - DEDUCT	Section 016: SD AG - STORM DRAIN (SCH40 PVC)	PAGE 006: P108 - P108	SCH 40-PVC-DWV CHARL	COUPLING - 100	3"	0	ea	0.75	0.2
OTHER 001: DEDUCT - DEDUCT	Section 016: SD AG - STORM DRAIN (SCH40 PVC)	PAGE 006: P108 - P108	SCH 40-PVC-DWV CHARL	PVC JOINTS	3"	1	ea	0.19	0.0
OTHER 001: DEDUCT - DEDUCT	Section 016: SD AG - STORM DRAIN (SCH40 PVC)	PAGE 006: P108 - P108	SCH 40-PVC-DWV CHARL	PVC PIPE CUT	3"	2	ea	0.00	0.6
OTHER 001: DEDUCT - DEDUCT	Section 016: SD AG - STORM DRAIN (SCH40 PVC)	PAGE 006: P108 - P108	INSULATION- NO PRICE	NON INSULATED SYSTEM	3"	17	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 016: SD AG - STORM DRAIN (SCH40 PVC)	PAGE 006: P108 - P108	INSULATION- NO PRICE	SURFACE AREA-P.C.	Unsize	21	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 016: SD AG - STORM DRAIN (SCH40 PVC)	PAGE 006: P108 - P108	INSULATION- NO PRICE	ALUM. BANDS-LBS.	Unsize	0	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 016: SD AG - STORM DRAIN (SCH40 PVC)	PAGE 006: P108 - P108	HANGERS, RC, etc.	R-C BK STL PLAIN 3573	3"	1	ea	8.76	0.4
			</						

OTHER	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext	Fid Ext
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	L-HARD TUBE - W/HGR	1/2"	92	'	116.69	8.1
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	L-HARD TUBE - W/HGR	3/4"	104	'	210.83	9.1
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	L-HARD TUBE - W/HGR	1"	92	'	273.18	9.4
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	L-HARD TUBE - W/HGR	1-1/2"	23	'	125.38	2.7
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	L-HARD TUBE - W/HGR	2"	12	'	101.10	1.5
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	L-HARD TUBE - NO HGR	1/2"	92	'	116.69	8.1
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	L-HARD TUBE - NO HGR	3/4"	69	'	93.70	4.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	L-HARD TUBE - NO HGR	1"	66	'	204.88	7.1
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	90 ELBOW CxC - 107C	1/2"	23	ea	8.50	13.4
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	90 ELBOW CxC - 107C	3/4"	23	ea	19.04	17.8
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	90 ELBOW CxC - 107C	1"	28	ea	56.11	25.4
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	90 ELBOW CxC - 107C	1-1/2"	1	ea	5.45	1.2
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	COUPLING - 100	1/2"	6	ea	1.59	3.3
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	COUPLING - 100	3/4"	5	ea	2.60	3.6
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	COUPLING - 100	1"	5	ea	5.59	4.6
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	COUPLING - 100	1-1/2"	1	ea	1.85	0.8
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	TEE - 111	2"	0	ea	1.55	0.4
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	TEE - 111	3/4"	3	ea	5.24	3.9
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	TEE - 111	1"	1	ea	5.41	1.5
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	TEE - 111	2"	1	ea	17.57	2.1
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	RED TEE BRANCH- 111	3/4" x1/2"	2	ea	3.36	2.3
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	RED TEE BRANCH- 111	1" x3/4"	1	ea	5.42	1.4
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	RED TEE BRANCH- 111	1-1/2" x3/4"	5	ea	33.53	6.1
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	REDUCED TEE - 3X - 111	3/4"	1	ea	2.06	1.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	ADAPTER CxM - 104	1/2"	1	ea	0.89	0.4
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	ADAPTER CxM - 104	3/4"	5	ea	5.96	1.9
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	ADAPTER CxM - 104	1"	1	ea	3.85	0.6
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	CAFS - 117	1"	7	ea	8.18	3.4
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	JOINT	1/2"	59	ea	6.45	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	JOINT	3/4"	90	ea	16.78	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	JOINT	1"	77	ea	16.95	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	JOINT	1-1/2"	13	ea	4.59	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	JOINT	2"	5	ea	2.23	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	PIPE CUT	1/2"	26	ea	0.00	3.5
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	PIPE CUT	3/4"	21	ea	0.00	3.9
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	PIPE CUT	1"	23	ea	0.00	4.8
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	PIPE CUT	1-1/2"	3	ea	0.00	0.9
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	PIPE CUT	2"	2	ea	0.00	0.5
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	COPPER L HARD 95/5	PIPE CUT	3/4"	3	ea	6.47	4.7
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	UNIONS/DIELECTRIC U	STAX FIX	NO SIZE	14	spec	45.54	4.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	1-1/2"	17	ea	14.29	5.3
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	1-3/4"	20	ea	19.76	6.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	2"	17	ea	17.43	5.3
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	2-1/2"	3	ea	5.67	1.2
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	3"	2	ea	4.69	0.8
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	1-1/2"	17	ea	94.32	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	1-3/4"	20	ea	106.90	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	2"	17	ea	94.32	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	2-1/2"	3	ea	24.89	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	3"	2	ea	16.58	0.0
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	60	ea	91.44	36.7
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	HANGERS, RC, etc.	INSERT	3/8"	60	ea	240.75	37.5
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	SWEAT VALVES	S585-70 BALL W/INSUL	3/4"	3	ea	59.32	2.8
OTHER 001: ADD - ADD	Section 005: DW A/G - DOMESTIC WTR (L COPPER)	PAGE 007: P109 - P109	SWEAT VALVES	JOINTS-SOLDER	3/4"	7	ea	1.14	0.0
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	SCH 40 BMI T&C-150#	BLK T&C PIPE - W/HGR	1/2"	12	'	8.26	1.2
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	SCH 40 BMI T&C-150#	BLK T&C PIPE- NO HGR	1/2"	12	'	8.26	1.2
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	SCH 40 BMI T&C-150#	90 ELBOW - 1101	1/2"	2	ea	2.37	1.7
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	SCH 40 BMI T&C-150#	NIPPLES	1/2"	5	ea	39.68	0.3
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	SCH 40 BMI T&C-150#	T&C JOINTS	1/2"	21	ea	0.23	0.0
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	SCH 40 BMI T&C-150#	PIPE CUT	1/2"	3	ea	0.00	0.4

OTHER	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext		Fid Ext
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	UNIONS/ELECTRIC U	150# BLK-UNION #463	1/2"	1	ea	5.24		1.1
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	HANGERS, RC, etc.	CLEVIS #B3100 N/INSL.	1/2"	2	ea	1.38		0.7
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	HANGERS, RC, etc.	R-C BK STL PLAIN 3373	1/2"	1	ea	5.28		0.5
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	2	ea	3.52		1.4
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	HANGERS, RC, etc.	INSERT	3/8"	2	ea	9.26		1.4
OTHER 001: ADD - ADD	Section 008: NG A/G - NATURAL GAS (STEEL)	PAGE 007: P109 - P109	THREADED VALVES	ML PLUG VL SCREWED	1/2"	1	ea	129.39		1.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	COPPER DWV	MALE ADPT- 5804&304	1-1/2"	1	ea	7.04		0.7
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	COPPER DWV	JOINT	1-1/2"	2	ea	0.84		0.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	PVC DWV SOLID PIP W/H	2"	23		18.63		2.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	L.S. 1/4 BEND - 304	2"	1	ea	2.78		0.5
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	1/8 BEND - 321	2"	1	ea	1.52		0.4
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	COUPLING - 100	2"	1	ea	0.31		0.2
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	RED SAN TEE - 401	2" x1-1/2"	1	ea	2.52		0.6
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	RED WYE - 601	4" x2"	1	ea	10.27		1.7
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	PVC JOINTS	1-1/2"	1	ea	0.09		0.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	PVC JOINTS	2"	9	ea	1.01		0.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	PVC JOINTS	4"	2	ea	0.51		0.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SCH 40-PVC-DWV CHARL	PVC PIPE CUT	2"	3	ea	0.00		0.8
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SPECIALTIES - #1	DESANCO - #301-7	1-1/2"	1	ea	10.33		0.2
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	SPECIALTIES - #1	JOINTS-SOLDER	1-1/2"	1	ea	0.41		0.0
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	HANGERS, RC, etc.	CLEVIS #B3100 N/INSL.	2"	7	ea	6.97		2.1
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	7	ea	10.55		4.2
OTHER 001: ADD - ADD	Section 012: W&V A/G - WASTE & VENT (SCH 40 PVC)	PAGE 007: P109 - P109	HANGERS, RC, etc.	INSERT	3/8"	7	ea	27.78		4.3
								2,641.14		291.6
								P109 Add		
								P109 Deduct	0.00	0.0
								P109 Total	2,641.14	291.6

OTHER	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat.Ext	Fid.Ext
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	L-HARD TUBE - WHGR	1"	60'		178.16	6.1
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	L-HARD TUBE - WHGR	1-1/4"	20'		84.42	2.3
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	L-HARD TUBE - WHGR	1-1/2"	200'		1,090.32	23.4
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	L-HARD TUBE - WHGR	2"	240'		2,109.74	31.5
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	90 ELBOW Cx-C - 107C	1"	6 ea		12.2	5.5
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	90 ELBOW Cx-C - 107C	1-1/4"	2 ea		6.08	2.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	COUPLING - 100	1"	186 ea		2.08	1.7
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	COUPLING - 100	1-1/4"	0.62 ea		1.22	0.6
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	COUPLING - 100	1-1/2"	6.2 ea		16.13	6.7
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	COUPLING - 100	2"	7.44 ea		32.34	9.2
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	RED TEE BRANCH- 111	2" x1"	2 ea		9.39	2.7
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	TEE - 111	2"	6 ea		71.37	9.2
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	JOINT	1"	27 ea		5.94	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	JOINT	1-1/4"	5 ea		1.49	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	JOINT	1-1/2"	3.63 ea		3.63	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	JOINT	2"	92 ea		44.53	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	PIPE CUT	1"	8.52 ea		0	1.8
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	PIPE CUT	1-1/4"	2.84 ea		0	0.7
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	PIPE CUT	1-1/2"	28.4 ea		0	7.5
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	COPPER L HARD 95/5	PIPE CUT	2"	34.08 ea		0	9.9
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	SMLS WELD PIPE-W/HGR	2-1/2"	40'		316	12.8
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	SMLS WELD PIPE-W/HGR	3"	340'		3,510.16	129.1
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	SMLS WELD PIPE-W/HGR	4"	340'		5,000.72	163.8
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	SMLS WELD PIPE-W/HGR	5"	40'		888.96	22.8
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	90 ELBOW - LR	2-1/2"	10 ea		120.62	53.9
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	90 ELBOW - LR	3"	17 ea		250.29	96.3
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	90 ELBOW - LR	4"	412.43		412.43	120.1
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	TEE	2-1/2"	6 ea		198.56	48.4
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	REDUCED TEE - BRANCH	2-1/2" x2"	2 ea		170.8	24.6
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	REDUCED TEE - BRANCH	3" x2"	6 ea		264.19	45.3
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	REDUCED TEE - BRANCH	4" x2"	14 ea		600.74	106.3
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	REDUCED TEE - BRANCH	5" x2"	20 ea		1,088.16	177.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	REDUCED TEE - BRANCH	5" x3"	6 ea		705.09	64.3
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	CONCENTRIC REDUCER	2-1/2" x2"	14 ea		265	67.7
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	CONCENTRIC REDUCER	3" x2"	8 ea		134.44	37.6
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	CONCENTRIC REDUCER	4" x2"	6 ea		147.16	31.4
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	CONCENTRIC REDUCER	5" x3"	3 ea		152.39	19.4
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	WELD JOINTS	2-1/2"	66 ea		193.84	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	WELD JOINTS	3"	96 ea		296.74	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	WELD JOINTS	4"	97 ea		373.45	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	WELD JOINTS	5"	23 ea		101.96	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	STEEL PIPE CUT	2-1/2"	5.68 ea		0	0.6
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	STEEL PIPE CUT	3"	48.28 ea		0	6.4
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	STEEL PIPE CUT	4"	48.28 ea		0	8.9
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	SMLS PIPE/WELD FTGS	STEEL PIPE CUT	5"	5.68 ea		0	1.2
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	1"	60 ea		0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	1-1/4"	20 ea		0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	1-1/2"	200 ea		0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	2"	240 ea		0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	2-1/2"	40 ea		0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	3"	340 ea		0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	4"	340 ea		0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	5"	40 ea		0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	INSULATION-NO PRICE	SURFACE AREA-P.C.	Unsize	2,137.20 ea		0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	CLEVIS #B3100 INSUL	4"	11 ea		27.04	4.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	CLEVIS #B3100 INSUL	5"	67 ea		231.69	25.4
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	CLEVIS #B3100 INSUL	6"	38 ea		172.79	15.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	CLEVIS #B3100 INSUL	7"	34 ea		253.71	13.9
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	CLEVIS #B3100 INSUL	8"	4 ea		29.85	1.6
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	22GA. GALV SHIELD B3151 4"	11 ea	97.37		0.0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	22GA. GALV SHIELD B3151 5"	67 ea	652.31		0.0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	22GA. GALV SHIELD B3151 6"	38 ea	558.45		0.0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	22GA. GALV SHIELD B3151 7"	34 ea	571.06		0.0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	22GA. GALV SHIELD B3151 8"	4 ea	82.69		0.0	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 001: M104A - M104A	HANGERS, RC etc.	HANGER ACCESSORIES	3/8"	11 ea		16.82	6.7

OTHER	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Est	Flt Est
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL/COPPER)	PAGE 001: M104A - M104A	HANGERS, RC, etc.	HANGER ACCESSORIES	1/2"	105 ea		330.33	69.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL/COPPER)	PAGE 001: M104A - M104A	HANGERS, RC, etc.	HANGER ACCESSORIES	5/8"	38 ea		197.3	26.6
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL/COPPER)	PAGE 001: M104A - M104A	HANGERS, RC, etc.	INSERT	3/8"	11 ea		44.29	6.9
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL/COPPER)	PAGE 001: M104A - M104A	HANGERS, RC, etc.	INSERT	1/2"	105 ea		422.73	65.9
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL/COPPER)	PAGE 001: M104A - M104A	HANGERS, RC, etc.	INSERT	5/8"	38 ea		152.99	38.8
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	COPPER L HARD 95/5	L-HARD TUBE - WHGR	2"	81		670.72	9.4
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	COPPER L HARD 95/5	COUPLING - 100	2"	2	ea	10.28	2.8
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	COPPER L HARD 95/5	RED TEE BRANCH- 111	2"x1"	5	ea	51.86	6.3
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	COPPER L HARD 95/5	JOINT	1"	5	ea	0.96	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	COPPER L HARD 95/5	JOINT	2"	37	ea	16.88	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	COPPER L HARD 95/5	PIPE CUT	2"	11	ea	0.00	3.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	SMLS WELD PIPE-WHGR	2-1/2"	138		1,033.32	39.5
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	SMLS WELD PIPE-WHGR	3"	138		1,350.38	46.6
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	SMLS WELD PIPE-WHGR	4"	161		2,244.44	69.1
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	SMLS WELD PIPE-WHGR	5"	138		2,906.90	70.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	90 ELBOW - LR	3"	2	ea	32.10	11.6
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	90 ELBOW - LR	4"	2	ea	52.89	14.5
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	90 ELBOW - LR	5"	2	ea	114.02	16.8
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	TEE	5"	5	ea	372.35	50.4
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	REDUCED TEE - BRANCH	2-1/2" x2"	12	ea	479.95	77.3
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	REDUCED TEE - BRANCH	3" x2"	7	ea	280.63	46.6
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	REDUCED TEE - BRANCH	4" x3"	9	ea	474.43	79.4
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	REDUCED TEE - BRANCH	5" x4"	9	ea	1,024.73	94.2
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	CONCENTRIC REDUCER	2-1/2" x2"	2	ea	41.27	9.9
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	CONCENTRIC REDUCER	3" x2"	2	ea	36.63	9.6
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	CONCENTRIC REDUCER	4" x3"	2	ea	43.79	12.5
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	CONCENTRIC REDUCER	5" x4"	2	ea	162.53	29.7
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	WELD JOINTS	2-1/2"	32	ea	89.64	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	WELD JOINTS	3"	39	ea	114.55	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	WELD JOINTS	4"	47	ea	172.06	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	WELD JOINTS	5"	48	ea	202.95	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	STEEL PIPE CUT	2-1/2"	20	ea	0.00	1.8
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	STEEL PIPE CUT	3"	20	ea	0.00	2.3
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	STEEL PIPE CUT	4"	23	ea	0.00	3.8
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	SMLS PIPE/WELD FTGS	STEEL PIPE CUT	5"	20	ea	0.00	3.7
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	2"	81	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	2-1/2"	138	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	3"	138	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	4"	161	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	INSULATION-NO PRICE	1-1/2 THK PIPE COVER	5"	138	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	INSULATION-NO PRICE	SURFACE AREA-P.C.	Unsize	1229	ea	0.00	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	5"	12	ea	37.69	3.9
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	6"	28	ea	118.97	9.7
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	7"	16	ea	113.85	5.9
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	8"	14	ea	97.60	5.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	5"	12	ea	106.12	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	6"	28	ea	384.44	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	7"	16	ea	256.30	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	22GA. GALV SHIELD B3151	8"	14	ea	270.39	0.0
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	HANGER ACCESSORIES	1/2"	39	ea	116.59	22.9
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	HANGER ACCESSORIES	5/8"	30	ea	147.14	18.7
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	INSERT	1/2"	39	ea	149.20	21.9
OTHER 001: DEDUCT - DEDUCT	Section 020: CHW A/G - CHILL WTR (STEEL/COPPER)	PAGE 008: M104A - M104A	HANGERS, RC, etc.	INSERT	5/8"	30	ea	114.10	27.2
									1632.8
									22,702.16
									-13,892.66
									-825.7
									8,809.50
									807.1
									M104A Add
									M104A Deduct
									M104A Total

OTHER	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext	Fid Ext
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	COPPER L HARD 95/5	L-HARD TUBE - W/HGR	3/4"	35	'	70.28	3.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	COPPER L HARD 95/5	L-HARD TUBE - NO HGR	3/4"	46	'	93.70	4.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	COPPER L HARD 95/5	90 ELBOW Cx-C - 107C	3/4"	9	ea	7.61	7.1
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	COPPER L HARD 95/5	COUPLING - 100	3/4"	2	ea	1.40	1.9
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	COPPER L HARD 95/5	TEE - 111	3/4"	2	ea	3.50	2.6
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	COPPER L HARD 95/5	JOINT	3/4"	30	ea	5.59	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	COPPER L HARD 95/5	PIPE CUT	3/4"	11	ea	0.00	2.1
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	FLOOR/WALL SLEEVES	FLOOR 18 GA SM	3/4"	2	ea	13.03	1.5
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	4"	7	ea	16.96	2.5
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	HANGERS, RC, etc.	22GA GALV SHIELD B3151	4"	7	ea	61.08	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	7	ea	10.55	4.2
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 002: M105A - M105A	HANGERS, RC, etc.	INSERT	3/8"	7	ea	27.78	4.3
				M105A Add				311.48	33.4
				M105A Deduct				0.00	0.0
				M105A Total				311.48	33.4

OTHER		Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext	Fid Ext
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	L-HARD TUBE - WHGR	1"	92	'	273.18	9.4
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	L-HARD TUBE - WHGR	1-1/4"	35	'	145.62	4.0
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	L-HARD TUBE - NO HGR	1-1/4"	46	'	194.17	5.4
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	90 ELBOW Cx-C - 107C	1"	18	ea	37.40	16.9
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	90 ELBOW Cx-C - 107C	1-1/4"	9	ea	27.98	9.4
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	COUPLING - 100	1"	3	ea	3.20	2.6
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	COUPLING - 100	1-1/4"	2	ea	4.91	2.6
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	RED TEE BRANCH- 111	1-1/4" x 1"	5	ea	31.59	6.4
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	REDUCED TEE - 3X - 111	1-1/4"	1	ea	10.37	1.6
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	JOINT	1"	46	ea	10.12	0.0
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	JOINT	1-1/4"	36	ea	10.59	0.0
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	PIPE CUT	1"	13	ea	0.00	2.8
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	PIPE CUT	1-1/4"	11	ea	13.03	2.7
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	FLOOR 18 GA SM	1-1/4"	2	ea	13.03	1.5
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	FLOOR/WALL SLEEVES	CLEVIS #B3100 INSUL	4"	17	ea	42.41	6.3
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	CLEVIS #B3100 INSUL	5"	6	ea	19.88	2.2
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	22GA GALV SHIELD B3151	4"	17	ea	152.70	0.0
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	22GA GALV SHIELD B3151	5"	6	ea	55.98	0.0
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	17	ea	26.38	10.6
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	HANGER ACCESSORIES	1/2"	6	ea	18.09	3.8
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	INSERT	3/8"	17	ea	69.45	10.8
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	INSERT	1/2"	6	ea	23.15	3.6
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	L-HARD TUBE - WHGR	1"	92	'	273.18	9.4
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	L-HARD TUBE - NO HGR	1"	17	'	51.22	1.8
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	90 ELBOW Cx-C - 107C	1"	12	ea	23.38	10.6
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	COUPLING - 100	1"	3	ea	3.80	3.1
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	TEE - 111	1"	2	ea	10.80	3.1
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	JOINT	1"	36	ea	7.84	0.0
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	PIPE CUT	1"	16	ea	0.00	3.3
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	COPPER L HARD 95/5	CLEVIS #B3100 INSUL	2"	17	ea	17.43	5.3
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	22GA GALV SHIELD B3151	2"	17	ea	94.32	0.0
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	17	ea	26.38	10.6
OTHER 001: ADD - ADD		Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 003: M106A - M106A	HANGERS, RC, etc.	INSERT	3/8"	17	ea	69.45	10.8
M106A Add									1,748.02	160.6
M106A Deduct									0.00	0.0
M106A Total									1,748.02	160.6

OTHER									
OTHER 001: ADD - ADD	Section	PAGE	Category	Item Desc	Size	Qty	UOM	Mat Ext	Fid Ext
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	COPPER L HARD 95/5	90 ELBOW Cx-C - 107C	3/4"	7	ea	5.72	5.3
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	COPPER L HARD 95/5	COUPLING - 100	3/4"	1	ea	0.40	0.6
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	COPPER L HARD 95/5	RED TEE BRANCH- 111	1-1/4" x3/4"	2	ea	15.79	3.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	COPPER L HARD 95/5	JOINT	3/4"	17	ea	3.23	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	COPPER L HARD 95/5	JOINT	1-1/4"	5	ea	1.37	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	COPPER L HARD 95/5	PIPE CUT	3/4"	3	ea	0.00	0.6
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	HANGERS, RC, etc.	CLAVIS #B3100 INSUL	4"	5	ea	11.30	1.7
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	HANGERS, RC, etc.	22GA GALV SHIELD B3151	4"	5	ea	40.72	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	HANGERS, RC, etc.	HANGER ACCESSORIES	3/8"	5	ea	7.04	2.8
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	HANGERS, RC, etc.	INSERT	3/8"	5	ea	18.52	2.9
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	SWEAT VALVES	SS85-70 BALL NINSUL	3/4"	2	ea	39.54	1.8
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A	SWEAT VALVES	JOINTS-SOLDER	3/4"	5	ea	0.76	0.0
OTHER 001: ADD - ADD	Section 020: CHW A/G - CHILL WTR (A53 STEEL /COPPER)	PAGE 004: M501A - M501A		Subtotal					
				M501A Add				144.38	18.8
				M501A Deduct				0.00	0.0
				M501A Total				144.38	18.8
Freight for Prefabricated Assemblies									
Consumables & Fuel									
Tool Rental									
Clean Up Labor									
OTHER 001: ADD - ADD								1,685.00	
OTHER 001: ADD - ADD								1,980.50	
OTHER 001: ADD - ADD								3,924.00	
OTHER 001: ADD - ADD									103.6
OTHER 001: ADD - ADD								36,096.61	1,657.5

Bernhard MCC, LLC
 8350248 - Marion Square
Labor Calculations

Clean Up

Total field labor for Change Order	1,657.50	
Crew		
Foreman	2	
Journeyman	4	
Laborer	2	
Total	8	
Hours per day	8	
	64	
Days per Week	5	
Total Hours per Week	320	
		Weeks to complete
Total Labor	1,657.50	5.2 Change Order
Hours Per Week	320	
Weeks to Complete Change Order	5.2	
Days Per Week	5	
Days to Complete Change Order	25.9	
Weeks to Complete		
Change Order	5.2	
# hours per Week	20	
Total Clean Up Hours	103.6	

Travel Lodging / Per Diem

Per Diem - Journeyman / Laborer	
# Men	4
Per Diem \$	\$ 20.00
Daily Total	\$ 80.00
# Days	25.9
Weekly Total	\$ 2,071.88

Per Diem - PM / Superintendent / Foreman	
# Men	3
Per Diem \$	\$ 86.00
Daily Total	\$ 258.00
# Days	25.9
Weekly Total	\$ 6,681.80

Quality Control	
Visits	1.5
Cost	\$ 1,500.00 \$ 2,250.00

Safety Manager	
Visits	1.5
Cost	\$ 3,000.00 \$ 4,500.00

Per Diem Total for Change Order	\$ 15,503.67
--	---------------------

Bernhard MCC, LLC
 8350248 - Marion Square
Material By Drawing

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

Drawing	Add	Deduct	
M104A	\$ 22,702.16	\$ (13,892.66)	
M105A	\$ 311.48		
M106A	\$ 1,748.02		
M501A	\$ 144.38		
P100		\$ (340.89)	
P103	\$ 17,345.63	\$ (4,997.52)	
P104		\$ (36.35)	
P105	\$ 842.75	\$ (1,135.68)	
P106	\$ 1,945.77	\$ (290.35)	
P107	\$ 212.85	\$ (36.35)	
P108	\$ 1,379.08	\$ (36.35)	
P109	\$ 2,641.14		
	\$ 49,273.26	\$ (20,766.15)	
	Net Add	\$ 49,273.26	
	Net Deduct	<u>\$ (20,766.15)</u>	
Material Per Take Off			\$ 28,507.11
Freight for Prebriacated Assemblies		\$ 1,685.00	
Consumables & Fuel		\$ 1,980.50	
Tool Rental		<u>\$ 3,924.00</u>	
Net Material Cost			\$ 36,096.61

[illegible]

Eric Stoehr

From: Avery.Harbour@Ferguson.com
Sent: Friday, July 15, 2016 3:32 PM
To: Eric Stoehr
Cc: Scott.Windsor@Ferguson.com; Craig Weaver
Subject: RE: The Hotel at Marion Square MOD 5

Here you go. Thank you.

Price Quotation # B510382

FERGUSON ENTERPRISES INC #23

4711 RIVERS AVE
N CHARLESTON, SC 29405-6645

Phone : 843-747-6301
Fax : 843-554-8799

Bid No.....: B510382

Bid Date...: 07/13/16

Quoted By: AJH

Customer.: MCC MECHANICAL LLC
 MARION SQUARE HOTEL
 3001 17TH STREET
 METAIRIE, LA 70002

Cust Phone: 504-846-5223

Terms.....: NET 10TH PROX

Ship To.....: MCC MECHANICAL LLC
 MARION SQUARE HOTEL
 3001 17TH STREET
 METAIRIE, LA 70002

Cust PO#...: P109

Job Name.: MARION SQUARE HOTEL

Item	Description	Quantity	Net Price	UM	Total
S696G2001XF	LF DBL LAV 3/8 F1807 *OXBOX L/ARRST	4	24.037	EA	96.15
S696SC1	OUT BX FRM INS W/ ACC OPG	4	4.683	EA	18.73
S5609QT04BP	3/4X4 NF HYD W/VB	2	140.990	EA	281.98
L270LF	LF TSTAT MIX VLV 1/2 BRZ 125# *Z	1	141.230	EA	141.23
WHY7256	6 NF HYD WALL W/ NB BX	1	181.170	EA	181.17
PFAAV20	20 DFU AAV W/ 1-1/2-2 PVC ADPT	1	19.113	EA	19.11
S654C	LF 1 WTR HAMM ARRST - C	3	35.857	EA	107.57
SP-M565SM	OUTDOOR SHWOWER	1	2620.000	EA	2620.00
EEDFPB114C	LF WHL CHR FTN COMP	1	1291.030	EA	1291.03
ELKFRB1	BX FR	1	514.170	EA	514.17
SP-OFSFS-200	32 FREE STANDING FOOT SHOWER	1	1096.430	EA	1096.43

Subtotal: \$6367.57

Inbound Freight: \$0.00

Tax: \$541.23

R - 1689



Proposal

(Valid for 30 days from Proposal date)

Page 28 of 41

PROPRIETARY AND CONFIDENTIAL PROPERTY OF Trane U.S. Inc.

DISTRIBUTION TO OTHER THAN THE NAMED RECIPIENT IS PROHIBITED

© 2016 Trane All rights reserved

Prepared For:
MCC Mechanical
Attn: Craig Weaver

Date: July 13, 2016

Proposal Number: F1-119912-5

Job Name:
The Hotel at Marion Square

Engineer:
Library & Associates

Bid Date: August 31, 2015

Delivery Terms:
Freight Allowed and Prepaid - F.O.B. Factory

Payment Terms:
Net 30 Days

Trane U.S. Inc. is pleased to provide the following proposal for your review and approval.

ADD Fan Coils Tagged HFCU-26, HFCU-27:

Fan Coil
Horizontal recessed
4 Chilled Water cooling only, 5.0 kw electric heat
Closed cell insulation with Microban antimicrobial product

With piping deluxe piping package

Stainless Steel Drain pan

Non-fused disconnect switch
1" MERV 8 filter (2 SETS)
2 way, 2 position, normally closed cooling control valve

Deluxe ball valves (supply & return) with Auto flow valve

Conventional Thermostat Interface ONLY

Condensate overflow detection
1st year parts only warranty

NOT INCLUDED: Controls (controller, thermostats, etc.), External Isolators, Smoke Detectors, Commissioning Support or Warranties beyond what shown above.

Notes/Clarifications:

1. All work associated with INNCOM system is excluding in its entirety.
2. Special Paint Colors beyond standard Trane color selection
3. Trane takes exception to requirement for Johns Manville Micromat. Trane standard closed cell insulation provided.

ADD Fan Coils Tagged VFCU-33 and DELETE Fan Coils Tagged VFCU-4,5,6 & 7

18 gauge cabinet designed for furred-in applications
1/2" cabinet liner, acrylic coated glass fiber
Flush mounted return air/access panel with 1/4 turn fasteners
Unit mounted double deflection steel supply air grilles
2 pipe change over chilled/hot water coils

Stainless steel pitched drain pan

Drain pan overflow switch
Ball type shut off valves
Nexus Stainless steel braided hose kit

Nexus automatic balancing valve and shut off valve
 Nexus strainer with blow down
 277/60/1
 PSC motor
 Non-fused disconnect switch
 2 way/2 position normally closed control valve
 1" disposable filter
 1st year parts only warranty

NOT INCLUDED:

- ✓ Remote mounted grilles, Duct plenum, flanges, collars, extensions (std knockout/opening provided for ducted connection)
- ✓ Thermostat or any controls
- ✓ Risers
- ✓ UL Fire rated chase- not supplying risers
- ✓ External Isolators
- ✓ Smoke Detectors
- ✓ Commissioning Support
- ✓ Warranties beyond what shown above.

Notes/Clarifications:

1. Units are 86" tall. Rooms indicated to be 106" tall. If grilles to be to the top of the room recommend ducting off the top to the desired height.
2. NC sound levels are a factor of installation that cannot be confirmed by the fan coil manufacturer. Sound power data is available upon request for analysis.
3. Exception is taken to note 6 requiring specifically Micromat by Johns Marville. The proposed fan coil does use a product by Johns Marville, but not specifically Micromat. Information can be provided upon request.

Tag Data – Trane Controls

Item	Tag(s)	Qty
B1	No Tag	1

Trane U.S. Inc BAS department proposes to provide and install a fully functional control system at the above referenced facility. We will provide all necessary labor and materials to engineer, program, checkout, test, and warranty this system and provide training for the system operators.

VFCU-33 (Qty: 1)

- Install and wire thermostat provided with unit.

Scope to exclude the following:

- Firefighters smoke station and all associated material shall be provided by others
- Motor Starters associated with the HVAC emergency shutdown/Fire alarm
- Wiring and control of all Guest room WSHPS
- Wiring and control of electric/gas unit heaters (integral tstats)
- Stairwell pressurization fans shall be by the electrical (DIV 16) contractor.
- Wiring and control of any life saving devices
- Smoke control systems
- Increased wages per Davis Bacon Act not included
- 3RD PARTY OR LEED COMMISSIONING
- Performance bonds.
- Power wiring of any mechanical equipment.
- Overtime is not included.
- Cutting, patching or painting.
- Fire dampers, fire/smoke dampers, isolation dampers.
- Startup of any mechanical equipment.
- Warranty work outside of normal business hours.
- Testing & balancing of the HVAC system.

➤ Any controls, equipment or services not quoted above.

Scope based on drawings dated 05-13-2016

All plenum installations, if applicable to the project, shall use plenum rated materials and shall comply with the requirements of NFPA, NEC, and Building Codes.

Equipment Change Order:

Total Net Price (Excluding Sales Tax)\$ 379.00 DELETE

Controls Change Order:

Total Net Price (Excluding Sales Tax)\$ 816.00 ADD

Sincerely,

Matthew Deitz - Trane U.S. Inc.

4501 South Tryon Street

Charlotte, NC 28217-0969

Phone: (704) 525-9600

Fax: (704) 525-8582

This proposal is subject to your acceptance of the attached Trane terms and conditions.

TERMS AND CONDITIONS – COMMERCIAL INSTALLATION

"Company" shall mean Trane U.S. Inc..

1. **Acceptance; Agreement.** These terms and conditions are an integral part of Company's offer and form the basis of any agreement (the "Agreement") resulting from Company's proposal (the "Proposal") for the commercial goods and/or services described (the "Work"). **COMPANY'S TERMS AND CONDITIONS ARE SUBJECT TO PERIODIC CHANGE OR AMENDMENT.** The Proposal is subject to acceptance in writing by the party to whom this offer is made or an authorized agent ("Customer") delivered to Company within 30 days from the date of the Proposal. If Customer accepts the Proposal by placing an order, without the addition of any other terms and conditions of sale or any other modification, Customer's order shall be deemed acceptance of the Proposal subject to Company's terms and conditions. If Customer's order is expressly conditioned upon Company's acceptance or assent to terms and/or conditions other than those expressed herein, return of such order by Company with Company's terms and conditions attached or referenced serves as Company's notice of objection to Customer's terms and as Company's counter-offer to provide Work in accordance with the Proposal and the Company terms and conditions. If Customer does not reject or object in writing to Company within 10 days, Company's counter-offer will be deemed accepted. Customer's acceptance of the Work by Company will in any event constitute an acceptance by Customer of Company's terms and conditions. This Agreement is subject to credit approval by Company. Upon disapproval of credit, Company may delay or suspend performance or, at its option, renegotiate prices and/or terms and conditions with Customer. If Company and Customer are unable to agree on such revisions, this Agreement shall be cancelled without any liability, other than Customer's obligation to pay for Work rendered by Company to the date of cancellation.

2. **Pricing and Taxes.** Unless otherwise noted, the price in the Proposal includes standard ground transportation and, if required by law, all sales, consumer, use and similar taxes legally enacted as of the date hereof for equipment and material installed by Company. Tax exemption is contingent upon Customer furnishing appropriate certificates evidencing Customer's tax exempt status. Company shall charge Customer additional costs for bonds agreed to be provided. Equipment sold on an uninstalled basis and any taxable labor/labour do not include sales tax and taxes will be added. Following acceptance without addition of any other terms and condition of sale or any other modification by Customer, the prices stated are firm provided that notification of release for immediate production and shipment is received at the factory not later than 3 months from order receipt. If such release is received later than 3 months from order receipt date, prices will be increased a straight 1% (not compounded) for each one-month period (or part thereof) beyond the 3 month firm price period up to the date of receipt of such release. If such release is not received within 6 months after date of order receipt, the prices are subject to renegotiation, or at Company's option, the order will be cancelled. Any delay in shipment caused by Customer's actions will subject prices to increase equal to the percentage increase in list prices during that period of delay and Company may charge Customer with incurred storage fees.

3. **Exclusions from Work.** Company's obligation is limited to the Work as defined and does not include any modifications to the Work site under the Americans With Disabilities Act or any other law or building code(s). In no event shall Company be required to perform work Company reasonably believes is outside of the defined Work without a written change order signed by Customer and Company.

4. **Performance.** Company shall perform the Work in accordance with industry standards generally applicable in the area under similar circumstances as of the time Company performs the Work. Company may refuse to perform any Work where working conditions could endanger property or put at risk the safety of persons. Unless otherwise agreed to by Customer and Company, at Customer's expense and before the Work begins, Customer will provide any necessary access platforms, catwalks to safely perform the Work in compliance with OSHA or state industrial safety regulations.

5. **Payment.** Customer shall pay Company's invoices within net 30 days of invoice date. Company may invoice Customer for all equipment or material furnished, whether delivered to the installation site or to an off-site storage facility and for all Work performed on-site or off-site. No retention shall be withheld from any payments except as expressly agreed in writing by Company, in which case retention shall be reduced per the contract documents and released no later than the date of substantial completion. Under no circumstances shall any retention be withheld for the equipment portion of the order. If payment is not received as required, Company may suspend performance and the time for completion shall be extended for a reasonable period of time not less than the period of suspension. Customer shall be liable to Company for all reasonable shutdown, standby and start-up costs as a result of the suspension. Company reserves the right to add to any account outstanding for more than 30 days a service charge equal to 1.5% of the principal amount due at the end of each month. Customer shall pay all costs (including attorneys' fees) incurred by Company in attempting to collect amounts due and otherwise enforcing these terms and conditions. If requested, Company will provide appropriate lien waivers upon receipt of payment. Customer agrees that, unless Customer makes payment in advance, Company will have a purchase money security interest in all equipment from Company to secure payment in full of all amounts due Company and its order for the equipment, together with these terms and conditions, form a security agreement. Customer shall keep the equipment free of all taxes and encumbrances, shall not remove the equipment from its original installation point and shall not assign or transfer any interest in the equipment until all payments due Company have been made.

6. **Time for Completion.** Except to the extent otherwise expressly agreed in writing signed by an authorized representative of Company, all dates provided by Company or its representatives for commencement, progress or completion are estimates only. While Company shall use commercially reasonable efforts to meet such estimated dates, Company shall not be responsible for any damages for its failure to do so.

7. **Access.** Company and its subcontractors shall be provided access to the Work site during regular business hours, or such other hours as may be requested by Company and acceptable to the Work site' owner or tenant for the performance of the Work, including sufficient areas for staging, mobilization, and storage. Company's access to correct any emergency condition shall not be restricted. Customer grants to Company the right to remotely connect (via phone modem, internet or other agreed upon means) to Customer's building automation system (BAS) and/or HVAC equipment to view, extract, or otherwise collect and retain data from the BAS, HVAC equipment, or other building systems, and to diagnose and remotely make repairs at Customer's request.

8. **Completion.** Notwithstanding any other term or condition herein, when Company informs Customer that the Work has been completed, Customer shall inspect the Work in the presence of Company's representative, and Customer shall either (a) accept the Work in its entirety in writing, or (b) accept the Work in part and specifically identify, in writing, any exception items. Customer agrees to re-inspect any and all excepted items as soon as Company informs Customer that all such excepted items have been completed. The initial acceptance inspection shall take place within ten (10) days from the date when Company informs Customer that the Work has been completed. Any subsequent re-inspection of excepted items shall take place within five (5) days from the date when Company informs Customer that the excepted items have been completed. Customer's failure to cooperate and complete any of said inspections within the required time limits shall constitute complete acceptance of the Work as of ten (10) days from date when Company informs Customer that the Work, or the excepted items, if applicable, has/have been completed.

9. **Permits and Governmental Fees.** Company shall secure (with Customer's assistance) and pay for building and other permits and governmental fees, licenses, and inspections necessary for proper performance and completion of the Work which are legally required when bids from Company's subcontractors are received, negotiations thereon concluded, or the effective date of a relevant Change Order, whichever is later. Customer is responsible for necessary approvals, easements, assessments and charges for construction, use or occupancy of permanent structures or for permanent changes to existing facilities. If the cost of such permits, fees, licenses and inspections are not included in the Proposal, Company will invoice Customer for such costs.

10. **Utilities During Construction.** Customer shall provide without charge to Company all water, heat, and utilities required for performance of the Work.

11. **Concealed or Unknown Conditions.** In the performance of the Work, if Company encounters conditions at the Work site that are (i) subsurface or otherwise concealed physical conditions that differ materially from those indicated on drawings expressly incorporated herein or (ii) unknown physical conditions of an unusual nature that differ materially from those conditions ordinarily found to exist and generally recognized as inherent in construction activities of the type and character as the Work, Company shall notify Customer of such conditions promptly, prior to significantly disturbing same. If such conditions differ materially and cause an increase in Company's cost of, or time required for, performance of any part of the Work, Company shall be entitled to, and Customer shall consent by Change Order to, an equitable adjustment in the Contract Price, contract time, or both.

12. **Pre-Existing Conditions.** Company is not liable for any claims, damages, losses, or expenses, arising from or related to conditions that existed in, on, or upon the Work site before the Commencement Date of this Agreement ("Pre-Existing Conditions"), including, without limitation, damages, losses, or expenses involving Pre-Existing Conditions of building envelope issues, mechanical issues, plumbing issues, and/or indoor air quality issues involving mold/mould and/or fungi. Company also is not liable for any claims, damages, losses, or expenses, arising from or related to work done by or services provided by individuals or entities that are not employed by or hired by Company.

13. **Asbestos and Hazardous Materials.** Company's Work and other services in connection with this Agreement expressly excludes any identification, abatement, cleanup, control, disposal, removal or other work connected with asbestos, polychlorinated biphenyl ("PCB"), or other hazardous materials (hereinafter, collectively, "Hazardous Materials"). Customer warrants and represents that, except as set forth in a writing signed by Company, there are no Hazardous Materials on the Work site that will in any way affect Company's Work and Customer has disclosed to Company the existence and location of any Hazardous Materials in all areas within which Company will be performing the Work. Should Company become aware of or suspect the presence of Hazardous Materials, Company may immediately stop work in the affected area and shall notify Customer. Customer will be exclusively responsible for taking any and all action necessary to correct the condition in accordance with all applicable laws and regulations. Customer shall be exclusively responsible for and, to the fullest extent permitted by law, shall indemnify and hold harmless Company (including its employees, agents and subcontractors) from and against any loss, claim, liability, fees, penalties, injury (including death) or liability of any nature, and the payment thereof arising out of or relating to any Hazardous Materials on or about the Work site, not brought onto the Work site by Company. Company shall be required to resume performance of the Work in the affected area only in the absence of Hazardous Materials or when the affected area has been rendered harmless. In no event shall Company be obligated to transport or handle Hazardous Materials, provide any notices to any governmental agency, or examine the Work site for the presence of Hazardous Materials.

14. **Force Majeure.** Company's duty to perform under this Agreement is contingent upon the non-occurrence of an Event of Force Majeure. If Company shall be unable to carry out any material obligation under this Agreement due to an Event of Force Majeure, this Agreement shall at Company's election (i) remain in effect but Company's obligations shall be suspended until the uncontrollable event terminates or (ii) be terminated upon 10 days notice to Customer, in which event Customer shall pay Company for all parts of the Work furnished to the date of termination. An "Event of Force Majeure" shall mean any cause or event beyond the control of Company. Without limiting



10801 Johnston Rd.
Suite 210
Charlotte, NC 28226
704-543-9140

QUOTATION

PROJECT: The Hotel at Marion Square LOCATION: Charleston, SC QUOTE TO: Bernhard MCC, LLC - CLT ATTENTION: Eric Stoechr QUOTE #: 41-3951(O)	BID DATE: 10/08/2015 ARCHITECT: ENGINEER: PLAN DATE: REVISION#:
---	--

We understand seismic requirements can be confusing. Our team has spent the last 20 years studying and applying the codes and standards, completing over 7,500 projects.

We have prepared this quotation to address only those items required by the specifications and building code to remove confusion and give you peace of mind.

NOTES:

1. Per plans and specifications this project is a seismic design category 'D'.
2. Seismic Calculations will determine anchors required for restraining equipment and/or roof curbs. We will not certify seismic worthiness of equipment and/or roof curbs provided by others.
3. We do not include seismic restraints for registers, grills, or diffusers.
4. We do not include sound or vibration testing.
5. This quote does not include a job site inspection by a licensed professional engineer. If required, it will be an additional charge of \$150 per hour.
6. A PE stamp is provided on all our seismic submittals.
7. Anchor bolts, hanger rods, and rod stiffeners by others. The size and location of restraints will be engineered based on as built pipe or duct drawings with hanger locations shown.

ITEM I HVAC- SEISMIC AND/OR VIBRATION ISOLATION

- Misc. Seismic Materials

YOUR TOTAL NET PRICE IS

\$395.00

For your seismic needs we will provide an engineering package, ship the materials, and support your field personnel. Rely on our expertise to avoid confusion and eliminate the hassle. Don't let this small area of your project bog you down. Allow us to address your seismic and vibration isolation needs.

The above price is F.O.B. factory, full freight allowed to the jobsite. The price does not include state sales tax. This quotation is subject to our standard terms and conditions and is good for 30 days, provided materials are released to production within 6 months of this quote.

SUBMITTED BY: dpallesen@chapmancompany.com	DATED: 5/5/2017	THRU ADDENDUM: - 0 -
--	-----------------	----------------------

R - 1694

**Plaintiff Balfour Beatty's
Trial Exhibit # 12**
(part 3 of 11)



KNIGHT & WILSON, INC.

www.knightwilson.com

1240 WILLIAMS ST.

MEMPHIS, TENNESSEE 38104

(901) 274-6978

Date: 7/14/2016

TO: BernhardMCC
ATTN: Eric Stoehr
RE: Hotel at Marion Square

Price to fabricate and install added duct and grills per MOD 5 drawings.
Grills priced as standard grills, not decorative grills.

Price...\$26,463.00

Thank you

*Jerry Petefish
Regional Project Manager
Knight and Wilson, Inc*

7/15/2016

R - 1697

GUY M. BEATY, INC.

INDUSTRIAL & COMMERCIAL INSULATION CONTRACTORS

9209 FORSYTH PARK DR.
CHARLOTTE, NC 28273

PHONE 704.583.1936
FAX 704.583.1940

July 15, 2016

To: Craig Weaver
MCC Mechanical

From: Tracy Huffstetler
Guy M. Beaty, Inc.

RE: The Hotel at Marion Square (Mod #5)
Charleston, SC

Craig,

We at Guy M Beaty, Inc. are pleased to submit our quotation to you for the above referenced project.

SCOPE OF WORK per our conversation:

HVAC: Changes associated with Mod #5 \$ 20,250.00

PLBG: Changes Associated with Mod #5 \$ 2,750.00

Exceptions: Insulation removal, Misc. Painting, Sleeves, Fire stopping, Plenum or Duct Lining, Pipe Identification, refrigerant piping, heat trace, underground piping, repairing or replacing existing insulation, Valve Tagging, ADA handicap covers, chiller insulation, Mechanical Joint (VIC) Piping, composite cleaning, painting or Color Code.

I want to thank you for the opportunity to quote you on this project. Please don't hesitate to contact me if you have any questions or need additional information.

Sincerely,
Tracy Huffstetler
Estimator/Project Mgr.

P.S. Prices on this proposal are good for 90 days from the date of this proposal.

MCC MECHANICAL

\$3,119

DATE	DESCRIPTION	AMOUNT	BALANCE
12/01/2023	DEPOSIT	\$1,200.00	\$1,200.00
12/05/2023	PAYROLL	\$500.00	\$700.00
12/10/2023	RENT	\$300.00	\$400.00
12/15/2023	UTILITIES	\$100.00	\$300.00
12/20/2023	SALES	\$800.00	\$1,100.00
12/25/2023	EXPENSES	\$200.00	\$900.00
12/30/2023	TOTAL	\$2,750.00	\$2,750.00

DIV 23 - HVAC:

DIV 23 - HVAC:		MCC MECHANICAL	
			\$40,500
EQUIPMENT COST:			
Relocate	Modify VPTAC changes		\$0
Relocate	Relocate cabana fans	LS	\$0
Relocate	Relocate VFCU-15 & VFCU-8, VFCU-17 & VFCU-9 VFCU-19 & VFCU-10, VFCU-11, VFCU-14, VFCU-22, VFCU-12, VFCU-24, VFCU-13	EA	\$0
Delete	Remove VFCU-3-7	EA	\$0
Add	Add HFCU-26 & HFCU-27, HFCU-10	EA	\$0
Add	Add VFCU-33	EA	\$0
Relocate	Relocate EF-42	EA	\$0
Relocate	Relocate EF-42	EA	\$0
PIPING OST:			
Add	Modify chiller lines and riser	1.0 LS	\$17,065.00
Relocate	Relocate chilled water riser	LS	\$17,065
DUCTWORK, SUPPLIES, GRILLES, DIFFUSERS, OTHERS COST:			
Add	Add ductwork	1.0 LS	\$540.00
Add	Add SAR	LS	\$0
Add	Access panels	EA	\$0
MISCELLANEOUS COST:			
Add	Parking, permit, seismic, field office, drawing, copies	1.0 LS	\$0
Add	Travel & lodging	1.0 LS	\$0
Add	Purchasing, quality control, consumables	1.0 LS	\$0
Add	Equipment rental	1.0 LS	\$0
Add	BIM changes	1.0 LS	\$0
SUB FEES:			
Add	Overhead	10%	\$17,605.00
Add	Profit	5%	\$17,693.03
Total			\$20,250



Concrete Sawing, Drilling, Scanning, and Breaking

PROPOSAL AND AGREEMENT

Created Date	10/9/2017	Quote Number	00055973
Name	Michael Schneida	Expire Date	11/8/2017
Account Name	MCC MECHANICAL	Phone	(504) 833-8291
Quote Name	MCC-MarionSquare-CD/Scan21	Email	mschneida@bernhardmcc.com
Prepared By	Shawn Conners	Address	3170 B Stanton Court
Phone	(843) 767-1881		North Charleston, South Carolina 29418
Mobile	(843) 708-9332		United States
Email	sconners@penhall.com		

Thank you for the opportunity to submit this proposal for your consideration. Listed below is a scope of work outlining what is included in the quoted price. Please contact me with any questions.

SCOPE OF WORK

GPR Scan for (3) 1" cores in 8" PT slab.

Core Drill (3) 1" cores in 8" PT slab.

- Customer responsible for layout of each location.
- Night & weekend work add 25%.

Proposal Price \$1,320.00

Standby Charges \$125.00

Per Hour

Minimum Charge \$550.00

Penhall recommends GPR concrete scanning and utility locating on all jobs. Please reach out to request more information or discuss pricing and availability.

EXCLUSIONS

- * Protection of surrounding areas including walls, floors, finishes, furniture, fixtures and equipment
- * Detailed cleaning, except vacuuming slurry and removal of concrete (if included in proposal)
- * Covering of holes and openings





Concrete Sawing, Drilling, Scanning, and Breaking

PROPOSAL AND AGREEMENT

- * Night, weekend, and holiday work
- * Layout, access, protecting public from harms way, shoring and bracing, traffic control and barricades, and locating, cutting, capping, and protection of utilities
- * Patching and painting of adjacent surfaces
- * Permits and inspections
- * Removal of any hazardous materials or generated debris
- * Temporary lighting and power
- * Testing of any hazardous materials
- * Utility location and protection
- * Bonds, retainage and liquidated damages

CONDITIONS

- * Proposal is provided based on information provided by Customer prior to a site visit by Penhall Company.
- * Customer understands that Penhall Company may need to revise the Scope of Work and/or Proposal Price based on actual site conditions.
- * Penhall Company shall not be bound by the Scope of Work and Proposal Price set forth herein unless and until a site visit has been performed and site conditions have been evaluated by Penhall Company.
- * Proposal is based on conditions described herein. Additional charges will apply with change of conditions.
- * Proposal based on using gas or diesel powered equipment.
- * One mobilization is included. Additional mobilizations will incur additional charges.
- * Proposal is based on over cuts being left in remaining concrete.
- * Standby or delays caused by others will be charged at an applicable hourly rate.
- * Quantities are estimated. Invoicing is based on actual field measured quantities.
- * Not responsible for any water damage that may occur.
- * Live utilities clearly marked and made safe by others.
- * Any subsequent contract will be on AIA doc.401(1997 Edition), AGC doc.640 or will have Penhall Company contract addendum attached.

The Proposal Price is based upon the Scope of Work, Conditions, and Exclusions listed above. Please read this entire Proposal carefully. Changes to the Scope of Work or Conditions may result in additional charges. The foregoing is a limited estimate only based on the information provided which does not account for a number of factors that could significantly impact this limited offer, including but not limited to an investigation of the site and conditions under which the work is to be performed neither of which may have been done prior to the communication of this limited offer. This is not an offer nor is it a guarantee and should not be relied upon for any purpose. Penhall expressly reserves the right to change this limited estimate as further information becomes available to it prior to the commencement of work or the execution of a contract or purchase order. The Proposal Price does not include sales tax, use tax, excise tax, business tax, or other similar taxes or duties. Customer shall pay all such taxes in addition to the Proposal Price, or, alternatively, shall provide Penhall with acceptable proof of tax exemption. Customer understands and agrees that Penhall's Standard Terms and Conditions (which are available on Penhall's website (www.penhall.com/us/standard-terms-conditions) or by request) are incorporated by reference into this Proposal and shall apply, in addition to the terms of this Proposal, to all transactions between Customer and Penhall related to this Proposal. Upon acceptance of this Proposal by Customer (indicated by Customer's authorized signature below), this Proposal, including the Standard Terms and Conditions incorporated by reference, represents the entire agreement between Penhall and Customer, and supersedes any prior negotiations, representations, or agreements, either written or oral. Payment is due upon receipt or 1% Net 15 days. Any billed amount that remains unpaid after 30 days from invoice date, could be subject to 1 1/2% per month.(18% annual percentage rate). Scanning services do not claim to be equivalent to an x-ray and no promise is made or implied that it represents anything other than a guide as to the location of buried or embedded objects within or below the survey material. Due to the physical aspects of the ground penetrating radar equipment and the various limitations attributed to the technology use, the results can vary depending on several factors. Due to these significant limitations in the equipment and the associated technology, results may be rendered inconclusive. Customer, its representative, and/or owner are aware that the information produced by scanning services is only to be used as a guide and customer accepts these limitations.

Accepted By: _____

Title: _____





Concrete Sawing, Drilling, Scanning, and Breaking

PROPOSAL AND AGREEMENT

Name: _____

Date: _____

Tab No. 118

Balfour Beatty Construction

June 6, 2017

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 118
RFI 451 Added Valves at Guestroom Manifolds

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 118 in the amount of Twenty-one thousand thirty-six (\$21,036.56) to provide additional work in accordance with the following qualifications:


The approved and ordered tub fillers and wall mount faucets do not have integral stops, per code contractor will have to add a shut off valve to the domestic water risers in the guestroom bathrooms. Pricing does not include access panels as they are already included at guestroom closets.

This change adds scope and time plumbing rough in durations, we reserve our right to analyze the schedule impact.

This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Nick Starcevic
Project Manager

cc:
Jennifer Faulkinberry
Taylor Walker
Jim Clements
Marty Wall
David Stanton
Tim Spano
Alec Dooley

RCO # 118 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 118± RFI 451 Added Valves at Guestroom Manifolds

The additional work for the **RFI 451 Added Valves at Guestroom Manifolds** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.51500000.40	RFI 0451 Plumbing Manifold Type	\$20,064.00

Total Items \$20,064.00

Total Markups \$972.56

RCO Total \$21,036.56

The total Cost to perform the work as described above is an ADD of Twenty-one thousand thirty-six (\$21,036.56).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 118



BERNHARD MCC, L.L.C.

2-9-17

Balfour Beatty Construction
306 Meeting St. /Suite 300
Charleston, SC 29401

Attn: Nicholas Starcevic/Tim Spano

REF: The Hotel at Marion Square
BBC Contract Number: 13026000
BMCC Project Number: 8350248

SUBJ: BMCC PCO No: 047
BBC RFI 0451 Plumbing Manifold Type/Added Valves

Gentlemen,

Bernhard MCC has received changes as defined in RFI 0451 Plumbing Manifold Type/Added Valves, and we have confirmed that our scope of work is impacted compared to contract drawings. The attached proposal collectively defines the impact identified in this issuance of this RFI.

The total costs are \$ 20,064.12

This PCO pricing is inclusive of the following:

- Pex ball valves
- Pex rings

The following clarifications and exclusions apply to this proposal:

1. The cost of this proposal includes only those direct costs for changes which are clearly identified (clouded) on the revised documents. If changes were made but not notated as such, we have not accounted for them and any such costs would be recovered at the point such are identified.
2. This proposal does not include any overtime or provisions for extended general conditions. If any such costs are required, we reserve the right to recover same.
3. Scope quoted herein aligns with the scope defined in our original subcontract and therefore all exclusions, clarifications, etc. apply equally to this proposal.
4. Scanning, X-raying and or concrete coring is excluded.
5. Architectural access door(s)

If you have any questions, please contact us as soon as possible. This proposal remains in effect for 30 days.

Sincerely,

Bernhard MCC, L.L.C.

Eric Stoehr
Project Manager

ES/SD
Attachment



MCC Mechanical of the Carolinas, LLC

Proposed Change Summary

Project: The Hotel at Marion Square
Location: Charleston, SC

Date: February 9, 2017

MCC Job No: 8350248
MCC PCO#: 47

Description: Added shutoff valves to domestic water per RFI 0451

Labor Breakdown

Std Hrs	Prem Hrs		Std Rate	Prem Rate	
0.0	0.0	Project Manager	\$80.00	\$120.00	\$0.00
0.0	0.0	Superintendent	\$75.00	\$112.50	\$0.00
6.5	0.0	Foreman	\$51.00	\$76.50	\$332.52
50.0	0.0	Journeyman	\$37.00	\$55.50	\$1,850.00
0.0	0.0	Start-up Technician	\$88.00	\$132.00	\$0.00
0.0	0.0	BIM Coordinator	\$70.00	\$105.00	\$0.00
0.0	0.0	Detailer	\$53.00	\$79.50	\$0.00
100.0	0.0	Laborer	\$23.00	\$34.50	\$2,300.00
0.0	0.0	Helper	\$19.00	\$28.50	\$0.00
0.0	0.0	Field Engineer	\$51.00	\$76.50	\$0.00
1.0	0.0	Safety	\$64.50	\$96.75	\$64.50
2.0	0.0	Clean Up	\$19.00	\$28.50	\$38.00
1.0	0.0	Estimator	\$51.00	\$76.50	\$51.00

Subtotal \$4,636.02

Field Office / Drawings / Copies

\$0.00

Travel & Lodging

\$0.00

Purchasing

5.0%

\$231.80

Small Tools

3.5%

\$162.26

Tool Rental

2.5%

\$115.90

Quality Control

4.5%

\$208.62

Consumables

2.0%

\$92.72

Subtotal \$811.30

Overhead & Profit: 15.0% \$817.10

Subtotal Labor \$5,453.12

Material Breakdown	Item Description	Cost	Tax	Net
PVF Materials	See attached Ferguson quote	\$11,709.88	\$995.34	\$12,705.22
Hardware		\$0.00	\$0.00	\$0.00
Equipment rental		\$0.00	\$0.00	\$0.00
Parking		\$0.00	\$0.00	\$0.00
Permits		\$0.00	\$0.00	\$0.00
Seismic		\$0.00	\$0.00	\$0.00
X-Ray/Core Drill	EXCLUDED T&M BASIS ONLY	\$0.00	\$0.00	\$0.00
Total Materials				\$12,705.22

Tax Rate: 8.50% \$995.34

Overhead & Profit: 15.0% \$1,905.78

Subtotal Material & Equipment \$14,611.00

Subcontract Breakdown	Item Description	Cost		Total
Sheet metal	Knight & Wilson	\$0.00		\$0.00
Insulation	Guy M. Beatty	\$0.00		\$0.00
Temperature Controls	Trane/ECS	\$0.00		\$0.00
Test & Balance (BY OTHERS)		\$0.00		\$0.00
Fire Caulk	AAA Firestop	\$0.00		\$0.00
Med Gas		\$0.00		\$0.00
Locate Services		\$0.00		\$0.00
BIM Coordinator		\$0.00		\$0.00
Subtotal				\$0.00

Overhead & Profit: 15.0% \$0.00

Subtotal Subcontractor Costs \$0.00

Total Cost \$20,064.12

Schedule Comments: Ten (10) days schedule extension requested for this change, however, we reserve the right to examine the impact of this change on the overall schedule at a later date, and request appropriate time or cost compensation should the accumulative effect of this or other changes warrant.

MARION SQUARE 2-6-17

Section

Section 005: DW A/G - DOMESTIC WTR AG PEX

Section 005: DW A/G - DOMESTIC WTR AG PEX

Section 005: DW A/G - DOMESTIC WTR AG PEX

Category	Size	Item Desc	Qty	UOM	Mat Ext	Fld Ext
PEX	1"	PEX VALVE	364	ea	12,022.92	54.6
PEX	1"	PEX COUPLINGS RING	728	ea	271.91	101.92
		Subtotal			12294.83	156.52
		GRAND TOTAL			12294.83	156.52



USE FERGUSON
QUOTE



USE
LABOR
FACTOR



1708 ELM HILL PIKE
NASHVILLE, TN 37210-3708

Please contact with Questions: 615-316-1800

INVOICE NUMBER	CUSTOMER	PAGE
6215155	182017	1 of 2

PLEASE REFER TO INVOICE NUMBER WHEN
MAKING PAYMENT AND REMIT TO:

FERGUSON ENTERPRISES INC #20
PO BOX 100286
ATLANTA, GA 30384-0286

SHIP TO:

MCC MECHANICAL - FAB SHOP
21180 JOHNSON ROAD
LONG BEACH, MS 39560

BERNHARD MCC LLC
FAB SHOP
PO BOX 7460
METAIRIE, LA 70010

SHIP WHSE.	SELL WHSE.	TAX CODE	CUSTOMER ORDER NUMBER	SALESMAN	JOB NAME	INVOICE DATE	BATCH
1717	1717	MSONLY	8350248358	MBS	MARION SQUARE	11/03/16	IO 218019

ORDERED	SHIPPED	ITEM NUMBER	DESCRIPTION	UNIT PRICE	UM	AMOUNT
			TAG: 8350248 SO# 2349			

31.35
x 182
11,411.40

46	46	ULFC4821010	LF 1X1 PEX BRS COMM FP BV	31.350	EA	1442.10
----	----	-------------	---------------------------	--------	----	---------

328	328	UQ4691000	1 PROPEX RNG W/ ST	0.410	EA	134.48
-----	-----	-----------	--------------------	-------	----	--------

.41
x 728
298.48
+ 11,411.40
11,709.88

TERMS: 2% 10TH NET 30TH

ORIGINAL INVOICE

TOTAL DUE

CONTINUED

All past due amounts are subject to a service charge of 1.5% per month, or the maximum allowed by law, if lower. If Buyer fails to pay within terms, then in addition to other remedies, Buyer agrees to pay Seller all costs of collection, including reasonable attorney fees. Complete terms and conditions are available upon request or at http://wolseley.com/terms_conditionsSale.html and are incorporated by reference. Seller may convert checks to ACH.

R-1711

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108



Request For Information

Project [13026000] - Hotel at Marion Square **Date** 4/22/2016

Balfour Beatty Construction, LLC
306 Meeting Street, Ste. 300
Charleston, SC 29401

RFI No. 0451

Primary Responder	Jennifer Faulkinberry Winford Lindsay Architect 344 West Pike Street Lawrenceville, GA 30046 Phone: 770-407-5786 Fax: 770-407-5817	Date	4/22/2016
		Status	Closed
CC From	Brandon Denney Balfour Beatty Construction, LLC	Resolved Date	
		Reason for Request	Insufficient
		Action Requested	Clarification
		Probable Cost Effect	T.B.D.
		Probable Time Effect	T.B.D.
		Priority	Medium
		Response Due	4/29/2016

Subject Plumbing Manifold Type

Drawing No.

Detail No./Paragraph

CSI Code

Schedule Activity ID

Information Requested

Please advise what type manifold is intended to be used for the domestic water distribution system to the rooms? Per code requirements you must provide valves on the manifolds, indicators of the fixture being served on the manifold and access to the manifold.

Question Revision (8/25/16) - After reviewing the guest room fixtures package, it has been determined that the tub filler and wall mount faucets do not have integral stops. By code, contractor will have to add a shut off valve to the domestic water risers feeding the guest room bathrooms. Access panels will have to be added in order to reach these valves. Please confirm that this is acceptable.

Recommendation

Posted to Drawings

Subcontractor Name

Subcontractor's RFI#

Response Information

Responder	Date	Response
Jennifer Faulkinberry	8/26/2016	This is acceptable.

Disclaimer

The Architect/Engineer and/or Owner has issued the attached information in response to the referenced RFI. Should this result in a change of the Scope of your Work, please provide detailed pricing analysis and schedule impact within seven (7) calendar days of receipt of this letter. Failure to submit timely information will constitute a waiver of your right to a change order for the work and may result in the incorporation of the changed work into your subcontract at no cost.

Jennifer Faulkinberry (Winford Lindsay Architect) 8/26/2016

Authorized Signature

Printed Name

Date

Supporting documents and attached files

This RFI has the following supporting documents and attached files:

Description	Date	Open as
 File Director: RFI-0451 Code table.pdf 48KB	4/22/2016	 
 File Director: RFI-0451 P502 - WATER RISERS.pdf 1095KB	4/22/2016	 

 Attached file
 Supporting document
Distribution

Recipient	Company	Method	Date
Alec Dooley	Balfour Beatty Construction, LLC	Email: adooley@balfourbeattyus.com	8/25/2016
Brandon Denney	Balfour Beatty Construction, LLC	Email: bdenney@balfourbeattyus.com	8/25/2016
Dan Ricci	Balfour Beatty Construction, LLC	Email: dricci@balfourbeattyus.com	8/25/2016
Jennifer Faulkinberry	Winford Lindsay Architect	Email: jfaulkinberry@lpbatlanta.com	8/25/2016
Jim Clements	Matrix Program Management Services	Email: jclements@matrixse.com	8/25/2016
John Eldridge	Balfour Beatty Construction, LLC	Email: jeldridge@balfourbeattyus.com	8/25/2016
Kim Brown	Library Associates, LLC	Email: kbrown@bennetthospitality.com	8/25/2016
Marc Cerino	S&ME, Inc	Email: MCerino@smeinc.com	8/25/2016
Marty Dale	Balfour Beatty Construction, LLC	Email: mdale@balfourbeattyus.com	8/25/2016
Nick Starcevic	Balfour Beatty Construction, LLC	Email: nstarcevic@balfourbeattyus.com	8/25/2016
Ryan Ledford	Balfour Beatty Construction, LLC	Email: Rledford@balfourbeattyus.com	8/25/2016
Stephanie Grainger Brown	Bennett Hospitality	Email: stephanie@bennetthospitality.com	4/22/2016
Tim Spano	Balfour Beatty Construction, LLC	Email: timspano@balfourbeattyus.com	8/25/2016

Dooley, Alec

From: Jennifer Faulkinberry <JFaulkinberry@lpbatlanta.com>
Sent: Friday, August 26, 2016 11:34 AM
To: Dooley, Alec; Denney, Brandon; Ricci, Daniel; jclements@matrixse.com; Eldridge, Johnny; kbrown@bennetthospitality.com; MCerino@smeinc.com; Dale, Marty; Starcevic, Nicholas; Ledford, Ryan; Spano, Tim
Cc: Taylor Walker
Subject: RE: Hotel at Marion Square - RFI:0451 - Plumbing Manifold Type
Attachments: RFI-0451.0-Plumbing_Manifold_Type.htm; RFI-0451 Code table.pdf; RFI-0451 P502 - WATER RISERS.PDF

Follow Up Flag: Follow up
Flag Status: Flagged

This is acceptable.

Jennifer G. Faulkinberry, AIA, NCARB
 Winford Lindsay Architect

344 West Pike Street
 jfaulkinberry@lpbatlanta.com

direct 770.407.5786 Lawrenceville, GA 30046
 cell 770.241.2473

fax 770.407.5817

-----Original Message-----

From: Alec Dooley [mailto:system@constructware.com]

Sent: Thursday, August 25, 2016 4:52 PM

To: adooley@balfourbeattyus.com; bdenney@balfourbeattyus.com; dricci@balfourbeattyus.com; Jennifer Faulkinberry; jclements@matrixse.com; jeldridge@balfourbeattyus.com; kbrown@bennetthospitality.com; MCerino@smeinc.com; mdale@balfourbeattyus.com; nstarcevic@balfourbeattyus.com; Rledford@balfourbeattyus.com; timspano@balfourbeattyus.com

Subject: Hotel at Marion Square - RFI:0451 - Plumbing Manifold Type

Jennifer,

As discussed during the OAC meeting. Please see the attached revised RFI for your review.

Thank you,

Alec Dooley | Senior Project Engineer

mobile: 704.614.4907 | email: adooley@balfourbeattyus.com Balfour Beatty Construction | 306 Meeting Street, Suite 300, Charleston, SC 29401 | www.balfourbeattyus.com

604.10.1 Manifold sizing. Hot water and cold water manifolds shall be sized in accordance with Table 604.10.1. The total gallons per minute is the demand of all outlets supplied.

**TABLE 604.10.1
MANIFOLD SIZING**



NOMINAL SIZE INTERNAL DIAMETER (inches)	MAXIMUM DEMAND (gpm)	
	Velocity at 4 feet per second	Velocity at 8 feet per second
$\frac{3}{8}$	2	5
$\frac{1}{2}$	6	11
1	10	20
$1\frac{1}{4}$	15	31
$1\frac{1}{2}$	22	44

For 5/8 inch = 25.4 mm, 1 gallon per minute = 3.785 L/min.

1 foot per second = 0.305 m/s.

604.10.2 Valves. Individual fixture shutoff valves installed at the manifold shall be identified as to the fixture being supplied.

604.10.3 Access. Access shall be provided to manifolds with integral factory- or field installed valves.

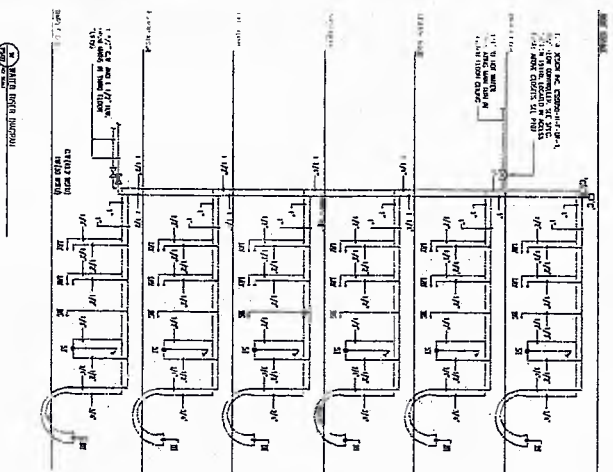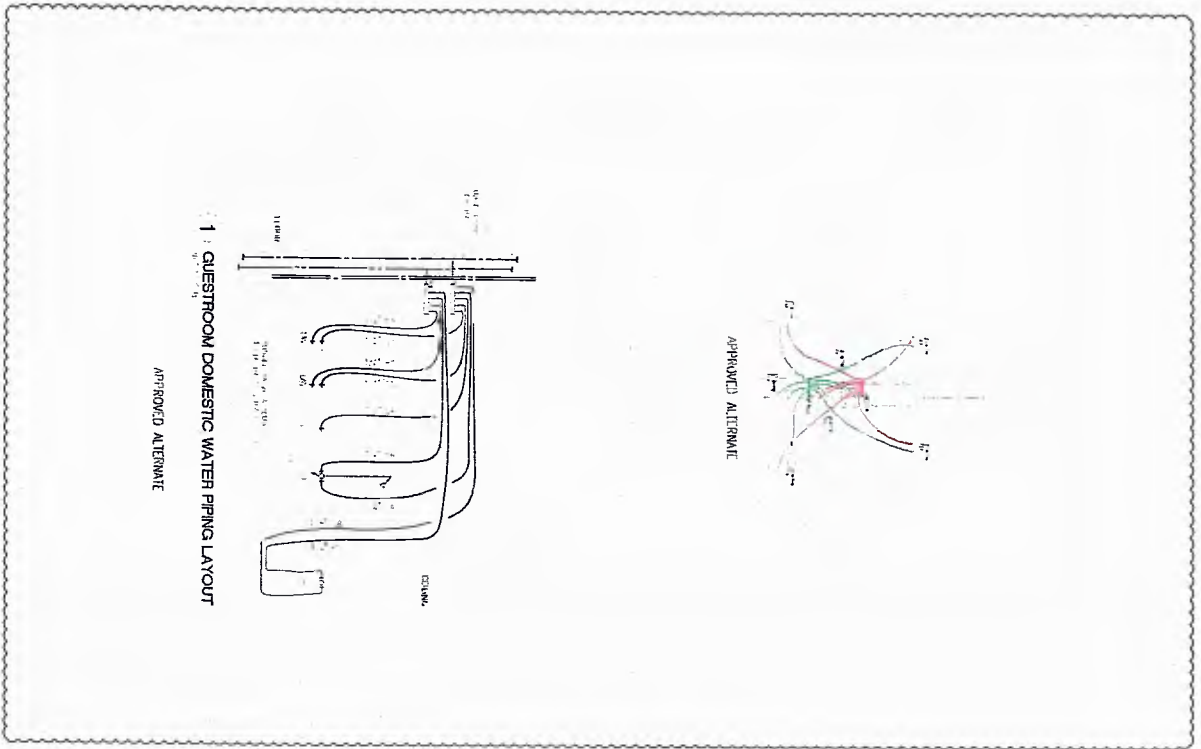

Tab No. 122

Balfour Beatty Construction

November 27, 2017

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 122R1
Structural Delay Claim

Dear Ms. Brown:

Please find attached a copy of Request for Change 122R1 for additional compensation and time due to the delays incurred during the installation of the structure on the above referenced project. This change order is for costs and time related to the delays incurred during the installation of the structural frame on the above referenced project. This change order replaces the previously submitted RCO and reflects reduction in costs from Lithco as well as costs for BBC. We are submitting, herewith, our Request for Change Order # 122 in the amount of One million twelve thousand, forty two (\$1,012,042.00) to provide additional work in accordance with the following qualifications:

L6, L8 and L9 Structural Delay Claim

This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



David Stanton
Operations Director

cc:

RCO # 122 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 122R1- Structural Delay Claim

The additional work for the **Structural Delay Claim** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1		BBC General Conditions	\$321,255.00
2		Hoisting, Staging, and Logistics	\$119,227.00
3	400.50300001.40	Lithko	\$383,720.00
4	400.51550000.40	Pasco	\$6,262.00
5	400.51500000.40	BMCC - L6	\$35,782.00
6	400.51600000.40	Watson Electrical	\$99,008.00

Total Items	\$965,253.00
Total Markups	\$46,789.00
RCO Total	\$1,012,042.00

The total Cost to perform the work as described above is an ADD of One million twelve thousand forty two (\$1,012,042.00).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: Kim Brown, Library Associates, LLC Date: _____

RCO# 122

Balfour Beatty Construction

STRUCTURAL DELAY CLAIM The Hotel at Marion Square

404 King Street
Charleston, SC 29403

PCM: Nick Starcavic
DATE: 11/27/2017

WORK TRADE:									
			L6	L7	L9	TOTAL:			
1	GENERAL CONDITIONS		\$ 115,862	\$ 42,132	\$ 163,261	\$ 321,255			
2	HOISTING, STAGING, LOGISTICS		INCLUDED	INCLUDED	119,227	\$ 119,227			
3	LITHKO		\$ 188,780	\$ 71,531	\$ 123,409	\$ 383,720			
4	PASCO		\$ 3,228	INCLUDED	\$ 3,036	\$ 6,262			
5	BMCC		\$ 35,782	N/A	N/A	\$ 35,782			
6	WATSON		\$ 38,620	INCLUDED	\$ 60,388	\$ 99,008			
7									
8						\$ 9			
9									
10	SUBTOTAL					\$ 965,253			
11	SUBGUARD	1.25%				\$ 12,066			
12	GENERAL LIABILITY	1.04%				\$ 10,039			
13	SUBTOTAL					\$ 987,358			
14	PROFIT	2.50%				\$ 24,684			
15	TOTAL					\$ 1,012,042			

Balfour Beatty Construction

DATE: 27-Nov-17

PROJECT: The Hotel at Marion Square

SUB LITHKO

PRECON MNGR: Nick Stancovic

Estimate Summary

SUBCONTRACTOR SCOPE SHEET

SUBCONTRACTOR	Structural Delay Claim		L6 22 Days	L7 8 Days	L8 21 Days	GENERAL CONTRACTOR ITEMS:	
						MATERIAL:	LABOR:
BASE BID:			\$198,700.00	\$71,531.00	\$123,409.00		
FURNISHED							
INSTALLED							
SALES TAX							
SCOPE ITEMS:	QTY	UNIT	UNIT PRICE	TOTAL			
Form Rental							
Early Return of 1900 sq foot tables							
HD Supply Scaffolding Rental							
Fork Lift							
Scaffold Lift							
Light Towers							
Water Lifting Edge							
Program Fuel Tank Rental							
Shoring Equipment							
Permit Costing							
General Conditions							
Inefficiencies							
Sub Tier - East Coast Labor							
Sales Tax							
Burden							
Profit							
TOTAL COST OF WORK			\$0.00	\$71,531	\$123,409	\$0	\$0

PROPOSED SUBCONTRACTOR : Structural Delay Claim
TOTAL SUBCONTRACTOR : \$383,720
TOTAL GC MATERIAL : \$0
TOTAL GC LABOR : \$0
TOTAL : \$383,720

[illegible]

[illegible]

TO BE COMPLETED BY CONTRACTOR												
A	B	C	D	E	F	G	H	I	J	K	L	M
Date Rec.	Description	Quantity	Unit of measure	Hours per Unit	Unit Price	Labor (\$)	Materials (\$)	Estimated daily cost	Emp. (\$)	Sub Contract (\$)	Notes 14a + 14b	Flow Unit (sq)
1	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days based on August salary	
2	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
3	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
4	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
5	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
6	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
7	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
8	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
9	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
10	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
11	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
12	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
13	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
14	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
15	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
16	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
17	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
18	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
19	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
20	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
21	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
22	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
23	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
24	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
25	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
26	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
27	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
28	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
29	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
30	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
31	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
32	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
33	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
34	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
35	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
36	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
37	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
38	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
39	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
40	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
41	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
42	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
43	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
44	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
45	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
46	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
47	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
48	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
49	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
50	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
51	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
52	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
53	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
54	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
55	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
56	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
57	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
58	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
59	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
60	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
61	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
62	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
63	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
64	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
65	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
66	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
67	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
68	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
69	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
70	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
71	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
72	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
73	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
74	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
75	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
76	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
77	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
78	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
79	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
80	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
81	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
82	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
83	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
84	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
85	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
86	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
87	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
88	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
89	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
90	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
91	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
92	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
93	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
94	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
95	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
96	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
97	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
98	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
99	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
100	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
101	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
102	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
103	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
104	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
105	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
106	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
107	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
108	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
109	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
110	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
111	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
112	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
113	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
114	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
115	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
116	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
117	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
118	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
119	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
120	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
121	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
122	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
123	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
124	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
125	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
126	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
127	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
128	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
129	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
130	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
131	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
132	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
133	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
134	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
135	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
136	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
137	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
138	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
139	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
140	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
141	2000 Ford Focus		8 day					1545.00			monthly and paid rate for 8 days	
142	2000 Ford Focus											

A	B	C	D	E	F	G	H	I	J	K	L	M	N
	Item No.	Description	Quantity	Unit of measure	Hours per Unit	Hour Rate	Labor Cost	Material Cost	Equipment Daily Rate	Exempt Cost	Risk Contract (\$)	Total Labor + Material + Equipment	Comments
		Agreement rent during down time for 3 lifts per lift #7 for pumps out of town	8 days	Days							1200.00		3 adjustments provided for duration. See attached backing
		Overhead pump truck and lane for ground	2 days	Days	60	\$1.00	250.00				1100.00		7 lifts x 20 min call per lift = 140 min. ECR put trucks away
		Water removal from site	1 day	Days	10	\$1.00	50.00						2 lifts x 10 min call per lift = 20 min. ECR put trucks away
													2 lifts x 10 min call per lift = 20 min. ECR put trucks away
		Sales Tax	1%				3000.00			30.00	2370.00		
		Bayonet on floor	30'				974.00			0.00	0.00		
		Subtotal					4044.00			0.00	2370.00		
		General Conditions	10%				404.40			0.00	0.00		
		Subtotal					4448.40			0.00	2370.00		
		Profit	5.00%				222.42			0.00	177.80		
		Total					\$1,484.40			\$0.00	\$2,550.00		
		TOTAL REQUEST THIS PAGE					\$1,484.40			\$0.00	\$2,550.00		

TO BE COMPLETED BY CONTRACTOR												
A	B	C	D	E	F	G	H	I	J	K	L	M
Item No.	Description	Quantity	Unit of Measure	Hours Per Unit	Labor Rate	Material	Subcontract	Inspection	Equipment	Per Sq. Ft.	Per Unit Cost	Comments
1	Site Exam (Partial)	21	Sq. Ft.						\$145.00	\$3,545.00		Pro rated Rate
2	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
3	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
4	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
5	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
6	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
7	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
8	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
9	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
10	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
11	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
12	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
13	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
14	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
15	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
16	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
17	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
18	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
19	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
20	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
21	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
22	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
23	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
24	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
25	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
26	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
27	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
28	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
29	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
30	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
31	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
32	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
33	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
34	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
35	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
36	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
37	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
38	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
39	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
40	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
41	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
42	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
43	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
44	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
45	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
46	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
47	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
48	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
49	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
50	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
51	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
52	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
53	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
54	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
55	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
56	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
57	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
58	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
59	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
60	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
61	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
62	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
63	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
64	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
65	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
66	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
67	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
68	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
69	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
70	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
71	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
72	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
73	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
74	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
75	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
76	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
77	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
78	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
79	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
80	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
81	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
82	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
83	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
84	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
85	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
86	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
87	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
88	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
89	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
90	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
91	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
92	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
93	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
94	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
95	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
96	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
97	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
98	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
99	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
100	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
101	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
102	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
103	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
104	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
105	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
106	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
107	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
108	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
109	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
110	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
111	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
112	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
113	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
114	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
115	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
116	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
117	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
118	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
119	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
120	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
121	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
122	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
123	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
124	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
125	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
126	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
127	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
128	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
129	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
130	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
131	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
132	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
133	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
134	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
135	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
136	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
137	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
138	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
139	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
140	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
141	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
142	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
143	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
144	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
145	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
146	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
147	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
148	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
149	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
150	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
151	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
152	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
153	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
154	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
155	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
156	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
157	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
158	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
159	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
160	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
161	Site Exam (Full)	21	Sq. Ft.									Pro rated Rate
162	Site Exam (Full)	21	Sq. Ft.									

[illegible]



Branch #72
1647 KING STREET EXTENSION
CHARLESTON, SC 29405-9330
Office: (843) 747-9158
www.sunbeltrentals.com

Watson Knight
Cell: (843) 514-6482
Watson.Knight@sunbeltrentals.com

STAIR TOWER QUOTE

CHARLESTON SCAFFOLDING PC072

May 03, 2016

Customer: **BBC-CHARLOTTE**

(#187039)
1930 CAMDEN ROAD
CHARLOTTE, NC 28203

BBC Charlotte / Stairunits in Stair 3 and Stair 6 /

Marion Square Hotel, Chas, SC (Active R1)
QUO-37564-R9C5R2
5/5/2016 to 7/29/2016

Marion Square Hotel-
Charleston
Job#1302600
404 King Street
Charleston, SC 29403

Dan Ricci
(704) 400-2290
Dricci@balfourbeattyus.com

Introduction

Thank you for allowing Sunbelt Rentals the opportunity to quote your scaffolding and access needs

Specifications

This proposal is for two systems stair units, each being 7' wide X 14'-8" long X 45' high with three landings, to be erected in Stair 3 and Stair 6 (one in each).

Scope

Sunbelt Rentals to provide labor and material for two systems stair units that will be erected in (one each) Stair 3 and Stair 6. The work will be performed in three phases. Phase one will be to install the units up to 26' high with one landing to the 1st floor. Phase 2 will be to continue up with the units (after the building is up efficient enough to all allow the securing of the stair unit to the building) and provide access to the 2nd floor. Phase 3 is to complete the units up to 45' in height and provide access to the 3rd floor.

Scaffolding stair units will include guard rails, toe boards and must be secured to the building.

Mobilization and Demobilization

Sunbelt will mobilize to the site, park and stage equipment in the closed area (road) and have the customer fly the material to the work area for each phase. Once Sunbelt has completed the install of both stair units Sunbelt will remove the excess equipment and leave the site. Both Stair units to be installed and dismantled during the mobilization and demobilization. Customer's crane to be used during all phases and during the demobilization.

Rental start

The full cost of the rental for both will start after the completion of the second phase.

Customer Responsibility

Customer is responsible for:

- providing the staging area, use of crane during all phases and demobilization, and placing equipment within 40' of the work area.
- any stand by time not caused directly by Sunbelt
- all permits and licenses required for this work to be performed.

General

This bid is based on straight time hours only, Monday thru Friday, 7am-3:30pm, with no overtime, weekend or holiday hours included.

Price is contingent on no standby time and crane being used for mobilization and demobilization.

Pricing Details

Equipment Rental: (4 week min.)	\$3,351.54 *
Daily Rental: (after initial 4 weeks)	\$119.70 *
Erection Price:	\$5,327.37 *
Dismantle Price:	\$3,702.07 *
Move Price: (see above)	\$0.00 *
Misc./Sales: (see above)	\$932.00 *
Rental Protection Plan:	\$0.00
Freight: (P/U-Del)	\$635.00 *

Quote Total: \$13,947.98*

*Plus applicable taxes

Terms and Conditions

PROJECT CONTRACT SPECIFICATIONS (a) Customer must be present at time of delivery to sign, inspect, count, and accept responsibility of equipment via Sunbelt Erection Inspection Checklist; (b) If Customer dismantles equipment, any equipment missing is Customer's responsibility and will be charged at replacement cost; (c) Should PE Stamped Drawings be required, additional charges apply. All such engineering work is limited to the Scaffold Design and Leg Loads and does not include analysis of job site structures; (d) Price herein assumes Sunbelt shall be exempted from participating in OCIP/ACCIP requirements. If not exempted, additional charges apply; (e) Our quoted price is based on the written terms of this Quote. If we are requested to sign an agreement you prepare, this Quote in its entirety or, must be incorporated into that agreement. If there is a conflict between your agreement and the written and included terms of our Quote, the terms of our Quote shall govern; (f) Both parties shall accept this Quote within 30 days of Date of Quote (above) or it may, at our option, be considered null and void; (g) It is a condition precedent to work being scheduled that this Quote is signed and received by the Scaffold Services Branch listed below; (h) Allow two (2) week lead times for scheduling all labor phases; (i) All work will be performed during straight time hours on day shift, Monday through Friday 7:00 am to 3:30 pm, unless specifically noted otherwise; (j) All work beyond the scope of work outlined above will be reimbursed based on Sunbelt Rentals, Inc. current Man-Hour Rates. These rates shall be made available upon request. The Customer will be responsible for verifying all time sheets. Delays (over 30 minutes), remobilizations, and unacceptable work conditions not attributable to Sunbelt, will be charged at the current Man-Hour Rates and may include a 4 hour minimum and/or additional travel time charges. (k) Scaffolds to be erected to meet or exceed OSHA 1926.451 Subpart L (or as indicated herein).

SCAFFOLD PRICE EXCLUSIONS. The pricing of this Quote does not include the following, unless specifically described on the front of this Quote: (a) expenses incurred if the Customer's or the Job Site Physical Address safety requirements exceed State and Federal codes; (b) toeboards, screens and nets; (c) costs associated with providing a firm, compacted and level grade for all scaffolding; (d) any foundations or re-shoring required below sidewalk level or sub-basement level; (e) tarpaulins or other sheeting (scaffolding must be modified to withstand the additional wind loads, with such sheeting); (f) any costs for proof of drug testing or employment drug screening whether it be pre-employment, site required, or otherwise; (g) moving, rigging towers; (h) lodging, meals, travel, transportation, or other extraordinary expenses; (i) performance bond, and/or OCIP/ACCIP requirements, if required; (j) sales taxes, use taxes, or tariffs; (k) sealed shop drawings or PE Stamped Drawings, if required; and (l) any other costs incurred due to the Job Site Physical Address conditions, delays, or safety considerations not attributed to Sunbelt will be invoiced to Customer on a time and material basis.

CUSTOMER RESPONSIBILITIES. Unless otherwise noted herein, Customer shall be responsible for the following, all at Customer's sole expense: (a) compliance with all laws and regulations related to the proper possession and use of scaffolding; (b) provide qualified, experienced, and adequate supervision of any and all users of the scaffolding including a competent person; (c) provide all training of all users as required by 29CFR1910, 29CFR1926, and other applicable local, state, and federal governing bodies, and all accepted industry standards; (d) all scaffold users have read and understand the Codes of Safe Practices; (e) provide a firm, compacted and level grade for all scaffolding; (f) provide suitable crane and fork lift support or other material handling, as needed for the Work; (g) verify that the existing structure will safely support the additional vertical and horizontal load from the scaffold; (h) repair all holes in existing structure left as a result of concrete anchors or other ties necessary to stabilize scaffold structure; (i) arrange with the Utilities Authority for all necessary safeguards, notifications and process lock-outs prior to erection date; (j) provide electric power and lighting to suit Sunbelt requirements; (k) supply any necessary flagmen or temporary barriers or signs, etc.; (l) if Sunbelt will be working in the vicinity of water, necessary batmen and boat as defined in OSHA regulations; (m) any ground protection i.e. for furniture, machines, carpets, landscaping, etc.; (n) toilets and wash facilities; (o) a firm, compacted and level grade laydown yard during both erection and dismantling; (p) security of Sunbelt equipment and materials with a laydown yard; (q) restoration of the laydown yard following completion of the Work; (r) all permits; (s) Falling Object Protection and any citations and/or fines OSHA may impose for failure to do so; (t) Customer's fall protection systems and methods during the use of the scaffolding that comply with all laws and be at Customer's risk; (u) assume all risks associated with the possession, custody and operation of and full responsibility for, the equipment, including but not limited to, personal injury, death, rental charges, losses, damages and destruction including customer transport, loading and unloading; and (v) maintain general and auto liability insurance of not less than \$2,000,000 per occurrence, including coverage for Customer's contractual liabilities herein (such as the indemnification clause); property insurance against loss by all risks to the Equipment in an amount at least equal to the fair market value thereof; and worker's compensation insurance. Such policies shall be primary (and not on an excess basis), on an occurrence basis, name Sunbelt as an additional insured and loss payee. Customer shall provide Sunbelt with certificates of insurance evidencing the coverage required above prior to any rental and any time upon Sunbelt's request.

SCAFFOLD CONDITIONS AND ASSUMPTIONS. Unless otherwise specified herein to the contrary: (a) the scaffolding will be erected and dismantled one time only; (b) any alterations not described herein will be charged at the applicable time and material rates; (c) any overtime work shall be invoiced at the applicable time and material rates; and (d) the work performed by Sunbelt will be done in accordance with applicable state and federal codes.

INDEMNIFICATION. Sunbelt indemnifies, releases, defends and holds Customer harmless from and against any third party claims including any and all liabilities, losses, damages, claims, penalties, fines and expenses, including attorney's fees for any damages to property and/or persons including death ("Claims") to the proportionate extent caused by Sunbelt or any of its contractors, suppliers, officers, agents, or employees negligent acts or omissions in the performance of this Agreement. Customer will (i) give Sunbelt prompt notice of any such Claim, and (ii) at Sunbelt's reasonable request, cooperate with Sunbelt in the defense and settlement of the Claim. Customer indemnifies, releases, defends and holds Sunbelt harmless from and against any third party claims including any and all Claims to the proportionate extent caused by Customer or any of its contractors, suppliers, officers, agents, or employees negligent acts or omissions in the performance of this Agreement. Sunbelt will (i) give Customer prompt notice of any such Claim, and (ii) at Customer's reasonable request, cooperate with Customer in the defense and settlement of the Claim. Notwithstanding anything contained in any agreement between the parties to the contrary, Sunbelt's requirement to provide additional insured, primary, non-contributory and waiver of subrogation status shall be limited to the extent of Sunbelt's indemnification obligations herein.

SCAFFOLD CHANGE ORDERS. If Customer requests a change in the Work, Sunbelt shall send Customer's "Point of Contact" a change order request in written form. Customer shall return a signed copy of the change order to Sunbelt; provided however, if no objection to the change order is received by Sunbelt, the change order shall be deemed approved by Customer.

INSPECTION AND ACCEPTANCE. On Customer's acceptance of the erected scaffold, Customer will be responsible for the maintenance, control, proper use and supervision of the scaffold until such time as the scaffold is fully dismantled and returned to Sunbelt for removal from the Job Site.

OTHER TERMS. The remaining provisions of this Quote are shown on the following page and incorporated herein by reference and can also be found at: <https://www.sunbeltrentals.com/services/scaffold/termsandconditions>

Quote Acceptance

BBC-CHARLOTTE
Dan Ricci

Acceptance Signature of Customer's Authorized Representative

Date

Sunbelt Rentals, Inc.
Watson Knight

Acceptance Signature of Sunbelt Rentals Authorized Employee

Date



SYSTEM SCAFFOLD QUOTE

Branch #72
1647 KING STREET EXTENSION
CHARLESTON, SC 29405-9330
Office: (843) 747-9158
www.sunbeltrentals.com

Watson Knight
Cell: (843) 514-6482
Watson.Knight@sunbeltrentals.com

CHARLESTON SCAFFOLDING PC072

April 14, 2016

Customer

BBC-CHARLOTTE
(#187039)
1930 CAMDEN ROAD
CHARLOTTE, NC 28203

BBC-Charlotte Overhead Protection on Marion
Square Hotel (Active R0)
QUO-35951-L3D0F3
4/29/2016 to 7/29/2016

Marion Square Hotel-
Charleston
Job#1302600
404 King Street
Charleston, SC 29403

Bob Cotherrmann
(704) 319-4000
rcotherman@balfourbeattyus.com

Introduction

Thank you for allowing Sunbelt Rentals the opportunity to quote your scaffolding and Overhead Protection needs.

Specifications

This bid is for 154' linear feet x 10' high of overhead protection.

Scope

Sunbelt Rentals to provide labor and material for 154' linear x 10' high of Overhead Protection (OHP). Systems scaffolding with aluminum beams and 3/4" pressure treated plywood will be used. Scaffolding will be set on no more than 7' bays. The clearance for the pedestrian traffic will be approx 5' wide x 8' high while the decking (beams and plywood with be no less than 10' at its lowest point closest to the wall. Deck will be higher on the road side (approx 20") and slope to the job site side. Customer will provide the 4' wide netting for Sunbelt to install on the top inside portion of the Overhead Protection. The Overhead protection will be anchored into the asphalt. Customer will be responsible for any repairs to the asphalt due to the anchoring.

Mobilization and Demobilization

Sunbelt will arrive, park and stage in the customer controlled area on King Street directly next to the work site and Marion Square itself. At this time the customer must have the parking/staging area and work area closed off (including any signage and traffic and pedestrian controls in place). Sunbelt will unload and start the install. Once the install has been completed Sunbelt will remove the excess equipment and leave the site. Customer must be present to sign for and have the overhead protection turned over to them. The dismantle will be performed in the same manner and will have the same requirements.

Customer Responsibility

Customer is responsible for:

- providing the parking and staging area as discussed (directly next to the work area and Marion Square on King Street.
- lighting for the Overhead Protection
- sidewalk closure
- all permits, traffic and pedestrian control
- netting (the Overhead protection will be approx 154' linear feet long)
- all permits and licenses required for this work to be performed

General

This bid is based on straight time hours only, Monday thru Friday, 6:30am-3pm) with no overtime, weekend or holiday hours included

Pricing Details

Equipment Rental: <i>(4 week min.)</i>	\$2,556.14*
Daily Rental: <i>(after initial 4 weeks)</i>	\$91.29*
Erection Price:	\$4,725.84*
Dismantle Price:	\$3,150.56*
Move Price: <i>(see above)</i>	\$0.00*
Misc./Sales: <i>(see above)</i>	\$2,509.00*
Rental Protection Plan:	\$0.00
Freight: <i>(P/U-Del)</i>	\$570.00*

Quote Total:**\$13,511.54****Plus applicable taxes

Terms and Conditions

PROJECT CONTRACT SPECIFICATIONS (a) Customer must be present at time of delivery to sign, inspect, count, and accept responsibility of equipment via Sunbelt Erection Inspection Checklist; (b) If Customer dismantles equipment, any equipment missing is Customer's responsibility and will be charged at replacement cost; (c) Should PE Stamped Drawings be required, additional charges apply. A full engineering work is limited to the Scaffold Design and Leg Loads and does not include analysis of job site structures; (d) Price herein assumes Sunbelt shall be exempted from participating in OCIP/CCIP requirements. If not exempted, additional charges apply; (e) Our quoted price is based on the written terms of this Quote. If we are requested to sign an agreement you prepare, this Quote in its entirety or, must be incorporated into that agreement. If there is a conflict between your agreement and the written and included terms of our Quote, the terms of our Quote shall govern; (f) Both parties shall accept this Quote within 30 days of Date of Quote (above) or it may, at our option, be considered null and void; (g) It is a condition precedent to work being scheduled that this Quote is signed and received by the Scaffold Services Branch listed below; (h) Allow two (2) week lead times for scheduling all labor phases; (i) All work will be performed during straight time hours on day shift, Monday through Friday 7:00 am to 3:30 pm, unless specifically noted otherwise; (j) All work beyond the scope of work outlined above will be reimbursed based on Sunbelt Rentals, Inc. current Man Hour Rates. These rates shall be made available upon request. The Customer will be responsible for verifying all time sheets. Delays (over 30 minutes), rework, set ups, and unacceptable work conditions not attributable to Sunbelt, will be charged at the current Man-Hour Rates and may include a 4 hour minimum and/or additional travel time charges; (k) Scaffolds to be erected to meet or exceed OSHA 1926.451 Subpart L (or as indicated herein);

SCAFFOLD PRICE EXCLUSIONS. The pricing of this Quote does not include the following, unless specifically described on the front of this Quote: (a) expenses incurred if the Customer's or the Job Site Physical Address safety requirements exceed State and Federal codes; (b) toeboards, screens and nets; (c) costs associated with providing a firm, compacted and level grade for all scaffolding; (d) any foundations or re-shoring required below sidewalk, level or sub-basement level; (e) tarpaulins or other sheeting (scaffolding must be modified to withstand the additional wind loads, with such sheeting); (f) any costs for proof of drug testing or employment drug screening whether it be pre-employment, site required, or otherwise; (g) moving rolling towers; (h) lodging, meals, travel, transportation, or other extraordinary expenses; (i) performance bond, and/or OCIP/CCIP requirements, if required; (j) sales taxes, use taxes, or tariffs; (k) sealed shop drawings or PE Stamped Drawings, if required; and (l) any other costs incurred due to the Job Site Physical Address conditions, delays, or safety considerations not attributed to Sunbelt will be invoiced to Customer on a time and material basis.

CUSTOMER RESPONSIBILITIES. Unless otherwise noted herein, Customer shall be responsible for the following, all at Customer's sole expense: (a) compliance with all laws and regulations related to the proper possession and use of scaffolding; (b) provide qualified, experienced, and adequate supervision of any and all users of the scaffolding including a competent person; (c) provide all training of all users as required by 29CFR 1910, 29CFR 1926, and other applicable local, state, and federal governing bodies, and all accepted industry standards; (d) all scaffold users have read and understand the Codes of Safe Practices; (e) provide a firm, compacted and level grade for a scaffolding; (f) provide suitable crane and forklift support, or other material handling, as needed for the Work; (g) verify that the existing structure will safely support the additional vertical and horizontal loading from the scaffold; (h) repair all holes in existing structure left as a result of concrete anchors or other ties necessary to stabilize scaffold structure; (i) arrange with the Utilities Authority for all necessary safeguards, notifications and process lock-outs prior to erection date; (j) provide electric power and lighting to suit Sunbelt requirements; (k) supply any necessary flagmen or temporary barriers or signs, etc.; (l) If Sunbelt will be working in the vicinity of water, necessary boatmen and boat as defined in OSHA regulations; (m) any ground protection, i.e. for furniture, machines, carpets, landscaping, etc.; (n) rollies and wash facilities; (o) a firm, compacted and level grade laydown yard during both erection and dismantling; (p) security of Sunbelt equipment and materials within laydown yard; (q) restoration of the laydown yard following completion of the Work; (r) all permits; (s) Falling Object Protection and any citations and/or fines OSHA may impose for failure to do so; (t) Customer's fall protection systems and methods during the use of the scaffolding that comply with all laws and be at Customer's risk; (u) assume all risks associated with the possession, custody and operation of and full responsibility for, the equipment, including but not limited to, personal injury, death, rental charges, losses, damages and destruction, including customer transport, loading and unloading; and (v) maintain general and auto liability insurance of not less than \$2,000,000 per occurrence, including coverage for Customer's contractual liabilities herein (such as the indemnification clause); property insurance against loss by all risks to the Equipment, in an amount at least equal to the fair market value thereof; and worker's compensation insurance. Such policies shall be primary (and not on an excess basis), on an occurrence basis, name Sunbelt as an additional insured and loss payee. Customer shall provide Sunbelt with certificates of insurance evidencing the coverage required above prior to any rental and any time upon Sunbelt's request.

SCAFFOLD CONDITIONS AND ASSUMPTIONS. Unless otherwise specified here to the contrary: (a) the scaffolding will be erected and dismantled one time only; (b) any alterations not described herein will be charged at the applicable time and material rates; (c) any overtime work shall be invoiced at the applicable time and material rates; and (e) the work performed by Sunbelt will be done in accordance with applicable state and federal codes.

INDEMNIFICATION. Sunbelt indemnifies, releases, defends and holds Customer harmless from and against any third party claims including any and all liabilities, losses, damages, claims, penalties, fines and expenses, including attorney's fees, for any damages to property and/or persons including death ("Claims") to the proportionate extent caused by Sunbelt or any of its contractors, suppliers, officers, agents, or employees negligent acts or omissions in the performance of this Agreement. Customer will (i) give Sunbelt prompt notice of any such Claim, and (ii) at Sunbelt's reasonable request, cooperate with Sunbelt in the defense and settlement of the Claim. Customer indemnifies, releases, defends and holds Sunbelt harmless from and against any third party claims including any and all Claims to the proportionate extent caused by Customer or any of its contractors, suppliers, officers, agents, or employees negligent acts or omissions in the performance of this Agreement. Sunbelt will (i) give Customer prompt notice of any such Claim, and (ii) at Customer's reasonable request, cooperate with Customer in the defense and settlement of the Claim. Notwithstanding anything contained in any agreement between the parties to the contrary, Sunbelt's requirement to provide additional insured, primary, non-contributory and waiver of subrogation status shall be limited to the extent of Sunbelt's indemnification obligations herein.

SCAFFOLD CHANGE ORDERS. If Customer requests a change in the Work, Sunbelt shall send Customer's "Point of Contact" a change order request in written form. Customer shall return a signed copy of the change order to Sunbelt; provided however, if no objection to the change order is received by Sunbelt, the change order shall be deemed approved by Customer.

INSPECTION AND ACCEPTANCE. On Customer's acceptance of the erected scaffold, Customer will be responsible for the maintenance, control, proper use and supervision of the scaffold until such time as the scaffold is fully dismantled and returned to Sunbelt for removal from the Job Site.

OTHER TERMS. The remaining provisions of this Quote are shown on the following page and incorporated herein by reference and can also be found at: <https://www.sunbeltrentals.com/services/scaffold/termsandconditions>

Quote Acceptance

BBC-CHARLOTTE
Bob Cothermann

Acceptance Signature of Customer's Authorized Representative

Date

Sunbelt Rentals, Inc.
Watson Knight

Acceptance Signature of Sunbelt Rentals Authorized Employee

Date



SYSTEM SCAFFOLD QUOTE

Branch #72
1647 KING STREET EXTENSION
CHARLESTON, SC 29405-9330
Office: (843) 747-9158
www.sunbeltrentals.com

Watson Knight
Cell: (843) 514-6482
Watson.Knight@sunbeltrentals.com

CHARLESTON SCAFFOLDING PC072

July 21, 2016

Customer: BBC-CHARLOTTE (#187039) 1930 CAMDEN ROAD CHARLOTTE, NC 28203	BBC Charlotte / OHP for Garage entrance /Hotel at Marion Square (Active RO) QUO-44594-L4M3N1 7/28/2016 to 10/25/2016
Marion Square Hotel-Charleston Job#1302600 404 King Street Charleston, SC 29403	Dan Ricci (704) 400-2290 Dricci@balfourbeattyus.com

Introduction

Thank you for allowing Sunbelt Rentals the opportunity to quote your scaffolding and Overhead Protection needs

Specifications

This bid is for Overhead Protection, systems scaffolding with layering (single layer of each), aluminum beams, OSHA wood planking, and 3/4" plywood secured on top directly in front of the garage opening.

Scope

Sunbelt Rentals to provide labor and material for overhead protection (OHP) being 10' wide x 28' long x approx 9' high. OHP will consist of aluminum beams, wood plank and 3/4" plywood secured on top. This is not to be considered a personnel work platform.

Mobilization and Demobilization

Sunbelt will mobilize and stage the equipment directly next to the work area and then start the install. Once the install have been completed Sunbelt will remove the excess equipment and leave the site. Customer to perform a walk down inspection of the scaffolding/OHP and sign the inspection. Once the customer has completed with use of the scaffolding Sunbelt will return, dismantle and demobilize from the site.

Customer Responsibility

Customer is responsible for:

- providing the staging area directly next to the work area.
- unloading of the scaffolding and placing it next to the work area if needed.
- allowing the closure of the work area while work is being performed for safety
- all permits and licenses required for this work to be performed.
- any lighting or signage that may be required

General

This bid is based on straight time hours only, Monday thru Friday, 7am-3:30pm, with no overtime, weekend or holiday hours included.

Pricing Details

Equipment Rental: (4 week min.)	\$729.17*
Daily Rental: (after initial 4 weeks)	\$26.04*
Erection Price:	\$1,308.99*
Dismantle Price:	\$872.66*
Move Price: (see above)	\$0.00*
Misc./Sales: (see above)	\$418.00*
Rental Protection Plan:	\$0.00
Freight: (P/U-Del)	\$370.00*

Quote Total: **\$3,698.82***

*Plus applicable taxes

Terms and Conditions

PROJECT CONTRACT SPECIFICATIONS (a) Customer must be present at time of delivery to sign, inspect, count, and accept responsibility of equipment via Sunbelt Erection Inspection Checklist; (b) If Customer dismantles equipment, any equipment missing is Customer's responsibility and will be charged at replacement cost; (c) Should PE Stamped Drawings be required, additional charges apply. All such engineering work is limited to the Scaffold Design and Leg Loads and does not include analysis of job site structures; (d) Price herein assumes Sunbelt shall be exempted from participating in OCIP/CCIP requirements. If not exempted, additional charges apply; (e) Our quoted price is based on the written terms of this Quote. If we are requested to sign an agreement you prepare, this Quote in its entirety or, must be incorporated into that agreement. If there is a conflict between your agreement and the written and included terms of our Quote, the terms of our Quote shall govern; (f) Both parties shall accept this Quote within 30 days of Date of Quote (above) or it may, at our option, be considered null and void; (g) It is a condition precedent to work being scheduled that this Quote is signed and received by the Scaffold Services Branch listed below; (h) Allow two (2) week lead times for scheduling all labor phases; (i) All work will be performed during straight time hours on day shift, Monday through Friday 7:00 am to 3:30 pm, unless specifically noted otherwise; (j) A work beyond the scope of work outlined above will be reimbursed based on Sunbelt Rentals, Inc. current Man-Hour Rates. These rates shall be made available upon request. The Customer will be responsible for verifying all time sheets. Delays (over 30 minutes), remobilizations, and unacceptable work conditions not attributable to Sunbelt will be charged at the current Man-Hour Rates and may include a 4 hour minimum and/or additional travel time charges; (k) Scaffolds to be erected to meet or exceed OSHA 1926.451 Subpart L (or as indicated herein);

SCAFFOLD PRICE EXCLUSIONS. The pricing of this Quote does not include the following, unless specifically described on the front of this Quote: (a) expenses incurred if the Customer's or the Job Site Physical Address safety requirements exceed State and Federal codes; (b) toeboards, screens and nets; (c) costs associated with providing a firm, compacted and level grade for all scaffolding; (d) any foundations or re-shoring required below sidewalk level or sub basement level; (e) tarpaulins or other sheeting (scaffolding must be modified to withstand the additional wind loads, with such sheeting); (f) any costs for proof of drug testing or employment drug screening whether it be pre-employment, site required, or otherwise; (g) moving/rolling towers; (h) lodging, meals, travel, transportation, or other extraordinary expenses; (i) performance bond, and/or OCIP/CCIP requirements, if required; (j) sales taxes, use taxes, or tariffs; (k) sealed shop drawings or PE Stamped Drawings, if required; and (l) any other costs incurred due to the Job Site Physical Address conditions, delays, or safety considerations not attributed to Sunbelt will be invoiced to Customer on a time and material basis.

CUSTOMER RESPONSIBILITIES. Unless otherwise noted herein, Customer shall be responsible for the following, all at Customer's sole expense: (a) compliance with all laws and regulations related to the proper possession and use of scaffolding; (b) provide qualified, experienced, and adequate supervision of any and all users of the scaffolding including a competent person; (c) provide all training of all users as required by 29CFR1910, 29CFR1926, and other applicable local, state and federal governing bodies, and all accepted industry standards; (d) all scaffold users have read and understand the Codes of Safe Practices; (e) provide a firm, compacted and level grade for all scaffolding; (f) provide suitable crane and forklift support, or other material handling, as needed for the Work; (g) verify that the existing structure will safely support the additional vertical and horizontal loading from the scaffold; (h) repair all holes in existing structure left as a result of concrete anchors or other ties necessary to stabilize scaffold structure; (i) arrange with the Utilities Authority for all necessary safeguards, notifications and process lock-outs prior to erection date; (j) provide electric power and lighting to suit Sunbelt requirements; (k) supply any necessary flagmen or temporary barriers or signs, etc.; (l) if Sunbelt will be working in the vicinity of water, necessary boatmen and boat as defined in OSHA regulations; (m) any ground protection, i.e. for furniture, machines, carpets, landscaping, etc.; (n) toilets and wash facilities; (o) a firm, compacted and level grade laydown yard during both erection and dismantling; (p) security of Sunbelt equipment and materials within laydown yard; (q) restoration of the laydown yard following completion of the Work; (r) all permits; (s) Falling Object Protection and any citations and/or fines OSHA may impose for failure to do so; (t) Customer's fall protection systems and methods during the use of the scaffolding that comply with all laws and be at Customer's risk; (u) assume all risks associated with the possession, custody and operation of and full responsibility for, the equipment, including but not limited to, personal injury, death, rental charges, losses, damages and destruction, including customer transport, loading and unloading; and (v) maintain general and auto liability insurance of not less than \$2,000,000 per occurrence, including coverage for Customer's contractual liabilities hereon (such as the indemnification clause); property insurance against loss by all risks to the Equipment, in an amount at least equal to the fair market value thereof; and worker's compensation insurance. Such policies shall be primary (and not on an excess basis), on an occurrence basis, name Sunbelt as an additional insured and loss payee. Customer shall provide Sunbelt with certificates of insurance evidencing the coverage required above prior to any rental and any time upon Sunbelt's request.

SCAFFOLD CONDITIONS AND ASSUMPTIONS. Unless otherwise specified herein to the contrary: (a) the scaffolding will be erected and dismantled one time only; (b) any alterations not described herein will be charged at the applicable time and material rates; (c) any overtime work shall be invoiced at the applicable time and material rates; and (e) the work performed by Sunbelt will be done in accordance with applicable state and federal codes.

INDEMNIFICATION. Sunbelt indemnifies, releases, defends and holds Customer harmless from and against any third party claims including any and all liabilities, losses, damages, claims, penalties, fines and expenses, including attorney's fees, for any damages to property and/or persons including death ("Claims") to the proportionate extent caused by Sunbelt or any of its contractors, suppliers, officers, agents, or employees negligent acts or omissions in the performance of this Agreement. Customer will (i) give Sunbelt prompt notice of any such Claim, and (ii) at Sunbelt's reasonable request, cooperate with Sunbelt in the defense and settlement of the Claim. Customer indemnifies, releases, defends and holds Sunbelt harmless from and against any third party claims including any and all Claims to the proportionate extent caused by Customer or any of its contractors, suppliers, officers, agents, or employees negligent acts or omissions in the performance of this Agreement. Sunbelt will (i) give Customer prompt notice of any such Claim, and (ii) at Customer's reasonable request, cooperate with Customer in the defense and settlement of the Claim. Notwithstanding anything contained in any agreement between the parties to the contrary, Sunbelt's requirement to provide additional insured, primary, non-contributory and waiver of subrogation status shall be limited to the extent of Sunbelt's indemnification obligations herein.

SCAFFOLD CHANGE ORDERS. If Customer requests a change in the Work, Sunbelt shall send Customer's "Point of Contact" a change order request in written form. Customer shall return a signed copy of the change order to Sunbelt, provided however, if no objection to the change order is received by Sunbelt, the change order shall be deemed approved by Customer.

INSPECTION AND ACCEPTANCE. On Customer's acceptance of the erected scaffold, Customer will be responsible for the maintenance, control, proper use and supervision of the scaffold until such time as the scaffold is fully dismantled and returned to Sunbelt for removal from the Job Site.

OTHER TERMS. The remaining provisions of this Quote are shown on the following page and incorporated herein by reference and can also be found at: <https://www.sunbeltrentals.com/services/scaffold/termsandconditions>

Quote Acceptance

BBC-CHARLOTTE
Dan Ricci

Acceptance Signature of Customer's Authorized Representative

Date

Sunbelt Rentals, Inc.
Watson Knight

Acceptance Signature of Sunbelt Rentals Authorized Employee

Date



PC#: 006
2411 CLEMENTS FERRY RD
CHARLESTON, SC 29492-7734
843-881-4945

SUNBELT RENTALS, INC.

Salesman: 00000
Typed By: MSPORDER

Job Site:

SIMMONS PARK
200 PIER VIEW DRIVE
CHARLESTON, SC 29492

C#: 704-319-4000 J#: 704-319-4000

Customer: 187039

BBC-CHARLOTTE
1930 CAMDEN ROAD
CHARLOTTE, NC 28203

RESERVATION

Contract #.. 61740650
Contract dt. 7/12/16
Date out.... 7/13/16 7:30 AM
Est return.. 7/18/16 7:30 AM
Job Loc..... 200 PIER VIEW DRIVE, CHARLESTON
Job No..... 1 - SIMMONS PARK
P.O. #..... TO BE PROVIDED
Ordered By.. Starcevic, Nick
NET DUE UPON RECEIPT

QTY	EQUIPMENT #	Min	Day	Week	4 Week	Amount
1.00	60' STR ELEC MANLIFT 0580609	344.00	344.00	871.00	1925.00	871.00
*** EQP MSG ***						
* Familiarization of the equipment stated on this contract has been offered to the customer.						
* An Operator's Manual and the Manual of Responsibilities has been provided with the equipment stated on this contract.						
* OSHA 1926.453 & ANSI Regulation A92 requires All Boom Lift occupants of the platform to wear Personal Fall Protection. Personal Fall Protection equipment is available for purchase from Sunbelt Rentals.						
SALES ITEMS:						
Qty	Item number	Unit	Price			
1	DLPKSRCHG	EA	15.300			15.30
1	TRANSPORTATION SURCHARGE					
1	ENVIRONMENTAL	EA	12.190			12.19
1	ENVIRONMENTAL					
1	SCHERS	EA	26.130			26.13
1	SC 3% HEAVY EQUIP. RENTAL SURCHARGE					
	DELIVERY CHARGE					85.00
	PICKUP CHARGE					85.00

Rate your rental experience www.sunbeltrentals.com/survey

IF THE EQUIPMENT DOES NOT WORK PROPERLY, NOTIFY THE OFFICE AT ONCE

MULTIPLE SHIFTS OR OVERTIME RATES MAY APPLY

CUSTOMER IS RESPONSIBLE FOR REFUELING, DAMAGES AND REPAIRS

- The total charges are an estimate based on the estimated rental period and other information provided by Customer.
- Customer assumes all risks associated with the Equipment during the Rental Period, including injury and damage to persons, property and the Equipment.
- Customer is responsible for and shall only permit properly trained, Authorized Individuals to use the Equipment.
- If the Equipment does not operate properly, is not suitable for Customer's intended use, does not have operating and safety instructions or Customer has any questions regarding use of the Equipment, Customer shall not use the Equipment and shall contact Sunbelt immediately.
- Equipment misuse or using damaged or malfunctioning Equipment may result in serious bodily injury or death and Customer agrees that Customer (i) assumes all risk associated thereunder, and (ii) indemnifies Sunbelt Entities for all claims or damages as a result of misuse or use of damaged or malfunctioning Equipment.
- Customer has received, read, understands and agrees to the estimated charges and all the terms on this page, plus all sections on the reverse side of this Contract ("Sections"), including Release and Indemnification in Section 9 and Environmental Fee in Section 15, which can also be found at www.sunbeltrentals.com/rentalcontract. * Delivery/Pickup Surcharge fee explanation is available at www.sunbeltrentals.com/surcharge.
- Customer must contact Sunbelt to request pickup of Equipment, retain the Pick-Up Number given by Sunbelt and will be responsible for Equipment until actually retrieved by Sunbelt.
- Customer waives its right to a jury trial in any dispute as set forth in Section 19.
- At the election of Sunbelt or Customer, Customer agrees to submit every dispute to arbitration and waives any right to bring a class action as set forth in Section 20.

Customer is declining Rental Protection Plan (see reverse side for details) _____ (Customer Initials)

Customer Signature

Date

Name Printed

Delivered By

Date

** www.sunbeltrentals.com **

PDFSHOLS (Rev 12/10/15)

R - 1737



PC#: 006
2411 CLEMENTS FERRY RD
CHARLESTON, SC 29492-7734
843-881-4945

SUNBELT RENTALS, INC.

Salesman: 00000
Typed By: MSPORDER

Job Site:

SIMMONS PARK
200 PIER VIEW DRIVE
CHARLESTON, SC 29492

C#: 704-319-4000 J#: 704-319-4000

Customer: 187039

BBC-CHARLOTTE
1930 CAMDEN ROAD
CHARLOTTE, NC 28203

RESERVATION

Contract #.. 61740650
Contract dt. 7/12/16
Date out.... 7/13/16 7:30 AM
Est return.. 7/18/16 7:30 AM
Job Loc..... 200 PIER VIEW DRIVE, CHARLESTON
Job No..... 1 **SIMMONS PARK**
P.O. #..... TO BE PROVIDED
Ordered By.. Starcevic, Nick
NET DUE UPON RECEIPT

QTY	EQUIPMENT #	Min	Day	Week	4 Week	Amount
-----	-------------	-----	-----	------	--------	--------

SALES ITEMS:

Qty	Item number	Unit	Price
-----	-------------	------	-------

Poc Nick Nick Starcevic PM Bbc (704) 361
-3265 Call when driver leaves yard Deliv
er to pier view street side

Sub-total: 1094.62
Tax: 85.48
Total: 1180.10

All amounts are in USD

Rate your rental experience www.sunbeltrentals.com/survey

IF THE EQUIPMENT DOES NOT WORK
PROPERLY, NOTIFY THE OFFICE AT ONCE

MULTIPLE SHIFTS OR
OVERTIME RATES MAY APPLY

CUSTOMER IS RESPONSIBLE FOR
REFUELING, DAMAGES AND REPAIRS

1. The total charges are an estimate based on the estimated rental period and other information provided by Customer.
2. Customer assumes all risks associated with the Equipment during the Rental Period, including injury and damage to persons, property and the Equipment.
3. Customer is responsible for and shall only permit properly trained, Authorized Individuals to use the Equipment.
4. If the Equipment does not operate properly, is not suitable for Customer's intended use, does not have operating and safety instructions or Customer has any questions regarding use of the Equipment, Customer shall not use the Equipment and shall contact Sunbelt immediately.
5. Equipment misuse or using damaged or malfunctioning Equipment may result in serious bodily injury or death and Customer agrees that Customer (I) assumes all risk associated thereunder, and (II) indemnifies Sunbelt Entities for all claims or damages as a result of misuse or use of damaged or malfunctioning Equipment.
6. Customer has received, read, understands and agrees to the estimated charges and all the terms on this page, plus all sections on the reverse side of this Contract ("Sections"), including Release and Identification in Section 8 and Environmental fee in Section 16, which can also be found at www.sunbeltrentals.com/rentalcontract. * Delivery/Pickup Surcharge fee explanation is available at www.sunbeltrentals.com/surcharge.
7. Customer must contact Sunbelt to request pickup of Equipment; retain the Pick-Up Number given by Sunbelt and will be responsible for Equipment until actually retrieved by Sunbelt.
8. Customer waives its right to a jury trial in any dispute as set forth in Section 19.
9. At the election of Sunbelt or Customer, Customer agrees to submit every dispute to arbitration and waives any right to bring a class action as set forth in Section 20.

Customer is declining Rental Protection Plan (see reverse side for details) _____ (Customer Initials)

Customer Signature

Date

Name Printed

Delivered By

Date

** www.sunbeltrentals.com **

PDFS/NLS (Rev 12/10-15)

R - 1738

SUNBELT ADDITIONAL TERMS AND CONDITIONS

1. **DEFINITIONS.** "Authorized Individuals" are those individuals that Customer directly or indirectly allows to use the Equipment, are properly trained to use the Equipment and are not under the influence of any drugs, alcohol, substances or otherwise impaired. "Customer" is identified on the front side hereof and includes any of its representatives, agents, officers, employees or anyone signing this Contract on its behalf. "Equipment" is the equipment and/or services identified on the front side hereof, together with all implements, repairs, additions, accessories and all future Equipment rental. "Incident" is any fire, theft, damage, theft, accident, casualty, loss, vandalism, injury, death or damage to person or property, including any person or entity that appears to have occurred in connection with the Equipment. Equipment is considered "Lost" when it is either stolen, its location is unknown or Customer is unable to recover it for a period of 30 days. "MSRP" is the Equipment manufacturer's suggested list price on or about the date of the incident relating to the Equipment. "One Shift" means not more than 8 hours per day and 40 hours per week. "Ordinary Wear and Tear" means normal deterioration considered reasonable in the equipment rental industry for One Shift use. "Pick-Up Number" is the number Customer obtains from Sunbelt evidencing the Customer's call to pick up Equipment. "Rental Period" commences when the Equipment is delivered to Customer or the Site Address and continues until the Equipment is returned to the Store or picked up by Sunbelt during normal business hours, provided Customer has otherwise complied with this Contract. "RPP" is the rental protection plan described in Section 10. "Site Address" is the location that Customer represents the Equipment will be located during the Rental Period, identified on the front side hereof. "Store" is the Sunbelt location identified on the front side hereof. "Sunbelt" is Sunbelt Rentals, Inc. "Sunbelt Entities" is Sunbelt and its affiliated companies, their respective officers, directors, employees and agents.

2. **TERMS.** Customer's rental of Equipment is conditioned upon Customer's agreement with this Contract and all of its terms. Customer's execution of this Contract or taking possession of the Equipment shall be deemed acceptance of the terms herein. All of the terms herein (including on the front side of this Contract) are incorporated into this and all past and future contracts between Sunbelt and Customer upon Customer's receipt of Sunbelt's Equipment under these contracts. Any reference to Customer's purchase order or other Customer documents to other terms that shall remain in full force and effect. Customer rents the Equipment from Sunbelt pursuant to this Contract. Customer shall pay Sunbelt the rental rates (including any minimum rental on the front side hereof) and other charges described herein when due, return the Equipment to Sunbelt as required herein and otherwise comply with this Contract. This Contract is a time leased. The Equipment (a) is and shall remain the personal property of Sunbelt and (b) shall not be affixed to any other property.

3. **PERMITTED USE.** Customer agrees that Sunbelt has no control over the manner in which the Equipment is operated during the Rental Period by Customer or any third party that Customer implicitly or explicitly permits. Customer warrants that: (a) prior to each use, Customer shall inspect the Equipment to confirm that it is in good condition, without defects, includes readable decals and operating and safety instructions and is suitable for Customer's intended use; (b) any apparent agent at the Site Address is authorized to accept delivery of the Equipment (and if Customer requests, Customer authorizes Sunbelt to leave the Equipment at the Site Address without requirement of written receipt); (c) Customer shall immediately notify Sunbelt if the Equipment is Lost, damaged, unsafe, defective, malfunctioning, seized upon, threatened with seizure, or if any incident occurs; (d) Customer has received from Sunbelt all information needed or requested regarding the operation of the Equipment; (e) Sunbelt is not responsible for providing operator or other training unless Customer specifically requests in writing and (f) all agents are to provide such training (Customer being responsible to obtain all training that Customer desires prior to the Equipment's use). (i) Only Authorized Individuals shall use and operate the Equipment. (ii) The Equipment's use shall be in a careful manner, in compliance with all operating and safety instructions provided on, in or with the Equipment and all applicable federal, state and local laws, permits and licenses, including but not limited to, OSHA as relevant; and (iii) the Equipment shall be kept in a secure location.

4. **PROHIBITED USE.** Customer shall not (a) alter or cover up any details or insignia on the Equipment or remove any operational or safety equipment or instructions; (b) assign (in whole or in part) this Contract; (c) move the Equipment from the Site Address without Sunbelt's written consent; (d) use the Equipment in a negligent, illegal, unauthorized or abusive manner, or in any publication (print, audiovisual or electronic); or (e) allow the use of the Equipment by any unauthorized individual. Customer acknowledges that the Equipment may be dangerous if used improperly or by untrained parties.

5. **MAINTENANCE.** Customer shall perform routine maintenance on the Equipment, including routine inspections and maintenance of fuel and oil levels, grease, cooling system, water, batteries, cutting edge, and cleaning in accordance with the manufacturer's specifications. All other maintenance or repairs may only be performed by Sunbelt or its agents, but Sunbelt has no responsibility during the Rental Period to perform any maintenance or repairs unless Customer requests a service call. If Sunbelt determines that repairs to the Equipment are needed other than Ordinary Wear and Tear, Customer shall pay the full repair charges and rental of the Equipment until the repairs are completed. Sunbelt has the right to inspect the Equipment wherever located. Customer has the authority to and hereby grants Sunbelt and its agents the right to enter the physical location of the Equipment for the purposes set forth herein. Sunbelt shall be responsible for repairs needed because of Ordinary Wear and Tear. Customer agrees that repair or replacement of the Equipment is Customer's exclusive remedy for Sunbelt's breach of this Section. Notwithstanding Sunbelt's service commitment, Sunbelt shall have no obligation if Customer breaches this Contract to stop the Rental Period, reimburse repairs or rent other equipment to Customer until Customer agrees to pay for such charges.

6. **CUSTOMER LIABILITY DURING THE RENTAL PERIOD.** CUSTOMER ASSUMES ALL RISK ASSOCIATED WITH THE POSSESSION, CONTROL, OR USE OF THE EQUIPMENT, INCLUDING BUT NOT LIMITED TO, PERSONAL INJURY, DEATH, RENTAL CHARGES, THEFT, LOSSES, DAMAGES AND DESTRUCTION, INCLUDING CUSTOMER TRANSPORTATION, LOADING AND UNLOADING WHETHER OR NOT THE CUSTOMER IS AT FAULT. After an Incident, Customer shall (a) immediately, notify Sunbelt, the police, if necessary and Customer's insurance carriers; (b) secure and maintain the Equipment and the surrounding premises in the condition existing at the time of such Incident, until Sunbelt or its agents investigate; (c) immediately, submit a report of the Incident to Sunbelt and (d) as applicable, pay Sunbelt, in addition to other sums due hereunder, the rental rate for the Equipment until the repairs are completed or Equipment replaced (but not less than the MSRP or full charges of repairs of damaged Equipment. Arrears rental charges shall not be applied against these amounts Sunbelt shall have the immediate right, but not obligation, to reclaim any Equipment involved in any Incident.

7. **NO WARRANTIES.** Sunbelt does not design or manufacture the Equipment and is not the agent of those that do. SUNBELT DISCLAIMS ALL REPRESENTATIONS AND WARRANTIES, EXPRESS OR IMPLIED, WITH RESPECT TO THE EQUIPMENT, ITS DURABILITY, CONDITION, MERCHANTABILITY, OR FITNESS FOR ANY PARTICULAR PURPOSE. CUSTOMER ACKNOWLEDGES ACCEPTANCE OF THE EQUIPMENT ON AN "AS IS, WHERE IS" BASIS, WITH ALL FAULTS, AND WITHOUT ANY RECOURSE WHATSOEVER AGAINST SUNBELT ENTITIES. CUSTOMER ASSUMES ALL RISKS ASSOCIATED WITH THE EQUIPMENT AND RELEASES SUNBELT ENTITIES FROM ALL LIABILITIES AND DAMAGES (INCLUDING, BUT NOT LIMITED TO, PERSONAL INJURY, AND SPECIAL, INCIDENTAL AND CONSEQUENTIAL DAMAGES) IN ANY WAY CONNECTED WITH THE EQUIPMENT, ITS OPERATION OR USE OR ANY DEFECT OR FAILURE THEREOF OR A BREACH OF SUNBELT'S OBLIGATIONS HEREIN.

8. **RELEASE AND INDEMNIFICATION.** TO THE FULLEST EXTENT PERMITTED BY LAW, CUSTOMER INDEMNIFIES, RELEASES, HOLDS SUNBELT ENTITIES HARMLESS AND AT SUNBELT'S REQUEST DEFENDS SUNBELT ENTITIES (WITH COUNSEL APPROVED BY SUNBELT), FROM AND AGAINST ALL LIABILITIES, CLAIMS, LOSSES, DAMAGES, AND EXPENSES (INCLUDING ATTORNEYS' AND/OR LEGAL FEES AND EXPENSES) HOWEVER ARISING OR INCURRED IN CONNECTION WITH ANY INCIDENT, DAMAGE TO PROPERTY, INJURY OR DEATH OF ANY PERSON, CONTAMINATION OR ALLEGED CONTAMINATION OR VIOLATION OF LAW OR REGULATION CAUSED BY OR CONNECTED WITH THE (a) USE, POSSESSION OR CONTROL OF THE EQUIPMENT DURING THE RENTAL PERIOD OR (b) BREACH OF THIS CONTRACT, WHETHER OR NOT CAUSED IN PART BY THE ACTIVE OR PASSIVE NEGLIGENCE OR OTHER FAULT OF ANY PARTY INDEMNIFIED HEREIN AND ANY OF THE FOREGOING ARISING OR IMPOSED IN ACCORDANCE WITH THE DOCTRINE OF STRICT OR ABSOLUTE LIABILITY. CUSTOMER ALSO AGREES TO WAIVE ITS WORKERS' COMPENSATION IMMUNITY TO THE EXTENT APPLICABLE. CUSTOMERS INDEMNITY OBLIGATIONS SHALL SURVIVE THE EXPIRATION OR TERMINATION OF THIS CONTRACT. All of Customer's indemnification obligations under this paragraph shall be joint and several.

9. **INSURANCE.** During the Rental Period, Customer shall maintain, at its own expense, the following minimum insurance coverage: (a) general liability insurance of not less than \$1,000,000 per occurrence, including coverage for Customer's contractual liabilities herein such as the release and indemnification clause contained in Section 8; (b) property insurance against loss with all risks to the Equipment, in an amount at least equal to the MSRP thereof, unless RPP is elected and paid for at the time of rental; (c) worker's compensation insurance as required by law; and (d) automobile liability insurance (including comprehensive and collision coverage, and uninsured/uninsured motorist coverage). In the same amount set forth in subsections (a) and (b), if the Equipment is to be used on any roadway, Sunbelt policies shall be primary, non-contributory, on an occurrence basis, contain a waiver of subrogation, name Sunbelt and its agents as additional insured (including an additional named insured) and has power, and provide for Sunbelt to receive at least 30 days prior written notice of any cancellation or material change. Any insurance that excludes damage or overruns to benefits. Customer shall provide Sunbelt with certificates of insurance evidencing the coverage required above prior to any rental and any time upon Sunbelt's request. To the extent Sunbelt Entities carry any insurance, Sunbelt Entities' insurance will be considered excess insurance. The insurance required herein does not relieve Customer of its responsibilities, indemnification, or other obligations provided herein, or for which Customer may be liable by law or otherwise.

10. **RENTAL PROTECTION PLAN.** Customer's repair or replacement responsibility in Sections 5 and 6 is modified by the RPP and Sunbelt shall limit the amount Sunbelt collects from Customer for the Equipment loss, damage or destruction to the following amounts for each piece of Equipment: (a) 10% of the MSRP for Lost Equipment, up to a maximum of \$50 per piece of Equipment; (b) 10% of the repair charges for accidental or accidental damage to Equipment, up to a maximum of \$50 per piece of Equipment; (c) charges in excess of \$50 per piece for the repair and (d) nothing for the rental charges which would otherwise accrue during the period when damaged or destroyed Equipment is being repaired or replaced by Sunbelt or Lost Equipment is being replaced; provided however, the foregoing RPP liability reduction only applies if the Conditions are satisfied and an Exclusion does not apply. The RPP is NOT INSURANCE and does NOT protect Customer from liability to Sunbelt or others arising out of possession, control or use of the Equipment, including injury or damage to persons or property. The RPP IS A CONTRACTUAL MODIFICATION OF CUSTOMERS LIABILITY. All of the following "Conditions" must be satisfied for the RPP and the corresponding liability reduction to apply: (a) Customer accepts the RPP in advance of the rental; (b) Customer pays 15% of the gross rental charges as the fee for the RPP (the applicable sales tax); (c) Customer fully complies with the terms of this Contract; (d) Customer's current claim at the time of the loss, theft, damage or destruction of the Equipment; and (e) none of the Exclusions apply. Customer assumes the Exclusion risks, meaning that if any Exclusion occurs the RPP does NOT reduce the liability of Customer to Sunbelt for the loss, theft, damage or destruction resulting from such Exclusion. "Exclusions" shall include loss, theft, damage or destruction of the Equipment: (i) due to intentional misuse; (ii) caused by Lost Equipment not returned by Customer to the police within 48 hours of discovery, and substituted by a written police report (temporarily delivered to

Sunbelt) (Y) due to Acts of God, such as floods, wind, storms or earthquakes; and (Z) accessories or Equipment for which Customer is not charged the RPP fee. THE EXCLUSIONS REMAIN THE LIABILITY OF CUSTOMER AND ARE NOT MODIFIED BY THE RPP. Notwithstanding anything to the contrary in this Contract, if Lost Equipment is later recovered, Sunbelt retains ownership of the Equipment regardless of any payment made by Customer or Customer's insurance company with respect to such Equipment, all of which payments are non-refundable. Customer agrees to promptly return any Equipment that is recovered. Sunbelt shall be subrogated to Customer's rights to recover against any person or entity relating to any loss, theft, damage or destruction to the Equipment. Customer shall cooperate with, assign Sunbelt all claims and proceeds arising from such loss, theft, damage or destruction, execute and deliver to Sunbelt whatever documents are required and take all other necessary steps to secure in Sunbelt such claims, at Customer's expense.

11. **RENTAL RATES.** The total charges specified in this Contract are: (a) estimated based upon Customer's representation of the estimated Rental Period identified on the front side hereof (rental rates beyond the estimated Rental Period may change); and other information conveyed by Customer to Sunbelt; and (b) for the Equipment a use for One Shift, unless otherwise noted. Weekly and 4 week rental rates shall not be prorated. Rental charges accrue during Saturdays, Sundays and holidays. The rental rates do not include and Customer is responsible for: in addition to all rental rates, and other charges shown in this Contract, (i) all consumables, fees, licenses, permits and future taxes and any other governmental charges based on Customer's possession and/or use of the Equipment, including additional fees for more than One Shift use; (ii) delivery and pick-up charges to and from the Store, including but not limited to any fuel, transportation, delivery, pickup and surcharge fees listed in this Contract; (iii) maintenance, repairs and replacements to the Equipment as provided herein; (iv) a cleaning fee if required; (v) miscellaneous charges, such as fees for lost keys; (vi) fuel used during the Rental Period and for refueling Equipment as described below; (vii) fines for use of dyed diesel fuel on on-road Equipment; and (viii) an Environmental Fee (described below). The convenience charge for off-road diesel fuel does not include governmental motor fuel taxes or charges. Sunbelt collects these fees as revenue and uses them at its discretion.

12. **PAYMENT.** Customer shall pay accounts due, without any offsets, in full at the time of rental, unless Sunbelt approves PAYMENT. Customer's executed credit application (credit customers must pay upon receipt of Sunbelt's invoice. Customer must notify Sunbelt in writing of any disputed amounts, including credit card charges, within 15 days after the receipt of the invoice; and Customer shall be deemed to have irrevocably waived its right to dispute such amounts. At Sunbelt's discretion, any credit account with a delinquent balance may be placed on a cash basis; deposits may be required and the Equipment may be picked up without notice. Due to the difficulty in facing actual damages caused by late payment, Customer agrees that a service charge equal to the lesser of 1.5% per month or the maximum rate permitted by law shall be assessed on all delinquent accounts, until paid in full. Customer shall pay a fee of \$75 for each check returned for lack of sufficient funds to compensate Sunbelt for its overhead for processing returned payment. Deposits will only be returned after all amounts are paid in full. Customer agrees that if a credit card is presented to pay for charges or to guarantee payment, Customer authorizes Sunbelt to charge the credit card statements shown on this Contract and charges subsequent to incurred by Customer including but not limited to, loss of or damage to the Equipment and extension of the Rental Period.

13. **RETURN OF EQUIPMENT.** Sunbelt may terminate this Contract at any time, for any reason. At the end of the Rental Period, the Equipment shall be returned to Sunbelt in the same condition it was received, less Ordinary Wear and Tear and free of any hazardous materials and contaminants. Customer will continue to be responsible for rental and other charges after the Rental Period if the Equipment is not returned in the condition required herein. If Sunbelt delivered the Equipment to Customer, Customer shall notify Sunbelt that the Equipment is ready to be picked up at the Site Address and obtain a Pick-Up Number, which Pick-Up Number Customer should keep as proof of the call; provided Customer remains liable for any loss, theft, damage to or destruction of the Equipment until Sunbelt confirms that the Equipment is returned in the condition required herein. Customer will not be charged the rental charges after the due date the Pick Up Number is given, provided Customer has otherwise complied with this Contract. No pickups occur on Sundays or statutory holidays; Saturday pickups are dependent on specific Store hours. If Customer picked up Equipment, Customer shall return Equipment to the same Store during that Store's normal business hours. If the Equipment is not returned by the estimated end of the Rental Period specified in the front side hereof, Customer agrees to pay the applicable rental rate for the Equipment until the end of the Rental Period.

14. **PURCHASES.** If this Contract identifies any Equipment, materials or other items that are to be purchased by Customer, Sunbelt shall deliver such items to Customer on an "AS IS, WHERE IS" basis, with all faults and without any warranties (other than manufacturer warranties, if any) in consideration for Customer's payment to Sunbelt of the full purchase price of the item. Sunbelt retains title to the item until Customer has paid in full.

15. **DEFAULT.** Customer shall be in default if Sunbelt deems that (a) Customer has not followed the terms of this Contract; (b) Customer has violated any provision of this Contract; (c) Customer has a delinquent account, or has failed to return the Equipment, or has failed to return the Equipment to its creditors under any insolvency legislation, ceased to carry on business, or lost its assets seized by any creditor; (d) fails to insure the Equipment as required, or otherwise places the Equipment at risk; (e) fails to return Equipment immediately upon Sunbelt's demand; or (f) is in default under any other contract with Sunbelt. If a Customer default occurs, Sunbelt shall have, in addition to all rights and remedies at law or in equity the right to repossess the Equipment without judicial process or prior notice. Customer shall pay all of Sunbelt's costs, including reasonable costs of collection, court costs, attorney and legal fees, incurred in exercising any of its rights or remedies herein. The use of false identification to obtain Equipment or the failure to return Equipment by the end of the Rental Period may be considered theft, subject to criminal prosecution and civil liability where permitted, pursuant to applicable laws. Sunbelt shall be liable due to seizure of Equipment by order of governmental authority. CUSTOMER WAIVES ANY RIGHT OF ACTION AGAINST SUNBELT ENTITIES FOR SUCH REPOSSESSION.

16. **ENVIRONMENTAL FEE.** To promote a clean and sustainable environment, Sunbelt takes various measures to comply with applicable environmental regulations, as well as with Sunbelt's own policies. Sunbelt also incurs a wide range of environmental related expenses (such as direct and indirect). These expenses may include waste disposal, construction and maintenance of cleaning facilities, acquisition of more fuel efficient equipment, lower costs, administration costs, etc. To help defray these and other costs, Sunbelt charges an environmental fee, plus applicable taxes directly to Customer's account with each rental. The fee is not a tax or governmentally mandated charge. The fee is not designated for any particular use or placed in an escrow account, but is a fee that Sunbelt collects as revenue and uses at its discretion.

17. **FUEL.** For Equipment that uses fuel, Customer has three options: (a) Prepay the Sunbelt Fuel Option. Customer may purchase a full tank of fuel for the Equipment at the start of the rental, in which case a "convenience charge" will appear on this Contract (calculated by multiplying the estimated fuel capacity of Equipment by the Prepay per gallon rate). As an added benefit, Customer may return the Equipment full of fuel and the convenience charge will be refunded (unless it is not returned full). Customer will not obtain any credit for fuel left in the Equipment upon return; (b) Return Full Tank Option. If Customer returns Equipment with less fuel than when received, Customer shall pay a refund charge (calculated by multiplying gallons required to refill tank with fuel to level when received by the Pay on Return per gallon rate); and (c) Return Empty Option. If Customer returns the Equipment with at least one week for as when received (Sunbelt Equipment comes with a full tank of fuel, but not all), no fuel charge will be assessed. The cost of Customer refueling Equipment fuel will generally be lower than the Prepay ("No Sweat") Fuel Option or the Pay on Return Option; however these options also allow for the convenience of not refueling.

18. **LIMITATION OF SUNBELT'S LIABILITY IN CONSIDERATION OF THE RENTAL OF EQUIPMENT.** CUSTOMER AGREES THAT SUNBELT'S LIABILITY UNDER THIS CONTRACT, INCLUDING ANY LIABILITY ARISING FROM SUNBELT'S, SUNBELT ENTITIES, OR ANY THIRD PARTY'S COMPARATIVE, CONCURRENT, CONTRIBUTORY, PASSIVE OR ACTIVE NEGLIGENCE OR OTHER ACTS AS A RESULT OF ANY STRICT OR ABSOLUTE LIABILITY SHALL NOT EXCEED THE TOTAL RENTAL CHARGES PAID BY CUSTOMER UNDER THIS CONTRACT.

19. **JURY TRIAL WAIVER.** IN ANY DISPUTE ARISING OUT OF, IN CONNECTION WITH, OR IN ANY WAY PERTAINING TO THIS CONTRACT, CUSTOMER AND SUNBELT HEREBY KNOWINGLY, VOLUNTARILY AND INTENTIONALLY WAIVE ANY RIGHT TO A TRIAL BY JURY. THIS WAIVER BEING A MATERIAL INDUCEMENT TO ENTERING INTO THIS CONTRACT.

20. **ARBITRATION AGREEMENT AND CLASS ACTION WAIVER.** AT THE ELECTION OF CUSTOMER OR SUNBELT ANY DISPUTE ARISING OUT OF, IN CONNECTION WITH OR IN ANY WAY PERTAINING TO THIS CONTRACT SHALL BE SETTLED BY ARBITRATION BROUGHT IN THE PARTIES' INDIVIDUAL CAPACITY AND NOT AS A PLAINTIFF IN A PURPORTED CLASS OR REPRESENTATIVE CAPACITY, ADMINISTERED BY THE AMERICAN ARBITRATION ASSOCIATION UNDER ITS COMMERCIAL ARBITRATION RULES OR BY JAMS PURSUANT TO ITS STREAMLINED ARBITRATION RULES AND PROCEDURES AND JUDGMENT ON THE AWARD RENDERED BY THE ARBITRATOR(S) MAY BE ENTERED IN ANY COURT HAVING JURISDICTION THEREOF. THERE SHALL BE NO RIGHT OR AUTHORITY FOR ANY CLAIMS TO BE ARBITRATED OR TRIED ON A CLASS ACTION BASIS.

21. **COMPLIANCE WITH EXPORT AND IMPORT LAWS.** Removal of the Equipment from the United States ("U.S.") is prohibited under this Contract. If Customer desires or causes the transport and/or operation of the Equipment outside of the U.S., Customer must (a) obtain Sunbelt's consent prior to taking such action, and (b) execute an agreement to this Contract, which amendment is incorporated herein. If Customer exports or re-exports without complying with the above sentence, Customer agrees that (i) the Equipment is subject to and must comply with all applicable export laws, including but not limited to the Export Administration Regulations; and (ii) Customer is responsible for: (A) determining whether and obtaining if necessary, export or re-export licenses or other authorizations as required prior to; exporting or re-exporting the Equipment; (B) obtaining any required documentation necessary for return of the Equipment; and (C) ensuring no unauthorized transfers or diversions of the Equipment occur. Refer to www.bis.doc.gov for information.

22. **GOVERNING LAW.** The parties expressly and irrevocably agree: (a) this Contract, including any related text claims, shall be governed by the laws of South Carolina, without regard to any conflicts of law principles and (b) if any Section of this Contract is prohibited by any law and Section shall be ineffective to the extent of such prohibition without invalidating the remaining Sections.

23. **AUSCANCEMENT.** This Contract, together with any Customer executed credit application, constitutes the entire agreement of the parties regarding the Equipment and may not be modified except by written amendments signed by the parties. Customer's obligations hereunder shall survive the termination of this Contract. This Contract and all of Customer's rights in and to the Equipment are subordinate to all rights in and interest of all persons (including Sunbelt's lenders) who have rights in the Equipment. Headings are for convenience only. To the extent that any terms in this Contract conflict, the parties agree that the more specific terms remain. A copy of this Contract shall be valid as the original. Any failure by Sunbelt to insist upon strict performance of any Section of this Contract shall not be construed as a waiver of the right to demand strict performance in the future. Customer and the person signing this Contract represent that: (a) they have full authority to execute, deliver and perform this Contract and (b) this Contract constitutes a legal, valid and binding obligation of Customer enforceable in accordance with its terms. When Customer is a buyer of Equipment, they acknowledge that Sunbelt has assigned to it all of its obligations in the agreement to sell the asset(s) described herein to Sunbelt Rentals Exchange, Inc., a real-estate intermediary, as part of Section 10(b) exchange, and Customer shall make the payee "Sunbelt Rentals Exchange, Inc."



SYSTEM SCAFFOLD QUOTE

Branch #72
1647 KING STREET EXTENSION
CHARLESTON, SC 29405-9330
Office: (843) 747-9158
www.sunbeltrentals.com

Watson Knight
Cell: (843) 514-6482
Watson.Knight@sunbeltrentals.com

CHARLESTON SCAFFOLDING PC072

November 04, 2016

Customer: **BBC-CHARLOTTE (#187039)**
1930 CAMDEN ROAD
CHARLOTTE, NC 28203

BBC-Charlotte / Two Transformer Protection
(Active RO)
QUO-53520-N3F2S8
11/8/2016 to 12/6/2016

**Marion Square Hotel-
Charleston**
Job#1302600
404 King Street
Charleston, SC 29403

Dan Ricci
(704) 400-2290
Dricci@ba-fourbeattyus.com

Introduction

Thank you for allowing Sunbelt the opportunity to quote your scaffolding and and OHP needs

Specifications

This bid is to provide top and side protection for two transformers. Each Transformer's protection will consist of systems scaffolding 10' wide x 21' long x 10' high, BBC Overhead protection on the top and only 3/4" plywood secured and used on the sides.

Scope

Sunbelt to mobilize, park and stage the equipment on the Hudson Street Entrance as close as possible to the work area. Sunbelt will start the install of the transformer protection and once complete will remove the excess equipment. Customer to inspect and sign for the material at this time. This scaffolding/protection is not to be used or considered to be as a personnel work platform.

Customer Responsibility

Customer is responsible for:

- Providing the parking and staging area for the equipment and equipment truck as close as possible to the work area or the means to mobilize the material to and from the work area during the erection and dismantle.
- all permits and licenses required for this work to be performed

General

Straight time and standby

This bid is based on straight time hours only, Monday thru Friday, 7am-3:30pm, with no overtime, weekend or holiday hours included

Any standby time or delays not caused by Sunbelt directly will be billed the customer on a time and material basis.

No Engineering is included in this bid

Pricing Details

Equipment Rental: (4 week min.)	\$1,427.52 *
Daily Rental: (after Initial 4 weeks)	\$50.98 *
Erection Price:	\$1,627.78 *
Dismantle Price:	\$1,331.82 *
Move Price: (see above)	\$0.00 *
Misc./Sales: (see above)	\$1,430.00 *
Rental Protection Plan:	\$0.00
Freight: (P/U-Del)	\$370.00 *

Quote Total:

\$6,187.12*

*Plus applicable taxes

Terms and Conditions

PROJECT CONTRACT SPECIFICATIONS (a) Customer must be present at time of delivery to sign, inspect, count, and accept responsibility of equipment via Sunbelt Erection Inspection Checklist; (b) If Customer dismantles equipment, any equipment missing is Customer's responsibility and will be charged at replacement cost; (c) Show PE Stamped Drawings be required, additional charges apply; All such engineering work is limited to the Scaffold Design and Leg Loads and does not include analysis of job site structures; (d) Price herein assumes Sunbelt shall be exempted from participating in OSHA/OSHA requirements. If not exempted, additional charges apply; (e) Our quoted price is based on the written terms of this Quote. If we are requested to sign an agreement you prepare, this Quote in its entirety or, must be incorporated into that agreement. If there is a conflict between your agreement and the written and included terms of our Quote, the terms of our Quote shall govern; (f) Both parties shall accept this Quote within 30 days of Date of Quote (above) or, if may, at our option, be considered null and void; (g) It is a condition precedent to work being scheduled that this Quote is signed and received by the Scaffold Services Branch listed below; (h) A low two (2) week lead times for scheduling all labor phases; (i) All work will be performed during straight time hours on day shift, Monday through Friday 7:00 am to 3:30 pm, unless specifically noted otherwise; (j) All work beyond the scope of work outlined above will be reimbursed based on Sunbelt Rentals, Inc. current Man Hour Rates. These rates shall be made available upon request. The Customer will be responsible for verifying all time sheets. Delays (over 30 minutes), rework, ratons and unacceptable work conditions not attributable to Sunbelt, will be charged at the current Man-Hour Rates and may include a 4 hour minimum and/or additional travel time charges; (k) Scaffolds to be erected to meet or exceed OSHA 1926.451 Subpart L (or as indicated herein).

SCAFFOLD PRICE EXCLUSIONS. The pricing of this Quote does not include the following, unless specifically described on the front of this Quote: (a) expenses incurred if the Customer's or the Job Site Physical Address safety requirements exceed State and Federal codes; (b) (de)boards, screens and nets; (c) costs associated with providing a firm, compacted and level grade for all scaffolding; (d) any foundations or re-shoring required below sidewalk level or sub-basement level; (e) tarpaulins or other sheeting (scaffolding must be modified to withstand the additional wind loads, with such sheeting); (f) any costs for proof of drug testing or employment drug screening whether it be pre-employment, site required, or otherwise; (g) moving rolling towers; (h) lodging, meals, travel transportation, or other extraordinary expenses; (i) performance bond, and/or OSHA/OSHA requirements, if required; (j) sales taxes, use taxes, or tariffs; (k) sealed shop drawings or PE Stamped Drawings, if required; and (l) any other costs incurred due to the Job Site Physical Address conditions, delays, or safety considerations not attributed to Sunbelt will be invoiced to Customer on a time and material basis.

CUSTOMER RESPONSIBILITIES. Unless otherwise noted herein, Customer shall be responsible for the following, all at Customer's sole expense: (a) compliance with all laws and regulations related to the proper possession and use of scaffolding; (b) provide qualified, experienced and adequate supervision of any and all users of the scaffolding including a competent person; (c) provide all training of all users as required by 29CFR1910, 29CFR1926, and other applicable local, state, and federal governing bodies, and all accepted industry standards; (d) a scaffold users have read and understand the Codes of Safe Practices; (e) provide a firm, compacted and level grade for all scaffolding; (f) provide suitable crane and forklift support, or other material handling, as needed for the Work; (g) verify that the existing structure will safely support the additional vertical and horizontal loading from the scaffold; (h) repair all holes in existing structure left as a result of concrete anchors or other ties necessary to stabilize scaffold structure; (i) arrange with the Utilities Authority for all necessary safeguards, notifications and process lock-outs prior to erection date; (j) provide electric power and lighting to suit Sunbelt requirements; (k) supply any necessary flagmen or temporary barriers or signs, etc.; (l) if Sunbelt will be working in the vicinity of water, necessary boathmen and boat as defined in OSHA regulations; (m) any ground protection, i.e. for furniture, machines, carpets, landscaping, etc.; (n) toilets and wash facilities; (o) a firm, compacted and level grade laydown yard during both erection and dismantling; (p) security of Sunbelt equipment and materials with a laydown yard; (q) restoration of the laydown yard following completion of the Work; (r) all permits; (s) Falling Object Protection and any citations and/or fines OSHA may impose for failure to do so; (t) Customer's fall protection systems and methods during the use of the scaffolding that comply with all laws and be at Customer's risk; (u) assume all risks associated with the possession, custody and operation of and full responsibility for, the equipment, including but not limited to, personal injury, death, rental charges, losses, damages and destruction, including customer transport, loading and unloading; and (v) maintain general and auto liability insurance of not less than \$2,000,000 per occurrence, including coverage for Customer's contractual liabilities herein (such as the indemnification clause); property insurance against loss by all risks to the equipment, in an amount at least equal to the fair market value thereof; and worker's compensation insurance. Such policies shall be primary (and not on an excess basis), on an occurrence basis, name Sunbelt as an additional insured and less payee. Customer shall provide Sunbelt with certificates of insurance evidencing the coverage required above prior to any rental and any time upon Sunbelt's request.

SCAFFOLD CONDITIONS AND ASSUMPTIONS. Unless otherwise specified herein to the contrary: (a) the scaffolding will be erected and dismantled one time only; (b) any alterations not described herein will be charged at the applicable time and material rates; (c) any overtime work shall be invoiced at the applicable time and material rates; and (d) the work performed by Sunbelt will be done in accordance with applicable state and federal codes.

INDEMNIFICATION. Sunbelt indemnifies, releases, defends and holds Customer harmless from and against any third party claims including any and all liabilities, losses, damages, claims, penalties, fines and expenses, including attorney's fees, for any damages to property and/or persons including death ("Claims") to the proportionate extent caused by Sunbelt or any of its contractors, suppliers, officers, agents, or employees negligent acts or omissions in the performance of this Agreement. Customer will (i) give Sunbelt prompt notice of any such Claim, and (ii) at Sunbelt's reasonable request, cooperate with Sunbelt in the defense and settlement of the Claim. Customer indemnifies, releases, defends and holds Sunbelt harmless from and against any third party claims including any and all Claims to the proportionate extent caused by Customer's or any of its contractors, suppliers, officers, agents, or employees negligent acts or omissions in the performance of this Agreement. Sunbelt will (i) give Customer prompt notice of any such Claim, and (ii) at Customer's reasonable request, cooperate with Customer in the defense and settlement of the Claim. Notwithstanding anything contained in any agreement between the parties to the contrary, Sunbelt's requirement to provide additional insured, primary, non-contributory and waiver of subrogation status shall be limited to the extent of Sunbelt's indemnification obligations herein.

SCAFFOLD CHANGE ORDERS. If Customer requests a change in the Work, Sunbelt shall send Customer's "Point of Contact" a change order request in written form. Customer shall return a signed copy of the change order to Sunbelt; provided however, if no objection to the change order is received by Sunbelt, the change order shall be deemed approved by Customer.

INSPECTION AND ACCEPTANCE. On Customer's acceptance of the erected scaffold, Customer will be responsible for the maintenance, control, proper use and supervision of the scaffold until such time as the scaffold is fully dismantled and returned to Sunbelt for removal from the Job Site.

OTHER TERMS. The remaining provisions of this Quote are shown on the following page and incorporated herein by reference and can also be found at: <https://www.sunbeltrentals.com/services/scaffold/termsandconditions>

Quote Acceptance

BBC-CHARLOTTE
Dan Ricci

Acceptance Signature of Customer's Authorized Representative

Date

Sunbelt Rentals, Inc.
Watson Knight

Acceptance Signature of Sunbelt Rentals Authorized Employee

Date



PC#: 006
2411 CLEMENTS FERRY RD
CHARLESTON, SC 29492-7734
843-881-4945

SUNBELT RENTALS, INC.

Salesman: 00000
Typed By: MSPORDER

Job Site:

MARION SQUARE HOTEL-CHARLESTON
404 KING STREET
CHARLESTON, SC 29403 6422

C#: 704-319-4000 J#: 919-316-0986

Customer: 187039

BBC-CHARLOTTE
1930 CAMDEN ROAD
CHARLOTTE, NC 28203

QUOTE

Contract #.. 60919822
Contract dt. 6/08/16
Date out.... 6/13/16 8:00 AM
Est return.. 7/11/16 8:00 AM
Job Loc..... 404 KING STREET, CHARLESTON
Job No..... 1 - MARION SQUARE HO
P.O. #..... QUOTE
Ordered By.. Dale, Marty
NET DUE UPON RECEIPT

QTY	EQUIPMENT #	Min	Day	Week	4 Week	Amount
1.00	6K 36' SHOOTING BOOM FORKLIFT 0560320	255.00	255.00	638.00	1488.00	1488.00
1.00	2 TON ELECTRIC CHAIN HOIST 120V 1PH 0810415	77.40	77.40	265.50	711.00	711.00
1.00	FORKLIFT LIFT & TOW ATTACHMENT 1560135	64.00	64.00	88.00	230.00	230.00
*** EQP MSG ***						
** ALWAYS REFER TO THE EQUIPMENT LOAD CHART AS TO ACTUAL LIFTING						
CAPACITIES IN ALL THE EQUIPMENT'S LOAD RANGES **						
WARNING - FORKLIFTS ARE NOT TO BE USED FOR LIFTING PERSONNEL						
SALES ITEMS:						
Qty	Item number	Unit	Price			
1	DLPKSRCHG	EA	34.000			34.00
	TRANSPORTATION SURCHARGE					
1	ENVIRONMENTAL	EA	20.830			20.83
	ENVIRONMENTAL					
1	SCHERS	EA	44.640			44.64
	SC 3% HEAVY EQUIP. RENTAL SURCHARGE					
	DELIVERY CHARGE					200.00
	PICKUP CHARGE					200.00

Rate your rental experience www.sunbeltrentals.com/survey

IF THE EQUIPMENT DOES NOT WORK
PROPERLY, NOTIFY THE OFFICE AT ONCE

MULTIPLE SHIFTS OR
OVERTIME RATES MAY APPLY

CUSTOMER IS RESPONSIBLE FOR
ROUTING, DAMAGES AND REPAIRS

- The total charges are an estimate based on the estimated rental period and other information provided by Customer.
- Customer assumes all risks associated with the equipment during the Rental Period, including injury and damage to persons, property and the Equipment.
- Customer is responsible for and shall only permit properly trained, Authorized Individuals to use the Equipment.
- If the Equipment does not operate properly, is not suitable for Customer's intended use, does not have operating and safety instructions or Customer has any questions regarding use of the Equipment, Customer shall not use the Equipment and shall contact Sunbelt immediately.
- Equipment misuse or using damaged or malfunctioning Equipment may result in serious bodily injury or death and Customer agrees that Customer (i) assumes all risk associated hereunder, and (ii) indemnifies Sunbelt Entities for all claims or damages as a result of misuse or use of damaged or malfunctioning Equipment.
- Customer has received, read, understands and agrees to the estimated charges and all the terms on this page, plus all sections on the reverse side of this Contract ("Sections"), including Release and Indemnification in Section 8 and Environmental fee in Section 16, which can also be found at www.sunbeltrentals.com/rentalcontract. * Delivery/Pickup Surcharge fee explanation is available at www.sunbeltrentals.com/surcharge.
- Customer must contact Sunbelt to request pickup of Equipment, retain the Pick-Up Number given by Sunbelt and will be responsible for Equipment until actually retrieved by Sunbelt.
- Customer waives its right to a jury trial in any dispute as set forth in Section 19.
- At the election of Sunbelt or Customer, Customer agrees to submit every dispute to arbitration and waives any right to bring a class action as set forth in Section 20.

Customer is declining Rental Protection Plan (see reverse side for details) _____ (Customer Initials)

Customer Signature

Date

Name Printed

Delivered By

Date

*** www.sunbeltrentals.com ***

PDFSINGLS (Rev 12/10/15)

R - 1743



PC#: 006
2411 CLEMENTS FERRY RD
CHARLESTON, SC 29492-7734
843-881-4945

SUNBELT RENTALS, INC.

Salesman: 00000
Typed By: MSPORDER

Job Site:

MARION SQUARE HOTEL-CHARLESTON
404 KING STREET
CHARLESTON, SC 29403 6422

C#: 704-319-4000 J#: 919-316-0986

Customer: 187039

BBC-CHARLOTTE
1930 CAMDEN ROAD
CHARLOTTE, NC 28203

QUOTE

Contract #.. 60919822
Contract dt. 6/08/16
Date out.... 6/13/16 8:00 AM
Est return.. 7/11/16 8:00 AM
Job Loc..... 404 KING STREET, CHARLESTON
Job No..... 1 - MARION SQUARE HO
P.O. #..... QUOTE
Ordered By.. Dale, Marty
NET DUE UPON RECEIPT

QTY	EQUIPMENT #	Min	Day	Week	4 Week	Amount
-----	-------------	-----	-----	------	--------	--------

SALES ITEMS:

Qty	Item number	Unit	Price
-----	-------------	------	-------

Marty 803-210-3723 freight accounts for
chain hoist coming from industrial resou
rces and hook attachment from Savannah

Sub-total:	2928.47
Tax:	245.13
Total:	3173.60

All amounts are in USD

Rate your rental experience www.sunbeltrentals.com/survey

IF THE EQUIPMENT DOES NOT WORK
PROPERLY, NOTIFY THE OFFICE AT ONCE

MULTIPLE SHIFTS OR
OVERTIME RATES MAY APPLY

CUSTOMER IS RESPONSIBLE FOR
REFUELING, DAMAGES AND REPAIRS

1. The total charges are an estimate based on the estimated rental period and other information provided by Customer.
2. Customer assumes all risks associated with the Equipment during the Rental Period, including injury and damage to persons, property and the Equipment.
3. Customer is responsible for and shall only permit properly trained, Authorized Individuals to use the Equipment.
4. If the Equipment does not operate properly, is not suitable for Customer's intended use, does not have operating and safety instructions or Customer has any questions regarding use of the Equipment, Customer shall not use the Equipment and shall contact Sunbelt immediately.
5. Equipment misuse or using damaged or malfunctioning Equipment may result in serious bodily injury or death and Customer agrees that Customer (i) assumes all risk associated thereunder, and (ii) indemnifies Sunbelt Entities for all claims or damages as a result of misuse or use of damaged or malfunctioning Equipment.
6. Customer has received, read, understands and agrees to the estimated charges and all the terms on this page, plus all sections on the reverse side of this Contract ("Sections"), including Release and Indemnification in Section 9 and Environmental Fee in Section 16, which can also be found at www.sunbeltrentals.com/rentalcontract. * Delivery/Pickup Surcharge fee explanation is available at www.sunbeltrentals.com/surcharge.
7. Customer must contact Sunbelt to request pickup of Equipment, retain the Pick-Up Number given by Sunbelt and will be responsible for Equipment until actually retrieved by Sunbelt.
8. Customer waives its right to a jury trial in any dispute as set forth in Section 19.
9. At the election of Sunbelt or Customer, Customer agrees to submit every dispute to arbitration and waives any right to bring a class action as set forth in Section 20.

Customer is declining Rental Protection Plan (see reverse side for details) _____ (Customer Initials)

Customer Signature

Date

Name Printed

Delivered By

Date

** www.sunbeltrentals.com **

PDFS/NOL3 (Rev 12/10/15)

R - 1744

SUNBELT ADDITIONAL TERMS AND CONDITIONS

1. **DEFINITIONS.** "Authorized Individuals" are those individuals that Customer directly or indirectly allows to use the Equipment, are properly trained to use the Equipment and are not under the influence of any drugs, alcohol, substances or otherwise impaired. "Customer" is identified on the front side hereof and includes any of its representatives, agents, officers, employees or anyone signing this Contract on its behalf. "Equipment" is the equipment and/or services identified on the front side hereof, together with all implements, repairs, additions, attachments and accessories and all future Equipment treated "Incidents" is any fire, climate, theft, or other, casualty, loss, vandalism, injury, death or damage to person or property claimed by any person or entity that appears to have occurred in connection with the Equipment. Equipment is considered "Lost" when it is either stolen, its location is unknown or Customer is unable to recover it for a period of 30 days. "MSRP" is the Equipment manufacturer's suggested list price on or about the date of the incident relating to the Equipment. "One Shift" means not more than 8 hours per day and 40 hours per week. "Ordinary Wear and Tear" means normal deterioration considered reasonable in the equipment rental industry for One Shift use. "Pick-Up Number" is the number Customer obtains from Sunbelt evidencing the Customer's call to pick up Equipment. "Rental Period" commences when the Equipment is delivered to Customer at the Site Address and continues until the Equipment is returned to the Store or picked up by Sunbelt during normal business hours, provided Customer has not otherwise complied with this Contract. "RPP" is the rental protection plan described in Section 10. "Site Address" is the location that Customer represents the Equipment will be located during the Rental Period identified on the front side hereof. "Store" is the Sunbelt location identified on the front side hereof. "Sunbelt" is Sunbelt Rentals, Inc., "Sunbelt Entities" is Sunbelt and its affiliated companies, their respective officers, directors, employees and agents.

2. **TERMS.** Customer's rental of Equipment is evidenced upon Customer's agreement with this Contract and all of its terms. Customer's execution of this Contract or taking possession of the Equipment shall be deemed acceptance of the terms herein. All of the terms herein (including on the front side of this Contract) are incorporated into this and all past and future contracts between Sunbelt and Customer upon Customer's receipt of Sunbelt's Equipment under these contracts. Any reference to Customer's purchase order or other Customer document to other terms that shall control this transaction shall be void. Customer rents the Equipment from Sunbelt pursuant to this Contract. Customer shall pay Sunbelt the rental rates (including any minimum rental on the front side hereof) and other charges described herein when due, return the Equipment to Sunbelt as required herein and otherwise comply with this Contract. This Contract is a true lease. The Equipment (a) is and shall remain the personal property of Sunbelt and (b) shall not be affixed to any other property.

3. **PERMITTED USE.** Customer agrees that Sunbelt has no control over the manner in which the Equipment is operated during the Rental Period by Customer or any third party of which Customer implicitly or explicitly permits. Customer warrants that: (a) prior to each use, Customer shall inspect the Equipment to confirm that it is in good condition, without defects, includes mandatory decals and operating and safety instructions and is suitable for Customer's intended use; (b) any agent acting as the Site Address is authorized to accept delivery of the Equipment (and if Customer requests, Customer authorizes Sunbelt to leave the Equipment at the Site Address without delivery of written receipt); (c) Customer shall immediately notify Sunbelt if the Equipment is Lost, damaged, unsafe, disabled, malfunctioning, leveled upon, threatened with seizure, or if any incident occurs; (d) Customer has received from Sunbelt all information needed or requested regarding the operation of the Equipment; (e) Sunbelt is not responsible for providing operator or other training unless Customer specifically requests in writing and Sunbelt agrees to provide such training (Customer being responsible to obtain all training that Customer desires prior to the Equipment's use); (f) only Authorized Individuals shall use and operate the Equipment; (g) the Equipment's use shall be in a careful manner, in compliance with all operating and safety instructions provided on, in or with the Equipment and all applicable federal, state and local laws, permits and licenses, including but not limited to, 35TSA, as revised; and (h) the Equipment shall be kept in a secure location.

4. **PROHIBITED USE.** Customer shall not (a) alter or cover up any decals or insignia on the Equipment or remove any operational or safety equipment or instructions (b) assign its rights under this Contract; (c) move the Equipment from the Site Address without Sunbelt's written consent; (d) use the Equipment in a negligent, illegal, unauthorized or abusive manner, or in any publication (print, audiovisual or electronic); or (e) allow the use of the Equipment by any unauthorized individual. (Customer acknowledging that the Equipment may be dangerous if used improperly or by untrained parties).

5. **MAINTENANCE.** Customer shall perform routine maintenance on the Equipment, including routine inspections and maintenance of fuel and oil levels, ground, ending system, lights, batteries, cutting edges, and clearing of obstructions with the manufacturer's specifications. All other maintenance or repairs may only be performed by Sunbelt or its agent, but Sunbelt has no responsibility during the Rental Period to inspect or perform any maintenance or repairs unless Customer requests a service call. If Sunbelt determines that repairs to the Equipment are needed, other than Ordinary Wear and Tear, Customer shall pay the full repair charges and rental of the Equipment until the repairs are completed. Sunbelt has the right to inspect the Equipment wherever located. Customer has the authority to and hereby grants Sunbelt and its agents the right to enter the physical location of the Equipment for the purposes set forth herein. Sunbelt shall be responsible for repairs needed because of Ordinary Wear and Tear. Customer agrees that repair or replacement of the Equipment is Customer's exclusive remedy for Sunbelt's breach of this Section. Notwithstanding Sunbelt's service commitment, Sunbelt shall have no obligation if Customer breaches this Contract to stop the Rental Period, commence repairs or return other equipment to Customer until Customer or its agent agrees to pay for such charges.

6. **CUSTOMER LIABILITY DURING THE RENTAL PERIOD.** CUSTOMER ASSUMES ALL RISK ASSOCIATED WITH THE POSSESSION, CONTROL, OR USE OF THE EQUIPMENT INCLUDING BUT NOT LIMITED TO, PERSONAL INJURY, DEATH, RENTAL CHARGES, THEFT, LOSSES, DAMAGES AND DESTRUCTION, INCLUDING CUSTOMER TRANSPORTATION, LOADING AND UNLOADING, WHETHER OR NOT THE CUSTOMER IS AT FAULT. After an Incident, Customer shall: (a) immediately notify Sunbelt, the police, if necessary and Customer's insurance carrier; (b) secure and maintain the Equipment and the surrounding premises in the condition existing at the time of such incident, until Sunbelt or its agents investigate; (c) immediately submit copies of all police or other third party reports to Sunbelt; and (d) as applicable, pay Sunbelt, in addition to other sums due herein the rental rate for Equipment until the repairs are completed or Equipment replaced plus either (i) the MSRP or (ii) the full charges of repairs of damaged Equipment. Accrued rental charges shall not be applied against these amounts. Sunbelt shall have the immediate right, but not obligation, to reclaim any Equipment involved in any incident.

7. **NO WARRANTIES.** Sunbelt does not design or manufacture the Equipment and is not the agent of those that the SUNBELT DISCLAIMS ALL REPRESENTATIONS AND WARRANTIES, EXPRESS OR IMPLIED, WITH RESPECT TO THE EQUIPMENT, ITS DURABILITY, CONDITION MERCHANTABILITY OR FITNESS FOR ANY PARTICULAR PURPOSE. CUSTOMER ACKNOWLEDGES ACCEPTANCE OF THE EQUIPMENT ON AN "AS IS, WHERE IS" BASIS, WITH ALL FAULTS, AND WITHOUT ANY RECOURSE WHATSOEVER AGAINST SUNBELT ENTITIES. CUSTOMER ASSUMES ALL RISKS ASSOCIATED WITH THE EQUIPMENT AND RELEASES SUNBELT ENTITIES FROM ALL LIABILITIES AND DAMAGES, INCLUDING LOST PROFITS, PERSONAL INJURY AND SPECIAL, INCIDENTAL AND CONSEQUENTIAL DAMAGES IN ANY WAY CONNECTED WITH THE EQUIPMENT, ITS OPERATION OR USE ON ANY DEFECT OR FAILURE THEREOF OR A BREACH OF SUNBELT'S OBLIGATIONS HEREIN.

8. **RELEASE AND INDEMNIFICATION TO THE FULLEST EXTENT PERMITTED BY LAW.** CUSTOMER INDEMNIFIES, RELEASES, HOLDS SUNBELT ENTITIES HARMLESS AND AT SUNBELT'S REQUEST DEFENDS SUNBELT ENTITIES (WITH COUNSEL APPROVED BY SUNBELT), FROM AND AGAINST ALL LIABILITIES, CLAIMS, LOSSES, DAMAGES, AND EXPENSES (INCLUDING ATTORNEYS' AND/OR LEGAL FEES AND EXPENSES) HOWEVER ARISING OR INCURRED IN CONNECTION WITH ANY INCIDENT, DAMAGE TO PROPERTY, INJURY OR DEATH OF ANY PERSON, CONTAMINATION OR ALLEGED CONTAMINATION, OR VIOLATION OF LAW OR REGULATION CAUSED BY OR CONNECTED WITH THE (a) USE, POSSESSION OR CONTROL OF THE EQUIPMENT DURING THE RENTAL PERIOD OR (b) BREACH OF THIS CONTRACT, WHETHER OR NOT CAUSED IN PART BY THE ACTIVE OR PASSIVE NEGLIGENCE OR OTHER FAULT OF ANY PARTY INDEMNIFIED HEREIN AND ANY OF THE FOREGOING ARISING OR IMPOSED IN ACCORDANCE WITH THE DOCTRINE OF STRICT OR ABSOLUTE LIABILITY. CUSTOMER ALSO AGREES TO WAIVE ITS WORKERS' COMPENSATION IMMUNITY, TO THE EXTENT APPLICABLE. CUSTOMERS INDEMNITY OBLIGATIONS SHALL SURVIVE THE EXPIRATION OR TERMINATION OF THIS CONTRACT. All of Customer's indemnification obligations under this paragraph shall be joint and several.

9. **INSURANCE.** During the Rental Period, Customer shall maintain at least the following minimum insurance coverage: (a) general liability insurance of not less than \$1,000,000 per occurrence, including coverage for Customer's contractual liabilities herein such as the release and indemnification, based on terms set forth in Section 8; (b) property insurance against loss by all risks to the Equipment, in an amount at least equal to the MSRP of the Equipment, until RPP is elected and paid for at the time of rental; (c) worker's compensation insurance as required by law; and (d) automobile liability insurance (including comprehensive and collision coverage, and uninsured/underinsured motorist coverage) in the same amounts set forth in subsections (a) and (b) if the Equipment is to be used on any roadway. Such plans shall be primary non-contributory on an occurrence basis, remain a waiver of subrogation, name Sunbelt and its agents as an additional insured (including an additional insured endorsement), and lastly, provide for Sunbelt to receive at least 30 days prior written notice of any cancellation or material change. Any insurance that is not in compliance with this Section is a breach. Customer shall provide Sunbelt with certificates of insurance evidencing the coverages required above prior to any rental and any time upon Sunbelt's request. To the extent Sunbelt Entities carry any insurance, Sunbelt Entities' insurance will be considered excess insurance. The insurance provided herein does not relieve Customer of its responsibilities, indemnification, or other obligations provided herein, or for which Customer may be liable by law or otherwise.

10. **RENTAL PROTECTION PLAN.** Customer's repair or replacement responsibility, in Sections 2 and 6 is modified by the RPP and Sunbelt shall limit the amount Sunbelt collects from Customer for the Equipment loss, damage or destruction in the following amounts for each piece of Equipment: (a) 10% of the MSRP for Lost Equipment, up to a maximum of \$500 per piece of Equipment; (b) 10% of the rental charges for accidental or architectural damage to Equipment, up to a maximum of \$500 per piece of Equipment; (c) changes in excess of \$500 per line for the repairs; and (d) nothing for the rental charges which would otherwise accrue during the period when damaged or destroyed Equipment is being repaired or replaced by Sunbelt or Lost Equipment is being replaced; provided however, the foregoing RPP liability reduction only applies if the Conditions are satisfied and an Exclusion does not apply. THE RPP IS NOT INSURANCE and does NOT protect Customer from liability to Sunbelt or others arising out of possession, control or use of the Equipment, including injury or damage to persons or property. THE RPP IS A CONTRACTUAL MODIFICATION OF CUSTOMERS LIABILITY. All of the following "Conditions" must be satisfied for the RPP and the corresponding liability reduction to apply: (i) Customer accepts the RPP in advance of the rental; (ii) Customer pays 10% of the gross rental charges as the fee for the RPP (on applicable cases); (iii) Customer fully complies with the terms of this Contract; (iv) Customer's request is entered at the time of the last theft, damage or destruction of the Equipment; and (v) none of the Exclusions apply. Customer assumes the Exclusion risks, meaning that if any Exclusion occurs the RPP does NOT reduce the liability of Customer to Sunbelt for the loss, theft, damage or destruction resulting from such Exclusion. "Exclusions" shall mean those theft, damage or destruction of the Equipment: (i) due to intentional actions; (ii) caused by Lost Equipment not returned by Customer to the place within 40 hours of discovery, and substituted by a written police report (purportedly delivered to

Sunbelt); (iii) due to Acts of God, such as floods, wind, storms or earthquakes; and (iv) accessories or Equipment for which Customer is not charged the RPP fee. THE EXCLUSIONS REMAIN THE LIABILITY OF CUSTOMER AND ARE NOT MODIFIED BY THE RPP. Notwithstanding anything to the contrary in this Contract, if Lost Equipment is later recovered, Sunbelt retains ownership of the Equipment regardless of any payments made by Customer or Customer's insurance purveyor with respect to such Equipment, all of which payments are non-refundable. Customer agrees to promptly return any Equipment that is recovered. Sunbelt shall be subrogated to Customer's rights to recover against any person or entity relating to any loss, theft, damage or destruction to the Equipment. Customer shall cooperate with, assign Sunbelt all claims and proceeds arising from such loss, theft, damage or destruction, estimate and deliver to Sunbelt whatever documents are required and take all other necessary steps to secure in Sunbelt such rights. At Customer's expense.

11. **RENTAL RATES.** The total charges specified in this Contract are: (a) estimated based upon Customer's representation of the estimated Rental Period identified on the front side hereof (rental rates beyond the estimated Rental Period may change and other information conveyed by Customer to Sunbelt); and (b) for the Equipment's use for One Shift, unless otherwise noted. Weekly and 4 week rental rates shall not be prorated. Rental charges accrue during Sundays, Saturdays and holidays. The rental rates do not include and Customer is responsible for, in addition to all rental rates and other charges shown in this Contract: (i) all taxes, fees, licenses, permits and future taxes and other governmental charges based on Customer's possession and/or use of the Equipment, including additional fees for more than One Shift use; (ii) delivery and pickup charges to and from the Store, including but not limited to any freight, transportation, delivery, pickup and surcharge fees based in this Contract; (iii) maintenance, repairs and replacements to the Equipment as required herein; (iv) a cleaning fee if required; (v) miscellaneous charges, such as fees for lost keys; (vi) fuel used during the Rental Period and for refueling Equipment as described below; (vii) fines from use of dyed diesel fuel in on-road Equipment; and (viii) an Environmental Fee (described below). The convenience charge for off road diesel fuel does not include governmental interior fuel taxes or charges. Sunbelt collects these fees as revenue and uses them at its discretion.

12. **PAYMENT.** Customer shall pay amounts due, without any offsets, in full at the time of rental, unless Sunbelt approves charges. Customer's receipted credit application (credit customers must pay upon receipt of Sunbelt's invoice). Customer must notify Sunbelt in writing of any disputed amounts, including credit card charges, within 15 days after the receipt of the invoice. Customer or Customer shall be deemed to have irrevocably waived its right to dispute such amounts. At Sunbelt's discretion, any credit account with a delinquent balance may be placed on a cash basis, deposits may be required and the Equipment may be impounded without notice. Due to the difficulty in listing annual charges caused by late payment, Customer agrees that a service charge equal to the lesser of 1.5% per month or the maximum rate permitted by law shall be assessed on all delinquent accounts, until paid in full. Customer shall pay a fee of \$25 for each check returned for lack of sufficient funds to compensate Sunbelt for its overhead for processing mailed payments. Deposits will only be returned after all amounts are paid in full. Customer agrees that if a credit card is presented to pay for charges or to guarantee payment, Customer authorizes Sunbelt to charge the credit card all amounts shown on this Contract and charges subsequently incurred by Customer, including but not limited to, loss of or damage to the Equipment and extension of the Rental Period.

13. **RETURN OF EQUIPMENT.** Sunbelt may terminate this Contract at any time, for any reason. At the end of the Rental Period, the Equipment shall be returned to Sunbelt in the same condition it was received, less Ordinary Wear and Tear and free of any hazardous materials and contaminants. Customer will continue to be responsible for rental and other charges after the Rental Period if the Equipment is not returned in the condition required herein. If Sunbelt delivered the Equipment to Customer, Customer shall notify Sunbelt that the Equipment is ready to be picked up at the Site Address and obtain a Pick-Up Number, which Pick-Up Number Customer should keep as proof of the call. Customer shall return the Equipment to Sunbelt in the condition required herein. Customer will not be charged the rental charges after the date the Pick-Up Number is given, provided Customer has otherwise complied with this Contract. No pickups occur on Sundays or statutory holidays and Saturday pickups are dependent on specific Store hours. If Customer picked up Equipment, Customer shall return Equipment to the same Store during that Store's normal business hours. If the Equipment is not returned by the estimated end of the Rental Period specified on the front side hereof, Customer agrees to pay the applicable rental rate for the Equipment until the end of the Rental Period.

14. **PURCHASES.** If this Contract identifies any Equipment, materials or other items that are to be purchased by Customer, Sunbelt will deliver such items to Customer on an "AS IS, WHERE IS" basis, with all faults and without any warranties (other than manufacturer warranties). If any consideration for the purchase of such items is provided to Sunbelt, the purchase price of the item, Sunbelt retains title to the item until Customer has paid in full.

15. **DEFAULT.** Customer shall be in default if Sunbelt deems that it incurs or if Customer: (a) fails to pay sums when due; (b) breaches any Section of this Contract; (c) becomes a debtor in a bankruptcy proceeding, goes into receivership, takes protection from its creditors under any insolvency legislation, ceases to carry on business, or has its assets seized by any creditor; (d) fails to insure the Equipment as required, or otherwise places the Equipment at risk; (e) fails to return Equipment immediately upon Sunbelt's demand; or (f) is in default under any other contract with Sunbelt. If a Customer default occurs, Sunbelt shall have, in addition to all sums due and remedies as set forth in or in equity, the right to repossess the Equipment without judicial process or prior notice. Customer shall pay all of Sunbelt's costs, including reasonable costs of collection, court costs, attorney and legal fees, incurred in exercising any of its rights or remedies herein. The use of false identification to obtain Equipment or the failure to return Equipment by the end of the Rental Period may be considered theft, subject to criminal prosecution and civil liability where permitted, pursuant to applicable laws. Sunbelt shall not be liable due to seizure of Equipment by order of governmental authority. CUSTOMER WAIVES ANY RIGHT OF ACTION AGAINST SUNBELT ENTITIES FOR SUCH REPOSSESSION.

16. **ENVIRONMENTAL FEE.** To promote a clean and sustainable environment, Sunbelt takes various measures to comply with applicable environmental regulations as well as with Sunbelt's own policies. Sunbelt also incurs a wide range of environmental related expenses (both direct and indirect). These expenses may include waste disposal, construction and maintenance of cleaning facilities, acquisition of more fuel efficient equipment, labor costs, administration costs, etc. To help defray these and other costs, Sunbelt charges an environmental fee plus applicable taxes shown in connection with certain rentals. The fee is a not a tax or governmentally mandated charge. The fee is not designed for any particular use or placed in an extreme amount, but is a fee that Sunbelt collects as revenue and uses at its discretion.

17. **FUEL.** For Equipment that uses fuel, Customer has three options: (a) **Pay-as-You-Go Fuel Option.** Customer may purchase a full tank of fuel for the Equipment at the start of the rental, in which case a "convenience charge" will appear on this Contract (calculated by multiplying the estimated fuel capacity of Equipment by the Pump per gallon rate). As an added benefit, Customer may return the Equipment full of fuel and the convenience charge will be refunded; however, if returned empty, Customer will not obtain any credit for fuel left in the Equipment upon return; (b) **Pay-as-You-Go Fuel Option.** If Customer returns Equipment with less fuel than when received, Customer shall pay a refueling charge (calculated by multiplying gallons required to refill tank with fuel level when received, by the Pay on Return gallon rate); and (c) **Return Full Option.** If Customer returns the Equipment with at least as much fuel as when it was received (Sunbelt Equipment comes with a full tank of fuel, but not all), no fuel charge will be assessed. The cost of Customer refueling Equipment itself will generally be lower than the Pay-as-You-Go Fuel Option or the Pay on Return Option; however these options each allow for the convenience of not refueling.

18. **LIMITATION OF SUNBELT'S LIABILITY IN CONSIDERATION OF THE RENTAL OF EQUIPMENT.** CUSTOMER AGREES THAT SUNBELT'S LIABILITY UNDER THIS CONTRACT INCLUDING ANY LIABILITY ARISING FROM SUNBELT'S, SUNBELT ENTITIES, OR ANY THIRD PARTIES' COMPARATIVE, CONCURRENT, CONTRIBUTORY PASSIVE OR ACTIVE NEGLIGENCE OR NEGLIGENCE AS A RESULT OF ANY STRICT OR ABSOLUTE LIABILITY SHALL NOT EXCEED THE TOTAL RENTAL CHARGES PAID BY CUSTOMER UNDER THIS CONTRACT.

19. **JURY TRIAL WAIVER.** IN ANY DISPUTE ARISING OUT OF IN CONNECTION WITH, OR IN ANY WAY PERTAINING TO THIS CONTRACT, CUSTOMER AND SUNBELT HEREBY KNOWINGLY, VOLUNTARILY AND INTENTIONALLY WAIVE ANY RIGHT TO A TRIAL BY JURY. THIS WAIVER BEING A MATERIAL INDUCEMENT TO ENTERING INTO THIS CONTRACT.

20. **ARBITRATION AGREEMENT & CLASS ACTION WAIVER.** AT THE ELECTION OF CUSTOMER OR SUNBELT, ANY DISPUTE ARISING OUT OF, IN CONNECTION WITH OR IN ANY WAY PERTAINING TO THIS CONTRACT SHALL BE SETTLED BY ARBITRATION BROUGHT IN THE PARTIES' INDIVIDUAL CAPACITY AND NOT AS A PLAINTIFF IN A PURPORTED CLASS OR REPRESENTATIVE CAPACITY ADMINISTERED BY THE AMERICAN ARBITRATION ASSOCIATION UNDER ITS COMMERCIAL ARBITRATION RULES OR BY JAMS PURSUANT TO ITS STREAMLINED ARBITRATION RULES AND PROCEDURES AND JUDGMENT ON THE AWARD RENDERED BY THE ARBITRATOR(S) MAY BE ENTERED IN ANY COURT HAVING JURISDICTION THEREOF. THESE SHALL BE NO RIGHT OR AUTHORITY FOR ANY CLAIMS TO BE ARBITRATED OR TRIED ON A CLASS ACTION BASIS.

21. **COMPLIANCE WITH EXPORT AND IMPORT LAWS.** Removal of the Equipment from the United States ("U.S.") is prohibited under this Contract. If Customer desires or causes the transport and/or operation of the Equipment outside of the U.S., Customer must (a) obtain Sunbelt's written prior approval to take such action, and (b) execute an amendment to this Contract, which amendment is incorporated herein. If Customer exports or re-exports without complying with the above, Customer agrees that: (i) the Equipment is subject to and must comply with all applicable export laws, including but not limited to the Export Administration Regulations; and (ii) Customer is responsible for: (A) determining whether and obtaining necessary export or re-export licenses or other authorizations as required prior to exporting or re-exporting the Equipment; (B) obtaining any required documentation necessary for return of the Equipment; and (C) meeting all unauthorized transfers or disclosures of the Equipment or use. Refer to www.eia.doe.gov for information.

22. **GOVERNING LAW.** The parties expressly and irrevocably agree: (a) this Contract, including any related tort claims, shall be governed by the laws of South Carolina, without regard to any conflicts of law principles and (b) if any Section of this Contract is prohibited by any law, such Section shall be ineffective to the extent of such prohibition without invalidating the remaining Sections.

23. **MISCELLANEOUS.** This Contract, together with any Customer created cash application, constitutes the entire agreement of the parties regarding the Equipment and may not be modified except by written amendment signed by the parties. Customer's obligations hereunder shall survive the termination of this Contract. This Contract and all of the Equipment's rights and to the Equipment are subordinate to all rights title and interest of all persons (including Sunbelt's lender) who have rights in the Equipment. Headings are for convenience only. To the extent that any terms in this Contract conflict, the parties agree that the more specific terms control. A copy of this Contract shall be valid as the original. Any failure by Sunbelt to insist upon strict performance of any Section of this Contract shall not be construed as a waiver of the right to demand strict performance in the future. Customer and the person signing this Contract represent that: (a) they both have full authority to execute, deliver and perform this Contract and (b) this Contract constitutes a legal, valid and binding obligation of Customer enforceable in accordance with its terms. When Customer is a buyer of Equipment, they are hereby notified that Sunbelt has assigned its rights that are its obligations in the agreement to sell the asset(s) described herein to Sunbelt Rentals Exchange, Inc., a qualified intermediary as part of Section 1011 exchange, and Customer shall make the purchase Sunbelt Rentals Exchange, Inc.



Charleston • Columbia • Atlanta

DATE:

03/08/17

C.O.#GC7

CHANGE ORDER PROPOSAL

JOB NAME:	Marion Square
CONTRACTOR	Balfour beatty
ADDRESS	
DATE OF EXISTING CONTRACT:	
CONTRACT #:	
ATT:	Alec Dooley
PH:	
Reference	

We hereby agree to make the following change's) specified below:

General Conditions for schedule push on level 7. 21 days.

NOTE: This Change Order reflects pricing for additional and/or revised work outside of the contacted scope of work.

WE AGREE hereby to make the change specified above at this price >>>>>>>>		\$3,225.75
PREVIOUS CONTRACT AMOUNT		
REVISED CONTRACT AMOUNT		
Signature (SUB-CONTRACTOR):		
ACCEPTED - The above prices and specifications of this work to be performed under the same terms and conditions as specified in the original contract unless otherwise specified. Price is valid for 30 days from receipt.	Accepted By: (Signature)	
	Date of Acceptance:	

Summary

DATE:

03/08/17

We hereby agree to make the following change(s) specified below:

General Conditions for schedule push on level 7. 21 days.

Fire Sprinkler

Contract Work

1.	Products (itemized breakdown attached):		\$0.00	
2.	Rent of Equipment (listed separately):*		\$0.00	
	Total of 1 + 2		\$0.00	(A)
3.	Labor (itemized breakdown attached):		\$2,805.00	
4.	security, or as otherwise required or specified):	0%	\$0.00	
	Total of (A) + 3 + 4		\$2,805.00	(B)
5.	Overhead and Profit (% of total (B)):	15%	\$420.75	
	Total of (B) + 5		\$3,225.75	(C)
6.	Sales Taxes on total (A):	8.5%	\$0.00	
	Total of (C) + 6		\$3,225.75	(D)
7.	Subcontract work (if applicable in a similar breakdown through total (D)):			
8.	Prime Contractor's overhead and profit on sub-bids (7):	10%	\$0.00	
	Total of 7 + 8		\$0.00	(E)
	Total of (D) + (E)		\$3,225.75	(F)
9.	Performance - Payment Bond on Total (F):	0.0%	\$0.00	(G)
	TOTAL QUOTATION (F) + (G)		\$3,225.75	

Extension of time requested: _____ calendar day(s)

LABOR

Date:

03/08/17

General Conditions for schedule push on level 7. 21 days.

LABOR - ITEMIZED BREAKDOWN

Design		hours at	75.00	per man hour =	\$0.00
Foreman		hours at	65.00	per man hour =	\$0.00
Fitter		hours at	55.00	per man hour =	\$0.00
Helper		hours at	45.00	per man hour =	\$0.00
Project Manager	17.0	hours at	85.00	per man hour =	\$1,445.00
Superintendent	17.0	hours at	80.00	per man hour =	\$1,360.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00

LABOR TOTAL: \$2,805.00



Charleston • Columbia • Atlanta

DATE:

03/08/17

C.O.#GC9

CHANGE ORDER PROPOSAL

JOB NAME:	Marion Square
CONTRACTOR	Balfour beatty
ADDRESS	
DATE OF EXISTING CONTRACT:	
CONTRACT #:	
ATT:	Alec Dooley
PH:	
Reference	

We hereby agree to make the following change's) specified below:

General Conditions for schedule push on level 9. 20 days.

NOTE: This Change Order reflects pricing for additional and/or revised work outside of the contacted scope of work.

WE AGREE hereby to make the change specified above at this price >>>>>>>>>		\$3,036.00
PREVIOUS CONTRACT AMOUNT		
REVISED CONTRACT AMOUNT		
Signature (SUB-CONTRACTOR):		
ACCEPTED - The above prices and specifications of this work to be performed under the same terms and conditions as specified in the original contract unless otherwise specified. Price is valid for 30 days from receipt.	Accepted By: (Signature)	
	Date of Acceptance:	

Summary

DATE:

03/08/17

We hereby agree to make the following change's) specified below:

General Conditions for schedule push on level 9. 20 days.

Fire Sprinkler

Contract Work

1.	Products (itemized breakdown attached:		\$0.00	
2.	Rent of Equipment (listed separately):*		\$0.00	
	Total of 1 + 2		\$0.00	(A)
3.	Labor (itemized breakdown attached:		\$2,640.00	
4.	security, or as otherwise required or specified):	0%	\$0.00	
	Total of (A) + 3 + 4		\$2,640.00	(B)
5.	Overhead and Profit (% of total (B)):	15%	\$396.00	
	Total of (B) + 5		\$3,036.00	(C)
6.	Sales Taxes on total (A):	8.5%	\$0.00	
	Total of (C) + 6		\$3,036.00	(D)
7.	Subcontract work (if applicable in a similar breakdown through total (D):			
8.	Prime Contractor's overhead and profit on sub-bids (7):	10%	\$0.00	
	Total of 7 + 8		\$0.00	(E)
	Total of (D) + (E)		\$3,036.00	(F)
9.	Performance - Payment Bond on Total (F):	0.0%	\$0.00	(G)
	TOTAL QUOTATION (F) + (G)		\$3,036.00	

Extension of time requested: _____ calendar day(s)

PASCO, Inc.

Page 4 of 5

LABOR**Date:****03/08/17****General Conditions for schedule push on level 9, 20 days.****LABOR - ITEMIZED BREAKDOWN**

Design		hours at	75.00	per man hour =	\$0.00
Foreman		hours at	65.00	per man hour =	\$0.00
Fitter		hours at	55.00	per man hour =	\$0.00
Helper		hours at	45.00	per man hour =	\$0.00
Project Manager	16.0	hours at	85.00	per man hour =	\$1,360.00
Superintendent	16.0	hours at	80.00	per man hour =	\$1,280.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00
					\$0.00

LABOR TOTAL: \$2,640.00



BERNHARD MCC, L.L.C.

October 11, 2016

Balfour Beatty Construction
306 Meeting St. /Suite 300
Charleston, SC 29401

Attn: Tim Spano/Nick Starcevic

REF: The Hotel at Marion Square
Contract Number: 13026000
BMCC Project Number: 8350248

SUBJ: BMCC PCO No: 054
Correspondence 000072-Hotel at Marion Square-Schedule Update 9/21/16

Gentlemen,

Bernhard MCC has received information from our third party scheduling consultant indicating a net 3 week extension to our duration on this job as defined in the Correspondence 000072. The attached summary sheet collectively defines the impact as requested. The cost of this change is \$ 35,781.68

The following clarifications and exclusions apply to this proposal:

1. Any future scheduling impacts on duration and scope.

If you have any questions, please contact us as soon as possible. This proposal remains in effect for 30 days.

Sincerely,

Bernhard MCC, L.L.C.

Eric Stoehr
Project Manager

ES/SD

Attachment



MCC Mechanical of the Carolinas, LLC

Proposed Change Summary

Project: The Hotel at Marion Square
Location: Charleston, SC

Date: October 4, 2016

MCC Job No: 8350248
MCC PCO #: 54

Description: Correspondence 000072 9-21-16 Schedule Update

Labor Breakdown

Std Hrs	Prem Hrs		Std Rate	Prem Rate	
120.0	0.0	Project Manager	\$80.00	\$120.00	\$9,600.00
120.0	0.0	Superintendent	\$75.00	\$112.50	\$9,000.00
120.0	0.0	Project Administrator	\$51.00	\$76.50	\$6,120.00
0.0	0.0	Journeyman	\$37.00	\$55.50	\$0.00
0.0	0.0	Start-up Technician	\$88.00	\$132.00	\$0.00
0.0	0.0	BIM Coordinator	\$70.00	\$105.00	\$0.00
0.0	0.0	Detailer	\$53.00	\$79.50	\$0.00
0.0	0.0	Laborer	\$23.00	\$34.50	\$0.00
0.0	0.0	Helper	\$15.00	\$22.50	\$0.00
0.0	0.0	Field Engineer	\$51.00	\$76.50	\$0.00
0.0	0.0	Safety	\$64.50	\$96.75	\$0.00
0.0	0.0	Clean Up	\$15.00	\$22.50	\$0.00
0.0	0.0	Estimator	\$51.00	\$76.50	\$0.00

Subtotal \$24,720.00

Field Office: Drawings / Copies		\$2,437.50
Travel & Lodging		\$765.00
Purchasing	0.0%	\$0.00
Small Tools	2.0%	\$494.40
Tool Rental	3.5%	\$865.20
Quality Control	4.5%	\$1,112.40
Consumables	0.0%	\$0.00
Subtotal		\$5,674.50

Overhead & Profit: 15.0% \$4,559.18

Subtotal Labor \$34,953.68

Material Breakdown	Item Description	Cost	Tax	Net
PVF Materials		\$0.00	\$0.00	\$0.00
Equipment		\$0.00	\$0.00	\$0.00
Equipment rental		\$0.00	\$0.00	\$0.00
Parking	3 @ 16 daily for 15 day	\$0.00	\$0.00	\$720.00
Permits		\$0.00	\$0.00	\$0.00
Seismic		\$0.00	\$0.00	\$0.00
X-Ray/Core Drill		\$0.00	\$0.00	\$0.00
Total Materials				\$720.00

Tax Rate: 8.50%

Overhead & Profit: 15.0% \$108.00

Subtotal Material & Equipment \$828.00

Subcontract Breakdown	Item Description	Cost		Total
Sheet metal		\$0.00		\$0.00
Insulation		\$0.00		\$0.00
Temperature Controls		\$0.00		\$0.00
Test & Balance (BY OTHERS)		\$0.00		\$0.00
Fire Caulk		\$0.00		\$0.00
Med Gas		\$0.00		\$0.00
Locate Services		\$0.00		\$0.00
BIM Coordinator		\$0.00		\$0.00
Subtotal				\$0.00

Overhead & Profit: 15.0% \$0.00

Subtotal Subcontractor Costs \$0.00

Total Cost \$35,781.68

Schedule Comments: Fifteen (15) days schedule extension requested for this change, however, we reserve the right to examine the impact of this change on the overall schedule at a later date, and request appropriate time or cost compensation should the accumulative effect of this or other changes warrant.

Balfour Beatty
Construction

DATE: 26-May-17

PROJECT: The Hotel at Marion Square

SUB WATSON

Electronic Summary

PRECON MNGR: Nick Starcevic

SUBCONTRACTOR SCOPE SHEET

SUBCONTRACTOR :	L6	L7 & L9	GENERAL CONTRACTOR ITEMS:	
			MATERIAL:	LABOR:
BASE BID:	20 Days \$38,620.00	32 Days \$60,388.00		
FURNISHED				
INSTALLED				
SALES TAX				
SCOPE ITEMS:				
Supervisor	INCLUDED	INCLUDED		
Superintendent	INCLUDED	INCLUDED		
Foreman	INCLUDED	INCLUDED		
Project Manager	INCLUDED	INCLUDED		
PM/Admin Assistant	INCLUDED	INCLUDED		
CAD Coordinator	INCLUDED	INCLUDED		
Safety Coordinator	INCLUDED	INCLUDED		
Sawyer L/H	INCLUDED	INCLUDED		
Main L/H - 20ft	INCLUDED	INCLUDED		
Truck	INCLUDED	INCLUDED		
Van	INCLUDED	INCLUDED		
Storage	INCLUDED	INCLUDED		
Temp Office	INCLUDED	INCLUDED		
Tools	INCLUDED	INCLUDED		
Equipment (Compilers / IPad)	INCLUDED	INCLUDED		
Cellphones	INCLUDED	INCLUDED		
TOTAL COST OF WORK :	\$38,620	\$60,388	\$0	\$0

WATSON ELECTRICAL-CHARLESTON, SC

General Conditions Extension

Personnel	Qty	Rate	Hrs/day	days	Sub Totals
Supervisor	1	\$ 40.00	8	20	\$ 6,400.00
Superintendent	1	\$ 35.00	8	20	\$ 5,600.00
Foreman	1	\$ 30.00	8	20	\$ 4,800.00
Foreman	0	\$ 30.00	0	20	\$ -
Foreman	0	\$ 30.00	0	20	\$ -
Project Manager	1	\$ 75.00	8	20	\$ 12,000.00
PM/Admin Assistant	1	\$ 35.00	4	20	\$ 2,800.00
CAD Coordinator	1	\$ 65.00	2	20	\$ 2,600.00
Safety Coordinator (based on 1 weekly trip)	1	\$ 65.00	1.6	20	\$ 2,080.00

Equipment by Month	Qty	Rate/Mon	# of Mon	
Scissor Lift 19 Ft	0	\$ 325.00	1	\$ -
One Man Lift 20 Ft	0	\$ 550.00	1	\$ -
Pick Up-vehicle #1-PM	1	\$ 400.00	1	\$ 400.00
Pick Up-vehicle #2-Supervisor	1	\$ 400.00	1	\$ 400.00
Van	2	\$ 400.00	1	\$ 800.00
Storage	0	\$ 100.00	1	\$ -
Temp Office Rental	0	\$ 150.00	1	\$ -
Tools (hours remng @ 20 day x rate)	0	\$ 0.30	1	\$ -

Equipment by Day		Rate/Day	# Days	
Computers/Ipad	2	\$ 6.50	20	\$ 260.00
Cell Phones	6	\$ 4.00	20	\$ 480.00

GRAND TOTAL				\$ 38,620.00
--------------------	--	--	--	---------------------

WATSON ELECTRICAL-CHARLESTON, SC

General Conditions Extension

Personnel	Qty	Rate	Hrs/day	days	Sub Totals
Supervisor	1	\$ 40.00	8	32	\$ 10,240.00
Superintendent	1	\$ 35.00	8	32	\$ 8,960.00
Foreman	1	\$ 30.00	8	32	\$ 7,680.00
Foreman	1	\$ 30.00	0	32	\$ -
Foreman	1	\$ 30.00	0	32	\$ -
Project Manager	1	\$ 75.00	8	32	\$ 19,200.00
PM/Admin Assistant	1	\$ 35.00	4	32	\$ 4,480.00
CAD Coordinator	1	\$ 65.00	2	32	\$ 4,160.00
Safety Coordinator (based on 1 weekly trip)	1	\$ 65.00	1.6	32	\$ 3,328.00

Equipment by Month	Qty	Rate/Mon	# of Mon		
Scissor Lift 19 Ft	0	\$ 325.00	1	1.15	\$ -
One Man Lift 20 Ft	0	\$ 550.00	1	1.15	\$ -
Pick Up-vehicle #1-PM	1	\$ 400.00	1	1.15	\$ 400.00
Pick Up-vehicle #2-Supervisor	1	\$ 400.00	1	1.15	\$ 400.00
Van	2	\$ 400.00	1	1.15	\$ 800.00
Storage	0	\$ 100.00	1	1.15	\$ -
Temp Office Rental	0	\$ 150.00	1	1.15	\$ -
Tools (hours remng @ 20 day x rate)	0	\$ 0.30	1	1.15	\$ -

Equipment by Day		Rate/Day	# Days		
Computers/Ipad	2	\$ 6.50	20	1.15	\$ 260.00
Cell Phones	6	\$ 4.00	20	1.15	\$ 480.00

GRAND TOTAL					\$ 60,388.00
--------------------	--	--	--	--	---------------------

Tab No. 159

Balfour Beatty Construction

August 21, 2017

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 159
FFE Changes

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 159 in the amount of Two hundred forty-two thousand six hundred thirty-three (\$242,633.32) to provide additional work in accordance with the following qualifications:

Westley's Expanded Scope

FFE "Responsibility Matrix" attached as Exhibit X. Westley's updated pricing includes but is not limited to the following:

1. Revision from fully assembled to knock down vanities, TV Walls, and headboards.
2. 3 months extended Storage due to items not delivering per schedule
3. Radios batteries not included.
4. Addition of guestroom and cabana safes
5. Corridor Ice Machines NOT included.
6. Roll-Away Beds NOT included
7. Baby Beds NOT included
8. Guestroom light bulbs install only, provided by others (NOT GC).
9. Irons and Iron Boards NOT included
10. Remote Programming NOT included
11. Telephone System terminations and switchboard NOT included
12. Wall mounted A/V units NOT included
13. Cashier's Safe and deposit box NOT included
14. Display fixtures and Racks NOT included
15. Hair Dryers NOT included
16. Manager's Apartment Appliances NOT included
17. Conduit & Cable & terminations for Public and Atrium Sound System NOT included
18. Added exercise equipment
19. Westley's warehousing and transportation excludes items they are not installing.

Extended Storage

Includes current storage and transportation fees for OFCI items not drop shipped directly to jobsite.
Includes demurrage fees paid by contractor for OFCI items not drop shipped per schedule.
Includes a \$40,000 allowance for projected continued storage and shipping for OFCI items not drop shipped to the jobsite.

Balfour Beatty

Construction

Clarifications:

1. Items marked as "F" in FFE Matrix are NOT included
2. All clarifications, qualifications, exclusions, and inclusions outlined in Exhibit B "Westley's Expanded Scope of Work" apply to this change order.

This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Nick Starcevic
Project Manager

cc:

Kim Brown
Marty Wall
Jim Clements
Woody Faust
David Stanton
Tim Spano
Alec Dooley

RCO # 159 – File

Exhibit X - HMS Revised FFE Final Responsibility Matrix_21July17.xlsx

Exhibit B Westley's Expanded Scope of Work.pdf

Exhibit C – Current Main Ocean Invoices

Exhibit D – BBC Demurrage Invoice

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 159- FFE Changes

The additional work for the **FFE Changes** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.51200001.40	Extended Warehousing Services	\$117,000.00
2	400.51200001.40	Expanded Installation Services	\$177,000.00
3	400.51200001.40	Debris Disposal (NOT INCLUDED)	\$0.00
4	400.51200001.40	Parking (Allowance)	\$5,000.00
5	400.51200001.40	TVs	\$11,275.00
6	400.51200001.40	Radios	\$3,800.00
7	400.51200001.40	Microwaves	\$3,800.00
8	400.51200001.40	Ice Machines	\$3,500.00
9	400.51200001.40	Iron & Board & Hangers	\$3,800.00
10	400.51200001.40	Employee Break Room Appliances	\$1,000.00
11	400.51200001.40	Provide & Install Batteries to Alarm Clock	\$1,950.00
12	400.51200001.40	Guestroom Safe	\$4,700.00
13	400.51200001.40	Umbrellas	\$5,000.00
14	400.51200001.40	Original Estimate	(\$213,000.00)
15	400.51200001.40	Extended Product Inspections	\$4,326.00
16		Current Extended Storage at 3rd Part Warehouse	\$42,407.00
17		Projected OFCI Extended Storage	\$40,000.00
18		Demurrage Fees	\$19,858.00

Total Items \$231,416.00

Total Markups \$11,217.32

RCO Total \$242,633.32

The total Cost to perform the work as described above is an ADD of Two hundred forty-two thousand six hundred thirty-three (\$242,633.32).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 159

RESPONSIBILITY MATRIX

A = Architect	FI = Furnishings Installer	LA = Landscape Architect	OP = Hotel Operator
BS = Building Signage Consultant	FS = FF&E Subcontractor	LC = Laundry Consultant	PA = FF&E Purchasing Agent (Hired By Owner)
F = FF&E Provided by Owner	GC = General Contractor	LD = Lighting Designer	SC = Sound Amplification Consultant
FD = Food and Beverage Designer	ID = Interior Designer	ME = MEP Engineers	WF = Water Feature Consultant

No.	Item Description	Designer Specifier	Construction Document	Purchase	Installation	Comments	BBC Breakdown
ALL BUILDING AREAS:							
1.	FLOOR & BASE:						
	A. Carpet / Pad	ID	ID / A	PA	GC		Flooring Services
	B. Ceramic & Quarry Tile	ID / A	ID / A	GC	GC		David Allen
	C. Stone / Marble	ID / A	ID / A	GC	GC		David Allen
	D. Vinyl Composite Tile	ID / A	ID / A	GC	GC		David Allen
	E. Other (Decorative)					Not In Contract	Not In Contract
	F. Sealers - Public Area	ID / A	ID / A	GC	GC		David Allen
	G. Special Coatings					Not In Contract	Not In Contract
	H. Transition Strips	ID / A	ID / A	GC	GC		David Allen
2.	WALL:						
	A. Paint	ID / A	ID / A	GC	GC		Merit
	B. Vinyl Wall Covering	ID / A	ID / A	F / PA	GC	To be stored by Westley	Merit
	C. VWC Frieze Strip					Not In Contract	Not In Contract
	D. Millwork / Marble	ID / A	ID / A	GC	GC		LCCM
	E. Mirror - Unframed (Fitness Room Only)	ID / A	ID / A	GC	GC		
	F. Mirror - Framed	ID / A	ID / A	F / PA	GC / FI		Westley
	F. Antimicrobial Fungicide Sealer (Adhesive)	ID / A	ID / A	GC	GC		
	G. Corner Guards	ID / A	ID / A	GC	GC		Warco
3.	CEILING:						
	A. Paint	ID / A	ID / A	GC	GC		Merit
	B. Suspended Drywall Lay-In	ID / A	ID / A	GC	GC		Precision Walls
	C. Applied Décor Millwork / Plaster Molding	ID / A	ID / A	GC	GC		Precision Walls
	D. Sprayed Acoustic Coating					Not In Contract	Not In Contract
4.	DOORS:						
	A. Frame & Door	ID / A	ID / A	GC	GC		Cook and Boardman
	B. Hardware (including Card Entry Syst.)	ID / A	ID / A	GC	GC		Cook and Boardman
	C. Applied Décor Millwork	ID / A	ID / A	GC	GC		LCCM
	D. Storefront	ID / A	ID / A	GC	GC		Koch
	E. Keying Equipment & Blanks	OP / A	A	GC	GC		Cook and Boardman
	F. Mechanical and Electrical Lock Sets, Intercom Systems, and a	OP / A	A	GC	GC		Cook and Boardman
5.	MILLWORK:						
	A. General Millwork	ID / A	ID / A	GC	GC		LCCM
	B. Plumbing Fixtures with Vanity (At Common Areas)	ID / A	ME/A	GC	GC		BMCC
	C. Electrical Within	ID / A	ME/A	GC	GC		Watson
6.	ELECTRICAL:						
	A. Conduit, Wire & All Devices	ME/A	ME/A	GC	GC		Watson
	B. Landscape / Grow Lighting / Atrium Décor					Not In Contract	Not In Contract
7.	LIGHTING:						
	A. Plug-In Fixtures	ID	ID	PA	GC / FI		Westley
	B. Direct Wire Including Sconces & Suite Pendants	ID/LD/A	ID / LD/ME/A	PA	GC		Watson
	C. Direct Wire / Public	LD / ID / A / ME	LD / ID / A / ME	PA	GC		Watson
	D. General Illumination	LD / ME	LD / ME / A	GC	GC		Watson
	E. Exterior Lighting	A / ME	ME/A	GC	GC		Watson
	F. Chandeliers	ID/LD/A/ME	ID/LD/A/ME	PA	GC		Watson
	G. Exterior Building Illumination	LD / ME / A	LD / ME / A	GC	GC		Watson
	H. Install all Light Fixtures on E601					Will price as listed on drawings and specs.	Will price as listed
	I. Light Bulbs			PA	OP	Thought the install was GC?	OP
8.	ELEVATORS:						
	A. Cab Interior Finishes (Millwork Allowance)	ID	ID	GC	GC		LCCM
	B. Handrails					Not In Contract	Not In Contract
	C. Carpet					Not In Contract	Not In Contract
	D. Porcelain Tile Floor	ID	ID	GC	GC		Flooring Services
9.	HVAC:						
	A. Diffusers	A/ME/ID	ID/A/ME	GC	GC		BMCC
	B. Atrium Smoke EVAC system					Not In Contract	Not In Contract
	C. HVAC Test and Balance Services	ME / A	ME / A	F	F	As per specs 01-101-1, Part 1.2, section E	
10.	PLUMBING:						
	A. Fixtures & Trim	A / ME	ME	GC	GC		BMCC
11.	FIRE PROTECTION:						
	A. Sprinkler (Including Heads & Escutcheons)	A / ME	A / ME	GC	GC		PASCO
12.	ALARM SYSTEM:						
	A. Conduit & Cable	ME	ME	GC	GC		Watson
	B. Smoke Detectors includes Guest Suites	A/ME	A/ME	GC	GC		Watson
	C. Emergency Voice Communication	A/ME	A/ME	GC	GC		Watson
13.	TELEPHONE SYSTEM:						
	A. Conduit (Empty)	FS / A / OP	A / ME	GC	GC		Watson
	B. Systems & Cable Terminations	FS / OP	ME	FS	FS		
	C. Communications System/Switchboard	FS / OP	A / ME	FS	FS		
14.	COMPUTER SYSTEMS:						
	A. Conduit with pull strings (Empty)	FS / OP / ME	A / ME	GC	GC		Watson
	B. Systems	FS / OP	ME	F	FS		
	C. Cable	OP / ME	A / ME	FS	FS		
	D. Dedicated Elect. Supply	ME	ME	GC	GC		Watson
	E. Property Management System	OP / ME		F	F		
15.	F & B "Point Of Sale" REGISTER SYSTEMS:						
	A. Conduit with pull strings (Empty)	FS / FB / OP / ME	A / FB / ME	GC	GC		Watson
	B. System	FS / FB / OP	FB / ME	F	FS		
	C. Cable	OP / ME	A / ME	FS	FS		
	D. Dedicated Elect. Supply	ME	ME	GC	GC		Watson

16. MATV AND HMS:

A. Conduit with pull strings (Empty)	FS / A / OP	A / ME	GC	GC	Watson
B. System & Cable & Terminations	FS / OP / ME	ME	F	FS	
C. Antenna Fndtns & Support Structure	A	A / ME	GC	GC	
D. Cable/Satellite Dishes/F.V. Roof Antennas	FS / OP / ME	A / ME	F	F	
E. Flat Panel Television Mounting Devices	FS / OP / ME	A / ME	F	GC	Westley

17. PUBLIC & ATRIUM SOUND SYSTEM (P/A & BACKGROUND MUSIC):

A. Conduit with pull strings (Empty)	OP / SC / ME	A / SC / ME	GC	GC	Watson
A. Conduit & Cable & Terminations	OP / SC / ME	A / SC / ME	FS	FS	
B. Equipment & Installation	OP / SC / ME / A	SC / ME / A	F	F	

18. SECURITY / TV SURVEILLANCE SYSTEMS:

A. Conduit with pull strings (Empty)	OP / ME / A	A / ME	GC	GC	Watson
B. System & Cable & Terminations	ME / OP / A	A / ME	F	FS	
C. Mobile Paging & Beeper & Limo Cellular Phone	OP	A / ME	OP	OP	
D. Security System	OP / ME / A	A / ME	F	F	

MISCELLANEOUS:19. INTERIOR LANDSCAPING:

A. Fixed Planters					
B. Movable Planter / Pots	ID / LA	ID / LA	PA	FI	Westley
C. Plants	ID / LA	ID / LA	OP	OP	
D. Planter Liners	A / LA	A	F	F	
E. Atrium Water Feature					Not In Contract

20. EXTERIOR LANDSCAPING:

A. Plants / Trees	LA / A	LA / A	GC	GC	Pleasant Places
B. Irrigation System	LA / A / ME	LA / A / ME	GC	GC	Pleasant Places
C. Water Feature					Not In Contract

21. DECORATIVE BANNER:

A. Decorative Banner					Not In Contract
----------------------	--	--	--	--	-----------------

22. EXTERIOR AWNINGS:

A. Exterior Awnings	A	A	GC	GC	Elite Awnings
---------------------	---	---	----	----	---------------

23. INTERIOR AWNINGS & CANOPIES:

A. Interior Awnings & Canopies					Not In Contract
--------------------------------	--	--	--	--	-----------------

24. MOVABLE UMBRELLAS:

A. Movable Umbrellas	ID	ID	PA	FI	Prem wants Fabric Plan. Westley
----------------------	----	----	----	----	---------------------------------

SPECIALTIES (BY AREAS):25. GUESTROOMS, SUITES & CORRIDORS:

A. Television Sets	OP	A / ME / ID	PA	FI	Westley
B. Radios	OP	A / ME / ID	PA	FI	Radios and Batteries OSE Westley
C. Bathroom Hardware & Fixtures	A / ME	A / ME	GC	GC	BMCC
D. Toilet Accessories	ID / A	A	GC	GC	Warco
E. Minor Closet Doors (If App.) - NONE SHOWN					Not In Contract
F. Microwave	OP / ID	A / ME	PA	FI	Westley
G. Refrigerators	OP / ID	A / ME	OP	FI	Westley
H. Vend. Machines	OP	A / ME	PA	FS	
I. Corridor Ice Machines	FB / OP	FB / ME / A	GC	GC	Added to kitchen equipment Westley
J. Draperies & Valances	ID	ID	PA	FS	Guestroom crown creates valance - By GC LCCM
K. Framed Suite Mirrors	ID	ID	PA	FI	Westley
L. Furnishings	OP / ID	ID	PA	FI	Westley
M. Unframed Mirrors			PA	GC	Framed Mirrors for Vanities By Owner Westley
N. Bedroom "Dry" Vanity w/Top			PA	GC	Not In Contract Westley
O. Bedroom "Wet" Vanity Base			PA	GC	Not In Contract Westley
P. Bedroom "Wet" Vanity (with Integrat Sink)			PA	GC	Not In Contract Westley
Q. Parlor Bar and Top (with Sink Cut-Out)			PA	GC	Not In Contract Westley
R. Parlor Bar Sink / Trim			PA	GC	Not In Contract Westley
S. Wet Vanity Towel Bar DEFINE?	ID / A	ID / A	GC	GC	Only at Manager's Suite Westley
T. Bedding with Correct Mattress Month	ID / A	ID / A	F / PA	GC / FI	
U. Connect and Program all Remotes for Televisions	A / ME	A / ME	F	OP	DCI commented this should be Hotel Staff
V. Provide and Install Batteries to Alarm Clocks	OP	OP	GC	OP	DCI commented this should be Hotel Staff
W. Assemble and Place Baby Beds/Roll-Away Beds	OP	OP	F	OP	DCI commented this should be Hotel Staff
X. Hair Dryers	OP	OP	F	OP	DCI commented this should be Hotel Staff
Y. Irons and Ironing Boards	OP	OP	F	OP	DCI commented this should be Ho
Z. Guestroom Shower Curtain Rod Cover and Shower Curtain					Not In Contract
AA. Framed Guestroom Dressing Mirrors	ID / A	ID / A	F / PA	GC	Westley
BB. Guestroom Iron Caddies	ID / A	ID / A	GC	GC	As per specs 10001 6, section 2.9 Warco
Guestroom Iron and Ironing Boards	OP	ID / A	F	OP	DCI commented this should be Hotel Staff
CC. Guestroom Undercounter Refrigerators	ID / A	ID / A	F	FI	Westley
Managers Apartment Appliances	ID / A	ID / A	GC	GC	BBC has \$5 k allowance. Warco
Employee Break Room Appliances	A	ID / A	F	GC	Westley
DD. Guestroom Safes	ID / A	ID / A	F / PA	GC	Westley
Cabana's Refrigerator and Safe	ID / A	ID / A	F	GC	Westley
EE. Guestroom Painted Closet Shelf units	ID / A	ID / A	GC	GC	LCCM
FF. Millwork Corner Units From Floor to Ceiling @ all Bedroom in Guestrooms	ID / A	ID / A	F / PA	GC	LCCM

26. BACK OF HOUSE / SERVICE AREAS:

A. Wall Protection Bumpers	A	A	GC	GC	Warco
B. Corner Guards	A	A	GC	GC	Warco
C. Fire Extinguisher	A	A	GC	GC	Warco
D. Trash Compactor	OP / A / FB	A / FB / ME	OP	FS	
Electrical Hook-Up	OP / A / FB	A / FB / ME	GC	GC	Watson
E. Lockers & Benches	A	A	GC	GC	Warco
F. Shelving (Fixed)	OP / FB / A	A / FB	GC	GC	Loose Shelving By Owner
G. Vending (Empl. Dining)					Not In Contract
H. Laundry Equipment	LC	LC / A / ME	F	F	No Bids - no po
I. Rough-In / Rigging / Hook-Up	LC / ME	ME	GC	GC	MCC has duct connection a
J. Assemble and Place Luggage Carts in Designated Locations	OP / FB / A	A / FB	F	OP	
K. Assemble and Place House Keeping and Maintenance Carts in Designated Locations	OP / FB / A	A / FB	F	OP	
L. Assemble and Place Ash/Trash Containers In Designated Areas	OP / FB / A	A / FB	F	OP	
M. Assemble and Set Housekeeping Vacuums	OP / FB / A	A / FB	F	OP	

Employee Linen Area Ice Machines						Not In Contract	Not In Contract
O. Co.	o'a	nd Roo	rk Table	OP / FB / A	F	GC	
P. Commercial Washers, Dryers, Drainage Trough, and Lint Filter							
				OP / FB / A	A / FB	F	F
27. KITCHEN & PANTRIES:							
A. Kitchen Hoods				FB	FB / ME	GC	GC
B. Kitchen Exhaust Ventilation Ductwork & Fns				FB / ME	ME	GC	GC
C. Installation - Fire Protection (Ansul System)				FB	FB / ME	GC	GC
D. Walk-IN Refrig. Pre-Fab Boxes & Refrig. System				FB	FB / ME / A	GC	GC
E. Insulated Floor Slab & Finish							Not In Contract
F. Conduit For Refrig. Lines				FB / ME	FB / ME	GC	GC
G. Kitchen Equip.				FB	FB	F	F
H. Rough-In / Rigging / Hook-Up				FB / ME	FB / ME	GC	GC
I. Blocking (as required)				FB / A	A	GC	GC
J. Hand Sinks				FB / ME	FB / ME	GC	GC
K. Floor Sinks				FB / ME	FB / ME	GC	GC
L. Trench Drains & Grates				FB / A	A / ME	GC	GC
M. Shelving (Stainless Steel or Loose Shelving)				FB	FB	GC	GC
N. Beverage Dispens. Sys. (Beer, Wine, Liquor, Soda)				FB	ME / FB	F	FS
O. Conduit (Soda Lines)				FB	A / ME	GC	GC
28. FOOD AND BEVERAGE / BANQUET FACILITIES:							
A. Track Lighting (including Lamps)				ID / LD	A / LD / ME	GC	GC
B. Dimming Systems				ID / LD / ME	A / LD / ME	GC	GC
C. Project Screens Motorized				ID / A	A / ME	GC	GC
D. Banquettes & Booths				ID	ID	PA	FS
E. Furnishings				ID	ID	PA	FI
F. Wall Mounted A / V Units				ID	ID / A	F	FS
G. Sound System				ME / A	ME / A	F	F
Conduits with pullstrings (Empty)				ME / A	ME / A	GC	GC
29. COMMERCIAL AREAS:							
A. Telephone Enclosures							Not In Contract
B. Toilet Accessories				A / ID	A	GC	GC
C. Sculpture / Artwork				ID / A	ID	PA	FI
D. Furnishings				ID	ID	PA	FI
F. Upholstered Seating				ID	ID	F	FI
30. ADMINISTRATION AREAS:							
A. Cashier's Drop Safe (Built-In)				OP/A/ID	A	GC	GC
B. Safe Deposit Boxes (Built In)				OP/A/ID	A	GC	GC
C. Front Desk Modules				OP/A/ID	A / ID	PA	GC
D. Furnishings				ID	ID	PA	F
E. Depository Safe for Front Office				A	A	GC	GC
F. Guest Safety Deposit Boxes				A	A	DELETE	DELETE
31. UPPER CRUST: Patisserie							
A. Equipment				FB/OP/ID/A	ID/ID/A/ME	GC	GC
B. Millwork				FB/OP/ID/A	FB/ID/A/ME	GC	GC
C. Finishes/Lighting				ID/A	ID / A/ME	GC	GC
D. Display Fixtures/Racks				ID/A	ID / A/ME	GC	GC
creational Areas:							
A. Pool Tables and Accessories							Not In Contract
B. Elect. Games							Not In Contract
C. Exercise Equipment				A/ID/OP	ID / A/ME	F	FS
D. Wall Mirror				ID/A	ID/A	GC	GC
E. Sauna							First Choice Glass
F. Furn. Rings				ID/A	ID/A	PA	3
G. Ext. Recreation Equipment							Not In Contract
H. Fitness Equipment				A/ID/OP	ID/A	F	F
33. Signage:							
A. Interior/Directional				ID	ID/A/ME	F	FS
B. Code/Life Safety				ID/A	ME/A	F	FS
C. Exterior				OP/A/BS	A/ME/BS	F	FS
D. Pavement Markings & Codes				A	A	GC	GC
E. Signage FNDTNS, Supplies							Not In Contract
F. Signs-H/C Parking & Guest Reg.				ID/A	A	F	F
G. Pool Deck Signage				BS/ID/A	A	F	F
H. Six Total Flags							Not In Contract
I. Site and Building Mounted Signs				ID/A	A	F	F
J. Bronze Letters at Exterior Canopies				ID/A	A	F	F
34. Parking Control Arm							
A. Equipment							Not In Contract
B. Power Rough-In							Not In Contract
C. Conduit (Empty)							Not In Contract
35. General Conditions:							
A. Site and Building Utility System Pressure Testing				A/ME	A/ME	GC	GC
B. Provide 40' Storage Containers for Owners FF&E				A	A	F	F
C. Window Treatments				ID	ID	F	FS
D. Building Permit and Impact Fees - (Environmental Impact Fees, Tap Fees, Encroachment Permit Fees, Utility Company Fees, User Fees, Development Fees and Assessments)				A	A	F	F
E. Builders Risk Insurance				A	A	F	F
F. Exterior Mock-Up				A	A	GC	GC
G. Appliances, Bar Equipment, Hotel Equipment, Office Furniture				A / ID	A / ID	F	OP
H. Entrance Mats				ID / OP	ID / OP	F	F
36. First Floor FFE:							
Foyer							
A. Built in Banquette w/Tufted Back				ID	ID	PA	GC
B. Table (Round)				ID	ID	PA	GC
Rotunda							
A. Mirrors				ID	ID	PA	GC
B. Chandelier				ID	ID	PA	GC
C. Wallcovering Mural				ID	ID	PA	GC
Stair 1 & 2							
A. Decorative Fixture				ID	ID	PA	GC
B. Carpet Pad				ID	ID	PA	GC

	C. Window Treatments	ID	ID	PA	OWNER		
	D. Window Treatments at Foyer	ID	ID	PA	OWNER		
	Concierge						
	A. Desk	ID	ID	PA	GC / FI		Westley
	B. Chairs	ID	ID	PA	GC / FI		Westley
	C. Wall Sconces	ID	ID	PA	GC		Watson
	D. Area Rug	ID	ID	PA	GC / FI		Westley
	Private Seating by Concierge						
	A. Sofa	ID	ID	F / PA	GC / FI		Westley
	B. Coffee Table	ID	ID	F / PA	GC / FI		Westley
	Elevator Lobby						
	A. Sculptures/Urns	ID	ID	F / PA	GC / FI		Westley
	Public Restrooms						
	A. Decorative Mirrors	ID	ID	F / PA	GC / FI		Westley
	B. Bench	ID	ID	F / PA	GC / FI		Westley
	Lobby (Option A)						
	A. Accessories	ID	ID	F / PA	GC / FI		Westley
	B. Medium Size Lounge Chairs	ID	ID	F / PA	GC / FI		Westley
	C. Square Ottoman	ID	ID	F / PA	GC / FI		Westley
	D. Table Lamps @ Console Tables	ID	ID	F / PA	GC / FI		Westley
	E. Chest	ID	ID	F / PA	GC / FI		Westley
	Ellipse Cocktail Lounge FFE:						
	A. Bar Stools	ID	ID	F / PA	GC / FI		Westley
	B. Drink Table (Round)	ID	ID	F / PA	GC / FI		Westley
	C. Floating Banquette	ID	ID	F / PA	GC / FI		Westley
	D. Built In Banquette / Tufted Back	ID	ID	F / PA	GC / FI		Westley
	E. Wall Sconces	ID	ID	F / PA	GC / FI		Westley
	F. Padded Walls	ID	ID	F / PA	GC / FI		LCCM
	Patisserie FFE:						
	A. Bar Stools	ID	ID	F / PA	GC / FI		Westley
	First Floor Restaurant (Option A) FFE						
	A. Oversized Armless L Shaped Banquette	ID	ID	F / PA	GC / FI		Westley
	B. Serving Buffett	ID	ID	F / PA	GC / FI		Trimark
	C. Pedestals	ID	ID	F / PA	GC / FI		Westley
	Restaurant Level 1 & 2						
	A. Drapery Treatment	ID	ID	FS	FS		
	Prefunction						
	A. Breakfront	ID	ID	F / PA	GC / FI		Westley
	Boardroom FFE						
	A. Drapery and Drapery Hardware Sets	ID	ID	FS	FS		
	B. Rug	ID	ID	F / PA	GC / FS		Westley
	Ballrooms (1-4)						
	A. Folding Tables	ID	ID	F / PA	GC / FS		Westley
	B. Console	ID	ID	F / PA	GC / FS		Westley
	C. Table Lamps at Console	ID	ID	F / PA	GC / FS		Westley
	Men's and Women's Public Bathrooms						
	A. Sconce at Vanity	ID	A / ME / ID / LD	F / PA	GC		Watson
	Bridal Suite						
	A. Tufted Sectional Sofa	ID	ID	F / PA	GC / FI		Westley
37.	Spa Reception - 2nd Floor FFE:						
	A. Decorative Ceiling Fixture	ID	A / ME / ID / LD	F / PA	GC		Watson
	Treatment Rooms						
	A. Spa Equipment by Others	F	F	F / PA	GC		Westley
	Bathing Stations						
	A. Shower Curtains	ID	ID	F / PA	GC / F		Westley
	Spa Retail First Floor						
	A. Retail Display - Built-In Millwork Unit	ID	A / ID	GC	GC	BBC only includes built-in wood millwork units.	LCCM
	A. Retail Display - Equipment Vendor Unit (By Vendor)	ID	A	F	FI	By Vendor.	By Vendor.
	B. Consultant Desk	ID	ID	F / PA	GC / FI		Westley
	Fitness Center						
	A. Towel Stations	ID	ID	F / PA	OP		
38.	Pool Area FFE:						
	Cabana						
	A. Ceiling Fans @ Pool	A / ID	A / ID	F / PA	GC		Watson
	Pool						
	A. Double Chaise Lounge	ID	ID	F / PA	GC / FI		Westley
	B. Planters - Portable	ID	ID	F / PA	GC / FI		Westley
	C. Feature Lighting	A	A	F	GC		Watson
39.	Concierge Lounge FFE:						
	Concierge Lounge						
	A. Cocktail Table (Small)	ID	ID	F / PA	GC / FI		Westley
40.	Guestroom FFE:						
	Typical King Guestrooms						
	A. Decorative Ceiling Fixture	ID	ID	F / PA	GC / FI		Watson
	B. Night Stands - Stone Tops	ID	ID	F / PA	GC / FI		Westley - stone top is not
	C. Reading Lights at Night Stands	ID	ID	F / PA	GC / FI		Not In Contract
	D. Lamp at Night Stands	ID	ID	F / PA	GC / FI		Westley
	E. Fully Upholstered Bed	ID	ID	F / PA	GC / FI	Change order required, not knockdown	Westley
	F. Decorative Pillow at Bed	ID	ID	F / PA	GC / FI		Westley
	G. TV Chest	ID	ID	F / PA	GC / FI	Change order required, not knockdown	Westley
	H. Upholstered Wall at TV/Chest Wall	ID	ID	F / PA	GC / FI	Change order required, not knockdown	Westley
	I. Bookcase	ID	ID	F / PA	GC / FI		LCCM
	J. Art & Accessories at Bookcases	ID	ID	F / PA	GC / FI		Westley
	K. Mattress and Boxspring	ID	ID	F / PA	GC / FI		Westley
	Typical King Suite						
	A. Upholstered Chair	ID	ID	F / PA	GC / FI		Westley
	B. Armore	ID	ID	F / PA	GC / FI		Westley

Tab No. 161

Balfour Beatty Construction

August 26, 2017

Ms. Kim Brown
Bennett Hospitality
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 161
Offsite Mock Up Drywall and Plumbing Reconciliation

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 161 in the amount of Seventeen thousand three hundred seventy-six (\$17,376.00) to provide additional work in accordance with the following qualifications:

- o Precision Walls cost for additional scope and rework – \$7,644
- o BMCC cost to install additional plumbing fixtures for owner selection - \$8,928

This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Alec Dooley
Assistant Project Manager

cc:
Melissa Pense
Marty Wall
Jim Clements
Jennifer Faulkinberry
Woody Faust
Nick Starcevic
Tim Spano
David Stanton

RCO # 161 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 161– Offsite Mock Up Drywall and Plumbing Reconciliation

The additional work for the **Offsite Mock Up Drywall and Plumbing Reconciliation** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.51500000.40	Offsite Mock Up Drywall and Plumbing Reconciliation	\$8,928.61
2	400.50925200.40	Offsite Mock Up Drywall and Plumbing Reconciliation	\$7,644.00

Total Items \$16,572.61

Total Markups \$803.39

RCO Total \$17,376.00

The total Cost to perform the work as described above is an ADD of Seventeen thousand three hundred seventy-six (\$17,376.00).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Bennett Hospitality

RCO# 161

**REQUEST FOR CHANGE ORDER**

Ref.# CO-17570

GC #

Date Sep 27, 2016

Job # 14-1278

To: **Balfour Beatty Construction**
 406 S McDowell Street, Suite 200
 Raleigh, NC 27601
 Phone: (919)233-5001

Project: **Hotel @ Marion Square**
 404 King Street
 Charleston, SC 29403

Description: Offsite Model Room Revisions per Owner/BBC Request

Labor	Total Hrs	Rate	Total
Metal Framing	182.00	42.00	\$7,644.00
	Total Labor		\$7,644.00
Material			
		Total Material	\$0.00
	Subtotal for Detail		\$7,644.00
Miscellaneous			Total
Freight and Delivery Expense			\$0.00
Tool & Equipment Expense 10%			\$0.00
	Total Miscellaneous Charges		\$0.00
Adjustments			Total
ROUNDING			\$0.00
	Total Adjustments		\$0.00

Notes: Make various offsite model room revisions due to drawing revisions / owner & BBC direction. Please reference attached extra work orders for verification of time. All labor ours are included in the metal framing category at our standard mechanic rate of \$42.00 per hour.

- Prices firm for 7 days and based on current job conditions
- Contract time extension of: 1 days
- Material delivery time of: 5 days
- We will not proceed with this work without a written Change Order


 Michael Thomas Zinna
 Project Manager

Adjustments Total:	\$0.00	
Sub Total:	\$7,644.00	
Sales Tax on Materials:	\$0.00	8.50%
OH&P (Material & Equipment):	\$0.00	15.00%
Sub Total:	\$7,644.00	
Total:	\$7,644.00	

EXTRA WORK ORDER

DATE 12-7-15

G.C. JOB #

PWI JOB # 14-RBPROJECT NAME: Marion Square HotelPROJECT MANAGER: Michal ZinnaTO: PRECISION WALLS, INC.FROM: Belfort

AUTHORIZATION FOR PAYMENT AND COMMENCEMENT OF WORK:

SIGNATURE

TITLE:

DATE:

BRIEF DESCRIPTION AND LOCATION OF WORK: Framed 6" curb at the tub, soffit for door at tub. Dropped beath hallway ceiling, changed Helder Hight at window in quins room. redo the blocking framed radias ciling, Faring, Hanging ciling and walls in room, Insulation.

QUANTITY	UNIT	DESCRIPTION OF MATERIAL OR EQUIPMENT	UNIT PRICE	EXTENSION

TOTAL MAT'L \$

NAME	CODE	MON	TUE	WED	THU	FRI	SAT	SUN	TOTAL HOURS	EXTENSION
Maxwell Brasington	103	8	8	8					24	24
Enrique Hernandez	103	8							8	8
HOZE	803	8							8	8
Enrique Hernandez	201			4	4	4			12	
	225			4	4	4			12	
HOZE	201			4	4				8	
HOZE	225			4	4	8			16	
Maxwell Brasington	100				8				8	8
									96	40

HOURS TO DATE: _____

WORK APPROVED

AS COMPLETED

SIGNATURE: Robert Coffman

48 Hr.
Verified
Repair

TITLE: _____ DATE: _____

SIGNATURE: _____

TITLE: _____ DATE: _____

____ INCOMPLETE ____ COMPLETE

This extra work order will/may increase the duration allotted for the performance of our work.

Please adjust the schedule accordingly.

WORK ORDER _____

EXTRA WORK ORDER

DATE 12-14-15

G.C. JOB # _____

PWI JOB # 14-1278PROJECT NAME: Hotel (mockup)PROJECT MANAGER: Michael Z. nraTO: PRECISION WALLS, INC.FROM: Balfor BeattyAUTHORIZATION FOR PAYMENT AND COMMENCEMENT
OF WORK:

SIGNATURE _____

TITLE _____

DATE _____

BRIEF DESCRIPTION AND LOCATION OF WORK: Reframed window, Hang drywall at window.
Tepe, fill screw holes corner bead. insulated walls. got trash out.

QUANTITY	UNIT	DESCRIPTION OF MATERIAL OR EQUIPMENT	UNIT PRICE	EXTENSION

TOTAL MAT'L \$ _____

NAME	CODE	MON	TUE	WED	THU	FRI	SAT	SUN	TOTAL HOURS	EXTENSION
Maxwell Brasington	400	4							4	
Maxwell Brasington	201	2	6	8	4	5			25	9
Maxwell Brasington	103	2	2						4	
Honey Garcia	301	8	8						16	
Maxwell Brasington	463				2				2	2
Maxwell Brasington	301				2				2	2
		18	8	8	8	5			53	13

HOURS TO DATE: _____

WORK APPROVED
AS COMPLETEDSIGNATURE: Maxwell BrasingtonTITLE: ForemanDATE: 12-14-15SIGNATURE: Robert Colman

TITLE: _____ DATE: _____

INCOMPLETE

COMPLETE

SUPERVISION

SAFETY

TOTAL LABOR \$ _____

OTHER DIRECT COSTS

TOTAL \$ _____

This extra work order will/may increase the duration allotted for
the performance of our work.
Please adjust the schedule accordingly.

WORK ORDER _____

Customer - White Project Manager - Canary GC Superintendent - Pink Foreman - Goldenrod

1 OF _____

R - 1772

EXTRA WORK ORDER

DATE 7-4-16

G.C. JOB #

PWI JOB # 14-12-16

PROJECT NAME:

PROJECT MANAGER:

TO: PRECISION WALLS, INC.

FROM: Debra Bontje

AUTHORIZATION FOR PAYMENT AND COMMENCEMENT OF WORK:

SIGNATURE

TITLE:

DATE: _____

BRIEF DESCRIPTION AND LOCATION OF WORK: Demo Bumpouts in the hallway, Hong Kong in that place. Demo Sefit by the tank and hang dry wall and Fin. move header of part 2015, Hang ~~SE~~

[illegible]

NAME	CODE	MON	TUE	WED	THU	FRI	SAT	SUN	TOTAL HOURS	EXTENSION
Omarwaen B	482			8	8	8	8		32	
Colby	482					10	10		20	
Maras Rosal do	301			4	8				12	
				12	6	18	18		64	

HOURS TO DATE:

WORK APPROVED

AS COMPLETED

SIGNATURE:

TITLE: _____ DATE: _____

SIGNATURE: _____

TITLE: _____ DATE: _____

_____ INCOMPLETE _____ COMPLETE

This extra work order will/may increase the duration allotted for the performance of our work.

Please adjust the schedule accordingly.

Customer - White Project Manager - Canary GC Superintendent - Pink Foreman - Goldenrod

1 OF _____

R - 1773

WORK ORDER

EXTRA WORK ORDER

DATE 1-25-65

G.C. JOE #

PWI JOB # 14-1278

PROJECT NAME: maxion sq hotel morad

PROJECT MANAGER: Michael Z. HKA

TO: PRECISION WALLS, INC.

FROM: Bol/For Beatty

AUTHORIZATION FOR PAYMENT AND COMMENCEMENT OF WORK:

SIGNATURE

TITLE:

DATE: _____

BRIEF DESCRIPTION AND LOCATION OF WORK: Installed 2 layers on the living room ceiling above the tub. Framed, Hand Finish soffits in entry of shower and toilet doors the concrete column and re Hang it. Frame, Hand Finish soffits in the Queens room. Patch a hole in the ceiling from Port Fan. Add Ac.

[illegible]

TOTAL MAT'L.

§

[illegible]

HOURS TO DATE: -
WORK APPROVED
AS COMPLETED
SIGNATURE:

TITLE: _____ DATE: _____

SIGNATURE: _____

TITLE: _____ DATE: _____

 INCOMPLETE COMPLETE

**This extra work order will/may increase the duration allotted for the performance of our work.
Please adjust the schedule accordingly.**

SUPERVISION

SAFETY

TOTAL LABOR

OTHER DIRECT COSTS

TOTAL

57

Customer - White Project Manager - Canary GC Superintendent - Pink Foreman - Goldenrod

1 OF _____

R - 1774

EXTRA WORK ORDER

DATE 7-21-16

G.C. JOB #

PWI JOB # 14-278

PROJECT NAME: Merion Savane

PROJECT MANAGER: Mike Zinner

**AUTHORIZATION FOR PAYMENT AND COMMENCEMENT
OF WORK:**

SIGNATURE

TITLE:

DATE: _____

TO: PRECISION WALLS, INC.

FROM:

BRIEF DESCRIPTION AND LOCATION OF WORK:

Interior Mock Ceiling Revisions

[illegible][illegible]

HOURS TO DATE: 23

WORK APPROVED

AS COMPLETED

SIGNATURE

TITLE:

DATE:

SIGNATURE:

TITLE:

DATE:

INCOMPLETE

COMPLETE

SUPERVISION

SAFETY

TOTAL LABOR

OTHER DIRECT COSTS

TOTAL

~~This extra work order will/may increase the duration allotted for the performance of our work.~~
~~Please adjust the schedule accordingly.~~

WORK ORDER



BERNHARD MCC, L.L.C.

June 3, 2016

Balfour Beatty Construction
306 Meeting St. /Suite 300
Charleston, SC 29401

Attn: Tim Spano

REF: The Hotel at Marion Square
Contract Number: 13026000
BMCC Project Number: 8350248

SUBJ: BMCC PCO No: 025
Mock Up Fixtures

Gentlemen,

Bernhard MCC has received changes as defined in the Mock-up Fixtures, and we have confirmed that our scope of work is impacted compared to contract fixture schedule. The attached proposals collectively define the impacts identified in each issuance of documents. The total cost of these changes is \$ 9,722.10

The following clarifications and exclusions apply to this proposal:

1. The cost of this proposal includes only those direct costs for changes which are clearly identified (clouded) on the revised documents. If changes were made but not notated as such, we have not accounted for them and any such costs would be recovered at the point such are identified.
2. This proposal does not include any overtime or provisions for extended general conditions. If any such costs are required, we reserve the right to recover same.
3. Scope quoted herein aligns with the scope defined in our original subcontract and therefore all exclusions, clarifications, etc. apply equally to this proposal.

If you have any questions, please contact us as soon as possible. This proposal remains in effect for 30 days.

Sincerely,

Bernhard MCC, L.L.C.

Eric Stoehr
Project Manager

ES/SD

Attachment



MCC Mechanical of the Carolinas, LLC

Proposed Change Summary

Project: **The Hotel at Marion Square**
Location: **Charleston, SC**

Date: May 26, 2016

MCC Job No: 8350248
MCC PCO #: 25

Description: Interior Mock Up Fixtures

Labor Breakdown					
Std Hrs	Prem Hrs		Std Rate	Prem Rate	
8.0	0.0	Project Manager	\$80.00	\$120.00	\$640.00
10.0	0.0	Superintendent	\$75.00	\$112.50	\$750.00
20.0	0.0	Foreman	\$51.00	\$76.50	\$1,020.00
0.0	0.0	Journeyman	\$37.00	\$55.50	\$0.00
0.0	0.0	Start-up Technician	\$88.00	\$132.00	\$0.00
0.0	0.0	BIM Coordinator	\$70.00	\$105.00	\$0.00
0.0	0.0	Detailer	\$53.00	\$79.50	\$0.00
16.0	0.0	Laborer	\$23.00	\$34.50	\$368.00
0.0	0.0	Helper	\$15.00	\$22.50	\$0.00
0.0	0.0	Field Engineer	\$51.00	\$76.50	\$0.00
1.0	0.0	Safety	\$64.50	\$96.75	\$64.50
1.0	0.0	Clean Up	\$15.00	\$22.50	\$15.00
0.0	0.0	Estimator	\$51.00	\$76.50	\$0.00
Subtotal					\$2,857.50
Field Office / Drawings / Copies					\$50.00
Travel & Lodging					\$0.00
Purchasing					\$142.88
Small Tools					\$0.00
Tool Rental					\$0.00
Quality Control					\$0.00
Consumables					\$57.15
Subtotal					\$250.03
Overhead & Profit: 15.0%					\$466.13
Subtotal Labor					\$3,573.65

Material Breakdown	Item Description	Cost	Tax	Net
PVF Materials		\$0.00	\$0.00	\$0.00
Equipment	Fixtures	\$4,927.63	\$418.85	\$5,346.48
Equipment rental		\$0.00	\$0.00	\$0.00
Parking		\$0.00	\$0.00	\$0.00
Permits		\$0.00	\$0.00	\$0.00
Seismic		\$0.00	\$0.00	\$0.00
X-Ray/Core Drill		\$0.00	\$0.00	\$0.00
Total Materials				\$5,346.48

Tax Rate: 8.50%

Overhead & Profit: 15.0% \$801.97

Subtotal Material & Equipment \$6,148.45

Subcontract Breakdown	Item Description	Cost		Total
Sheet metal		\$0.00		\$0.00
Insulation		\$0.00		\$0.00
Temperature Controls		\$0.00		\$0.00
Test & Balance (BY OTHERS)		\$0.00		\$0.00
Fire Caulk		\$0.00		\$0.00
Med Gas		\$0.00		\$0.00
Locate Services		\$0.00		\$0.00
BIM Coordinator		\$0.00		\$0.00
Subtotal				\$0.00

Overhead & Profit: 15.0% \$0.00

Subtotal Subcontractor Costs \$0.00

Total Cost \$9,722.10

Schedule Comments: (0) days schedule extension requested for this change, however, we reserve the right to examine the impact of this change on the overall schedule at a later date, and request appropriate time or cost compensation should the accumulative effect of this or

R - 1777

other changes warrant.



FERGUSON ENTERPRISES INC #23
4711 RIVERS AVE
N CHARLESTON, SC 29405-6645

Deliver To: scott.windsor@ferguson.com
From: Scott Windsor
Comments:

21:09:45 MAY 10 2016

FERGUSON ENTERPRISES INC #34

Price Quotation
Phone : 843-747-6301
Fax : 843-554-8799

Page # 1

PCD 025

Bid No.....: B330740

Bid Date.....: 04/14/16

Quoted By.: MBH

Cust 504-846-5223

Terms.....: NET 10TH PROX

Customer: MCC MECHANICAL LLC
MARION SQUARE HOTEL
3001 17TH STREET
METAIRIE, LA 70002

Ship To: MCC MECHANICAL LLC
MARION SQUARE HOTEL
3001 17TH STREET
METAIRIE, LA 70002

Cust PO#...: MOCK UPS

Job Name: MARION SQUARE HOTEL

Item	Description	Quantity	Net Price	UM	Total
	QUEEN SUITE				
	TUB				
SP-MS196	MTI S196 ALISSA 4 SOAKING TUB	1	2099.000	EA	2099.00
SP-MTIWIOBN	*MTI*DRAIN COLOR UPCHARGE BN	1	0.000	EA	0.00
K16210-4A-BN	CCY 2HDL LEV BATH FCT W/ H/SHWR BN	1	1332.670	EA	1332.67
K101-BN	WM ADPT KIT *ANTIQU BN	1	228.100	EA	228.10
	SUBTOTAL				3659.77

	LAVATORY				
	LAVATORY BY OTHERS				
M9700	LF 2HDL 2H WM VLV ADJ 1/2 CC CONN	1	86.480	EA	86.48
MT6107BN	CCY LF TRIM KIT F/ 2HDL WM BN 1.2	1	241.860	EA	241.86
M123816BN	GRID DRN W O O FLOW BN	1	55.801	EA	55.80
PFPTB101	1-1/4 17GA P TRAP W/CO CP	1	22.350	EA	22.35
	NO SUPPLY KIT				
	SUBTOTAL				406.49

	TOILET				
K5626-0	CCY 1.28 12 EB *COMHEI BOWL WHIT	1	212.189	EA	212.19
K4434-0	CCY @ CLST TANK *MEMSTA WHIT 1.28	1	141.890	EA	141.89
K4636-0	@ EB PLAS CLST SEAT *CACHET WHIT	1	26.470	EA	26.47
K1160316-BN	TRIP LEV SERV KIT VBN1	1	45.250	EA	45.25
MB208BN	LF 1/2 SWT X 3/8 COMP ANG VLV BN	1	40.780	EA	40.78
MB241BN	3/8X12 RIGID CLST TUBE PVBN	1	10.070	EA	10.07
PFWR	STD WAX RING	1	0.690	EA	0.69
PFC9110	1/4X3-1/2 BRS CLST BLT OVAL PR	1	1.360	PR	1.36
	SUBTOTAL				478.70

USE IN HOTEL

354.08



FERGUSON ENTERPRISES INC #34

Price Quotation

Page # 2

21:09:45 MAY 10 2016

Phone : 843-747-6301

Fax : 843-554-8799

Reference No: B330740

Item	Description	Quantity	Net Price	UM	Total

SHOWER					
KP304-KS-NA	2.5 GPM WM P/BAL VLV *RITTEM	1	58.460	EA	58.46
KT16117-4A-BN	1HDL P/BAL VLV TRIM *REVIVA BN	1	193.110	EA	193.11
K10591-BN	CCY MFUNC SHWRHD *BANCRO BN	1	65.610	EA	65.61
K7397-BN	@ SHWR ARM & FLG BN	1	51.070	EA	51.07
K9136-BN	@ TI SQ SHWR DRN	1	60.820	EA	60.82
	SUBTOTAL				429.07

KING SUITE					
SP-MS196	MTI S196 ALISSA 4 SOAKING TUB	1	2099.000	EA	2099.00
SP-MTIWIOBN	*MTI*DRAIN COLOR UPCHARGE BN	1	0.000	EA	0.00
K16210-4A-BN	CCY 2HDL LEV BATH FCT W/ H/SHWR BN	1	1332.670	EA	1332.67
K126-BN	26 BATH FCT RSR TUBE *ANTIQU BN	1	155.000	EA	155.00
	SUBTOTAL				3586.67

LAVATORY					
BOWL BY OTHERS					
M69000	LF 2.0 2HDL W/SPRD LAV RI VLV	1	56.815	EA	56.82
MT6125BN	CCY LF 2HDL LEV W/SPRD TRIM BN 1.2	1	258.143	EA	258.14
PFPTB101	1-1/4 17GA P TRAP W/CO CP	1	22.350	EA	22.35
BR1912AXC	LF CP 1/2X12 SWT ANG LAV SPLY KIT	1	28.000	EA	28.00
	SUBTOTAL				365.31

TOILET					
K5626-0	CCY 1.28 12 EB *COMHEI BOWL WHIT	1	212.189	EA	212.19
K4434-0	CCY @ CLST TANK *MEMSTA WHIT 1.28	1	141.890	EA	141.89
K4636-0	@ EB PLAS CLST SEAT *CACHET WHIT	1	26.470	EA	26.47
K1160316-BN	TRIP LEV SERV KIT VBN	1	45.250	EA	45.25
MB208BN	LF 1/2 SWT X 3/8 COMP ANG VLV BN	1	40.789	EA	40.79
MB241BN	3/8X12 RIGID CLST TUBE PVB	1	10.070	EA	10.07
PFWR	STD WAX RING	1	0.690	EA	0.69
PFC9110	1/4X3-1/2 BRS CLST BLT OVAL PR	1	1.360	PR	1.36
	SUBTOTAL				478.71

SHOWER					
KP304-KS-NA	2.5 GPM WM P/BAL VLV *RITTEM	1	58.460	EA	58.46
KT16117-4A-BN	1HDL P/BAL VLV TRIM *REVIVA BN	1	193.110	EA	193.11
K10591-BN	CCY MFUNC SHWRHD *BANCRO BN	1	65.610	EA	65.61
K7397-BN	@ SHWR ARM & FLG BN	1	51.070	EA	51.07

USE IN HOTEL

354.08

R - 1780

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108



FERGUSON ENTERPRISES INC #34

Price Quotation

Page # 3

21:09:45 MAY 10 2016

Phone : 843-747-6301

Fax : 843-554-8799

Reference No: B330740

Item	Description	Quantity	Net Price	UM	Total
K9136-BN	@ TI SQ SHWR DRN	1	60.820	EA	60.82
	SUBTOTAL				429.07
Net Total:					\$9833.79 - 4906.16
Tax:					\$835.93
Freight:					\$0.00 4927.63
Total:					\$10669.72

Quoted prices are based upon receipt of the total quantity for immediate shipment (48 hours). SHIPMENTS BEYOND 48 HOURS SHALL BE AT THE PRICE IN EFFECT AT TIME OF SHIPMENT UNLESS NOTED OTHERWISE. Seller not responsible for delays, lack of product or increase of pricing due to causes beyond our control, and/or based upon Local, State and Federal laws governing type of products that can be sold or put into commerce. This quote is offered contingent upon the buyer's acceptance of Seller's terms and conditions, which are incorporated by reference and found either following this document, or on the web at http://wolseley.com/terms_conditionsSale.html. Govt Buyers: All items are open market unless noted otherwise.

LEAD LAW WARNING: It is illegal to install products that are not "lead free" in accordance with US Federal or other applicable law in potable water systems anticipated for human consumption. Products with "NP" in the description are NOT lead free and can only be installed in non-potable applications. Buyer is solely responsible for product selection.

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

Tab No. 178

Balfour Beatty Construction

October 10, 2017

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 178
Delivery and Storage for DC-67

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 178 in the amount of Two thousand two hundred forty-five (\$2,245.84) to provide additional work in accordance with the following qualifications:


Storage for (2) months: \$462.
Delivery Charges \$420 (min) x 4 Deliveries = \$1,680.

Total: \$2,142.00

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set forth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Nick Starcevic
Project Manager

cc:
Jennifer Faulkinberry
Marty Wall
Jim Clements
Woody Faust
David Stanton
Tim Spano
Alec Dooley

RCO # 178 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 178— Delivery and Storage for DC-67

The additional work for the **Delivery and Storage for DC-67** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.51200001.40	Storage and Devliery for DC-67	\$1,680.00
2	400.51200001.40	(2) months storage for DC-67	\$462.00

Total Items \$2,142.00

Total Markups \$103.84

RCO Total \$2,245.84

The total Cost to perform the work as described above is an ADD of Two thousand two hundred forty-five (\$2,245.84).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 178

Starcevic, Nicholas

From: Robin Money <robin@westleycontract.com>
Sent: Tuesday, October 10, 2017 8:21 AM
To: Starcevic, Nicholas
Subject: RE: DC-67 Storage/Delivery

Storage for Oct & Nov 2017: \$462.
Delivery Charges \$420(min) x 4 Deliveries = \$1,680.

Total: \$2,142.00

Robin Money
Westley Contract Services, LLC
6175 Northbelt Parkway A-1
Norcross, GA 30071
770-797-9400 Phone
770-797-9404 Fax

Visit us at www.westleycontract.com

From: Starcevic, Nicholas [<mailto:NStarcevic@Balfourbeattyus.com>]
Sent: Tuesday, October 10, 2017 8:17 AM
To: Robin Money <robin@westleycontract.com>
Subject: Re: DC-67 Storage/Delivery

4

Nick Starcevic | Balfour Beatty Construction
Cell: 704.361.3265

On Oct 10, 2017, at 8:16 AM, Robin Money <robin@westleycontract.com> wrote:

How many deliveries do you want me to account for?

Robin Money
Westley Contract Services, LLC

6175 Northbelt Parkway A-1
Norcross, GA 30071
770-797-9400 Phone
770-797-9404 Fax

Visit us at www.westleycontract.com

From: Starcevic, Nicholas [<mailto:NStarcevic@Balfourbeattyus.com>]
Sent: Tuesday, October 10, 2017 8:08 AM
To: Robin Money <robin@westleycontract.com>
Subject: Re: DC-67 Storage/Delivery

What's the total to store everything for 2 months?

Nick Starcevic | Balfour Beatty Construction
Cell: 704.361 3265

On Oct 10, 2017, at 8:01 AM, Robin Money <robin@westleycontract.com> wrote:

Nick- Please see quote below to receive, store and deliver the DC-67 fixtures for Marion Square.

Warehouse Handling In & Out: \$150.
Monthly Storage: \$75/per Calendar Month
Valuation: \$26./per Calendar Month
Drayage: \$105/per hour (4 hour Min per delivery)
Admin Fee: \$110.

Please let me know if you want to go ahead and arrange to ship the items to the warehouse.

Thanks.
Robin Money
Westley Contract Services, LLC
6175 Northbelt Parkway A-1
Norcross, GA 30071
770-797-9400 Phone
770-797-9404 Fax

Tab No. 184

Balfour Beatty Construction

November 9, 2017

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 184
Hurricane Irma Prep and Recovery

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 184 in the amount of Fifty-seven thousand four hundred sixty-seven (\$57,467.82) to provide additional work in accordance with the following qualifications:

Pursuant to the terms in Section 8.3.2 and 10.6 in the contract agreement, see below request for additional compensation and extension of time.

On 9/6/17, S.C. Gov Henry McMaster issued a State of Emergency in Charleston County. BBC implanted their Hurricane preparation and included the following costs.

- Premier Exteriors -
 - o Demolition of plank boards and debris netting – 162 man hours.
 - o Replace plank boards and debris netting – 256 man hours
- 1st Choice Glass -
 - o Replace (2) doors on L6 damaged due to Hurricane.
- Balfour Beatty (include Staff Zone) hourly labor -
 - o Stack and bind loose material
 - o Remove and reinstall construction fence netting
 - o Install plywood on to secure doors and over openings in building envelope
 - o Install sand bags at perimeter
 - o Ordered 2" pump to assists in excess water removal
 - o Water removal post Hurricane

We are also requesting a (1) day extension to substantial completion due to the jobsite being closed 9/11/17.

*This change order does not include any mold remediation from water intrusion. The total cost of remediation has not been determined at this time.

Balfour Beatty Construction

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Nick Starcevic
Project Manager

cc:

Jennifer Faulkinberry
Marty Wall
Jim Clements
David Stanton
Tim Spano
Alec Dooley

RCO # 184 - File



Hotel at Marion Square

Request for Change Order # 184– Hurricane Irma Prep and Recovery

The additional work for the **Hurricane Irma Prep and Recovery** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50922050.40	Premier Exteriors Hurricane Irma Prep and Recovery	\$18,810.00
2	400.50880000.40	replace (2) doors from Hurricane Irma	\$20,486.00
3	400.50306510.40	General Labor for Prep	\$15,515.00

Total Items \$54,811.00

Total Markups \$2,656.82

RCO Total \$57,467.82

The total Cost to perform the work as described above is an ADD of Fifty-seven thousand four hundred sixty-seven (\$57,467.82).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 184

Trade: **Stucco**
Sub's Name: **Premier Exteriors, LLC**
Project: **Marion Square Hotel**
Date: **9/29/2017**

Remove and reset all scaffold plank and debris netting in preparation for Hurricane Irma.

Page of

1: All change orders need to be approved before work can commence via written letter or email.

PREMIER EXTERIORS

Jay Bremer (D1)

Inspection Status: Pass

First Inspector: [Premier Exteriors, LLC]

Rodriguez, Jose Luis (Inspection-Superintendent Inspection (91.45.01))

Last Inspector: Rodriguez, Jose Luis

Inspected: 09/07/2017



Last Entry: 09/07/2017

Premier Exteriors, LLC Report #:

1064146


General-Daily Report (CT169)

Project Information	
Builder/Client	Balfour Beatty (1005)
Job	Marion Hotel (1005-1)

Checkpoint	Notes	
DAILY REPORT		
Date:	9-7-17	
Job Name:	Marion square	
#Tradesman/Trade:	25 stucco plasters	
#Laborers:		
Area Working/Work Completed:	North west and south side taking boards and netting down	
		
		
Issues:	West side castone coins need cleaning 6 terrace east and west side stucco need repair South center flashing damage	



Inspection: Pass 9/7/17
Inspector: [Premier Exteriors, LLC] Rodríguez, Jose Luis



General-Daily Report (CT169)

Project Information	
Builder/Client	Balfour Beatty (1005)
Job	Marion Hotel (1005-1)

Inspection Status: Pass

First Inspector: [Premier Exteriors, LLC]

Rodriguez, Jose Luis (Inspection-Superintendent Inspection (91.45.01))

Last Inspector: Rodriguez, Jose Luis

Inspected: 09/13/2017

Last Entry: 09/13/2017

Premier Exteriors, LLC Report #:

1068622

Checkpoint	Notes
DAILY REPORT	
Date:	9-13-17
Job Name:	Marion square
#Tradesman/Trade:	16 stucco plasters
#Laborers:	
Area Working/Work Completed:	North side and west side Install planks
Issues:	

Inspection: Pass 9/13/17

Inspector: [Premier Exteriors, LLC] Rodriguez, Jose Luis



Jay Bremer (D1)

Inspection Status: Pass

First Inspector: [Premier Exteriors, LLC]

Rodriguez, Jose Luis (Inspection-Superintendent Inspection (91.45.01))

Last Inspector: Rodriguez, Jose Luis

Inspected: 09/14/2017

Last Entry: 09/29/2017

Premier Exteriors, LLC Report #:

1069464

General-Daily Report (CT169)

Project Information

Builder/Client	Balfour Beatty (1005)
Job	Marion Hotel (1005-1)

Checkpoint	Notes
DAILY REPORT	
Date:	9-14-17
Job Name:	Marion square
#Tradesman/Trade:	16 stucco plasters 1 super
#Laborers:	
Area Working/Work Completed:	North side install netting West side install planks South side and horseshoe install planks
 	
Issues:	

Inspection: Pass 9/14/17

Inspector: [Premier Exteriors, LLC] Rodriguez, Jose Luis

Change Order Request



Change Order Request

3221-A Westwood Industrial Drive, Monroe, NC – Phone: 704-291-7711 – Fax: 704-291-7011

Submit To:

Change Order Request Number: 000

Name: Tim Spano		Date: 9/29/2017
Company: Balfor Beatty		Fax:
Address:		
City:	State:	Zip:
Reference: Marion Square		

Due to unforeseen complications, adjustments and/or at the customers' request, 1st Choice Glass, Inc... deems it necessary to adjust the agreed upon Job Proposal/Contract as noted per the Warranty & Disclaimer footnote. 1st Choice Glass reserves the right to alter contract in conjunction with customer negotiation to complete and/or vary from the described task. Note that adjustment with description and explanation shall be documented with approval below. Please note, that the requested work can not begin until Change Order Request is Signed and Approved, or Contractor Change Order is Issued.

DESCRIPTION OF WORK	LABOR	MATERIALS	OTHER
Supply and install 2 terrace doors that were damaged by a hurricane.	\$ 1,300.00	\$ 15,503.00	
			\$ -
SUB-TOTAL:	\$ 1,300.00	\$ 15,503.00	\$ -
SALES TAX:		\$ 1,162.73	
10% O/H:	\$ 130.00	\$ 1,550.30	\$ -
5% Profit:	\$ 65.00	\$ 775.15	\$ -
BONDING if Required:	\$ -	\$ -	\$ -
TOTAL:	\$ 1,495.00	\$ 18,991.18	\$ -
TOTAL AMOUNT OF APPROVED CHANGE ORDER:	\$20,486		

Customer Acceptance Signature X _____

1st Choice Glass Warranty & Disclaimer:

(1) Reliability of Quoted Costs. Labor costs and material costs are firm for thirty (30) days from the date of proposal stated above. If the time between the proposal date and installation exceeds thirty (30) days, 1st Choice Glass, Inc. reserves the right to amend the proposal and to add any surcharges and/or additional costs to any and all labor and/or materials.

(2) Warranty. Unless otherwise agreed in writing, 1st Choice Glass, Inc. warrants that all application and labor completed by 1st Choice Glass, Inc. shall be free from defect for one (1) year following its completion. Said warranty does not include (1) damage arising from abnormal use, negligence, misuse, or accident, which occurs as a result of no fault of 1st Choice Glass, Inc. or (2) material damaged by tear-out, retro-fit, or remodel. 1st Choice Glass, Inc. reserves the right to respond to such warranty claims by first making repairs to the defect; such repairs shall be subject to the satisfaction of the customer. 1st Choice Glass, Inc. does not warrant raw material or manufacturers' products; any warranty for such materials or products shall be limited to the manufacturer's warranty. 1ST CHOICE GLASS, INC. EXPRESSLY DISCLAIMS ANY IMPLIED WARRANTY OF MERCHANTABILITY or IMPLIED WARRANTY OF FITNESS FOR A PARTICULAR PURPOSE.

(3) Estimate of Work Required & Changes. The work proposed herein is based on initial estimates and may require changes, alterations, and/or adjustments to complete the job as described, agreed or required by applicable codes and/or government inspections; if such changes or alterations are necessary, customer agrees to execute a written change order which shall indicate the change in the work to be completed or the materials to be used and the agreed upon price for such work and/or materials; such change order shall become an amendment to the contract and the customer shall pay all additional charges agreed upon in the change order at the time the change order is delivered by the customer to 1st Choice Glass, Inc.

(4) Specifications. Unless otherwise specified, all systems are designed to the governing codes (ie: International Building Codes) for the location where the work is to be completed. A maximum deflection of $L/175 - 3/4$ shall apply for units less than 13'-6" in height and a maximum deflection of $L/240 + 1/4$ " shall apply for units exceeding 13'-6" in height, but less than 40'-0" in height. Individual glass lite deflection shall be limited to .75" of the glass edge.

(5) Time Frame. A minimum of two (2) weeks from the date that all shop drawings and submittals are approved is required for delivery. Installation shall be completed within a minimum of two (2) weeks after the delivery of materials if the project schedule does not delay installation.

(6) Deposit & Payment. A deposit or joint supplier payment(s) may be required at the discretion of 1st Choice Glass, Inc. and may be due to 1st Choice Glass, Inc. prior to startup. Once ordered, any and all nonrefundable special order material costs are the sole liability of the customer and shall be payable on demand. Payments of retainage are due no later than sixty (60) days from the final invoice unless otherwise agreed upon in writing. All other payments are due in net thirty (30) unless otherwise agreed in writing.

(7) Inclusions & Exclusions. All proposals include indicated labor, materials, and applicable taxes. Exclusions from this proposal include, but are not limited to, any cleaning, protection or sealing of glass or metal, any and all "Wood Blocking" required on plans or necessary for systems warranty, and additional glass, metals, labor, shop drawings, or miscellaneous materials not listed on proposed shop drawings, or addendums to such shop drawings or this proposal. All Inclusions and Exclusions contained within this Paragraph shall supersede any and all requirements related to the same identified in bid drawings, construction documents, specifications, clarifications, contracts, and any attachments, exhibits, or addendums thereto.

(8) Binding Contract. This proposal shall be considered a valid and binding contract upon 1st Choice Glass, Inc. and the customer upon the signing of all parties. Once signed by the parties, this contract and any addendums and exhibits attached hereto comprise the entire agreement between the parties hereto and supersede all prior negotiations. This contract may only be amended by a written instrument signed by both parties hereto.

(9) Headings. The headings of the paragraphs herein are for convenience only and shall not affect the meaning or interpretation of the contents thereof.

(10) Authority. Each party signing this proposal represents to the other that the terms of this proposal are accepted, and that the resulting contract, the rights and obligations contemplated herein, and the execution and delivery hereof are authorized or have been duly authorized by all necessary limited liability company or corporate proceedings and actions, as applicable, pursuant to applicable law.

ACCEPTED:

1st Choice Glass, Inc.

Customer Name:

By: _____

Mike Tsiukes

Title: President

By: _____

Title: _____

Date: _____

Date: _____

Paul Dustin

From: Dawn Heiland <dheiland@grahamwindows.com>
Sent: Thursday, September 28, 2017 9:25 AM
To: Paul Dustin; Tim Cooper
Cc: Greg Grindstaff; Robert Wielhouwer
Subject: RE: Damage From Irma

Good Morning Paul,

I apologize for the delay in getting you this quote. The quote to provide (2) type J2 doors (or two pair) is \$15,503 (including freight via common carrier). We were able to save you the cost of 8 set ups and an additional finish fee, however we have to order 4 shapes.

Lead time for these doors is 14-16 weeks due to the extrusions needing processed on the CNC machine.

Let me know if this quote is approved and I will send over a Sales Contract Change Order for signature.

Thank you,

Dawn Heiland
 Project Manager
 Graham Architectural Products
 1551 Mt Rose Avenue
 York, PA 17403
 Office: 717-849-8140
 Cell: 717-472-3128
 Fax: 717-849-6454
 dheiland@grahamwindows.com
 www.grahamwindows.com

-----Original Message-----

From: Paul Dustin [mailto:pauldustin@glass1st.net]
 Sent: Wednesday, September 27, 2017 4:46 PM
 To: Dawn Heiland <dheiland@grahamwindows.com>; Tim Cooper <tcooper@grahamwindows.com>
 Cc: Greg Grindstaff <greggrindstaff@glass1st.net>; Robert Wielhouwer <robertwielhouwer@glass1st.net>
 Subject: RE: Damage From Irma

I need this ASAP. I have a short window to make an insurance claim. Thanks.

Paul Dustin
 Project Manager
 704-507-8264

-----Original Message-----

From: Dawn Heiland [mailto:dheiland@grahamwindows.com]
 Sent: Tuesday, September 26, 2017 3:26 PM
 To: Paul Dustin <pauldustin@glass1st.net>; Tim Cooper <tcooper@grahamwindows.com>
 Cc: Greg Grindstaff <greggrindstaff@glass1st.net>; Robert Wielhouwer <robertwielhouwer@glass1st.net>

Balfour Beatty Construction									11/7/2017 Hotel at Marlon Square GENERAL CONDITIONS	
2.50 DAYS			Hurricane Irma						Nstarcevic	
DESCRIPTION:	QTY:	UNIT:	Hourly Rate	9/6/2017	9/7/2017	9/8/2017	9/9/2017	9/12/2017	9/13/2017	TOTAL
LABOR		Days								
Labor - Hourly Payroll (Peanut)	58.0	Hour	\$ 17.64	12.00	12.00	12.00	11.00	11.00		1,023
Labor - Hourly Payroll (Flynn)	22.5	Hour	\$ 26.46		12.00	10.50	0.00			595
Gen Labor - Staff Zone	124.0	Hours	\$ 11.89	0.00	42.00	58.00	0.00	24.00	20.00	1,474
Semi Skilled Labor - Staff Zone	56.0		\$ 16.89	20.00	20.00	20.00		16.00	20.00	946
Labor Total				32.00	86.00	100.50	11.00	51.00	40.00	4,039
EQUIPMENT AND MATERIAL										
Sunbelt Equipment (Dehumid & Pump)							1909.60	867.31		2,777
Lumber (Buck)			\$ 676.51	707.27						1,384
Misc Material					341.72	911.63				1,253
Equip and Material Total										5,414
Combined										13,491
OH&P									0.15	2,024
Total										15,515

ZONE

Atlanta-Doraville
770-220-9950
Atlanta-East Point
404-762-2512
Atlanta-Marietta
678-903-6545
Atlanta
706-724-9585
Austin
512-452-8367
Birmingham
205-703-9701
Brunswick
912-264-5500
Charleston
843-308-9663
Charleston 2
843-202-1551
Charlotte
704-714-9663
Columbia
803-399-9663
Columbus
706-324-1780
Dallas
972-258-9663
Denver
720-638-4972
Ft Worth
817-900-9000
Greensboro
336-553-2970
Greenville
864-271-0004
Huntsville
256-964-7274
Jacksonville
904-634-0052
Jaxville
615-242-9663
Orlando
407-413-5066
Raleigh
919-863-9663
Richmond
804-644-9663
Savannah
912-965-9120
Tempe
813-972-9663

Date: 10.17

Company:
(Bill To)Job Site Name
& Address:

Report to:

Time:

No of Workers Needed: 2

Job Description:

Repeat Work Order?

☒ Yes ☐ No

(Circle Day Needed)

Mon Tues Wed Thurs

How Many? 2 Time? 7 Report

X Authorized Signature

Reachable Phone Number:

Remarks:

SAFETY
FIRST

Our MOD

Employee Name	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Total
B. Bacon			10					
B. Bamberger			10					

SUPERVISION REQUIRED

TOTAL BILLABLE HOURS: 20 hr

By signature above, customer agrees to the terms & conditions set on the reverse side of this form and that employees performed hours worked satisfactorily

CUSTOMER COPY

ZONE

Atlanta-Doraville
770-220-9950
Atlanta-East Point
404-762-2512
Atlanta-Marietta
678-903-6545
Atlanta
706-724-9585
Austin
512-452-8367
Birmingham
205-703-9701
Brunswick
912-264-5500
Charleston
843-308-9663
Charleston 2
843-202-1551
Charlotte
704-714-9663
Columbia
803-399-9663
Columbus
706-324-1780
Dallas
972-258-9663
Denver
720-638-4972
Ft Worth
817-900-9000
Greensboro
336-553-2970
Greenville
864-271-0004
Huntsville
256-964-7274
Jacksonville
904-634-0052
Jaxville
615-242-9663
Orlando
407-413-5066
Raleigh
919-863-9663
Richmond
804-644-9663
Savannah
912-965-9120
Tempe
813-972-9663

Date: 10.17

Company:
(Bill To)Job Site Name
& Address:

Report to:

Time:

No of Workers Needed: 1

Job Description:

Repeat Work Order?

☐ Yes ☐ No

(Circle Day Needed)

Mon Tues Wed Thurs Fri Sat Sun

How Many? 1 Time? 7 Report to: 2011

X Authorized Signature

Print Name

Reachable Phone Number:

Remarks:

SAFETY
FIRST

Our MOD Rate is .82

Employee Name	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Total
B. Bamberger			10					

SUPERVISION REQUIRED

TOTAL BILLABLE HOURS: 10 hr

By signature above, customer agrees to the terms & conditions set on the reverse side of this form and that employees performed hours worked satisfactorily

CUSTOMER COPY

R-1800

Date 11-17-77	Company (Bill To)	Job Site Name & Address:	Repeat Work Order? ☒ Yes ☐ No (Circle Day Needed) Mon Tues Wed Thurs Fri Sat Sun	How Many? _____ Time? _____ Report to: _____	Authorized Signature 	Print Name Hurricane Relief
No of Workers Needed: _____			Reachable Phone Number: _____		Remarks: <u>OK with</u>	
Job Description: _____			Our MOD Rate is .82		TOTAL BILLABLE HOURS: 8.0	
Employee Name			Mon	Tue	Wed	Thu
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____
_____			_____	_____	_____	_____

[illegible]



170594

Date: 10/1/01

Company: (Bill To) 101 KING ST
CHARLY TON at 201
HARLOW SQUARE WY
HARTY DALL PATTEN

Job Site Name & Address: 101 KING ST
CHARLY TON at 201
HARLOW SQUARE WY
HARTY DALL PATTEN

Print Name: Hurricane relief

Authorized Signature: [Signature]

Reachable Phone Number: [Number]

How Many? 24 hr

Time? 8:00 AM - 5:00 PM

Report to: [Name]

Repeat Work Order? ☐ Yes ☒ No

(Circle Day Needed)
Mon Tues Wed Thurs Fri Sat Sun

Remarks: BUSHEN/PAE
CO. 10/1/01

Job Description: [Blank]

No of Workers Needed: 7

One-MOD Rate: \$0.00

Employee Name	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Total
170583-4972								
817-800-0000								
510-353-2770								
864-711-0004								
256-904-7274								
904-674-0052								
015-242-5651								
407-115-0006								
910-803-9663								
883-643-0061								
912-665-9120								
818-912-9653								

SUPERVISION REQUIRED

TOTAL BILLABLE HOURS: 24 hr

By Signature: [Signature] **Date:** 10/1/01

[illegible]

Repeat Work Order?

☐ Yes ☐ No
(Circle Day Needed)

Mon Tues Wed Thurs Fri Sat Sun

How Many? _____ Time? _____ Report to _____

Authorized Signature
Theresa Kane
Reliable Phone Number: _____

Job Description:

No of Workers Needed: _____

Company: _____
(Bill To)

Job Site Name
& Address: _____

Report to: _____

Time: _____

Remarks:

Call 800-451-7000-15 82

Employee Name

Mon Tue Wed Thu Fri Sat Sun

Total

Sat Sun Mon Tues Wed Thurs Fri Sat Sun

SUPERVISION REQUIRED

Supervisor Name: _____

TOTAL BILLABLE HOURS:

CUSTOMER COPY

[illegible]

[illegible][illegible][illegible]



INVOICE
SEND ALL PAYMENTS TO:
SUNBELT RENTALS, INC.
PO BOX 409211
ATLANTA, GA 30384-9211



INVOICE NO. 69810419-0004
ACCOUNT NO. 187039
INVOICE DATE 9/18/17

PAGE 1 of 1

INVOICE TO

102-1392 1749
BBC-CHARLOTTE-MAIN OFFICE ONLY
1930 CAMDEN RD
CHARLOTTE NC 28203-4777



JOB ADDRESS
MARION SQUARE HOTEL-CHARLESTON
404 KING STREET
CHARLESTON, SC 29403
704-319-4000

RECEIVED BY DALE, MARTY
CONTRACT NO. 69810419

PURCHASE ORDER NO

PER MARTY

JOB NO

5 - MARION SQUARE HO

BRANCH

CHARLESTON CC PC457
7630 SANDLAPPER PARKWAY NORTH
NORTH CHARLESTON, SC 29420-28
843-494-9009

QTY	EQUIPMENT #	Min	Day	Week	4 Week	Amount
8	25GPD REFRIGERANT DEHUMIDIFIER	67.00	67.00	220.00	640.00	5120.00
Rental Sub-total:						5120.00

SALES	ITEMS:	Unit	Price	Amount
Qty	Item number	EA	71.680	71.68
1	ENVIRONMENTAL			
	ENVIRONMENTAL			
BILLED FOR FOUR WEEKS 9/01/17 THRU 9/28/17.				

Batch # 2509127
Doc # 1541739
Paid: 9/26/17



Vendor # 118530 PA CA 9/26/17
Bus unit/Job# Cost Type/object acct Cost Code/supplementary Amount
15304400 430/35 10142200 \$ 5,658.93
\$
MGR APPROVAL ESS Rate page 1 0 \$

Equipment. Service. Guaranteed.

IT TO:

SUNBELT RENTALS, INC.
PO BOX 409211
ATLANTA, GA 30384-9211

NET DUE UPON RECEIPT

Invoices not paid within 30 days may be subject
to a 1-1/2% per month charge.

R - 1805

SUBTOTAL	5,191.68
SALES TAX	467.25
INVOICE TOTAL	5,658.93

4 WEEK BILL

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108



SEND ALL PAYMENTS TO:

SUNBELT RENTALS, INC.
PO BOX 409211
ATLANTA, GA 30384-9211



INVOICE NO. 72165300-0001
ACCOUNT NO. 187039
INVOICE DATE 9/20/17
PAGE 1 of 1

INVOICE TO

102-854-1076
BBC-CHARLOTTE-MAIN OFFICE ONLY
1930 CAMDEN RD
CHARLOTTE NC 28203-4777

RECEIVED BY SPANO, TIM
PURCHASE ORDER NO 72165300

13026000

JOB NO

2 - MARION SQUARE HO

BRANCH

JOB ADDRESS

MARION SQUARE HOTEL-CHARLESTON
404 KING STREET
CHARLESTON, SC 29403 6422
704-319-4000

MYRTLE BEACH PC020
604 CANNON RD
MYRTLE BEACH, SC 29577-6538
843-445-9960

QTY	EQUIPMENT #	Min	Day	Week	4 Week	Amount
1	3" GAS TRASH PUMP 743600 Make: MQ Model: QP3TH Ser #: 3TH-27447 Billed from 9/07/17 thru 9/15/17	57.00	57.00	163.00	425.00	220.00
1	3" X 20' SUCTION HOSE	6.00	6.00	17.00	40.00	23.00
4	3" X 50' DISCHARGE HOSE	6.00	6.00	17.00	40.00	92.00
	Rental Sub-total:					335.00

SALES QTY	ITEMS: Item number	Unit	Price	Amount
1	SBR0430230	EA	9.500	9.50
1	FUEL CONVENIENCE CHARGE	EA	38.000	38.00
1	DLPKSRCHG	EA	5.500	5.50
1	TRANSPORTATION SURCHARGE	EA		N/C
1	ENVIRONMENTAL	EA		N/C
1	RF	EA		N/C
1	RETURNED FULL	EA		N/C
1	SCHERS3	EA	8.380	8.38
	SC 2.5% HEAVY EQUIP. RENTAL SURCHARGE			
	DELIVERY CHARGE			200.00
	PICKUP CHARGE			200.00

QTY	EQUIPMENT #	Min	Day	Week	4 Week	Amount
-----	-------------	-----	-----	------	--------	--------

FINAL BILL: 9/07/17 12:00 PM THRU 9/15/17 02:00 PM.

Batch # 2517894

Doc # 1546908

Paid 10/2/17

Vendor # 11582	PA CR	2017	
Bus. unit/Job#	Cost Type/ object acct	Cost Code/ subsidiary	Amount
13-0640	10035	1042200	\$ 867.31

MGR APPROVAL LESS Retenage Withheld

Equipment. Service. Guaranteed.

IT TO:

SUNBELT RENTALS, INC.
PO BOX 409211
ATLANTA, GA 30384-9211

NET DUE UPON RECEIPT

Invoices not paid within 30 days may be subject
to a 1-1/2% per month charge.

R - 1806

SUBTOTAL	796.38
SALES TAX	70.93
INVOICE TOTAL	867.31

RENTAL RETURN

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

BUCK

Lumber & Building
Supply, Inc.

1911 Maybank Hwy.
Charleston, SC 29412-2115
843-795-0150
Fax: 843-795-0165
www.bucklumber.com

PAGE :

TRANSACTION TYPE
CHARGE SALE

STORE NAME
BUCK LUMBER

SOLD TO: BALFOUR BEATTY CONST LLC
1930 CAMDEN RD SUITE 280

CHARLOTTE, NC 28203

SHIP TO:

AUTH: XXXXXXXXXXXXXXXXXXXXXXXXXXXXXXXX

BALFB HOTEL MARION SQ
404 KING ST

CHARLESTON, SC 29403

CUST CODE	TIME	TRANS#	DATE	STR	SLS#	W/B	TILL	O/Q#	ORDER DT	DATE WANTED	ZONE
BALFB98	12:48	1581911	090717	J	14	40	041	118191	09/06/17	09/08/17	
REFERENCE NUMBER		CUSTOMER ORDER#		ORDERED BY		BUCK PO#		DUE IN DATE		SALESMAN	
		054-HOTEL @ M S								BYRON CLARK	

LN	ITEM CODE	ORD	SHIP	DESCRIPTION	PRICE/UNIT	EXTENSION
1	COVER	1	1	COVER ENTIRE LOAD	0.000 EACH	0.00
2	2412P	36	36	2X4-12' SOU YEL PINE D4S #2	4.300 PC	154.80
3	716OSB	35	35	7/16-4x8 (OSB) WAFER BOARD	13.310 PC	465.85
				Total Ship Units: 2530.800 LB		
Vendor # <u>342307</u> PA <u>CA 9/8/17</u> Bus. unit/Job# <u>1302406</u> Cost Type/ <u>42045</u> Cost Code/ <u>50810060</u> Amount <u>676.51</u> _____ MGR APPROVAL LESS Retainage Withheld _____ _____ Net Amount Due _____						

Batch # 2498595

Doc # 1534319

Paid 9/8/17

Payment number: 207879

NET AMT	DISC	TAX%	TAX AMT	TOTAL AMT
676.51		9.000	55.86	676.51

Inspect Shipments Upon Receipt. Any errors or irregularities must be reported to us in writing within 24 hours of receipt. All Special Orders Are Not Returnable for Credit Signature

ORIGINAL INVOICE

R - 1807



1911 Maybank Hwy.
Charleston, SC 29412-2115
843-795-0150
Fax: 843-795-0165
www.bucklumber.com

PAGE 1

TRANSACTION TYPE
CHARGE SALE

STORE NAME
BUCK LUMBER

AUTH: xxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxx

SOLD TO: BALFOUR BEATTY CONST LLC
1930 CAMDEN RD/SUITE 280

SHIP TO:

BALFB/HOTEL@MARION SQ
404 KING ST

CHARLOTTE, NC 28203

CHARLESTON, SC 29403

CUST CODE	TIME	TRANS#	DATE	STR	SLS#	W/B	TILL	O/Q#	ORDER DT	DATE WANTED	ZONE
BALFB98	06:15	1578201	090717	1	14	40	041	157820	09/05/17	09/07/17	
REFERENCE NUMBER		CUSTOMER ORDER#		ORDERED BY		BUCK PO#		DUE IN DATE		SALESMAN	
NENE		054-HOTEL @ M S		PETER						BYRON CLARK	

LN	ITEM CODE	ORD	SHIP	DESCRIPTION	PRICE/UNIT	EXTENSION
1	COVER			COVER ENTIRE LOAD	0.000 EACH	0.00
2	SOTRTD			2X6X12' FIRE TREATED SOID 73907 ***** stock below	15.030 EACH	240.48
5	34CDFR			3/4 X 4 X 8 CD FIRE RETARDANT	39.050 PC	390.50
6	72914			1-1/4" DRYWALL SCREW F/T 5#	17.890 BOX	17.89
				Total Ship Units: 768.000 LB		
Vendor # <u>3423000</u> to <u>CA</u> <u>9/18/17</u> Bus. unit/Job# <u>13026400</u> Cost <u>42045</u> object acct <u>50810060</u> Cost Center <u>707.27</u> subsidiary MGR APPROVAL LESS Retainage Withheld \$ Net Amount Due \$						

Batch # 247595

Doc # 1534318

Paid 9/18/17

Payment number- 207879

NET AMT	DISC	TAX%	TAX AMT	TOTAL AMT
648.87		9.000	58.40	707.27

Inspect Shipments Upon Receipt. Any errors or irregularities must be reported to us in writing within 24 hours of receipt. All Special Orders Are Not Returnable for Credit/Signature

ORIGINAL INVOICE

R - 1808



CONSTRUCTION SUPPLY CO.

ACCOUNTS RECEIVABLE DEPARTMENT
(205) 714-3300 / (800) 890-1988
FAX# (205) 322-6311

Please Remit To:
RAM Tool A/R Dept.
P.O. Box 743487
Atlanta, GA 30374-3487

Page 1 of 1

Invoice

93922982

09/07/2017

Sold-To Party : 105588


BALFOUR BEATTY CONSTRUCTION
ATTN: CANDICE ASHE
1930 CAMDEN ROAD, SUITE 280
CHARLOTTE NC 28203

CUMENTS

as Order: 3905515

. No.: PETE / MARION SQUARE

Batch # 2513854
Doc # 1545549 Paid - 9/29/17



Ship-To-Party : 5210434

MARION SQUARE

CORNER OF KING AND HUTSON STREET
CHARLESTON SC 29403

INFORMATION

Incoterm

Branch Location

Total Invoice Amount

Terms of Payment

004 Truck Delivery

SC01 CHARLESTON, SC

341.72 USD

Net due in 30 days

Item	Material/Description	Quantity	Price unit	Value
10	UTC-145202	24 ROL	11 55000	277.20
	2IN X 180FT 30 DAY RED STUCCO TAPE			
20	RAW-02724	2 BOX	18 15000	36.30
	TAPPER+ HWH 1/4 X 2 1/4 (100/BX)			
Subtotal Before Tax				313.50
Total Sales Tax				28.22
Total Invoice in USD				341.72

Please code

Vendor# 117022 PA CA 9/15/17

Bus. unit/Job#	Cost Type/ object code	Cost Code/ subsidiary	Amount
.13026400	.10146000		\$ 341.72
			\$
MGR	LESS Retainage Withheld		\$
APPROVAL			\$
	Net Amo	Due	\$

DID YOU KNOW: Invoices can be sent electronically and are also available via our NEW Online Customer Portal.

Please contact us to learn more and sign up today Thank you for your business! Email: arcustomerrequest@ram-tool.com

R - 1809

ELECTRONICALLY FILED 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

STATE OF OHIO

Common Pleas Court
Charleston, Ohio

Case No. _____

Plaintiff's Name _____

Defendant's Name _____

Case No. _____

Plaintiff's Name _____

Case No. _____

Case No. _____

Case No. _____

Case No.	Case Title	Case Type	Case Status	Case Date	Case Time	Case Location	Case Judge	Case Clerk	Case Attorney	Case Defendant	Case Plaintiff	Case Other
2019-001108	State of Ohio vs. [Name]	Common Pleas	Case No. 2019-001108	May 12, 2023	11:36 AM	Charleston, Ohio	Case No. 2019-001108	Case No. 2019-001108	Case No. 2019-001108	Case No. 2019-001108	Case No. 2019-001108	Case No. 2019-001108

2019-001108
Case No. 2019-001108

State of Ohio vs. [Name]
Case No. 2019-001108

Our Density

Employees	Avg. age	Coverage %
Designated	% covered / non-covered	

1. *Chlorophyll a* (Chl *a*)

2. *Chlorophyll b* (Chl *b*)

3. *Chlorophyll c* (Chl *c*)

4. *Chlorophyll d* (Chl *d*)

5. *Chlorophyll e* (Chl *e*)

6. *Chlorophyll f* (Chl *f*)

7. *Chlorophyll g* (Chl *g*)

8. *Chlorophyll h* (Chl *h*)

9. *Chlorophyll i* (Chl *i*)

10. *Chlorophyll j* (Chl *j*)

11. *Chlorophyll k* (Chl *k*)

12. *Chlorophyll l* (Chl *l*)

13. *Chlorophyll m* (Chl *m*)

14. *Chlorophyll n* (Chl *n*)

15. *Chlorophyll o* (Chl *o*)

16. *Chlorophyll p* (Chl *p*)

17. *Chlorophyll q* (Chl *q*)

18. *Chlorophyll r* (Chl *r*)

19. *Chlorophyll s* (Chl *s*)

20. *Chlorophyll t* (Chl *t*)

21. *Chlorophyll u* (Chl *u*)

22. *Chlorophyll v* (Chl *v*)

23. *Chlorophyll w* (Chl *w*)

24. *Chlorophyll x* (Chl *x*)

25. *Chlorophyll y* (Chl *y*)

26. *Chlorophyll z* (Chl *z*)

27. *Chlorophyll aa* (Chl *aa*)

28. *Chlorophyll ab* (Chl *ab*)

29. *Chlorophyll ac* (Chl *ac*)

30. *Chlorophyll ad* (Chl *ad*)

31. *Chlorophyll ae* (Chl *ae*)

32. *Chlorophyll af* (Chl *af*)

33. *Chlorophyll ag* (Chl *ag*)

34. *Chlorophyll ah* (Chl *ah*)

35. *Chlorophyll ai* (Chl *ai*)

36. *Chlorophyll aj* (Chl *aj*)

37. *Chlorophyll ak* (Chl *ak*)

38. *Chlorophyll al* (Chl *al*)

39. *Chlorophyll am* (Chl *am*)

40. *Chlorophyll an* (Chl *an*)

41. *Chlorophyll ao* (Chl *ao*)

42. *Chlorophyll ap* (Chl *ap*)

43. *Chlorophyll aq* (Chl *aq*)

44. *Chlorophyll ar* (Chl *ar*)

45. *Chlorophyll as* (Chl *as*)

46. *Chlorophyll at* (Chl *at*)

47. *Chlorophyll au* (Chl *au*)

48. *Chlorophyll av* (Chl *av*)

49. *Chlorophyll aw* (Chl *aw*)

50. *Chlorophyll ax* (Chl *ax*)

51. *Chlorophyll ay* (Chl *ay*)

52. *Chlorophyll az* (Chl *az*)

53. *Chlorophyll aza* (Chl *aza*)

54. *Chlorophyll abz* (Chl *abz*)

55. *Chlorophyll acz* (Chl *acz*)

56. *Chlorophyll adz* (Chl *adz*)

57. *Chlorophyll aez* (Chl *aez*)

58. *Chlorophyll afz* (Chl *afz*)

59. *Chlorophyll agz* (Chl *agz*)

60. *Chlorophyll ahz* (Chl *ahz*)

61. *Chlorophyll aiz* (Chl *aiz*)

62. *Chlorophyll ajz* (Chl *ajz*)

63. *Chlorophyll akz* (Chl *akz*)

64. *Chlorophyll alz* (Chl *alz*)

65. *Chlorophyll amz* (Chl *amz*)

66. *Chlorophyll anz* (Chl *anz*)

67. *Chlorophyll aoz* (Chl *aoz*)

68. *Chlorophyll apz* (Chl *apz*)

69. *Chlorophyll aqz* (Chl *aqz*)

70. *Chlorophyll arz* (Chl *arz*)

71. *Chlorophyll asz* (Chl *asz*)

72. *Chlorophyll atz* (Chl *atz*)

73. *Chlorophyll auz* (Chl *auz*)

74. *Chlorophyll avz* (Chl *avz*)

75. *Chlorophyll awz* (Chl *awz*)

76. *Chlorophyll axz* (Chl *axz*)

77. *Chlorophyll ayz* (Chl *ayz*)

78. *Chlorophyll azz* (Chl *azz*)

79. *Chlorophyll azaa* (Chl *aza*)

80. *Chlorophyll abz* (Chl *abz*)

81. *Chlorophyll acz* (Chl *acz*)

82. *Chlorophyll adz* (Chl *adz*)

83. *Chlorophyll aez* (Chl *aez*)

84. *Chlorophyll afz* (Chl *afz*)

85. *Chlorophyll agz* (Chl *agz*)

86. *Chlorophyll ahz* (Chl *ahz*)

87. *Chlorophyll aiz* (Chl *aiz*)

88. *Chlorophyll ajz* (Chl *ajz*)

89. *Chlorophyll akz* (Chl *akz*)

90. *Chlorophyll alz* (Chl *alz*)

91. *Chlorophyll amz* (Chl *amz*)

92. *Chlorophyll anz* (Chl *anz*)

93. *Chlorophyll aoz* (Chl *aoz*)

94. *Chlorophyll apz* (Chl *apz*)

95. *Chlorophyll aqz* (Chl *aqz*)

96. *Chlorophyll arz* (Chl *arz*)

97. *Chlorophyll asz* (Chl *asz*)

98. *Chlorophyll atz* (Chl *atz*)

99. *Chlorophyll auz* (Chl *auz*)

100. *Chlorophyll avz* (Chl *avz*)

101. *Chlorophyll awz* (Chl *awz*)

102. *Chlorophyll axz* (Chl *axz*)

103. *Chlorophyll ayz* (Chl *ayz*)

104. *Chlorophyll azz* (Chl *azz*)

105. *Chlorophyll azaa* (Chl *aza*)

106. *Chlorophyll abz* (Chl *abz*)

107. *Chlorophyll acz* (Chl *acz*)

108. *Chlorophyll adz* (Chl *adz*)

109. *Chlorophyll aez* (Chl *aez*)

110. *Chlorophyll afz* (Chl *afz*)

111. *Chlorophyll agz* (Chl *agz*)

112. *Chlorophyll ahz* (Chl *ahz*)

113. *Chlorophyll aiz* (Chl *aiz*)

114. *Chlorophyll ajz* (Chl *ajz*)

115. *Chlorophyll akz* (Chl *akz*)

116. *Chlorophyll alz* (Chl *alz*)

117. *Chlorophyll amz* (Chl *amz*)

118. *Chlorophyll anz* (Chl *anz*)

119. *Chlorophyll aoz* (Chl *aoz*)

120. *Chlorophyll apz* (Chl *apz*)

121. *Chlorophyll aqz* (Chl *aqz*)

122. *Chlorophyll arz* (Chl *arz*)

123. *Chlorophyll asz* (Chl *asz*)

124. *Chlorophyll atz* (Chl *atz*)

125. *Chlorophyll auz* (Chl *auz*)

126. *Chlorophyll avz* (Chl *avz*)

127. *Chlorophyll awz* (Chl *awz*)

128. *Chlorophyll axz* (Chl *axz*)

129. *Chlorophyll ayz* (Chl *ayz*)

130. *Chlorophyll azz* (Chl *azz*)

131. *Chlorophyll azaa* (Chl *aza*)

132. *Chlorophyll abz* (Chl *abz*)

133. *Chlorophyll acz* (Chl *acz*)

134. *Chlorophyll adz* (Chl *adz*)

135. *Chlorophyll aez* (Chl *aez*)

136. *Chlorophyll afz* (Chl *afz*)

137. *Chlorophyll agz*

Item	Unit	Quantity	Rate	Amount	Remarks
1. Cement	kg	100	1.50	150.00	
2. Sand	kg	100	0.50	50.00	
3. Aggregate	kg	100	0.80	80.00	
4. Labour	hr	100	0.20	20.00	
5. Water	litre	100	0.05	5.00	
6. Total				305.00	

ZONE

Atlanta-Doraville
770-220-9950
Atlanta-East Point
404-762-2512
Atlanta-Marietta
678-903-6545
Augusta
706-724-9585
Columbus
512-452-8367
Cincinnati
205-703-9701
Cincinnati
912-264-5500
Charleston
843-308-9663
Charleston
843-202-1551
Charlotte
704-714-9663
Columbia
803-399-9663
Columbus
706-324-1780
Dallas
972-258-9663
Denver
720-638-4972
Ft Worth
817-900-9000
Greensboro
336-553-2970
Greenville
864-271-0004
Huntsville
256-964-7274
Jacksonville
904-634-0052
Joplin
615-242-9663
Orlando
407-413-5066
Raleigh
919-863-9663
Richmond
804-644-9663
Savannah
912-965-9120
Tampa
813-972-9663

Date:

Company:
(Bill To)Job Site Name
& Address:

Report to:

Time:

No of Workers Needed:

Job Description:

Repeat Work Order?

☒ Yes ☐ No

(Circle Day Needed)

Mon ☒ Tues ☒ Wed ☒ Thurs ☒How Many? 2 Time? 7 ReportX Hurricane
Authorized Signature

Reachable Phone Number:

Remarks:

SAFETY
FIRST

Our MOD

Employee Name	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Total
Bacon			10					
Bamberg			10					

SUPERVISION REQUIRED

TOTAL BILLABLE HOURS:

20 hr

By signature above, customer agrees to the terms & conditions set on the reverse side of this form and that employees performed hours worked satisfactorily

CUSTOMER COPY

ZONE

Atlanta-Doraville
770-220-9950
Atlanta-East Point
404-762-2512
Atlanta-Marietta
678-903-6545
Augusta
706-724-9585
Columbus
512-452-8367
Cincinnati
205-703-9701
Cincinnati
912-264-5500
Charleston
843-308-9663
Charleston
843-202-1551
Charlotte
704-714-9663
Columbia
803-399-9663
Columbus
706-324-1780
Dallas
972-258-9663
Denver
720-638-4972
Ft Worth
817-900-9000
Greensboro
336-553-2970
Greenville
864-271-0004
Huntsville
256-964-7274
Jacksonville
904-634-0052
Joplin
615-242-9663
Orlando
407-413-5066
Raleigh
919-863-9663
Richmond
804-644-9663
Savannah
912-965-9120
Tampa
813-972-9663

Date:

Company:
(Bill To)Job Site Name
& Address:

Report to:

Time:

No of Workers Needed:

Job Description:

Repeat Work Order?

☒ Yes ☐ No

(Circle Day Needed)

Mon ☒ Tues ☒ Wed ☒ Thurs ☒ Fri ☒ Sat ☒ SunHow Many? 1 Time? 7 Report to: CEIX Hurricane
Authorized Signature

Print Name

Reachable Phone Number:

Remarks:

SAFETY
FIRST

Our MOD Rate is .82

Employee Name	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Total
Bamberg			10					

SUPERVISION REQUIRED

TOTAL BILLABLE HOURS:

10 hr

By signature above, customer agrees to the terms & conditions set on the reverse side of this form and that employees performed hours worked satisfactorily

CUSTOMER COPY

[illegible][illegible][illegible]

[illegible][illegible][illegible][illegible][illegible]

[illegible][illegible]

[illegible][illegible][illegible]

BUCK

Lumber & Building
Supply, Inc.

1911 Maybank Hwy.
Charleston, SC 29412-2115
843-795-0150
Fax: 843-795-0165
www.bucklumber.com

PAGE :

TRANSACTION TYPE
CHARGE SALE

STORE NAME
BUCK LUMBER

SOLD TO: BALFOUR BEATTY CONST LLC
1930 CAMDEN RD SUITE 280

CHARLOTTE, NC 28203

SHIP TO:

AUTH: XXXXXXXXXXXXXXXXXXXXXXXXXXXXXXXX

BALFB HOTEL@MARION SQ
404 KING ST

CHARLESTON, SC 29403

CUST CODE	TIME	TRANS#	DATE	STR	SLS#	W/B	TILL	O/Q#	ORDER DT	DATE WANTED	ZONE
BALFB98	12:48	1581911	090717	1	14	40	041	158191	09/06/17	09/08/17	
REFERENCE NUMBER		CUSTOMER ORDER#		ORDERED BY		BUCK PO#		DUE IN DATE		SALESMAN	
		054-HOTEL @ M S								BYRON CLARK	

LN	ITEM CODE	ORD	SHIP	DESCRIPTION	PRICE/UNIT	EXTENSION
1	COVER	1	1	COVER ENTIRE LOAD	0.000 EACH	0.00
2	2412P	36	36	2X4-12' SOU YEL PINE D4S #2	4.300 PC	154.80
3	716OSB	35	35	7/16-4x8 (OSB) WAFER BOARD	13.310 PC	465.85
				Total Ship Units: 2530.800 LB		
Vendor # 34230m PA CA 9/8/17 Est. unit/Job Cost Type/ object acct Cost Code/ subsidiary Amount 13022406 42045 50810060 676.51 MGR APPROVAL LESS Retainage Withheld Net Amount Due						

Batch # 2498595

Doc # 1534319

Paid 9/8/17


Payment number: 207879

NET AMT	DISC	TAX%	TAX AMT	TOTAL AMT
676.51		9.000	55.86	676.51

Inspect Shipments Upon Receipt. Any errors or irregularities must be reported to us in writing within 24 hours of receipt. All Special Orders Are Not Returnable for Credit/Signature

ORIGINAL INVOICE

R - 1818



1911 Maybank Hwy.
Charleston, SC 29412-2115
843-795-0150
Fax: 843-795-0165
www.bucklumber.com

PAGE 1

TRANSACTION TYPE
CHARGE SALE

STORE NAME
BUCK LUMBER

AUTH: xxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxxx

SOLD TO: BALFOUR BEATTY CONST LLC
1930 CAMDEN RD/SUITE 280

SHIP TO:

BALFB/HOTEL@MARION SQ
404 KING ST

CHARLOTTE, NC 28203

CHARLESTON, SC 29403

CUST CODE	TIME	TRANS#	DATE	STR	SLS#	W/B	TILL	O/Q#	ORDER DT	DATE WANTED	ZONE
BALFB98	06:15	1578201	090717	1	14	40	041	157820	09/05/17	09/07/17	
REFERENCE NUMBER		CUSTOMER ORDER#		ORDERED BY		BUCK PO#		DUE IN DATE		SALESMAN	
WETE		054-HOTEL @ M S		PETER						BYRON CLARK	

LN	ITEM CODE	ORD	SHIP	DESCRIPTION	PRICE/UNIT	EXTENSION
1	COVER	1		COVER ENTIRE LOAD	0.000 EACH	0.00
2	SOTRTD	6	1	2X6X12' FIRE TREATED SOLD 73907 ***** stock below	15.030 EACH	240.48
5	34CDFR	10	1	3/4 X 4 X 8 CD FIRE RETARDANT	39.050 PC	390.50
6	72914	1	1	1-1/4" DRYWALL SCREW F/T 5#	17.890 BOX	17.89
				Total Ship Units: 768.000 LB		
Vendor # <u>3423000</u> to <u>CA</u> <u>9/18/17</u> Bus. unit/Job# <u>13026400</u> Cost Code/object acct <u>42045</u> Cost Code/subsidiary <u>50810060</u> Amount <u>707.27</u> MGR APPROVAL LESS Retainage Withheld \$ Net Amount Due \$						

Batch # 2478595

Doc # 1534318

Paid 9/18/17

Payment number. 207879

NET AMT	DISC	TAX%	TAX AMT	TOTAL AMT
648.87		9.000	58.40	707.27

Inspect Shipments Upon Receipt. Any errors or irregularities must be reported to us in writing within 24 hours of receipt. All Special Orders Are Not Returnable for Credit/Signature

ORIGINAL INVOICE

R - 1819



CONSTRUCTION SUPPLY CO.

ACCOUNTS RECEIVABLE DEPARTMENT
(205) 714-3300 / (800) 890-1988
FAX# (205) 322-6311

Please Remit To:
RAM Tool A/R Dept.
P.O. Box 743487
Atlanta, GA 30374-3487

Page 1 of 1

Invoice

93922982

09/07/2017

Sold-To Party : 105588


BALFOUR BEATTY CONSTRUCTION
ATTN: CANDICE ASHE
1930 CAMDEN ROAD, SUITE 280
CHARLOTTE NC 28203

DOCUMENTS

as Order: 3905515

. No.: PETE / MARION SQUARE

Patch # 2513854
Doc # 1545549 Paid - 9/29/17



Ship-To-Party : 5210434

MARION SQUARE

CORNER OF KING AND HUTSON STREET
CHARLESTON SC 29403

INFORMATION

Incoterm

Branch Location

Total Invoice Amount

Terms of Payment

004 Truck Delivery

SC01 CHARLESTON, SC

341.72 USD

Net due in 30 days

Item	Material/Description	Quantity	Price unit	Value
10	UTC-145202 2IN X 180FT 30 DAY RED STUCCO TAPE	24 ROL	11 55000	277.20
20	RAW-02724 TAPPER+ HWH 1/4 X 2 1/4 (100/BX)	2 BOX	18 15000	36.30
Subtotal Before Tax				313.50
Total Sales Tax				28.22
Total Invoice in USD				341.72

Please code

Vendor # 117022 PA CA 9/15/17
Bus. unit/object Cost Type/object acct Cost Code/subsidiary Amount
.13026400.10146000 \$ 341.72
\$
MGR APPROVAL LESS Retainage Withheld \$
Ne' Amo 1 Due \$

DID YOU KNOW: Invoices can be sent electronically and are also available via our NEW Online Customer Portal.
Please contact us to learn more and sign up today Thank you for your business! Email: arcustomerrequest@ram-tool.com



CONSTRUCTION SUPPLY CO.

ACCOUNTS RECEIVABLE DEPARTMENT
(205) 714-3300 / (800) 890-1988
FAX# (205) 322-6311

Please Remit To:
RAM Tool A/R Dept.
P.O. Box 743487
Atlanta, GA 30374-3487

Page 1 of 1

Invoice

93922981

09/07/2017


Sold-To Party : 105588

BALFOUR BEATTY CONSTRUCTION
ATTN: CANDICE ASHE
1930 CAMDEN ROAD, SUITE 280
CHARLOTTE NC 28203

DOCUMENTS

as Order: 3905311

. No.: MARION SQUARE



Ship-To-Party : 5210434

MARION SQUARE

CORNER OF KING AND HUTSON STREET
CHARLESTON SC 29403

INFORMATION

Incoterm

004 Truck Delivery

Branch Location

SC01 CHARLESTON, SC

Total Invoice Amount

911.63 USD

Terms of Payment

Net due in 30 days

Item	Material/Description	Quantity	Price unit	Value
10	POL-2FR FIRE RET R	4 ROL	209.09000	836.36
	6 MIL 20X100 FIRE RET STRING REINFORCED			
	Subtotal Before Tax			836.36
	Total Sales Tax			75.27
			Total Invoice in USD	911.63

Batch # 2513854
Doc # 1545551

please code

Vendor # 117022 PA CA 9/15/17

Proj. Unit/Job# Cost Type/object acct Cost Code/subsidiary Amount

13026400, 10146000 \$ 911.63

MGR APPROVAL LESS Retainage Withheld \$

Amo \$

DID YOU KNOW: Invoices can be sent electronically and are also available via our NEW Online Customer Portal.
Please contact us to learn more and sign up today. Thank you for your business! Email: arcustomerrequest@ram-tool.com

R - 1821

ELECTRONICALLY FILED 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108



INVOICE
SEND ALL PAYMENTS TO:
SUNBELT RENTALS, INC.
PO BOX 409211
ATLANTA, GA 30384-9211



INVOICE NO. 69810419-0004
ACCOUNT NO. 187039
INVOICE DATE 9/18/17
PAGE 1 of 1

INVOICE TO

102 1392 1749
BBC-CHARLOTTE-MAIN OFFICE ONLY
1930 CAMDEN RD
CHARLOTTE NC 28203-4777



JOB ADDRESS
MARION SQUARE HOTEL-CHARLESTON
404 KING STREET
CHARLESTON, SC 29403

704-319-4000

RECEIVED BY DALE, MARTY
CONTRACT NO. 69810419

PURCHASE ORDER NO

PER MARTY

JOB NO

5 - MARION SQUARE HO

BRANCH

CHARLESTON CC PC457
7630 SANDLAPPER PARKWAY NORTH
NORTH CHARLESTON, SC 29420-28
843-494-9009

QTY	EQUIPMENT #	Min	Day	Week	4 week	Amount
8	25GPD REFRIGERANT DEHUMIDIFIER	67.00	67.00	220.00	640.00	\$120.00
Rental Sub-total:						\$120.00

SALES ITEMS:

Qty	Item number	Unit	Price	
1	ENVIRONMENTAL	EA	71.680	71.68
ENVIRONMENTAL				
BILLED FOR FOUR WEEKS 9/01/17 THRU 9/28/17.				

Batch # 2509127
Doc # 1541739
Paid: 9/26/17



Vendor # 118532 PA CA 9/26/17
Bus. unit/Job# Cost Type/ object acct Cost Code/ subsidiary Amount
13026400 42035 10142200 \$ 5,658.93

MGR APPROVAL ESS Rate page 1 of 1 \$

Equipment. Service. Guaranteed.

IT TO:

SUNBELT RENTALS, INC.
PO BOX 409211
ATLANTA, GA 30384-9211

NET DUE UPON RECEIPT
Invoices not paid within 30 days may be subject
to a 1.2% per month charge.

R - 1822

SUBTOTAL	5,191.68
SALES TAX	467.25
INVOICE TOTAL	5,658.93

4 WEEK BILL

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108



SEND ALL PAYMENTS TO:

SUNBELT RENTALS, INC.
PO BOX 409211
ATLANTA, GA 30384-9211INVOICE NO. 72165300-0001
ACCOUNT NO. 187039
INVOICE DATE 9/20/17
PAGE 1 of 1

INVOICE TO

102-894 1076
BBC-CHARLOTTE-MAIN OFFICE ONLY
1930 CAMDEN RD
CHARLOTTE NC 28203-4777RECEIVED BY SPANO, TIM
PURCHASE ORDER NO 72165300

13026000

JOB NO

2 - MARION SQUARE HO

BRANCH

MYRTLE BEACH PC020
604 CANNON RD
MYRTLE BEACH, SC 29577-6538
843-445-9960

JOB ADDRESS

MARION SQUARE HOTEL-CHARLESTON
404 KING STREET
CHARLESTON, SC 29403 6422
704-319-4000

QTY	EQUIPMENT #	Min	Day	Week	4 Week	Amount
1	3" GAS TRASH PUMP 743600 Make: MQ Model: QP3TH Ser #: 3TH-27447 Billed from 9/07/17 thru 9/15/17	57.00	57.00	163.00	425.00	220.00
1	3" X 20' SUCTION HOSE	6.00	6.00	17.00	40.00	23.00
4	3" X 50' DISCHARGE HOSE	6.00	6.00	17.00	40.00	92.00
Rental Sub-total:						335.00

SALES ITEMS:

Qty	Item number	Unit	Price	
1	SBR0430230	EA	9.500	9.50
1	FUEL CONVENIENCE CHARGE	EA	38.000	38.00
1	TRANSPORTATION SURCHARGE	EA	5.500	5.50
1	ENVIRONMENTAL ENVIRONMENTAL	EA		N/C
1	RF RETURNED FULL	EA		8.38
1	SCHERS3	EA	8.380	200.00
	SC 2.5% HEAVY EQUIP. RENTAL SURCHARGE			200.00
	DELIVERY CHARGE			
	PICKUP CHARGE			

QTY	EQUIPMENT #	Min	Day	Week	4 Week	Amount
-----	-------------	-----	-----	------	--------	--------

FINAL BILL: 9/07/17 12:00 PM THRU 9/15/17 02:00 PM.

Batch # 251894

Doc # 1546908

Paid 10/2/17

Vendor # 118532	PA CA 10/2/17
Bus. unit/Job# 1302600	Cost Type/object acct 1042200
	Amount \$ 867.31

MGR APPROVAL LESS Retenage Withheld

Equipment. Service. Guaranteed.

IT TO:

SUNBELT RENTALS, INC.
PO BOX 409211
ATLANTA, GA 30384-9211

NET DUE UPON RECEIPT

Invoices not paid within 30 days may be subject
to a 1.2% per month charge.

R - 1823

SUBTOTAL	796.38
SALES TAX	70.93
INVOICE TOTAL	867.31

RENTAL RETURN

ELECTRONICALLY FILED - 2023 May 12 11:36 AM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

Tab No. 212

Balfour Beatty Construction

October 19, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 212R1
Use Robert Thomas for Decorative Brackets_Revised

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 212R1 in the amount of ~~Twenty-nine thousand eight hundred eighty-one~~ ^{JK} ~~(\$21,253.00)~~ provide additional work in accordance with the following qualifications:

- ~~Use owner's preferred bracket vendor at L6 Canopies.~~ Includes 50 additional brackets and 1 mock up bracket already fabricated as directed by Jim Clements. ^{As Approved by City of Charleston BAE JK}
- Acceptance of this change order means acceptance of the subcontractor's terms including but not limited to 60% initial down payments to release fabrication. 30% due upon substantial completion and final 10% due upon installation.
- No retention held.
- Credit included for installation of the eyebrow brackets ~~no credit given for material because they are fabricated and will be turned over to at substantial completion~~ ^{per Ruling of WLA JK} Brackets were fabricated and released per approved shop drawings "Reviewed 05-700-01 Ornamental-Iron-Work-Shop-Drawings.pdf"
- BBC support during installation included.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set forth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for fourteen (14) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Nick Starcevic
Project Manager

cc:
Jennifer Faulkinberry
Jim Clements
Marty Wall

Balfour Beatty Construction

David Simonton
Tim Spano
Shanti Pieniak

RCO # 212R1 – File
Reviewed 05 700-01 Ornamental Iron Work Shop Drawings.pdf
Estimate_1130_from_Robert_Thomas_Iron_Design (1).pdf

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 212R1- Use Robert Thomas for Decorative Brackets_Revised

The additional work for the **Use Robert Thomas for Decorative Brackets_Revised** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50523000.40	Use Robert Thomas for	\$27,050.00
2	400.50523000.40	Per WLA credit \$4K material and \$3K labor	-\$7,000
3		BBC Supervision	\$2,640.00

Total Items	\$28,190.00	\$20,050.00
Total Markups	\$1,691.41	\$ 1,203.00
RCO Total	\$21,253.00	

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: 
Kim Brown, Library Associates, LLC

Date: 11-1-2019

RCO# 212R1

Tab No. 215

Balfour Beatty Construction

August 14, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 215
Lutron Lighting Control Revision

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 215 in the amount of Fourteen thousand nine hundred thirty-seven (\$14,937.63) to provide additional work in accordance with the following qualifications:

Update lighting controls package to include new OFCI lights at Rooftop Bar (Supplemental Instruction 040 and 040R1) and added CFCI light locations in public areas thru Supplemental Instructions 39. This change order does not include the added lights as they were already change ordered in RCO 149R2, RCO 120, and RCO 048.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Alec Dooley
Assistant Project Manager

cc:
Marty Wall
Jim Clements
Melissa Pense
Jennifer Faulkinberry
Nick Starcevic
David Simonton

RCO # 215 - File

The Hotel at Marion Square – RCO 215

R - 1829

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 215– Lutron Lighting Control Revision

The additional work for the **Lutron Lighting Control Revision** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.51600000.40	Lutron Lighting Control Revision	\$13,793.82

Total Items \$13,793.82

Total Markups \$1,143.81

RCO Total \$14,937.63

The total Cost to perform the work as described above is an ADD of Fourteen thousand nine hundred thirty-seven (\$14,937.63).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 215

PROPOSED CHANGE ORDER

Watson Electrical

3215 Fortune Drive, Suite 109
North Charleston, South Carolina 29418

CCN #

159

Date:

1/8/2018

Project Name:

Marion Square Hotel

Project Number:

21046

Page Number:

1

Client Address:

Balfour Beatty Construction

306 Meeting Street
Charleston, South Carolina

Work Description

We reserve the right to correct this quote for errors and omissions.

This price includes:

Lutron lighting controls upgrades due to the cumulative and individual affect of multiple change orders.

Extended and additional trips for prewire coordination and on site programming time.

Lutron field upgrades to existing equipment to accomodate changes.

Additional components and labor to install.

This change proposal only covers executed change orders to. It does not cover outstanding or anticipated changes.

This quote covers direct costs only and we reserve the right to claim for impact and consequential costs.

This price is good for acceptance within 30 days from the date of receipt.

We request a time extension of 6 days.

We will supply and install all materials, labor, and equipment as per your instructions on <>.

Itemized Breakdown

Description	Qty	Net Price	U	Total Mat.	Labor	U	Total Hrs.
GRAFIK EYE 3/6 ZONE DIM PNL	2	0.00	E	0.00	1.35	E	2.70
LIGHTING CONTROL RELAY PANEL 16CK	1	0.00	E	0.00	7.25	E	7.25
Totals	3			0.00			9.95

Summary

LIGHT CONTROLS 1		8,325.00
LIGHT CONTROLS 2		2,100.00
Material Tax	(@ 9.000 %)	938.25
Material Total		11,363.25
JOURNEYMAN	(9.95 Hrs @ \$52.00)	517.40
FOREMAN @ 15%	(1.49 Hrs @ \$55.00)	81.95
MILEAGE	(11.44 @ 0.00 @ \$2.50 + 0.000 % + 0.000 % + 0.000 %)	28.60
CONSUMABLES	(11.44 @ 0.00 @ \$0.30 + 0.000 % + 0.000 % + 0.000 %)	3.43
Subtotal		11,994.63
Overhead/Markup	(@ 15.000 %)	1,799.19
Subtotal		13,793.82

ORIGINAL

R - 1831

PROPOSED CHANGE ORDER**Watson Electrical**3215 Fortune Drive, Suite 109
North Charleston, South Carolina 29418

Client Address:

Balfour Beatty Construction306 Meeting Street
Charleston, South Carolina

CCN #

159

Date:

1/8/2018

Project Name:

Marion Square Hotel

Project Number:

21046

Page Number:

2

Summary (Cont'd)

Final Amount

\$13,793.82**CONTRACTOR CERTIFICATION**

Name: _____

Date: _____

Signature: _____

I hereby certify that this quotation is complete and accurate based on the information provided.

CLIENT ACCEPTANCE

CCN #: 159

Final Amount: \$13,793.82

Name: _____

Date: _____

Signature: _____

Change Order #: _____

I hereby accept this quotation and authorize the contractor to complete the above described work.

ORIGINAL

R - 1832

Plaintiff Balfour Beatty's
Trial Exhibit # 12
(part 4 of 11)



ORDER ACKNOWLEDGEMENT QUOTE ORDER

Phone:(843)879-0232
www.shealyelectrical.com

Cust. #: 18398

Ship To: **WATSON ELECT CONST CHARLESTON** Correspondence To: **Shealy - Ladson**
3215 FORTUNE DRIVE 10009 Highway 78
SUITE 109 Ladson, SC 29456
NORTH CHARLESTON, SC 29418

Bill To: **WATSON ELECT CONST CHARLESTON**
PO BOX 40697
Charleston, SC 29418

(843)879-0232

Order #	8226147-00
Date	07/20/17
PO #	MARION DC42/43 QUOTE
UPC Vendor	
Page #	1
Ship Point	Shealy - Ladson
Ship Via	Best way
Shipped Date	
Terms	Passalong

Instructions

Ln#	Product # Description	Quantity Ordered	Quantity Backordered	Quantity Shipped	Qty UM	Unit Price	Price UM	Discount Multiplier	Net Amount
1	LUTRON BOM C2037668.1.C2	00000	1	1	each	2100.00	each	0.00	2100.00
1	Lines Total		Quantity Total	1				Total Taxes Invoice Total	2100.00 189.00 2289.00



PROPOSED CHANGE ORDER contained herein is based upon currently executed Purchase Order for Lutron quotation , C 2037668.1.10 (referred to collectively as the "Blanket"), in addition to the change order request documents referenced below. This proposed change shall NOT be incorporated into Lutron's scope of work until executed in writing via a change to the Purchase Order. Should additional changes or other directives affect Lutron's scope of work prior to the execution of the proposed change contained herein, or if other proposed changes have a compounding effect on Lutron's scope of work, Lutron reserves the right to issue a revised or separate quotation for this change order. The Lutron Services Company line items for warranty, LSC-XXX, and start-up, LSC-OS-XXX-QTM, if listed below, are representative of the services associated with the entire Blanket order and not only this change order. Please refer to the Blanket for service(s) included for this project or contact Lutron for further information."

Job Name: The Hotel at Marion Square The Hotel at Marion Square

Job Location: Charleston, SC

Quoted To: Carolina Controls Group

Name: Ken Breeggemann

Job No: 2037668

Quoted By: Ed Watts

Quotation Based Upon:

Q1C2 - Based on request for quote from Rep for interfaces for the DC-42 and DC-43 fixtures that changed from INC to ELV-7/19/17 TMS.

Quote Specific Qualifiers and Exceptions:

1. Notes & Exceptions:

Bill of Material:

Qty. Model Number

BILL OF MATERIAL

- | | |
|---|--|
| 3 | <p>PHPM-PA-DV-WH
120/277V dual voltage phase control input phase-adaptive output power module. Dimensions (inches(mm)): 5.1(129.5)H x 6.3(160)W x 1.2(30.5)D. Mounts in a standard 2-gang US wallbox. Mounts in a 4 x 4 in (102 mm), 2.1 in (53 mm) deep US junction box. Mounts in a 4 x 4 in (102 mm), 2.1 in (53 mm) deep US junction box with barrier. Color: WHITE</p> |
| 1 | <p>LSC-B2
2 year warranty providing 100% replacement parts & 100% Lutron labor coverage with a first-available response time.</p> |



Product Lead Time: Please contact Lutron with your desired product delivery date. Typical lead times for Lutron system products are 4 weeks or less after receipt of approved submittal and release. To best enable Lutron to meet your delivery requirements, please submit your construction schedule with your hold for release purchase order.

For this Quote, the estimated Lead Time (in weeks) After Release is 4 weeks.

Visit www.lutron.com/incentives for location specific information on rebates and incentives that promote energy efficient lighting systems. Financial assistance to purchase and install energy efficient products can come from local and state utilities, state energy efficiency programs, EAct tax incentives, and federal stimulus monies that focus on energy efficiency.

Qualifiers:

1. Refer to description column on quote for dimming panel feeder requirements.
2. 3-wire fluorescent dimming ballasts are required to dim fluorescent fixtures from a GP panel and may not be included in this quotation.
3. Distributor is responsible for ensuring that system provided meets project specifications.
4. Feed-thru panels (NO BREAKERS) require a 20 amp/single pole circuit breaker per circuit, which are to be SUPPLIED BY OTHERS.
5. Grafik Systems and Home Systems software is available in English only.
6. The user must contact Lutron for written approval prior to installation/upgrade of third party software on the lighting control computer. Lutron is not responsible for compatibility issues stemming from third-party software installations and upgrades.
7. It is the responsibility of the End-User to provide and install equipment for network and Internet connection.
8. It is the responsibility of the End-User to provide and install adequate network security (eg. Firewall, etc).
9. EcoSystem ballast module C5-BMF* and C5-BMJ* allows integration of Lutron's 3-wire phase controlled dimming ballast into EcoSystem Bus.
10. If included, Factory Startup pricing is based on full access to all affected rooms during normal business hours. Other charges will apply if access during normal business hours is not provided.
11. The distributor is responsible for ensuring compatibility of EcoSystem ballast/ballast module interface with fixtures.
12. EcoSystem ballasts and modules terminals only accept solid wire. Class 2 sensor inputs require #22AWG solid wire and line voltage inputs and the EcoSystem bus accept #16 AWG or #18 AWG. See product documentation for more details.
13. All fixtures for use with Ecosystem dimming ballasts require rapid-start sockets.
14. Lutron recommends EcoSystem Cable, or suitable alternative, for (Class 2) Sensors and (Class 1 or 2) EcoSystem Bus wiring. Quotation and purchase of cable does not imply agreement by fixture manufacturers to pre-install ballasts and cabling.
15. Domestic Quantum system does not support DALI ballasts.
16. Quantum Manager must be located within 300 feet of a network switch or hub.
17. All QSG units are ready to accept up to 3 Lutron shade groups. A new faceplate kit (QSGF*) may be ordered to add Lutron shade groups.
18. For systems including shade control, startup scope does not include the installation of the shade and shade systems. Installation is the responsibility of the shade installer.
19. If electronic transformers or LED drivers that require a reverse phase dimming signal are used with a QSG unit, an electronic low voltage interface (PHPM-PA-DV-WH) is required. Magnetic transformers do not require an interface.
20. If 3-wire fluorescent dimming ballasts are used with a QSG unit, a fluorescent dimming ballast interface (PHPM-3F-DV-WH) is required. Lutron's Tu-Wire fluorescent ballast does not require an interface. Lutron's EcoSystem ballasts require a GrafikEye with EcoSystem bus supply.
21. If any Lutron panel(s) or EcoSystem ballast(s)/module(s) are designated as emergency equipment, an upstream normal/emergency automatic transfer switch (by others) is required to feed normal/emergency Lutron panel(s) and EcoSystem ballast(s)/module(s). Upon loss of normal power and application of emergency power, all normal/emergency Lutron panel(s) and EcoSystem ballast(s)/module(s) default to full intensity and remain there until normal power is restored.
22. See Load Schedule for dimmer module circuit ratings and controllable dimming load types.
23. Lutron requires electronic AutoCAD drawings in order to provide graphic floorplan layouts in Quantum Vue.
24. No handheld programmer is available for use with Quantum. Review product data sheet for mobile control and programming license for mobile control capabilities.
25. LRF2 sensors are wireless, ceiling-mounted, battery-powered sensors that automatically control lights via RF communication to compatible dimming or switching devices.
26. Compatible dimming or switching devices are not included with LRF2 sensors and must be purchased separately. Refer to www.lutron.com/rps for



compatible products.

27. LRF2 sensors must be located within 60 ft (18 m) line of sight or 30 ft (9 m) through walls of a compatible dimming or switching device.

28. LRF2 sensors can communicate with up to 10 compatible dimming and switching devices.

29. LRF2 occupancy/vacancy sensors ability to detect motion requires line-of-sight of room-occupants. Sensor must have an unobstructed view of the room. DO NOT mount behind or near tall cabinets, shelves, hanging fixtures, ceiling fans, etc.

30. LRF2 occupancy/vacancy sensors cannot see through glass objects such as patio or shower doors.

31. Hot objects and moving air currents can affect LRF2 occupancy/vacancy sensor performance. To ensure proper operation, sensor should be mounted at least 4 ft (1.2 m) away from light bulbs below the ceiling line and HVAC vents.

32. LRF2 occupancy/vacancy sensor performance depends on a temperature differential between the ambient room temperature and that of room occupants. Warmer rooms may reduce the sensor's ability to detect occupants.

33. Normal and emergency power cannot be mixed in the same ESN unit.

34. Consult local codes for mixing 120V and 277V feeds in the same ESN unit.

35. Unless otherwise noted, Factory Commissioning is not included in quotation.

36. Lutron all-in-one cable for QS control links or sensors is not included in this quotation unless otherwise noted.

37. If a system does not include an ECO node and also does not include an ESN Programmer (model QSE-CI-AP-D) then system functionality is limited to what can be achieved via manual button programming. Consult ESN product submittal cut sheets for details of included functionality.

38. A WIRELESS ROUTER and an Apple IPOD TOUCH, IPHONE or IPAD (supplied by others) are required for programming. (An ESN Programmer is also required if the system does not include an ECO node).

39. iPod programming requires Energi Savr Node iPod application downloadable from the Apple App Store at no cost. Search the app store for ESN.

40. ESN Ecosystem is not compatible with the C-PDA-CLR or C-USB-IR (Ecosystem Programmers).

41. A WIRELESS ROUTER and an Apple IPOD TOUCH, IPHONE or IPAD (supplied by others) are required for programming

42. Ecosystem ballasts and modules terminals only accept one solid wire - from # 16 - #18 AWG.

43. This bill of materials may contain products that are not Buy American Act (BAA-US Country of Origin) nor Trade Agreements Act (TAA) compliant. Please refer to the project's Federal Acquisition Rules (FARs) which can be found in the original project solicitation/statement of work, RFP, or Division 1 of the specification, to confirm if the project requires products that meet these compliance requirements. Please contact Lutron should your project require products manufactured in the United States or a TAA country.

44. XP panels are not to be used to power EcoSystem ballasts or ESN's.

45. Lutron will provide submittals as electronic files. If Lutron is requested to provide paper hardcopies, Lutron will issue a quote based on the number of sheets, size of sheets, number of submittal sets required, and standard ground shipping. Minimum charge for paper hard copies will start at \$100 per set and increase in price depending on size and number of sheets. Paper hardcopies will also be subject to an increased lead time.

46. The standard lead-time for submittal information is 10 working days for projects under \$150K; 15 working days for projects from \$150-250K; 20 working days for all projects from \$250-500K; 25 working days for projects from \$500K-1M and a minimum of 30 working days for projects greater than \$1M. Product data sheets based upon the quoted bill of materials can be provided within 3 days of receipt of order at Lutron Electronics. Lutron's project management team will contact the installing electrical contractor to discuss the specific submittal requirements and together will determine an acceptable submittal schedule.

47. The lead-time for submittal drawings begins from Lutron's receipt of purchase order or other authorized intent to purchase and receipt of all other required documents.

48. On jobs that include EcoSystem ballasts, Lutron will require electronic files of the lighting plans to create project specific EcoSystem installation drawings. Lutron can accept AutoCAD or PDF electronic files. An additional 3-5 working days are required for submittals if files are provided in PDF format because they are more time consuming for Lutron to mark-up to show the proper Ecosystem installation.

49. The standard submittal information includes the following: (1) Bill of material with product descriptions (2) Product data sheets for all products shown on the bill of materials (3) Single-line diagrams and/or lighting plan overlays indicating the low-voltage wiring requirements (4) Panel schedules indicating the loads to be landed in each dimming/switching panel provided (5) Sequence of operation indicating Lutron's current understanding of the programming intent for the system. If Lutron has been informed of, or identified in the project specification, requirements for the project submittals that are in addition to the standard submittal information provided by Lutron, standard submittal lead-times may not apply to this project. These additional requirements will need to be discussed with the project team to determine the required submittal lead-time.

50. No shades, shade power supplies, or shade controls are included on this quote unless otherwise noted on the bill of material. The current bill of material may not have capacity for additional shade-related equipment. If shades are to be included on this project please contact Lutron.

51. Please see Quantum Vue spec sheet for specific feature details.

52. Quantum® Vue is a web-based software interface which allows for control and programming of a Quantum® system via any networked PC or tablet. Network configuration must be established by the customer, with general best practices provided by Lutron.

53. Lutron can only guarantee compatibility with dimmable CFL and LED loads that appear on our published product compatibility lists found on www.lutron.com. It is the responsibility of the installing contractor to verify compatibility of these loads with the quoted product.

54. Any deviation from this bill of material is subject to a new quotation.

55. All controls are provided with a white finish unless noted otherwise in the product description of the bill of material.

56. Lutron All-In-One Cable for any control links is not included in this quotation, unless otherwise noted.

57. If Lutron is providing the computer, the Server/Computer must be stored in a clean, climate controlled, lockable space. Failure to do so will void the warranty. Otherwise, the customer is responsible for providing a computer which meets Lutron's specifications.

58. An AutoCAD reflected ceiling floor plan is required at submittal stage for all jobs that include ecosystem control.

59. A copy of the database will be provided to the end user in an electronic format after commissioning. It is the responsibility of the customer to maintain backups of changes to the database.

60. No software applications other than Q-Admin or Q-Vue should be installed on Q-Manager.

61. Remote diagnostics for Quantum system requires an internet connection.



(Quote to complying Authorized Stocking Distributor only)

Date Revised: 19-Jul-2017

62. Required Ethernet network switches for inter-processor communication of the lighting control and Network equipment used to connect corporate networks to the lighting control system will be provided by others. This includes but is not limited to Routers, Switches, Ethernet cables and jacks.
63. If Green Glance is required and included in this quotation, it requires a separate PC. This PC is NOT included in this quotation. Display monitor for Green Glance is also to be provided by others.
64. Lutron recommends installation of a dedicated Lutron inter-processor network. If building network is to be used, contact Lutron for specific network requirements.
65. A dedicated control circuit may be required for power panels. See panel product data sheet for specific requirements.
66. For EcoSystem LED Drivers, Quantum version 3.0 or later is required for lower than 1% dimming.
67. The installer is responsible for ensuring that UL Listed LED drivers and/or remote mounted drivers are mounted in a position where they can be easily located and accessed if service or troubleshooting is necessary.

LUTRON ELECTRONICS CO., INC. QUOTATION TERMS AND CONDITIONS

All sales of Lutron products are pursuant to Lutron's Terms and Conditions of Sale (T&Cs), which are attached to this quotation and are also available in Lutron's price books, via DIMS at <http://dims.lutron.com>, at <http://www.lutron.com/general/Terms-ConditionsOfSale/Pages/Terms-Conditions-of-Sale.aspx>, and upon request. No terms and conditions other than the T&Cs, including any terms and conditions in any document attached to or incorporated by reference into any order accepted by

Quotation/Design:

Change Order prices are firm three (3) months from date of quotation or until made invalid by the execution of other, separately priced, change order(s). After three (3) months and up to six (6) months, all quotations will be subject to a maximum of 10% escalation to cover increased costs of labor and materials. All quotations must be re-quoted after six (6) months.

This Quotation is based on Lutron's interpretation of provided documents and includes Lutron's standard design, finish and construction unless indicated otherwise.

Compliance with project specific plans and/or specifications is not the responsibility of Lutron, and Lutron's acceptance of an order does not suggest or confirm such compliance. For all custom orders, the end-user or other authorized representative for a project must approve all drawings. Changes in drawings and/or Bill of Materials will require a new quotation.

Order:

This change order revision may only be ordered via a revision to the existing Purchase Order.

An order may be placed against this quotation on a Hold-for-Release basis. An order will not be considered firm unless accepted in writing by Lutron. Acceptance of an order does not imply conformance to plans and specifications. Prices are firm for 3 months from date of order acceptance. The price of all hold-for-release orders not released for immediate shipment within 3 months from the date of order acceptance will be increased up to 10% over the initial order price to cover increased cost of labor and material. All hold-for-release orders not released for immediate shipment within 6 months from the date of order acceptance may be cancelled by Lutron and subject to a 25% cancellation

Country of Origin:

Upon written request, Lutron will provide country of origin for the products quoted.

Terms:

Terms of sale shall be, at Lutron's option, one of the following: (a) your normal Lutron credit limit and terms as set by Lutron's credit department; or (b) credit limit and terms as approved by Lutron's credit department. Lutron reserves the right to require cash in advance or a confirmed, irrevocable letter of credit for each order. Further, Lutron may elect, at its discretion, not to quote or accept an order above your normal credit limit. If this quotation exceeds your credit limit, you should contact Lutron's credit department to discuss credit and terms in

Cancellations:

Orders for standard Lutron products may only be revised or canceled prior to the date of loading at the place of shipment, and only with Lutron's prior consent. Orders for nonstandard or custom Lutron products may only be revised or canceled prior to the commencement of production, and only with Lutron's prior consent. Any product which Lutron has the capability of producing but does not inventory is considered a nonstandard or custom product. All cancelled orders, whether for standard products or nonstandard or custom products, shall

Returned Goods Policy:

New and unopened products may be returned in accordance with Lutron's Returned Goods Policy in effect on the date each order is accepted and as authorized by Lutron on a Return Good Authorization, with the exception of non-standard, custom products and metal wall plates which are not returnable. Customer will be charged a minimum restocking charge of 25% of the cost of the returned goods and shall be responsible for freight and duties to return the products to Lutron. Lutron's Returned Goods Policy is available in Lutron's Price List, via

**LUTRON ELECTRONICS CO., INC. TERMS AND CONDITIONS OF SALE**

- 1. Acceptance of Orders/Terms:** All orders are subject to acceptance by Lutron Electronics Co., Inc. ("SUPPLIER") at its Coopersburg, PA headquarters. SUPPLIER reserves the right to reject any order. Possession of a price list does not constitute an offer to sell. Acceptance of any order by SUPPLIER is expressly conditioned on Customer's assent to the terms and conditions set forth herein ("Terms") and the waiver by Customer of any terms and conditions contained in any order form, confirmation, or any other communication of Customer, whether previously or hereafter delivered to SUPPLIER, which either add to, differ from, modify, conflict with or are otherwise inconsistent with any term or condition herein. SUPPLIER hereby gives notice of its objection to any additional or different terms or conditions in any such order form, confirmation or communication. Customer's failure to object in writing to these Terms prior to the earlier of Customer's acceptance of the products ordered or fifteen (15) days after delivery thereof to Customer will constitute agreement by Customer to these Terms. SUPPLIER hereby gives notice of its
- 2. Hold for Release Orders:** An order may be placed on a hold-for-release basis. Prices are firm for 3 months from date of order acceptance. The price of all hold-for-release orders not released by Customer for immediate shipment within 3 months from the date of order acceptance will be increased up to 10% increase over the initial order price to cover additional cost of labor and material. All hold-for-release orders not released for immediate shipment within 6 months from the date of order acceptance may be cancelled by SUPPLIER and subject to a 25% cancellation charge based on the price of the order.
- 3. Product Changes:** SUPPLIER reserves the right to discontinue the manufacture or sale of any product ("Supplier Product") at any time or to alter, modify or redesign the Supplier Products.
- 4. Use of Trademarks:** Customer shall use SUPPLIER's trademarks, logos or other identifiers in accordance with SUPPLIER's Corporate ID Guidelines and Style Guide found at .
- 5. Price:** All prices are subject to change without notice. Should any governmental action or request prevent SUPPLIER from implementing any price or continuing any price already in effect, SUPPLIER may at its option cancel Customer's order or any part thereof.
- 6. Taxes/Duties:** All prices exclude Taxes (as defined in Article 14) and are the sole responsibility of the Customer.
- 7. Credit Approval:** Customer credit approval is required prior to any shipment. If SUPPLIER determines at any time that Customer's financial condition does not justify the extension of credit to Customer, then SUPPLIER may at its option require cash payments in advance or other satisfactory security prior to delivery.
- 8. Cancellation/Change Orders:** Orders for standard Supplier Products may only be revised or canceled by Customer prior to the date of loading at the place of shipment, and only with SUPPLIER's prior consent. Orders for nonstandard or custom Supplier Products may only be revised or canceled by Customer prior to the commencement of production, and only with SUPPLIER's prior consent. Any product which SUPPLIER has the capability of producing but does not inventory is considered a nonstandard or custom product. All cancelled orders, whether for standard Supplier Products or nonstandard or custom Supplier Products, shall be subject to a cancellation charge of 25% of the order price. If
- 9. Packaging/Shipping/Risk of Loss:** Unless otherwise agreed by SUPPLIER in writing (i) SUPPLIER shall select the method of shipment and carrier, and (ii) costs for shipping shall be billed to Customer in accordance with the carrier's then current price list. Costs for special packaging and/or handling requested by Customer shall be the responsibility of Customer. The risk of loss, damage or shortage of SUPPLIER Products shall pass to Customer upon delivery to the carrier regardless of notice to Customer. SUPPLIER assumes no responsibility for insuring shipments unless specifically agreed to in writing by SUPPLIER, in which case the cost of insurance shall be for Customer's account.
- 10. Title:** Title to the Supplier Products shall only pass to the Customer upon the occurrence of any one of the following events: (i) the Customer having paid to the SUPPLIER all sums (including any default interest, if applicable) due from it to the SUPPLIER under the applicable invoice between the SUPPLIER and the Customer and SUPPLIER having received such payment as defined in the these Terms, or (ii) the SUPPLIER serving on the Customer notice in writing specifying that title to the Supplier Product has passed. Until title to the Supplier Product has passed to the Customer as set forth herein, the Customer shall possess the Supplier Product as a fiduciary and bailee of the Seller. If the SUPPLIER so requires, Customer shall store the Supplier Product separately from other goods and shall ensure that they are clearly identifiable as belonging to the SUPPLIER. The SUPPLIER may recover Supplier Product in respect of which title has not passed to the Customer at any time and the Customer irrevocably licenses the SUPPLIER, its officers, employees and agents to enter upon any premises of the Customer, with or without vehicles, for the purpose either of recovering goods in respect of which title has not passed to Customer or confirming that the Supplier Product is
- 11. Delivery:** Quoted shipping and/or delivery dates are based on estimates at the time of order. SUPPLIER shall use reasonable commercial efforts to meet such shipping and/or delivery dates, but SUPPLIER shall not be liable for any direct or indirect costs or damages, including without limitation incidental or consequential damages, resulting from late deliveries. Except as expressly provided otherwise herein, Customer agrees to purchase and pay for all material ordered as specified on SUPPLIER's invoice
- 12. Claims for Loss, Damage or Shortage:** Any claims for damage, loss or shortage should be filed by Customer with the respective transportation carrier in writing immediately upon receipt of the Supplier Products. In no event shall SUPPLIER be liable for damage or loss to a shipment caused by a carrier. If shortage exists with respect to any shipment and it is not concealed, Customer shall secure a notation of such shortage from the carrier on the freight bill or delivery receipt. If shortage is concealed, Customer must notify the carrier and SUPPLIER within 15 days. No claims for damage, loss or shortage will be allowed unless they are accompanied by an inspection report or signed delivery receipt
- 13. Return of SUPPLIER PRODUCT:** Customer may return new and unopened Supplier Product in accordance with Supplier's Returned Goods Policy in effect on the date each order is accepted and as authorized by Supplier on a Return Good Authorization, with the exception of non-standard, custom Products and metal wall plates which are not returnable. Customer will be charged a minimum restocking charge of 25% of the cost of the returned goods and shall be responsible for freight and duties to return the Supplier Product. SUPPLIER's Returned Goods Policy may be found in SUPPLIER's Price List as well as at <http://dims.lutron.com>. SUPPLIER reserves the right to amend its Returned Goods



(Quote to complying Authorized Stocking Distributor only)

Date Revised: 19-Jul-2017

14. Payment: All invoices, whether partial or in full, shall be due and payable in full by Customer pursuant to the terms set forth thereon. Invoices not timely paid are subject to an interest charge of 1.5% per month on any unpaid balance or the maximum rate allowed by law, which interest charges shall accrue beginning on the invoice due date. If Customer (i) becomes insolvent, files or has filed against it a petition in bankruptcy, makes any assignment for the benefit of creditors, or has a receiver or trustee appointed for it or its property, (ii) takes action to liquidate or otherwise cease doing business as a going concern, (iii) undergoes a change in ownership, (iv) fails to provide adequate assurance or security for credit extended, or (v) takes any other action that SUPPLIER determines in its sole discretion adversely impacts the conditions under which credit was extended, then all amounts outstanding from Customer hereunder shall at SUPPLIER's option become immediately due and payable. ALL PAYMENTS, WHETHER UNDER THE STANDARD PAYMENT TERMS OR OTHERWISE, SHALL BE CONSIDERED RECEIVED BY SUPPLIER AS FOLLOWS: (A) FOR PAYMENTS BY CHECK; WHEN THE CHECK IS RECEIVED AT SUPPLIER'S DESIGNATED PAYMENT LOCATION, AND (B) FOR PAYMENTS BY ELECTRONIC FUNDS TRANSFER, THE BUSINESS DAY ON WHICH THE FUNDS ARE IMMEDIATELY AVAILABLE TO SUPPLIER. Customer shall pay all undisputed invoices regardless of any dispute that may exist as to other

Customer shall make and remit any payments due SUPPLIER free and clear of, and without deduction or withholding for, any present or future taxes, levies, imposts, duties, fees, assessments or other charges of whatever nature ("Taxes") now or hereafter imposed by any jurisdiction or by any political subdivision or taxing authority thereof or therein with respect to such payments and all interest, penalties or similar liabilities with respect thereto. If Customer or any other person is required by any law or regulation to make any deduction or withholding on account of any Taxes from any payment to the SUPPLIER due under this Agreement, Customer shall, together with such payment, pay such additional amount ("gross up") as to ensure that SUPPLIER receives full payment. Customer represents and warrants to SUPPLIER that the full amount of any such deductions or withholding shall be accurately and timely paid over to the relevant authorities and Customer shall promptly forward to SUPPLIER copies of official receipts or other evidence satisfactory to SUPPLIER regarding such payment. Customer shall also agree to fully indemnify and

Notwithstanding the generality of the forgoing, Customer shall be responsible for any provincial, state or local tax (excluding taxes based on SUPPLIER'S income or profits) that results from the transfer of title or sale or delivery of the Products purchased hereunder unless a valid and correct tax exemption certificate is furnished to SUPPLIER prior to delivery.

15. SUPPLIER Obligations/Limitation of Liability: SUPPLIER PRODUCT DELIVERED HEREUNDER AND ALLEGED TO BE DEFECTIVE OR OTHERWISE OPENED AND THEN RETURNED TO CUSTOMER BY AN END-USER MAY BE RETURNED BY CUSTOMER TO SUPPLIER FOR A PERIOD UP TO ONE (1) YEAR FROM THE DATE OF SALE BY CUSTOMER TO END-USER. UPON RETURN OF SUPPLIER PRODUCT BY CUSTOMER, SUPPLIER MAY ELECT, AT ITS SOLE OPTION, TO RETURN THE CONSIDERATION PAID BY CUSTOMER TO SUPPLIER FOR SUCH RETURNED PRODUCT OR TO DELIVER CONFORMING PRODUCTS TO CUSTOMER. THE PRODUCT-SPECIFIC WRITTEN WARRANTIES PROVIDED IN OR WITH THE SUPPLIER PRODUCT ARE INTENDED EXCLUSIVELY FOR THE BENEFIT OF THE END-USER AND NOT CUSTOMER. THE FOREGOING IS THE ONLY OBLIGATION OF SUPPLIER TO CUSTOMER RELATING TO DEFECTIVE PRODUCTS AND IS IN LIEU OF ALL OTHER OBLIGATIONS OR WARRANTIES, EXPRESSED OR IMPLIED, ORAL OR WRITTEN, INCLUDING THE IMPLIED WARRANTIES OF MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. IN NO EVENT SHALL SUPPLIER BE RESPONSIBLE

16. Remedies of Customer: THE SOLE AND EXCLUSIVE REMEDY OF CUSTOMER AND THE SOLE AND EXCLUSIVE OBLIGATION OF SUPPLIER FOR ANY BREACH OF CONTRACT CLAIM THAT SUPPLIER PRODUCTS DELIVERED DO NOT OTHERWISE CONFORM TO THE ACCEPTED ORDER SHALL BE EITHER THE RETURN OF CONSIDERATION PAID BY CUSTOMER TO SUPPLIER RELATED TO THE BREACH, OR UPON SUPPLIER'S ELECTION, THE DELIVERY OF CONFORMING SUPPLIER PRODUCTS TO CUSTOMER. WITH RESPECT TO SUPPLIER'S NONCOMPLIANCE WITH ANY OTHER OBLIGATION OF SUPPLIER HEREUNDER, THE SOLE AND EXCLUSIVE REMEDY OF CUSTOMER AND THE SOLE AND EXCLUSIVE OBLIGATION OF SUPPLIER WILL BE AS SUPPLIER IN ITS DISCRETION WILL DETERMINE AS FOLLOWS: (1) SUPPLIER MAY ELECT TO CURE SUCH NONCOMPLIANCE WITHIN A REASONABLE PERIOD OF TIME, OR (2) IF SUPPLIER FAILS TO CURE SUCH NONCOMPLIANCE, CUSTOMER MAY RECOVER AN EQUITABLE AMOUNT NOT TO EXCEED SUCH CHARGES AS WERE PREVIOUSLY PAID TO SUPPLIER BY CUSTOMER RELATING TO THE BREACH. CUSTOMER WAIVES ALL OTHER REMEDIES, STATUTORY OR OTHERWISE, INCLUDING, WITHOUT LIMITATION, THE REMEDIES OF SPECIFIC PERFORMANCE AND REPLEVIN. ANY ACTION BROUGHT BY CUSTOMER IN CONNECTION WITH SUPPLIER'S PERFORMANCE HEREUNDER MUST BE COMMENCED WITHIN SIX (6) MONTHS AFTER SUCH CAUSE OF ACTION ACCRUES OR IT WILL BE DEEMED WAIVED. SUPPLIER'S LIABILITY TO CUSTOMER, REGARDLESS OF WHETHER SUCH LIABILITY ARISES IN CONTRACT, TORT (INCLUDING, WITHOUT LIMITATION, NEGLIGENCE OR STRICT LIABILITY) OR OTHERWISE, SHALL IN NO EVENT EXCEED AMOUNTS PAID BY CUSTOMER TO SUPPLIER FOR THE SUPPLIER PRODUCTS INVOLVED, AND CUSTOMER RELEASES SUPPLIER FROM ALL CLAIMS AND LIABILITIES IN EXCESS OF THIS

17. Excused Performance: SUPPLIER shall be under no liability for any failure to perform any of its obligations under these Terms or any contract if and to the extent that the failure is caused by reason of any cause outside the control of the SUPPLIER. Delivery suspended or not made by reason of force majeure shall be canceled without liability, but the Terms shall otherwise remain unaffected. SUPPLIER may allocate its available supply of Supplier Products or materials among itself and its customers in its sole discretion and without liability to Customer

18. Compliance with Laws, Regulations & Orders: Customer warrants that it will comply at all times with all laws (including customs, import and export laws), ordinances, rules, requirements and regulations applicable to the Products and when requested, shall furnish evidence to SUPPLIER of such compliance, including without limitation U.S. laws and regulations relating to exports, export controls, and foreign corrupt practices. SUPPLIER hereby certifies that the Supplier Products sold hereunder that were produced in the United States were produced in compliance with all applicable requirements of Sections 6, 7 and 12 of the Fair Labor Standards Act, as amended, and of regulations and orders

When SUPPLIER sells Products to Customers outside of the United States, Customer shall be responsible for obtaining any and all necessary import licenses, certificates of origin or other requested documents and for paying all applicable customs duties and levies, insurances, transportation costs as specified in the purchase order, Taxes and any other expenses in respect of the importation of the SUPPLIER Products into any country outside the United States. If required by SUPPLIER all the corroborative documentation must be presented to SUPPLIER upon

19. Entire Agreement. The terms and conditions contained herein constitute the entire agreement between SUPPLIER and Customer and supersede any and all prior agreements, whether oral, written or implied. No modification of these terms and conditions shall be effective unless made in writing and executed by SUPPLIER.



(Quote to complying Authorized Stocking Distributor only)

Date Revised: 19-Jul-2017

20. General: This agreement shall not be assigned by Customer without the prior written consent of SUPPLIER, and any assignment made without such consent shall be null and void. This agreement shall inure to the benefit of and be binding upon the parties hereto and their respective successors and permitted assigns. This agreement shall be governed by and construed in accordance with the laws of the Commonwealth of Pennsylvania, without giving effect to its conflicts of law provisions. Customer hereby expressly consents to the exclusive jurisdiction of the Pennsylvania courts to settle any disputes arising from these terms or the sale of Supplier Product to Customer.



ORDER ACKNOWLEDGEMENT QUOTE ORDER

Phone: (803) 252-5668
www.shealyelectrical.com

Cust. #: 18398

Ship To: **WATSON ELECT CONST CHARLESTON**
HOTEL AT MARION SQUARE
404 KING STREET
CHARLESTON, SC 29403

Correspondence To: **Shealy - West Columbia**
120 Saxe Gotha Road
West Columbia, SC 29172

(803) 252-5668

Bill To: **WATSON ELECT CONST CHARLESTON**
PO BOX 40697
Charleston, SC 29418

Order #	2476366-00
Date	05/19/17
PO #	SI # 39 QUOTE
UPC Vendor	
Page #	1
Ship Point	Shealy - West Columbia
Ship Via	Salesman Del
Shipped Date	
Terms	Passalong

Instructions

Ln#	Product # Description	Quantity Ordered	Quantity Backordered	Quantity Shipped	Qty UM	Unit Price	Price UM	Discount Multiplier	Net Amount
***** CONTACT: KEVIN SLOAN 843-708-9323 *****									
1	LUTRON BOM 00000 # C2037668.1.C.1 Dept Code: SI39	1		1	each	8325.00	each	0.00	8325.00
1	Lines Total		Quantity Total	1				Total Taxes Invoice Total	8325.00 749.25 9074.25



PROPOSED CHANGE ORDER contained herein is based upon currently executed Purchase Order for Lutron quotation , C 2037668.1.10 (referred to collectively as the "Blanket"); in addition to the change order request documents referenced below. This proposed change shall NOT be incorporated into Lutron's scope of work until executed in writing via a change to the Purchase Order. Should additional changes or other directives affect Lutron's scope of work prior to the execution of the proposed change contained herein, or if other proposed changes have a compounding effect on Lutron's scope of work, Lutron reserves the right to issue a revised or separate quotation for this change order. The Lutron Services Company line items for warranty, LSC-XXX, and start-up, LSC-OS-XXX-QTM, if listed below, are representative of the services associated with the entire Blanket order and not only this change order. Please refer to the Blanket for service(s) included for this project or contact Lutron for further information."

Job Name: The Hotel at Marion Square The Hotel at Marion Square

Job Location: Charleston, SC

Quoted To: Carolina Controls Group

Name: Ken Breeggemann

Job No: 2037668

Quoted By: Ed Watts

Quotation Based Upon:

Q1C1 - Based changes from SI #39 drawings dated 3/15/17-5/19/17 TMS.

Quote Specific Qualifiers and Exceptions:

1. Notes & Exceptions:

Q1C1 - The specifications for the added panel, model # GP3-1204M-20, must be reviewed and approved. If a different panel specification is required then please advise Lutron and a new quote will be issued.

Bill of Material:

Qty. Model Number

BILL OF MATERIAL

1 QSGRJ-6E-TWH

GRAFIK Eye QS with EcoSystem 6 zone E120 series control unit capable of setting 16 preset scenes of lighting, four of which are selectable on face of unit, and 0 shade columns. First 3 zones are line-voltage dimming zones and can be optionally programmed to be EcoSystem zones. EcoSystem bus is integral to the unit, supporting up to 64 EcoSystem ballasts, which can be assigned to one of the 6 zones. Integral support for daylight and occupancy sensors attached to EcoSystem ballasts or interfaces, including the ability to link EcoSystem-connected daylight and occupancy sensors to the 3 line-voltage outputs. The unit contains a 434 mhz radio frequency antenna for wireless functionality. The GRAFIK Eye has wireless interconnects to Lutron wireless devices such as occupancy sensors and keypads. Features include an adjustable 0 second to 60 minute fade rate per scene, an integral infrared receiver, and an integral astronomic timeclock. Control mounts in a standard 4-gang US wallbox, 2 3/4 in

1 QSGRJ-3P-TWH

GRAFIK Eye QS 3 zone control unit capable of setting 16 preset scenes of lighting, four of which are selectable on face of unit, and 0 shade columns. The unit contains a 434 mhz radio frequency antenna for wireless functionality. The GRAFIK Eye has wireless interconnects to Lutron wireless devices such as occupancy sensors and keypads. Features include an adjustable 0 second to 60 minute fade rate per scene, an integral infrared receiver, and an integral astronomic timeclock. Control mounts in a standard 4-gang US wallbox, 2 3/4 in min. depth (3 1/2 in recommended). Dimensions (inches (mm)): 4 11/16(119)H x 9 3/8(239)W x 3/8(10)D. Unengraved. Unit Color: TRANSLUCENT & WHITE

2 QSGFP-TIV

Face Plate Kit / standard color combination /0 Shades/MATTE/ Ivory Translucent / Engraving Certificate

1 GP3-1204M-20

Pre-assembled dimming panel containing three dimmers, each protected by a 20A-1P circuit breaker, with a 16A continuous rating per dimmer circuit. Each dimmer is capable of controlling incandescent, magnetic and electronic low voltage, Hi-lume and ECO-10 fluorescent ballasts, neon/cold cathode, and non-dim loads. Load types and circuit zone assignments are selectable at the dimming panel without the need for additional equipment. Panel accepts a 120/208V, 3 phase, 4 wire, 20A feed. (can also be configured as 1 phase, 2 wire, 40A.) Dimensions (inches(mm)): 18(460)H x 11(280)W x 6.25(160)D. Weight (w/o packaging): 30lbs(14kg.)

**1 LSC-B2**

2 year warranty providing 100% replacement parts & 100% Lutron labor coverage with a first-available response time.

1 LSC-OS-PST-QTM

Quantum Onsite Startup for this system includes the following visits: Quantum Prewire Visit Onsite visit by a Lutron Services Company Representative typically held with the electrical contractor, project manager, and owner's representative to discuss the project scope and timeline. Additionally, the mounting and wiring of system devices, including panels, controls, and sensors is discussed. Quantum Startup Visit Onsite visit by a Lutron Services Company Representative held after Lutron equipment is installed. Equipment installation is verified and system is programmed and tested during this time. Quantum Training Onsite visit by a Lutron Services Company Representative held with the end user of the lighting control system. During this visit, Lutron Services Company Representative provides instruction on system maintenance and operation, including the use of any system software.

Product Lead Time: Please contact Lutron with your desired product delivery date. Typical lead times for Lutron system products are 4 weeks or less after receipt of approved submittal and release. To best enable Lutron to meet your delivery requirements, please submit your construction schedule with your hold for release purchase order.

For this Quote, the estimated Lead Time (in weeks) After Release is 4 weeks.

Visit www.lutron.com/incentives for location specific information on rebates and incentives that promote energy efficient lighting systems. Financial assistance to purchase and install energy efficient products can come from local and state utilities, state energy efficiency programs, EAct tax incentives, and federal stimulus monies that focus on energy efficiency.

Qualifiers:

1. Refer to description column on quote for dimming panel feeder requirements.
2. 3-wire fluorescent dimming ballasts are required to dim fluorescent fixtures from a GP panel and may not be included in this quotation.
3. Distributor is responsible for ensuring that system provided meets project specifications.
4. Feed-thru panels (NO BREAKERS) require a 20 amp/single pole circuit breaker per circuit, which are to be SUPPLIED BY OTHERS.
5. Grafik Systems and Home Systems software is available in English only.
6. The user must contact Lutron for written approval prior to installation/upgrade of third party software on the lighting control computer. Lutron is not responsible for compatibility issues stemming from third-party software installations and upgrades.
7. It is the responsibility of the End-User to provide and install equipment for network and internet connection.
8. It is the responsibility of the End-User to provide and install adequate network security (eg. Firewall, etc).
9. EcoSystem ballast module C5-BMF* and C5-BMJ* allows integration of Lutron's 3-wire phase controlled dimming ballast into EcoSystem Bus.
10. If included, Factory Startup pricing is based on full access to all affected rooms during normal business hours. Other charges will apply if access during normal business hours is not provided.
11. The distributor is responsible for ensuring compatibility of EcoSystem ballast/ballast module interface with fixtures.
12. EcoSystem ballasts and modules terminals only accept solid wire. Class 2 sensor inputs require #22AWG solid wire and line voltage inputs and the EcoSystem bus accept #16 AWG or #18 AWG. See product documentation for more details.
13. All fixtures for use with Ecosystem dimming ballasts require rapid-start sockets.
14. Lutron recommends EcoSystem Cable, or suitable alternative, for (Class 2) Sensors and (Class 1 or 2) EcoSystem Bus wiring. Quotation and purchase of cable does not imply agreement by fixture manufacturers to pre-install ballasts and cabling.
15. Domestic Quantum system does not support DALI ballasts.
16. Quantum Manager must be located within 300 feet of a network switch or hub.
17. All QSG units are ready to accept up to 3 Lutron shade groups. A new faceplate kit (QSGF*) may be ordered to add Lutron shade groups.
18. For systems including shade control, startup scope does not include the installation of the shade and shade systems. Installation is the responsibility of the shade installer.
19. If electronic transformers or LED drivers that require a reverse phase dimming signal are used with a QSG unit, an electronic low voltage interface



(Quote to complying Authorized Stocking Distributor only)

Date Revised: 19-May-2017

(PHPM-PA-DV-WH) is required. Magnetic transformers do not require an interface.

20. If 3-wire fluorescent dimming ballasts are used with a QSG unit, a fluorescent dimming ballast interface (PHPM-3F-DV-WH) is required. Lutron's Tu-Wire fluorescent ballast does not require an interface. Lutron's EcoSystem ballasts require a GrafikEye with EcoSystem bus supply.

21. If any Lutron panel(s) or EcoSystem ballast(s)/module(s) are designated as emergency equipment, an upstream normal/emergency automatic transfer switch (by others) is required to feed normal/emergency Lutron panel(s) and EcoSystem ballast(s)/module(s). Upon loss of normal power and application of emergency power, all normal/emergency Lutron panel(s) and EcoSystem ballast(s)/module(s) default to full intensity and remain there until normal power is restored.

22. See Load Schedule for dimmer module circuit ratings and controllable dimming load types.

23. Lutron requires electronic AutoCAD drawings in order to provide graphic floorplan layouts in Quantum Vue.

24. No handheld programmer is available for use with Quantum. Review product data sheet for mobile control and programming license for mobile control capabilities.

25. LRF2 sensors are wireless, ceiling-mounted, battery-powered sensors that automatically control lights via RF communication to compatible dimming or switching devices.

26. Compatible dimming or switching devices are not included with LRF2 sensors and must be purchased separately. Refer to www.lutron.com/rps for compatible products.

27. LRF2 sensors must be located within 60 ft (18 m) line of sight or 30 ft (9 m) through walls of a compatible dimming or switching device.

28. LRF2 sensors can communicate with up to 10 compatible dimming and switching devices.

29. LRF2 occupancy/vacancy sensors ability to detect motion requires line-of-sight of room occupants. Sensor must have an unobstructed view of the room. DO NOT mount behind or near tall cabinets, shelves, hanging fixtures, ceiling fans, etc.

30. LRF2 occupancy/vacancy sensors cannot see through glass objects such as patio or shower doors.

31. Hot objects and moving air currents can affect LRF2 occupancy/vacancy sensor performance. To ensure proper operation, sensor should be mounted at least 4 ft (1.2 m) away from light bulbs below the ceiling line and HVAC vents.

32. LRF2 occupancy/vacancy sensor performance depends on a temperature differential between the ambient room temperature and that of room occupants. Warmer rooms may reduce the sensor's ability to detect occupants.

33. Normal and emergency power cannot be mixed in the same ESN unit.

34. Consult local codes for mixing 120V and 277V feeds in the same ESN unit.

35. Unless otherwise noted, Factory Commissioning is not included in quotation.

36. Lutron all-in-one cable for QS control links or sensors is not included in this quotation unless otherwise noted.

37. If a system does not include an ECO node and also does not include an ESN Programmer (model QSE-CI-AP-D) then system functionality is limited to what can be achieved via manual button programming. Consult ESN product submittal cut sheets for details of included functionality.

38. A WIRELESS ROUTER and an Apple IPOD TOUCH, IPHONE or IPAD (supplied by others) are required for programming. (An ESN Programmer is also required if the system does not include an ECO node).

39. iPod programming requires Energi Savr Node iPod application downloadable from the Apple App Store at no cost. Search the app store for ESN.

40. ESN Ecosystem is not compatible with the C-PDA-CLR or C-USB-IR (Ecosystem Programmers).

41. A WIRELESS ROUTER and an Apple IPOD TOUCH, IPHONE or IPAD (supplied by others) are required for programming

42. Ecosystem ballasts and modules terminals only accept one solid wire - from # 16 - #18 AWG.

43. This bill of materials may contain products that are not Buy American Act (BAA-US Country of Origin) nor Trade Agreements Act (TAA) compliant. Please refer to the project's Federal Acquisition Rules (FARs) which can be found in the original project solicitation/statement of work, RFP, or Division 1 of the specification, to confirm if the project requires products that meet these compliance requirements. Please contact Lutron should your project require products manufactured in the United States or a TAA country.

44. XP panels are not to be used to power EcoSystem ballasts or ESN's.

45. Lutron will provide submittals as electronic files. If Lutron is requested to provide paper hardcopies, Lutron will issue a quote based on the number of sheets, size of sheets, number of submittal sets required, and standard ground shipping. Minimum charge for paper hard copies will start at \$100 per set and increase in price depending on size and number of sheets. Paper hardcopies will also be subject to an increased lead time.

46. The standard lead-time for submittal information is 10 working days for projects under \$150K; 15 working days for projects from \$150-250K; 20 working days for all projects from \$250-500K; 25 working days for projects from \$500K-1M and a minimum of 30 working days for projects greater than \$1M. Product data sheets based upon the quoted bill of materials can be provided within 3 days of receipt of order at Lutron Electronics. Lutron's project management team will contact the installing electrical contractor to discuss the specific submittal requirements and together will determine an acceptable submittal schedule.

47. The lead-time for submittal drawings begins from Lutron's receipt of purchase order or other authorized intent to purchase and receipt of all other required documents.

48. On jobs that include EcoSystem ballasts, Lutron will require electronic files of the lighting plans to create project specific EcoSystem installation drawings. Lutron can accept AutoCAD or PDF electronic files. An additional 3-5 working days are required for submittals if files are provided in PDF format because they are more time consuming for Lutron to mark-up to show the proper Ecosystem installation.

49. The standard submittal information includes the following: (1) Bill of material with product descriptions (2) Product data sheets for all products shown on the bill of materials (3) Single-line diagrams and/or lighting plan overlays indicating the low-voltage wiring requirements (4) Panel schedules indicating the loads to be landed in each dimming/switching panel provided (5) Sequence of operation indicating Lutron's current understanding of the programming intent for the system. If Lutron has been informed of, or identified in the project specification, requirements for the project submittals that are in addition to the standard submittal information provided by Lutron, standard submittal lead-times may not apply to this project. These additional requirements will need to be discussed with the project team to determine the required submittal lead-time.

50. No shades, shade power supplies, or shade controls are included on this quote unless otherwise noted on the bill of material. The current bill of material may not have capacity for additional shade-related equipment. If shades are to be included on this project please contact Lutron.



51. Please see Quantum Vue spec sheet for specific feature details.
52. Quantum® Vue is a web-based software interface which allows for control and programming of a Quantum® system via any networked PC or tablet. Network configuration must be established by the customer, with general best practices provided by Lutron.
53. Lutron can only guarantee compatibility with dimmable CFL and LED loads that appear on our published product compatibility lists found on www.lutron.com. It is the responsibility of the installing contractor to verify compatibility of these loads with the quoted product.
54. Any deviation from this bill of material is subject to a new quotation.
55. All controls are provided with a white finish unless noted otherwise in the product description of the bill of material.
56. Lutron All-In-One Cable for any control links is not included in this quotation, unless otherwise noted.
57. If Lutron is providing the computer, the Server/Computer must be stored in a clean, climate controlled, lockable space. Failure to do so will void the warranty. Otherwise, the customer is responsible for providing a computer which meets Lutron's specifications.
58. An AutoCAD reflected ceiling floor plan is required at submittal stage for all jobs that include ecosystem control.
59. A copy of the database will be provided to the end user in an electronic format after commissioning. It is the responsibility of the customer to maintain backups of changes to the database.
60. No software applications other than Q-Admin or Q-Vue should be installed on Q-Manager.
61. Remote diagnostics for Quantum system requires an internet connection.
62. Required Ethernet network switches for inter-processor communication of the lighting control and Network equipment used to connect corporate networks to the lighting control system will be provided by others. This includes but is not limited to Routers, Switches, Ethernet cables and jacks.
63. If Green Glance is required and included in this quotation, it requires a separate PC. This PC is NOT included in this quotation. Display monitor for Green Glance is also to be provided by others.
64. Lutron recommends installation of a dedicated Lutron inter-processor network. If building network is to be used, contact Lutron for specific network requirements.
65. A dedicated control circuit may be required for power panels. See panel product data sheet for specific requirements.
66. For EcoSystem LED Drivers, Quantum version 3.0 or later is required for lower than 1% dimming.
67. The installer is responsible for ensuring that UL Listed LED drivers and/or remote mounted drivers are mounted in a position where they can be easily located and accessed if service or troubleshooting is necessary.

**LUTRON ELECTRONICS CO., INC. QUOTATION TERMS AND CONDITIONS**

All sales of Lutron products are pursuant to Lutron's Terms and Conditions of Sale (T&Cs), which are attached to this quotation and are also available in Lutron's price books, via DIMS at <http://dims.lutron.com>, at <http://www.lutron.com/general/Terms-ConditionsofSale/Pages/Terms-Conditions-of-Sale.aspx>, and upon request. No terms and conditions other than the T&Cs, including any terms and conditions in any document attached to or incorporated by reference into any order accepted by

Quotation/Design:

Change Order prices are firm three (3) months from date of quotation or until made invalid by the execution of other, separately priced, change order(s). After three (3) months and up to six (6) months, all quotations will be subject to a maximum of 10% escalation to cover increased costs of labor and materials. All quotations must be re-quoted after six (6) months.

This Quotation is based on Lutron's interpretation of provided documents and includes Lutron's standard design, finish and construction unless indicated otherwise.

Compliance with project specific plans and/or specifications is not the responsibility of Lutron, and Lutron's acceptance of an order does not suggest or confirm such compliance. For all custom orders, the end-user or other authorized representative for a project must approve all drawings. Changes in drawings and/or Bill of Materials will require a new quotation.

Order:

This change order revision may only be ordered via a revision to the existing Purchase Order.

An order may be placed against this quotation on a Hold-for-Release basis. An order will not be considered firm unless accepted in writing by Lutron. Acceptance of an order does not imply conformance to plans and specifications. Prices are firm for 3 months from date of order acceptance. The price of all hold-for-release orders not released for immediate shipment within 3 months from the date of order acceptance will be increased up to 10% over the initial order price to cover increased cost of labor and material. All hold-for-release orders not released for immediate shipment within 6 months from the date of order acceptance may be cancelled by Lutron and subject to a 25% cancellation

Country of Origin:

Upon written request, Lutron will provide country of origin for the products quoted.

Terms:

Terms of sale shall be, at Lutron's option, one of the following: (a) your normal Lutron credit limit and terms as set by Lutron's credit department; or (b) credit limit and terms as approved by Lutron's credit department. Lutron reserves the right to require cash in advance or a confirmed, irrevocable letter of credit for each order. Further, Lutron may elect, at its discretion, not to quote or accept an order above your normal credit limit. If this quotation exceeds your credit limit, you should contact Lutron's credit department to discuss credit and terms in

Cancellations:

Orders for standard Lutron products may only be revised or canceled prior to the date of loading at the place of shipment, and only with Lutron's prior consent. Orders for nonstandard or custom Lutron products may only be revised or canceled prior to the commencement of production, and only with Lutron's prior consent. Any product which Lutron has the capability of producing but does not inventory is considered a nonstandard or custom product. All cancelled orders, whether for standard products or nonstandard or custom products, shall

Returned Goods Policy:

New and unopened products may be returned in accordance with Lutron's Returned Goods Policy in effect on the date each order is accepted and as authorized by Lutron on a Return Good Authorization, with the exception of non-standard, custom products and metal wall plates which are not returnable. Customer will be charged a minimum restocking charge of 25% of the cost of the returned goods and shall be responsible for freight and duties to return the products to Lutron. Lutron's Returned Goods Policy is available in Lutron's Price List, via

**LUTRON ELECTRONICS CO., INC. TERMS AND CONDITIONS OF SALE**

1. Acceptance of Orders/Terms: All orders are subject to acceptance by Lutron Electronics Co., Inc. ("SUPPLIER") at its Coopersburg, PA headquarters. SUPPLIER reserves the right to reject any order. Possession of a price list does not constitute an offer to sell. Acceptance of any order by SUPPLIER is expressly conditioned on Customer's assent to the terms and conditions set forth herein ("Terms") and the waiver by Customer of any terms and conditions contained in any order form, confirmation, or any other communication of Customer, whether previously or hereafter delivered to SUPPLIER, which either add to, differ from, modify, conflict with or are otherwise inconsistent with any term or condition herein. SUPPLIER hereby gives notice of its objection to any additional or different terms or conditions in any such order form, confirmation or communication. Customer's failure to object in writing to these Terms prior to the earlier of Customer's acceptance of the products ordered or fifteen (15) days after delivery thereof to Customer will constitute agreement by Customer to these Terms. SUPPLIER hereby gives notice of its

2. Hold for Release Orders: An order may be placed on a hold-for-release basis. Prices are firm for 3 months from date of order acceptance. The price of all hold-for-release orders not released by Customer for immediate shipment within 3 months from the date of order acceptance will be increased up to 10% increase over the initial order price to cover additional cost of labor and material. All hold-for-release orders not released for immediate shipment within 6 months from the date of order acceptance may be cancelled by SUPPLIER and subject to a 25% cancellation charge based on the price of the order.

3. Product Changes: SUPPLIER reserves the right to discontinue the manufacture or sale of any product ("Supplier Product") at any time or to alter, modify or redesign the Supplier Products.

4. Use of Trademarks: Customer shall use SUPPLIER's trademarks, logos or other identifiers in accordance with SUPPLIER's Corporate ID Guidelines and Style Guide found at .

5. Price: All prices are subject to change without notice. Should any governmental action or request prevent SUPPLIER from implementing any price or continuing any price already in effect, SUPPLIER may at its option cancel Customer's order or any part thereof.

6. Taxes/Duties: All prices exclude Taxes (as defined in Article 14) and are the sole responsibility of the Customer.

7. Credit Approval: Customer credit approval is required prior to any shipment. If SUPPLIER determines at any time that Customer's financial condition does not justify the extension of credit to Customer, then SUPPLIER may at its option require cash payments in advance or other satisfactory security prior to delivery.

8. Cancellation/Change Orders: Orders for standard Supplier Products may only be revised or canceled by Customer prior to the date of loading at the place of shipment, and only with SUPPLIER's prior consent. Orders for nonstandard or custom Supplier Products may only be revised or canceled by Customer prior to the commencement of production, and only with SUPPLIER's prior consent. Any product which SUPPLIER has the capability of producing but does not inventory is considered a nonstandard or custom product. All cancelled orders, whether for standard Supplier Products or nonstandard or custom Supplier Products, shall be subject to a cancellation charge of 25% of the order price. If

9. Packaging/Shipping/Risk of Loss: Unless otherwise agreed by SUPPLIER in writing (i) SUPPLIER shall select the method of shipment and carrier, and (ii) costs for shipping shall be billed to Customer in accordance with the carrier's then current price list. Costs for special packaging and/or handling requested by Customer shall be the responsibility of Customer. The risk of loss, damage or shortage of SUPPLIER Products shall pass to Customer upon delivery to the carrier regardless of notice to Customer. SUPPLIER assumes no responsibility for insuring shipments unless specifically agreed to in writing by SUPPLIER, in which case the cost of insurance shall be for Customer's account.

10. Title: Title to the Supplier Products shall only pass to the Customer upon the occurrence of any one of the following events: (i) the Customer having paid to the SUPPLIER all sums (including any default interest, if applicable) due from it to the SUPPLIER under the applicable invoice between the SUPPLIER and the Customer and SUPPLIER having received such payment as defined in the these Terms, or (ii) the SUPPLIER serving on the Customer notice in writing specifying that title to the Supplier Product has passed. Until title to the Supplier Product has passed to the Customer as set forth herein, the Customer shall possess the Supplier Product as a fiduciary and bailee of the Seller. If the SUPPLIER so requires, Customer shall store the Supplier Product separately from other goods and shall ensure that they are clearly identifiable as belonging to the SUPPLIER. The SUPPLIER may recover Supplier Product in respect of which title has not passed to the Customer at any time and the Customer irrevocably licenses the SUPPLIER, its officers, employees and agents to enter upon any premises of the Customer, with or without vehicles, for the purpose either of recovering goods in respect of which title has not passed to Customer or confirming that the Supplier Product is

11. Delivery: Quoted shipping and/or delivery dates are based on estimates at the time of order. SUPPLIER shall use reasonable commercial efforts to meet such shipping and/or delivery dates, but SUPPLIER shall not be liable for any direct or indirect costs or damages, including without limitation incidental or consequential damages, resulting from late deliveries. Except as expressly provided otherwise herein, Customer agrees to purchase and pay for all material ordered as specified on SUPPLIER's invoice.

12. Claims for Loss, Damage or Shortage: Any claims for damage, loss or shortage should be filed by Customer with the respective transportation carrier in writing immediately upon receipt of the Supplier Products. In no event shall SUPPLIER be liable for damage or loss to a shipment caused by a carrier. If shortage exists with respect to any shipment and it is not concealed, Customer shall secure a notation of such shortage from the carrier on the freight bill or delivery receipt. If shortage is concealed, Customer must notify the carrier and SUPPLIER within 15 days. No claims for damage, loss or shortage will be allowed unless they are accompanied by an inspection report or signed delivery receipt.

13. Return of SUPPLIER PRODUCT: Customer may return new and unopened Supplier Product in accordance with Supplier's Returned Goods Policy in effect on the date each order is accepted and as authorized by Supplier on a Return Good Authorization, with the exception of non-standard, custom Products and metal wall plates which are not returnable. Customer will be charged a minimum restocking charge of 25% of the cost of the returned goods and shall be responsible for freight and duties to return the Supplier Product. SUPPLIER's Returned Goods Policy may be found in SUPPLIER's Price List as well as at <http://dims.lutron.com>. SUPPLIER reserves the right to amend its Returned Goods



(Quote to complying Authorized Stocking Distributor only)

Date Revised: 19-May-2017

14. Payment: All invoices, whether partial or in full, shall be due and payable in full by Customer pursuant to the terms set forth thereon. Invoices not timely paid are subject to an interest charge of 1.5% per month on any unpaid balance or the maximum rate allowed by law, which interest charges shall accrue beginning on the invoice due date. If Customer (i) becomes insolvent, files or has filed against it a petition in bankruptcy, makes any assignment for the benefit of creditors, or has a receiver or trustee appointed for it or its property, (ii) takes action to liquidate or otherwise cease doing business as a going concern, (iii) undergoes a change in ownership, (iv) fails to provide adequate assurance or security for credit extended, or (v) takes any other action that SUPPLIER determines in its sole discretion adversely impacts the conditions under which credit was extended, then all amounts outstanding from Customer hereunder shall at SUPPLIER's option become immediately due and payable. ALL PAYMENTS, WHETHER UNDER THE STANDARD PAYMENT TERMS OR OTHERWISE, SHALL BE CONSIDERED RECEIVED BY SUPPLIER AS FOLLOWS: (A) FOR PAYMENTS BY CHECK, WHEN THE CHECK IS RECEIVED AT SUPPLIER'S DESIGNATED PAYMENT LOCATION, AND (B) FOR PAYMENTS BY ELECTRONIC FUNDS TRANSFER, THE BUSINESS DAY ON WHICH THE FUNDS ARE IMMEDIATELY AVAILABLE TO SUPPLIER. Customer shall pay all undisputed invoices regardless of any dispute that may exist as to other

Customer shall make and remit any payments due SUPPLIER free and clear of, and without deduction or withholding for, any present or future taxes, levies, imposts, duties, fees, assessments or other charges of whatever nature ("Taxes") now or hereafter imposed by any jurisdiction or by any political subdivision or taxing authority thereof or therein with respect to such payments and all interest, penalties or similar liabilities with respect thereto. If Customer or any other person is required by any law or regulation to make any deduction or withholding on account of any Taxes from any payment to the SUPPLIER due under this Agreement, Customer shall, together with such payment, pay such additional amount ("gross up") as to ensure that SUPPLIER receives full payment. Customer represents and warrants to SUPPLIER that the full amount of any such deductions or withholding shall be accurately and timely paid over to the relevant authorities and Customer shall promptly forward to SUPPLIER copies of official receipts or other evidence satisfactory to SUPPLIER regarding such payment. Customer shall also agree to fully indemnify and

Notwithstanding the generality of the foregoing, Customer shall be responsible for any provincial, state or local tax (excluding taxes based on SUPPLIER'S income or profits) that results from the transfer of title or sale or delivery of the Products purchased hereunder unless a valid and correct tax exemption certificate is furnished to SUPPLIER prior to delivery.

15. SUPPLIER Obligations/Limitation of Liability: SUPPLIER PRODUCT DELIVERED HEREUNDER AND ALLEGED TO BE DEFECTIVE OR OTHERWISE OPENED AND THEN RETURNED TO CUSTOMER BY AN END-USER MAY BE RETURNED BY CUSTOMER TO SUPPLIER FOR A PERIOD UP TO ONE (1) YEAR FROM THE DATE OF SALE BY CUSTOMER TO END-USER. UPON RETURN OF SUPPLIER PRODUCT BY CUSTOMER, SUPPLIER MAY ELECT, AT ITS SOLE OPTION, TO RETURN THE CONSIDERATION PAID BY CUSTOMER TO SUPPLIER FOR SUCH RETURNED PRODUCT OR TO DELIVER CONFORMING PRODUCTS TO CUSTOMER. THE PRODUCT-SPECIFIC WRITTEN WARRANTIES PROVIDED IN OR WITH THE SUPPLIER PRODUCT ARE INTENDED EXCLUSIVELY FOR THE BENEFIT OF THE END-USER AND NOT CUSTOMER. THE FOREGOING IS THE ONLY OBLIGATION OF SUPPLIER TO CUSTOMER RELATING TO DEFECTIVE PRODUCTS AND IS IN LIEU OF ALL OTHER OBLIGATIONS OR WARRANTIES, EXPRESSED OR IMPLIED, ORAL OR WRITTEN, INCLUDING THE IMPLIED WARRANTIES OF MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. IN NO EVENT SHALL SUPPLIER BE RESPONSIBLE

16. Remedies of Customer: THE SOLE AND EXCLUSIVE REMEDY OF CUSTOMER AND THE SOLE AND EXCLUSIVE OBLIGATION OF SUPPLIER FOR ANY BREACH OF CONTRACT CLAIM THAT SUPPLIER PRODUCTS DELIVERED DO NOT OTHERWISE CONFORM TO THE ACCEPTED ORDER SHALL BE EITHER THE RETURN OF CONSIDERATION PAID BY CUSTOMER TO SUPPLIER RELATED TO THE BREACH, OR UPON SUPPLIER'S ELECTION, THE DELIVERY OF CONFORMING SUPPLIER PRODUCTS TO CUSTOMER. WITH RESPECT TO SUPPLIER'S NONCOMPLIANCE WITH ANY OTHER OBLIGATION OF SUPPLIER HEREUNDER, THE SOLE AND EXCLUSIVE REMEDY OF CUSTOMER AND THE SOLE AND EXCLUSIVE OBLIGATION OF SUPPLIER WILL BE AS SUPPLIER IN ITS DISCRETION WILL DETERMINE AS FOLLOWS: (1) SUPPLIER MAY ELECT TO CURE SUCH NONCOMPLIANCE WITHIN A REASONABLE PERIOD OF TIME, OR (2) IF SUPPLIER FAILS TO CURE SUCH NONCOMPLIANCE, CUSTOMER MAY RECOVER AN EQUITABLE AMOUNT NOT TO EXCEED SUCH CHARGES AS WERE PREVIOUSLY PAID TO SUPPLIER BY CUSTOMER RELATING TO THE BREACH. CUSTOMER WAIVES ALL OTHER REMEDIES, STATUTORY OR OTHERWISE, INCLUDING, WITHOUT LIMITATION, THE REMEDIES OF SPECIFIC PERFORMANCE AND REPLEVIN. ANY ACTION BROUGHT BY CUSTOMER IN CONNECTION WITH SUPPLIER'S PERFORMANCE HEREUNDER MUST BE COMMENCED WITHIN SIX (6) MONTHS AFTER SUCH CAUSE OF ACTION ACCRUES OR IT WILL BE DEEMED WAIVED. SUPPLIER'S LIABILITY TO CUSTOMER, REGARDLESS OF WHETHER SUCH LIABILITY ARISES IN CONTRACT, TORT (INCLUDING, WITHOUT LIMITATION, NEGLIGENCE OR STRICT LIABILITY) OR OTHERWISE, SHALL IN NO EVENT EXCEED AMOUNTS PAID BY CUSTOMER TO SUPPLIER FOR THE SUPPLIER PRODUCTS INVOLVED, AND CUSTOMER RELEASES SUPPLIER FROM ALL CLAIMS AND LIABILITIES IN EXCESS OF THIS

17. Excused Performance: SUPPLIER shall be under no liability for any failure to perform any of its obligations under these Terms or any contract if and to the extent that the failure is caused by reason of any cause outside the control of the SUPPLIER. Delivery suspended or not made by reason of force majeure shall be canceled without liability, but the Terms shall otherwise remain unaffected. SUPPLIER may allocate its available supply of Supplier Products or materials among itself and its customers in its sole discretion and without liability to Customer

18. Compliance with Laws, Regulations & Orders: Customer warrants that it will comply at all times with all laws (including customs, import and export laws), ordinances, rules, requirements and regulations applicable to the Products and when requested, shall furnish evidence to SUPPLIER of such compliance, including without limitation U.S. laws and regulations relating to exports, export controls, and foreign corrupt practices. SUPPLIER hereby certifies that the Supplier Products sold hereunder that were produced in the United States were produced in compliance with all applicable requirements of Sections 6, 7 and 12 of the Fair Labor Standards Act, as amended, and of regulations and orders

When SUPPLIER sells Products to Customers outside of the United States, Customer shall be responsible for obtaining any and all necessary import licenses, certificates of origin or other requested documents and for paying all applicable customs duties and levies, insurances, transportation costs as specified in the purchase order, Taxes and any other expenses in respect of the importation of the SUPPLIER Products into any country outside the United States. If required by SUPPLIER all the corroborative documentation must be presented to SUPPLIER upon

19. Entire Agreement. The terms and conditions contained herein constitute the entire agreement between SUPPLIER and Customer and supersede any and all prior agreements, whether oral, written or implied. No modification of these terms and conditions shall be effective unless made in writing and executed by SUPPLIER.



(Quote to complying Authorized Stocking Distributor only)

Date Revised: 19-May-2017

20. **General:** This agreement shall not be assigned by Customer without the prior written consent of SUPPLIER, and any assignment made without such consent shall be null and void. This agreement shall inure to the benefit of and be binding upon the parties hereto and their respective successors and permitted assigns. This agreement shall be governed by and construed in accordance with the laws of the Commonwealth of Pennsylvania, without giving effect to its conflicts of law provisions. Customer hereby expressly consents to the exclusive jurisdiction of the Pennsylvania courts to settle any disputes arising from these terms or the sale of Supplier Product to Customer.

Tab No. 221

Change Order Request Summary



Strong Tower Construction, LLC, dba Koch Corporation
1131 Logan Street
Louisville, KY 40204

Date (mm/dd/yy) January 31, 2018
Change Order Request Koch # 011

Project Name Hotel at Marion Square
Project Number 2759 Charleston, SC
Subcontract No./Package

Change Order Type CO Request #
Pricing Type
Type of Contract Lump Sum
Time Extension Work Days

Description of Work: Furnish and apply blackout film at (2) Type G windows

Engineering/Drafting not required.

A. Labor Summary (including fringe benefits)

Standard Hours and Rate				Premium Hours and Rate				Classification	
Fab	hours	x	\$ 54.71 /hour	+	hours	x	\$ 82.07 /hour	=	\$ - Shop Labor, Curtain 13-10
Fab Super	hours	x	\$ 64.68				\$ 97.02 /hour	=	\$ - Shop Labor - Super 13-52
Fab Delivery	hours	x	\$ 54.71 /hour	+	hours	x	\$ 82.07 /hour	=	\$ - Shop Labor, Load, C 13-15
Field	hours	x	\$ 54.71 /hour	+	hours	x	\$ 82.07 /hour	=	\$ - Curtain Wall, Ladder 1-50
Field	hours	x		+	hours	x	\$ -	=	\$ - Shop Labor, Curtain 13-10
Field	hours	x		+	hours	x	\$ -	=	\$ - #N/A
Field	hours	x		+	hours	x	\$ -	=	\$ - #N/A
Field Foreman	hours	x	\$ 71.58 /hour	+	hours	x	\$ 107.37 /hour	=	\$ - Field, Superintendent 1-100
Field Superinter	hours	x	\$ 86.93 /hour	+	hours	x	\$ 130.40 /hour	=	\$ - Field, General Super 1-90
Project Mgr	2	hours	x	\$ 135.00 /hour				=	\$ 270.00 Project Management 15
Engineering	hours	x	\$ 125.00 /hour					=	\$ - Drafting and Engine 13
Drafting	hours	x	\$ 85.00 /hour					=	\$ - Drafting and Engine 13

Labor Summary (including Fringe and Burden)

B. Equipment Rental

C. Owned Equipment

D. Trucking (\$3.25 / mile for Flatbed Truck, to Site and back to Shop)

Miles One Way =

E. Other (type Description of item)

F. Travel and Per Diem

Blackout film

Material Subtotal 1	\$ 353.55
Material Subtotal 2	\$ -
Material Subtotal 3	\$ -
Material Subtotal 4	\$ -
Material Subtotal 5	\$ -
Material Subtotal 6	\$ -
Material Subtotal 7	\$ -
Material Subtotal 8	\$ -
Material Subtotal 9	\$ -
Material Subtotal 10	\$ -
Material Subtotal 11	\$ -
Material Subtotal 12	\$ 50.31

Miscellaneous Material

G. Material (Tax is included if a non-exempt job)

H. General Conditions

I. Worker's Comp, General Liability Insurance

x 1.53% (0% if enrolled in CCIP)

J. Koch Overhead

x 10.0%

K. Koch Profit

x 5.0%

L.

M.

N.

x

O.

P. Bond

x 2.24%

Q.

Material Total (G)	\$ 403.86
Total (H)	
Total (I)	\$ 10.31
Total (J)	\$ 68.42
Total (K)	\$ 37.63
Total (L)	\$ 790.21

Total (M)

Total (N)

Sub Total (A - N)

Total (P)

GRAND TOTAL (Sub Total + P)

Print Name: PM - Larry Vihlidal

Prepared By Signature:

Print Name: Operations Manager - Mike Hall

Reviewed By Signature:

Print Name: President - Benjamin Feinn

Approved By Signature:

R - 1852

PM Form-011-032017 Change Order Request Form - CASE#2019CP1001108

Palmetto Tint Shop
2116 Hayne St
North Charleston, SC 29406

Estimate

Date	Estimate #
12/14/2017	100

Name / Address
Koch Corporation

			Project
Description	Qty	Cost	Total
Blackout vinyl (2) windows	34.3	9.50	325.85
34.3ft2			
Sales Tax		8.50%	28.00
2759 Marion Square		Total	353.85

Customer Signature _____



R - 1854

Tab No. 223

Balfour Beatty Construction

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 223
RFI 1093 - Guestroom 603 TV Wall Conflict

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 223 in the amount of Three thousand three hundred four (\$3,304.78) to provide additional work in accordance with the following qualifications:

Per RFI 1093, the wall surrounding the door along the east wall of guestroom 603 needs to be demolished to allow for the door frame to relocate. The entire cased opening needs to be furred out as well in order to fit the electrical devices located behind a fan coil unit.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,

Alec Dooley
Assistant Project Manager

cc:

RCO # 223 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 223– RFI 1093 - Guestroom 603 TV Wall Conflict

The additional work for the **RFI 1093 - Guestroom 603 TV Wall Conflict** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50925200.40	RFI 1093 - Guestroom 603 TV Wall Conflict	\$3,152.00

Total Items \$3,152.00

Total Markups \$152.78

RCO Total \$3,304.78

The total Cost to perform the work as described above is an ADD of Three thousand three hundred four (\$3,304.78).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 223

Tab No. 227

Balfour Beatty Construction

February 6, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 221
Additional Tinting on Hope's Windows

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 221 in the amount of Eight hundred forty-six (\$846.12) to provide additional work in accordance with the following qualifications:

Tint (2) Type G windows at Men's Locker Room and Stair 6 on North Elevation per SI 65.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,

Nick Starcevic
Project Manager

cc:
Jennifer Faulkinberry
Marty Wall
Jim Clements
Woody Faust
David Simonton
David Stanton
Tim Spano
Alec Dooley

RCO # 221 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 221– Additional Tinting on Hope's Windows

The additional work for the **Additional Tinting on Hope's Windows** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50840000.40	Additional Tinting on Hope's Windows	\$807.00

Total Items \$807.00

Total Markups \$39.12

RCO Total \$846.12

The total Cost to perform the work as described above is an ADD of Eight hundred forty-six (\$846.12).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 221

Balfour Beatty Construction

April 9, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 227
Warehousing and Handling - Mirrors

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 227 in the amount of Nine thousand one hundred sixty-nine (\$9,169.01) to provide additional work in accordance with the following qualifications:

Storage for mirrors delivered to contractor's warehouse on 5/22/17 and stored through 4/27/18 (49 weeks). This change order only covers the costs to store the mirrors through 4/27/18. One time unloading and loading costs are included. These mirrors are not being used on the project so any costs associated for them are not included in the GMP (storage, handling, repairs, etc).

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Nick Starcevic
Project Manager

cc:
Jennifer Faulkinberry
Jim Clements
Marty Wall
David Simonton
Tim Spano
Alec Dooley

RCO # 227 - File

Starcevic, Nicholas

From: Tim Mahoney <tim.mahoney@mainocean.com>
Sent: Wednesday, March 28, 2018 8:59 AM
To: Starcevic, Nicholas
Cc: Marc Loa
Subject: Re: Pricing - Mirrors

I show two containers and we billed storage on them from May 22nd thru Aug 5th (11 weeks total) to you guys.

Billing rate was 75.00 per week per container

OOLU735381-4 - 11 weeks @ 75.00 = 825.00
OOLU731604-5 - 11 Weeks @ 75.00 = 825.00

Total Storage - 1650.00

R - 1862
Handling was 650.00 per container to unload/loadout

OOLU735381-4 @ 650.00
OOLU731604-5 @ 650.00

Total Handling - 1300.00

Thanks

Tim Mahoney
MainOcean Carolinas | Director of Operations
O 843-971-1167 | charleston@mainocean.com

+38 weeks for August 5th - April 28.

Tab No. 246

Balfour Beatty Construction

September 4, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 246R1
SI 67 Elevator Cab Finishes

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 246R1 in the amount of Thirty-one thousand one hundred fifty-seven (\$31,157.12) to provide additional work in accordance with the following qualifications:

Balfour Beatty to provide elevator cab finishes as shown on sheet ID-903.2 issued in Supplemental Instructions 067.

- SI 67 – Millwork Revisions - **\$1,558.00**
 - Add ¾"x4" crown backer board (D/903.2)
 - Add ¾"x2-7/8" ceiling casing (9/993.1)
 - All trim to be prefinished pecky cypress.
- SI 67 – Electrical Revisions - **\$27,331.00**
 - Furnish and install 32 D1 Luna 1 down lights (8 at each elevator cab) per Supplemental Instruction 067.
 - Furnish and install tape lighting above prefinished crown at each elevator cab per Supplemental Instruction 067
- SI 67 – Revised Handrail Finish - **\$1,995.00**
 - Credit Gold/Bronze Satin handrail. *(\$6,510.00)*
 - Add Oxidized Bronze handrail to match Gunderlin sample. *\$8,505.00*
- MOD 1 – Elevator Cab Millwork Reduction – **(\$1,491.00)**
 - Reduced and revised panel layout.
 - Delete wood chair rail.

Qualifications: This cost keeps the elevator cab tile to be in a grid pattern and *not* diagonally cut as shown on SI 67. This change order does not address special finishes in the elevator cab. This cost assumes that voltage coordination for the additional lighting fixtures has been performed by the Engineer of record.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Balfour Beatty Construction

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Alec Dooley
Assistant Project Manager

cc:

Melissa Pense
Marty Wall
Jennifer Faulkinberry
Jim Clements
Woody Faust
David Simonton
Nick Starcevic

RCO # 246R1 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 246R1– SI 67 Elevator Cab Finishes

The additional work for the **SI 67 Elevator Cab Finishes** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50640000.40	SI 67 Added Elevator Trim	\$1,558.00
2	400.51600000.40	SI 67 - Electrical Revisions	\$27,331.51
3	400.51420000.40	SI 67 Elevator Handrail Revision	\$1,995.00
4	400.50640000.40	LCCM MOD 1 Elevator Cab Finishes	(\$1,491.00)

Total Items \$29,393.51

Total Markups \$1,763.61

RCO Total \$31,157.12

The total Cost to perform the work as described above is an ADD of Thirty-one thousand one hundred fifty-seven (\$31,157.12).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 246R1



LOW COUNTRY CASE & MILLWORK
 3270 Benchmark Drive
 Ladson, SC 29456
 (843) 797-0881



Page No. 1 of 2

CHANGE ORDER

PROPOSAL SUBMITTED TO Balfour Beatty		TODAY'S DATE 9/4/2018	DATE OF PLANS/PAGE #'S MOD # 1-8
PHONE NUMBER	FAX NUMBER	SPECIFICATIONS AND ADDENDUMS (Include dates) None Provided - See Note 1	
JOB NAME Hotel at Marion Square CO - Elevator Mod Millwork		JOB LOCATION Charleston, SC	

We propose to furnish material, labor, tools, and equipment to complete the following work in accordance with the plans and specifications:

NOTES

1. If project specifications are not provided, LCCM reserves the right to alter the amount of this proposal.
2. LCCM standard work hours are 8:00 a.m. - 5:00 p.m., Monday - Thursday. Up-charges will apply to any work that is required for any reason to be performed before or after the hours listed.
3. **LCCM standard lead time is 4-6 weeks from receipt of approved submittals and field verified site conditions (field verified site conditions include metal stud walls/soffits framed, plumbing and electrical rough-ins complete). An up-charge of 10% will be added to any jobs that require a lead time of 4 weeks or less.**
4. All millwork is priced per AWI specifications for custom grade.

EXCLUSIONS

- Anything not listed on this proposal
- In Wall Blocking
- SF-01 Finish
- Mirrors
- Metal frame
- Upholstery

CHANGE ORDER

Elevator Cabs (x4) - Mod 1

- Removed chair rail
 - Reconfigured paneling (A/903)
- (\$1,448)

SUBTOTAL = (\$1,448.00)

AWI FEE (0.5%) = (\$7.00)

BONDING (2.5%) = (\$36.00)

TOTAL ADDITIONAL COST = (\$1,491.00)

We propose hereby to furnish material and labor - complete in accordance with above specifications for the sum of:
 MINUS ONE THOUSAND FOUR HUNDRED NINETY ONE***** dollars (\$ -1,491.00)
 Payment as follows: Progress payments for stored materials to be billed monthly.
 Balance due upon completion of LCCM's scope.

All material is guaranteed to be as specified. All work to be completed in a substantial workmanlike manner according to specifications submitted, per standard practices. Any alteration or deviation from above specifications involving extra costs will be executed only upon written orders, and will become an extra charge over and above the estimate. All agreements contingent upon strikes, accidents or delays beyond our control. Owner to carry fire, tornado and other necessary insurance. Our workers are fully covered by Workmen's Compensation Insurance. If either party commences legal action to enforce its rights pursuant to this agreement, the prevailing party in said legal action shall be entitled to recover its reasonable attorney's fees and costs of litigation relating to said legal action, as determined by a court of competent jurisdiction.

Authorized
Signature

Christian Datz

Note: this proposal may be withdrawn by us
if not accepted within 30 days.

ACCEPTANCE OF PROPOSAL The above prices, specifications and conditions are satisfactory and are hereby accepted. You are authorized to do the work as specified. Payment will be made as outlined above.

Signature _____

Signature _____

Date of Acceptance _____



LOW COUNTRY CASE & MILLWORK
 4144 Carolina Commerce Parkway
 Ladson, SC 29456
 (843) 797-0881



Page No. 1 of 2

CHANGE ORDER

PROPOSAL SUBMITTED TO Balfour Beatty		TODAY'S DATE 6/27/2018	DATE OF PLANS/PAGE #'S SI #67 6/12/2018
PHONE NUMBER	FAX NUMBER	SPECIFICATIONS AND ADDENDUMS (Include dates) None Provided - See Note 1	
JOB NAME HMS Common CO - SI #67 Elevator Cab		JOB LOCATION Charleston, SC	

We propose to furnish material, labor, tools, and equipment to complete the following work in accordance with the plans and specifications:

NOTES

1. If project specifications are not provided, LCCM reserves the right to alter the amount of this proposal.
2. LCCM standard work hours are 8:00 a.m. - 5:00 p.m., Monday - Thursday. Up-charges will apply to any work that is required for any reason to be performed before or after the hours listed.
3. **LCCM standard lead time is 4-6 weeks from receipt of approved submittals and field verified site conditions (field verified site conditions include metal stud walls/soffits framed, plumbing and electrical rough-ins complete). An up-charge of 10% will be added to any jobs that require a lead time of 4 weeks or less.**
4. All millwork is priced per AWI specifications for custom grade.

EXCLUSIONS

- Anything not listed on this proposal
- Blocking

ELEVATOR CABS

A total of (4) elevators to receive the following added trim:

- Crown Backer (3/4"x4") D/903.2
- Casing (3/4"x2-7/8") 9/993.1
- Trim to be prefinished pecky cypress

RAW MATERIAL & MANUFACTURING = \$640.00

INSTALL LABOR = \$675.00

15% MARK-UP = \$197.00

SUBTOTAL = \$1,512.00

AWI FEE (0.5%) = \$8.00

BONDING (2.5%) = \$38.00

TOTAL ADDITIONAL COST = \$1,558.00

We propose hereby to furnish material and labor – complete in accordance with above specifications for the sum of:

ONE THOUSAND FIVE HUNDRED FIFTY EIGHT AND NO/100***** dollars (\$1,558.00)

Payment as follows: Progress payments for stored materials to be billed monthly.
Balance due upon completion of LCCM's scope.

All material is guaranteed to be as specified. All work to be completed in a substantial workmanlike manner according to specifications submitted, per standard practices. Any alteration or deviation from above specifications involving extra costs will be executed only upon written orders, and will become an extra charge over and above the estimate. All agreements contingent upon strikes, accidents or delays beyond our control. Owner to carry fire, tornado and other necessary insurance. Our workers are fully covered by Workmen's Compensation Insurance. If either party commences legal action to enforce its rights pursuant to this agreement, the prevailing party in said legal action shall be entitled to recover its reasonable attorney's fees and costs of litigation relating to said legal action, as determined by a court of competent jurisdiction.

Authorized
Signature Christian Datz

Note: this proposal may be withdrawn by us
if not accepted within 30 days.

ACCEPTANCE OF PROPOSAL The above prices, specifications and conditions are satisfactory and are hereby accepted. You are authorized to do the work as specified. Payment will be made as outlined above.

Signature _____

Signature _____

Date of Acceptance _____

PROPOSED CHANGE ORDER

Watson Electrical

3215 Fortune Drive, Suite 109
North Charleston, South Carolina 29418

CCN # 182
Date: 7/6/2018
Project Name: Marion Square Hotel
Project Number: 21046
Page Number: 1

Client Address:

Balfour Beatty Construction

306 Meeting Street
Charleston, South Carolina

Work Description

We reserve the right to correct this quote for errors and omissions.

Furnish and Install (32) downlights per Supplemental Instruction 67.

Cutting in of 32 downlights by others. Opening dimensions to be coordinated with Watson.

Patching if necessary by others.

Coordination with elevator contractor by other.

Pricing assumes that circuit loading calculations were established by architect/engineer.

Pricing includes safety factor for working in elevator / elevator shafts.

The proposal is per Supplemental Instruction #67 as received and only includes elevators 1-4 as indicated. Manufacturer's terms and conditions apply.

NO MATERIALS OR LABOR WILL BE PROCURED OR EXPENDED WITHOUT FULLY EXECUTED CHANGE ORDER.

Lead times:

Tape Lighting 4-6 weeks ESD plus 1 week estimated transit time.

Downlights No lead time available at the time of quote. Will forward once received from manufacturer.

This quote covers direct costs only and we reserve the right to claim for impact and consequential costs.

This price is good for acceptance within 10 days from the date of receipt.

We request a time extension of 11 days.

We will supply and install all materials, labor, and equipment as per your instructions on <Supplemental Instruction #67>.

Itemized Breakdown

System	Material(\$)	Labor Hrs
III ELEVATOR LIGHTING	273.17	175.88
Total	273.17	175.88

ELEVATOR LIGHTING

Description	Qty	Net Price	U	Total Mat.	Labor	U	Total Hrs.
#12/2C CABLE MC - STL ARMOR	240	417.74	M	100.26	45.00	M	12.96
#12/2C CABLE MC - ALUM ARMOR	244	439.73	M	107.29	45.00	M	13.18
3/8" CONN SADDLEGRIP DC FOR FLEX / AC-90 / MC	66	76.44	C	50.45	9.00	C	7.13
WIRE CONN RED	64	10.41	C	6.66	9.00	C	6.91
4x 2 1/8" SQ BOX COMB KO	8	69.32	C	5.55	40.00	C	3.84
4" SQ BLANK COVER	8	16.67	C	1.33	10.00	C	0.96
#8 TO #10x 7/8 PLAS ANCHOR (3/16)	16	1.28	C	0.20	22.50	C	4.32
#10x 1 P/H SELF-TAP SCREW	16	8.93	C	1.43	8.25	C	1.58

ORIGINAL

R - 1871

PROPOSED CHANGE ORDER

Client Address:

Watson Electrical3215 Fortune Drive, Suite 109
North Charleston, South Carolina 29418**Balfour Beatty Construction**306 Meeting Street
Charleston, South Carolina

CCN #

182

Date:

7/6/2018

Project Name:

Marion Square Hotel

Project Number:

21046

Page Number:

2

Description	Qty	Net Price	U	Total Mat.	Labor	U	Total Hrs.
DOWNLIGHT HOUSING AND TRIM	32	0.00	E	0.00	1.95	E	62.40
LED COVE LIGHT (per ft)	244	0.00	E	0.00	0.25	E	61.00
LAMP	32	0.00	E	0.00	0.05	E	1.60
Totals	970			273.18			175.88

Summary

General Materials		273.18
LIGHTING FIXTURES DOWNLIGHTS		5,185.00
LIGHTING FIXTURES TAPE		5,795.00
Material Tax (@ 9.000 %)		1,012.79
Material Total		12,265.97
JOURNEYMAN (175.88 Hrs @ \$52.00)		9,145.76
FOREMAN @ 15% (26.38 Hrs @ \$55.00)		1,450.90
SAFETY @ 3.5% (6.16 Hrs @ \$52.00)		320.32
MILEAGE (208.42 @ 0.00 @ \$2.50 + 0.000 % + 0.000 % + 0.000 %)		521.05
CONSUMABLES (208.42 @ 0.00 @ \$0.30 + 0.000 % + 0.000 % + 0.000 %)		62.53
Subtotal		23,766.53
(@ 15.000 %)		3,564.98
Subtotal		27,331.51
Final Amount		\$27,331.51

CONTRACTOR CERTIFICATION

Name: _____

Date: _____

Signature: _____

I hereby certify that this quotation is complete and accurate based on the information provided.

CLIENT ACCEPTANCE

CCN #: 182

Final Amount: \$27,331.51

Name: _____

Date: _____

Signature: _____

Change Order #: _____

I hereby accept this quotation and authorize the contractor to complete the above described work.

ORIGINAL

R - 1872

**BORDER STATES**

Supply Chain Solutions™

Border States Electric Supply
 Shealy Electrical Wholesalers | Kriz-Davis
 K-D Chapman Metering

Shealy Electrical Whsirs - CHS
 Division of Border States
 1553 King St Ext. Ste B
 Charleston SC 29405-9386
 Phone: 843-853-7044

Watson Elec-21046 Hotel At Marion
 Job-21046 Hotel At Marion Square
 PO Box 40697
 North Charleston SC 29423-0697

Quote

Page: 1 of 1

BSE Quote: 24819670
 Sold-To Acct #: 187297
 Valid From: 07/06/2018 To: 07/13/2018
 PO No: ELEVATOR LIGHTS

Created By: Wylie Doyle
 Tel No: 843-879-0232
 Fax No:

Inco Terms:
 FOB ORIGIN

Payment Terms:
 2.0 % 10th prox net 25th (25)

Cust Item	BSE Item	Material MFG - Description	Quantity	Price	Per	UoM	Value
	000010	- 32 DWNLGTS D1LUNA10327A3SBKNOD NO HOUSING-DRIVER NON DIM	1 EA	5,185.00	/ 1	EA	5,185.00
	000020	- TAPE LIGHT, DBL SIDED TAPE, & DRIVERS PRICE PER FT / 61FT TOTAL	61 EA	95.00	/ 1	EA	5,795.00

Total \$				10,980.00
State Tax \$	6.000 %	658.80		
County Tax \$	1.000 %	109.80		
Local Tax \$	0.000 %	0.00		
Other Tax1 \$	2.000 %	219.60		
Other Tax2 \$	0.000 %	0.00		
Other Tax3 \$	0.000 %	0.00		
Tax Subtotal \$	9.000 %			988.20

Net Amount \$ 11,968.20

To access BSE's Terms and Conditions of Sale, please go to
<https://www.borderstateselectric.com>

The quoted sales tax is an estimate only based upon the information provided in this quote and will be finalized at the time of Invoice based upon the material purchased, quantity purchased, and delivery location.

Shipping and handling fees in this quote are an estimate only and will be finalized at the time of Invoice.

This quote has not been reviewed for compliance with the Buy American Act or the American Recovery and Reinvestment Act requirements. BSE reserves the right to amend both our bill of material and our proposal accordingly if BAA/ARRA compliance is required.

R - 1873

ELECTRONICALLY FILED - 2023 May 12 2:07 PM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

WINFORD LINDSAY ARCHITECT

344 West Pike Street
Lawrenceville, GA 30046
Tel. 770-963-8989
FAX 770-822-9492

Supplemental
Instructions No. 67

Date: 6/12/18
Project: The Marion Square Hotel

Project No.: 209007

Copies To:

- ☒ Owner
- ☒ Contractor
- ☐ Contractor Field
- ☒ Architect File
- ☒ Engineer
- ☐ Other

The work shall be carried out in accordance with the following supplemental instructions issued in accordance with the contract documents without change in contract sum or contract time. Proceed in accordance with these instructions.

Detail References

ID-903.2

Problem Description

A "redesign" was necessary to coordinate the elevators interior millwork.

Solution

Please see attached sheet & lighting specifications including the "redesign" of the elevator cabs millwork as discussed on site and via phone with BBC. Please proceed immediately.

By Jennifer Faulkinberry

Elevator Downlight: D1-LUNA1-3.5-27-A-3-S-PER ID-N-0-D. Finish as selected by Interior Designer. Voltage to be verified by Electrical Engineer.

ZANIBONI®
LIGHTING

Project

Type

Contact

N/A

LVD Comments
2018-05-22



DCI COMMENTS
2018-05-23




LUNA 1 1 Light Sources

1 in. | 494 lm / per light source
Round | Fixed | No | Downlight


Performace Options	3W	7W
Source Lumens	404 lm	685 lm
Delivered Lumens	291 lm	494 lm
Lumens / Watt	97 lm	71 lm
Current	350 mA	700 mA

CRI/CCT Multiplier	2700°K	3000°K	3500°K	4000°K
80 CRI	0.93	1.00	1.00	1.07
95 CRI	0.69	0.75	0.81	0.87

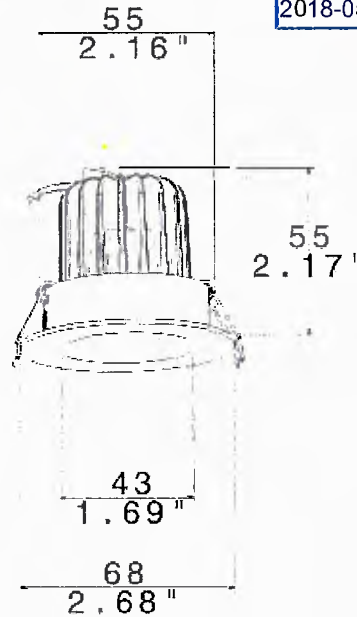

706 Lux @ 1 m

Lumen 494



D1 LUNA1

OPTICS	MODEL	WATTAGE	KELVIN	CRI	BEAM	LENS	COLOR	DRIVER	HOUSING	I.P. RATING
D1	LUNA1:Luna 1	O3:03W 07:07W	27:2700° 30:3000° 35:3500° 40:4000° AM:Amber° WD:Warm Dim°	A 80 B:95	3:36°	C:Clear F:Frosted P:Prismatic S Solite	WS:Matte White BK:Matte Black WK:White / Black Inter Splay CC:Custom (Min Qty: 20pc) PER ID	Z:0-10V Dimmable to 1% O:No Driver E:ELV Dimmable T:Lutron™ (2-wire) L:Lutron™ (3-wire) N:Non-Dimmable F:ELV Dimmable +EM Backup M:Lutron™ (3-wire) +EM Backup U:Lutron™ (2-wire) +EM Backup Q:Non-Dimmable +EM Backup D:DALI A:0-10V Dimmable to 1% +EM Backup	O:No Housing / Enclosure R:Retro-Fit Enclosure RL:Retro-Fit for Lutron™	D:Dry IP 20 W:Wet IP 65

Generated on 05-22-2018

1

Zaniboni Lighting · Ph +17274622526 · Fx +17276839720 · www.zanibonilighting.com · 101 N Garden Ave Suite 230 Clearwater, FL 33755
The manufacturer reserves the right to change or modify the design, dimensions, and photometric information at any time without notice.
The Manufacturer accepts no liability for consequential damage which is occasioned to the user based on the data provided.

Specifications

This Specification Grade LED downlight offers a wide selection of LED module options to address design requirements in the spaces it illuminates. Many additional custom options are available; please contact manufacturer for details.

LED source

Tool-free field-replaceable LED module.
Proprietary high performance aluminum die cast heatsink for maximum LED life.

Optics

Computer-optimized reflector design. High reflectance finished aluminum. Tool-free field-interchangeable reflectors and lens.

Body

Die-cast aluminum frame and body

Trim

Die-cast aluminum CNC machine finished.
Minimal thickness. White can be field painted to match adjacent finishes

Fixture retention

Two torsion springs hold the fixture tight to the ceiling accommodating ceiling thickness from 1/16" to 1". Special springs for thicker ceiling available on request.

Life

Rated for 50,000 hours at 70% lumen maintenance.

Labels

ETL listed for US and Canada. CE labeled. CCC label available on request.

Warranty 5 years limited warranty.

Wet location

(If option is available and selected on page 1)


Sealed lens and integral silicon gasket behind the trim.

Emergency Battery Backup

Required remote installation.


Dimming Compatibility

ZANIBONI fixtures are compatible with all major dimming protocols in the Industry. Please refer to www.zanibonilighting.com for general compatibility and wiring diagrams. ZANIBONI recommends testing your unique dimming configuration as the the exact full configuration (Dimmer, drivers, fixture quantities, voltage) may affect dimming performance.




N: Non-Dimmable

- 110-277 V, 50/60Hz.
- Economic solution for ON-OFF applications not requiring dimming.




E: ELV Dimmable

- 110-277 V, 50/60Hz.
- For ELV (Electronic Low Voltage) dimmers. Best for new construction applications. Dims down to less than 10% light output (most cases). Consult dimming manufacturer for installation instructions. Must meet dimmer Minimum Load Requirements.




Z: 0-10V Dimmable

- 110-277 V, 50/60Hz.
- Prevalent solution on commercial projects. Integrates into a variety of building management and daylighting controls. Dims down to less than 10% light output (most cases). Must meet dimmer Minimum Load Requirements. Consult dimming manufacturer for installation instructions.



L: Lutron Hi-Lume A L3D

- 120-277 V, 50/60Hz.
- For 3-wire LUTRON dimming systems. Continuous dimming to 1%.
- Consult dimming manufacturer for installation instructions.



T: Lutron Hi-Lume A LTE

- 120 V, 50/60Hz.
- For 2-wire Forward Phase Controls. Continuous dimming to 1%.
- Consult dimming manufacturer for installation instructions.


N & E: Non-Dimmable & ELV Drivers

MEASUREMENTS	LWH IN MM	LWH IN INCHES
7W, 9W, 13W	85.5*38*27.7	3.36"*1.49"*1.09"
18W, 26W	89*41*31.5	3.5"*1.62"*1.24"
36W, 50W	89*41*31.5	3.5"*1.62"*1.24"

Z: 0-10V Dimmable


MEASUREMENTS	LWH IN MM	LWH IN INCHES
7W, 9W	85.3*38*27.7	3.36"*1.49"*1.09"
13W, 18W	89*41*31.5	3.5"*1.62"*1.24"
26W, 36W, 50W	138*47*32	5.43"*1.85"*1.25"

Enclosures




A: Class 1, IC

- For installation in ceilings with insulation. Driver "on board".




B: Class 1, Non-IC

- For installation on ceiling without insulation. Driver "on board".
- National or municipal codes must be followed regarding set back of thermal insulating material from fixture. Fixtures are not designed for direct contact with thermal insulation.



D: Class 2, Non-IC

- For installation on ceilings without insulation. Driver is remote.
- National or municipal codes must be followed regarding set back of thermal insulating material from fixture. Fixtures are not designed for direct contact with thermal insulation.



E: Airtight Enclosure


- For installation where AT (Air-Tight) standards is required.

F: Chicago Plenum

- Enclosure complies with Chicago Plenum requirements.


G: Title 24 for Residential

- Enclosure complies with California Title 24 requirements for specific residential applications. Please consult with your local inspector.




R: Retro-Fit Enclosure

- Available in assorted cutout sizes for easy installation of light fixture. For installation in plaster or t-b ar ceilings.
- National or municipal codes must be followed regarding set back of thermal insulating material from fixture. Fixtures are not designed for direct contact with thermal insulation.



R: Retro-Fit Enclosure Coupled With Lutron Hi-Lume Driver

- When the Retro-Fit Enclosure is paired with any Lutron Driver, the Lutron Driver will be mounted atop the Retro-Fit enclosure with the line voltage connection inside the junction box.



R: Retro-Fit Mini

- Used with our 1" aperture Lunas & Albas.
- National or municipal codes must be followed regarding set back of thermal insulating material from fixture. Fixtures are not designed for direct contact with thermal insulation.

Elevator Tapelight: RBHI-65-24-2.2-27

Provide remote drivers in quantities as required. Provide lengths as shown in drawings. Voltage per Electrical Engineer.

2.2 STATIC WHITE RIBBONLYTE

LVD Comments
2018-05-22



DCI COMMENTS
2018-05-23

**2.2 STATIC WHITE RIBBONLYTE**

Whether you want to imitate the warm glow of candlelight, or provide a high visibility work environment similar to a bright afternoon, our Static White RibbonLyte can provide a solution to fill your needs.

With 50% more light output than RibbonLyte 1.5, and higher efficiency, our 2.2 W/ft RibbonLyte is another great low power choice. With an LED pitch of 1.3", if pixel density is a concern, 1.5 or 3.0 may be a better option.


- 2.2 W/ft (7.2 W/m)
- Create a custom fixture with our channels
- 6 color temperatures of white
- 90+ CRI
- 2-Step MacAdam's ellipse binning

APPLICATIONS:


- Commercial
- Entertainment
- Healthcare
- Hospitality
- Museums
- Public Spaces
- Residential
- Retail



COVES



TOE KICKS



UNDER CABINET



BACK LIGHTING



ACCENT LIGHTING

CERTIFICATIONS:

RoHS

**IP 20****IP 65****IP 68****AVAILABLE COLOR TEMPERATURES**

2400K
Candle White

2700K
Incandescent White

3000K
Warm White

3500K
Neutral White

4000K
Cool White


6000K
Bright White

2.2 STATIC WHITE RIBBONLYTE SPECIFICATIONS / DIAGRAM

SPECIFICATIONS

2.2 STATIC WHITE RIBBONLYTE

Operating Voltage	24 V					
Power Consumption	2.2 W/ft (7.2 W/m)					
Current (mA) - 24V	92 mA/ft (302 mA/m)					
LED Pitch	9 LEDs/ft (30 LEDs/m)					
Protection Rating IP20	✓					
Protection Rating IP65	✓					
Protection Rating IP68	✓					
Dimming/Control	MLV / 0-10 Volt / DMX / Lutron A-Series 1% dimming LED drivers					
Operating Temperature	-40° F to 158° F (-40° C to 70° C)					
Colors Temperatures	2400K	2700K	3000K	3500K	4000K	6000K
MacAdam's Ellipses (SDCM)	2-Step Binning					
Lumens	145 lm/ft (476 lm/m)	146 lm/ft (479 lm/m)	171 lm/ft (561 lm/m)	173 lm/ft (568 lm/m)	164 lm/ft (538 lm/m)	163 lm/ft (535 lm/m)
Binning Tolerance	+/- 100K					
LED Beam Angle	160°					
Lamp Life	43,000 hrs L70 @ 131° F (55° C)					
Cuttable Length - 24V	6.55 in (166.4 mm)					
CRI - All Color Temp.	90+ CRI					
Lumens/Watt	65.9 lm/W	66.4 lm/W	77.7 lm/W	78.6 lm/W	74.5 lm/W	74.1 lm/W
Constant Voltage	✓					
Cable Length	12 in (30.5 cm)					
Certifications	ETL Listed: UL 2108 Issued: 2004/02/27 Ed: 1 Rev: 2014/02/24 Low Voltage Lighting Systems CSA C22.2#9.0 Issued: 1996/06/01 Ed: 1 (R2011) General Requirements for Luminaires; with Gen. Inst. 1: 1997, Gen Inst. 2: 1998. ROHS compliant. UL 2108 - Low Voltage Lighting Systems UL 8750 - Light Emitting Diode (LED) Equipment for Use in Lighting Products UL 1598 / CSA 250.0-08 - Luminaires					



CUTTABLE EVERY: 6.55 in (166.4 mm) WIDTH IP20 + IP65: 0.39 in (10 mm) WIDTH IP68: 0.52 in (13.3 mm)

24 V DIMENSIONS

2.2 STATIC WHITE RIBBONLYTE

IP20	Width	0.39 in (10 mm)
	Max Length*	45 ft 11.2 in (14 m)
	Height	0.09 in (2.3 mm)
IP65	Width	0.39 in (10 mm)
	Max Length*	32 ft 9.7 in (9 m)
	Height	0.172 in (4.4 mm)
IP68	Width	0.52 in (13.3 mm)
	Max Length*	32 ft 9.7 in (10 m)
	Height	0.19 in (4.8 mm)

*Max length before additional power is introduced

STATIC WHITE RIBBONLYTE PART NUMBER BUILDER

RBHI + _____ + 24 + 2.2 + _____ = _____
 Category Waterproof Voltage Wattage Color temp

1 - Category

RBHI - RibbonLyte

2 - Waterproof

Blank - None (IP20)

65 - IP65

68 - IP68

3 - Voltage

24 - 24 V

4 - Wattage

2 2 - 2.2 W/ft (7.2 W/m)

5 - Color temp

24 - 2400K

27 - 2700K

30 - 3000K

35 - 3500K

40 - 4000K

60 - 6000K

CONNECTION OPTIONS


1.



Default Option

Please specify if using a different connector type.


2.



3.



4.



1 - End Feed for Hard Wired Connection

2 - Back Feed Through Back of Channel


3 - Soldered Daisy-Chain

4 - Side Feed



5 - IP20 Connectors

6 - IP68 Connectors

5.



6.



2.2 STATIC WHITE RIBBONLYTE CHANNEL COMPATIBILITY / USAGE GUIDELINES

20 - IP20	65 - IP65	68 - IP68
CHANNELS	2.2 STATIC WHITE	
	20/65	68
AC1	✓	✓
AC2	✓	✓
AC3	✓	
AC4	✓	✓
AC5	✓	✓
AP1	✓	✓
AR1	✓	✓
AR2	✓	✓
AR3	✓	✓
AS1	✓	✓
AS2	✓	✓
AS3	✓	✓
AS6	✓	✓
AS20G	✓	
AT4	✓	✓
AT5	✓	✓
AT11	✓	✓
C22	✓	✓
GL1	✓	✓
GL2	✓	✓
ROUND	✓	✓
W31	✓	✓
WH35	✓	✓

USAGE GUIDELINES

- When installing this product take into account the surface temperature of the material this product is mounted to. Many building surfaces which are exposed to direct sunlight exceed the 70° C / 158° F maximum that our product is rated for. High risk locations like this should be avoided.
- Our IP65 can be used in wet, outdoor locations around swimming pools and spa tubs, but our products are not intended to be submerged in pools and fountains and do not carry UL676 certification to do so.
- Please refer to our What NOT to do with RibbonLyte Guide for more information. Available for download at www.acolyteled.com
- Compatible with a wide variety of control products including the entire line of Lutron dimming systems.
- For use with Acolyte drivers, 0-10V dimming modules and interface controllers (DMXINF models).
- Use with non-Acolyte supplied triac, MLV or ELV drivers is not supported or warranted.
- Due to the nature of the product, RibbonLyte cuttable lengths are generally longer or shorter than the customer requested length. Unless specified, RibbonLyte is factory cut at the shorter cuttable point.
- We reserve the right to make changes to product lineup, specifications, design and finishes at any time without notice.

STATIC WHITE RIBBONLYTE CHANNEL OPTIONS

LENS OPTIONS

C - CLEAR

F - FROSTED

M - MILKY

G - GRAZER

SURFACE MOUNT CHANNELS



AC1
C, F, M



AC2
C, F, M



AC3
C, F, M



AC4
C, F, M



AC5
C, F, M



AP1
C, F, M



AS1
C, F, M



AS2
C, F, M



AS3
C, F, M



AS6
M



AS20G
G



AT4
C, F, M



AT5
C, F, M



AT11
C, F, M



C22
C, F, M



GL1
C, F, M



GL2
C, F, M



ROUND
C, F, M



WH35
C, F, M

RECESSED CHANNELS



AR1
C, F, M



AR2
C, F, M



AR3
C, F, M



W31
C, F, M


REV.15MAY2018

DISCLAIMER

When installing this product take into account the surface temperature of the material this product is mounted to. Many building surfaces which are exposed to direct sunlight exceed the 70° C/158° F maximum that our product is rated for. High risk locations like this should be avoided.

Our IP 68 product is not intended to be submerged in pools and fountains and does not carry UL 676 certification to do so.

01/12/00 16:50
SBR3042.dwg

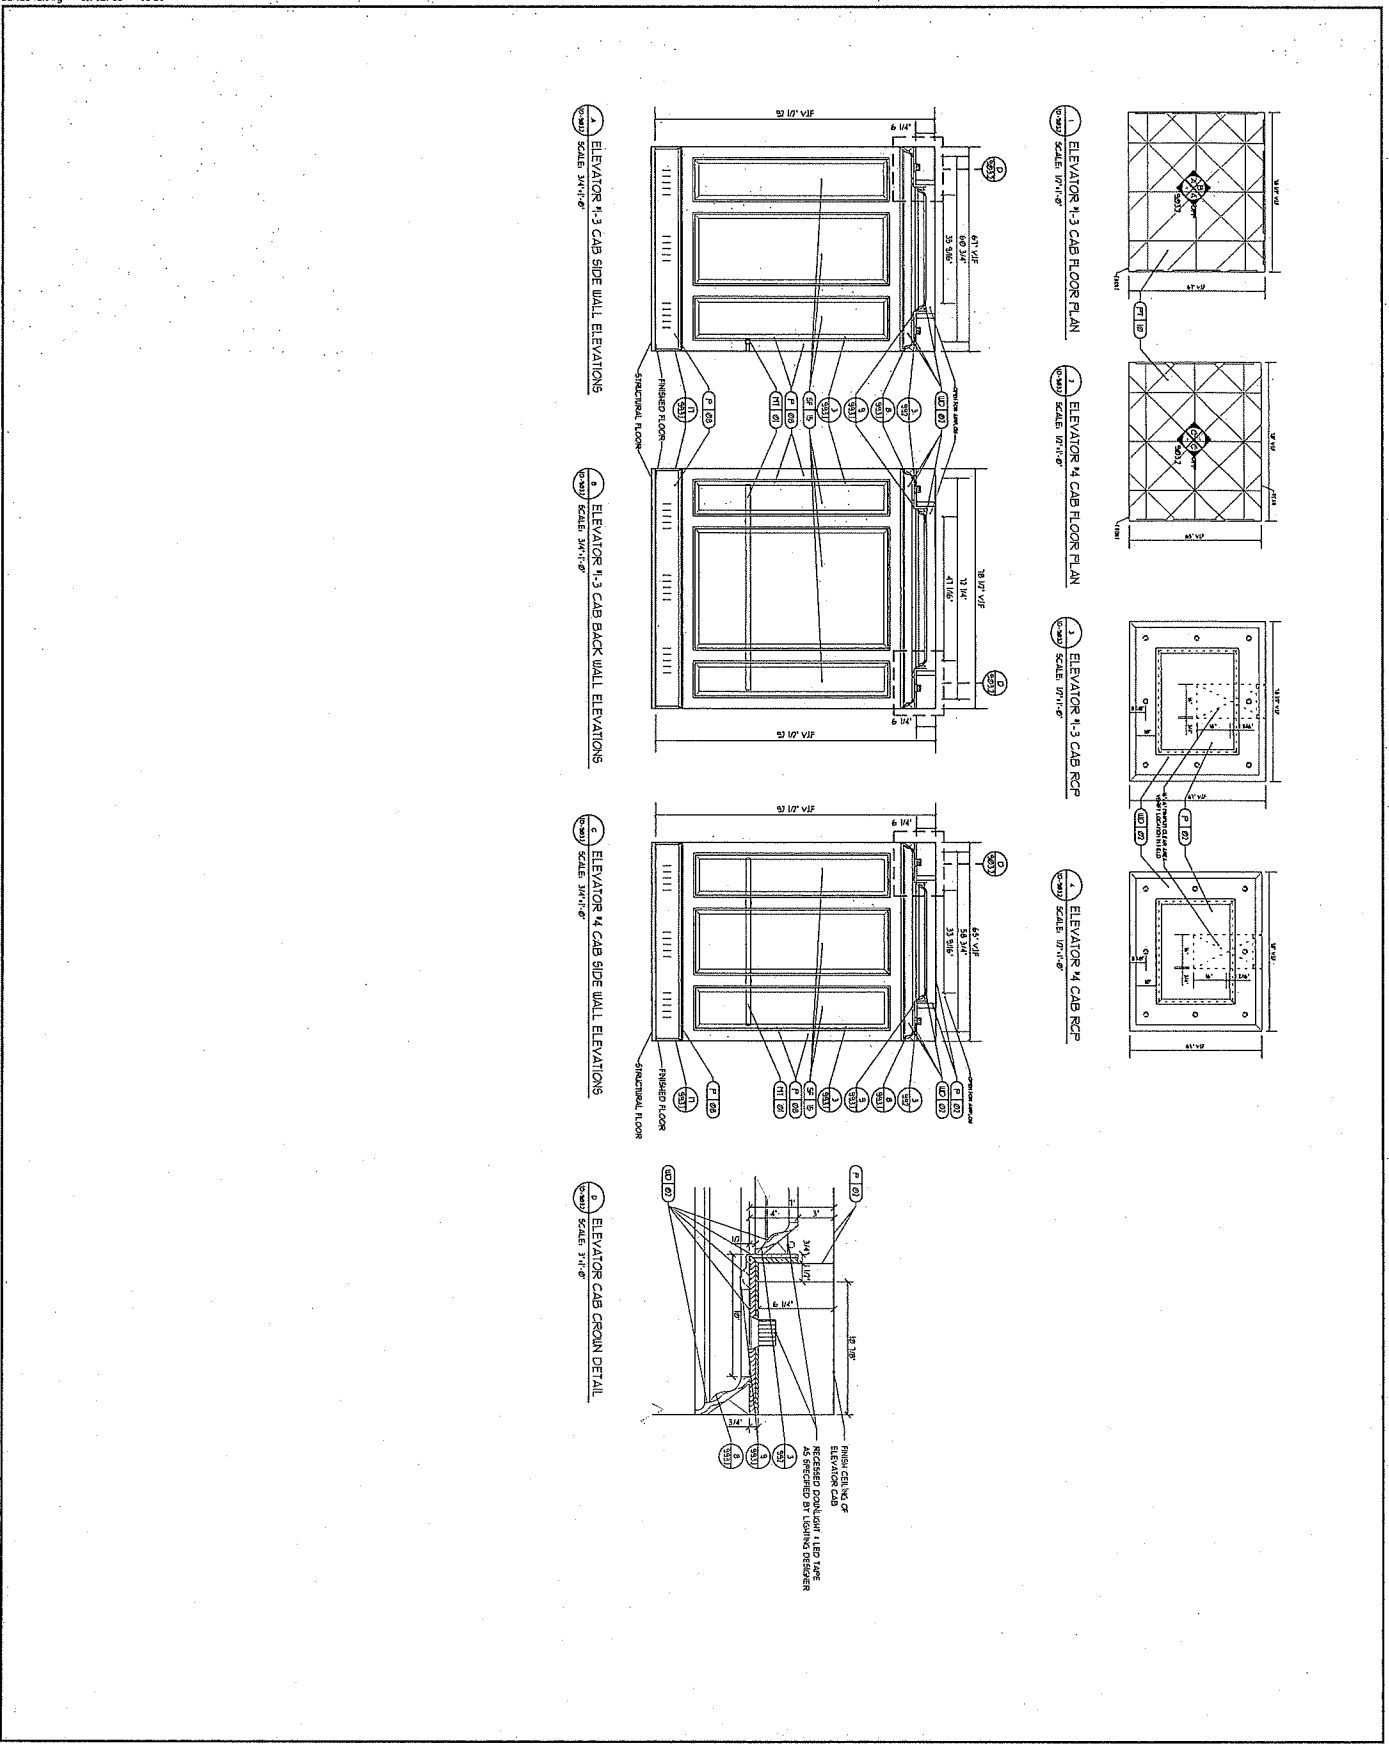

THE HOTEL AT MARION SQUARE

404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403

R - 1883

DESIGN CONTINUUM INCORPORATED

44 BROAD STREET, 10TH FLOOR, ATLANTA, GEORGIA 30303
TEL: 404-525-1000 FAX: 404-525-1001

NO.	DESCRIPTION	DATE	BY	CHKD.
1	ELEVATOR CAB DETAIL SHEET	01/12/00	...	...
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				
46				
47				
48				
49				
50				



GUNDERLIN LTD

ISO 9001:2008 CERTIFIED
800-327-8490 * FAX 305-696-6078
www.gunderlin.com

CUSTOMER: .OTIS ELEVATOR
OFFICE: .GREENVILLE, SC
ATTN: .CHASE HOSKINSON

QUOTE NO: CW-HOTEL

DATE: 7/18/2018 REV 7/20
INFO FROM: E-MAIL - SEE BELOW FOR DETAILS
QUOTE IS BASED ON OUR BEST INTERPRETATION OF THE INFO PROVIDED
JOB NAME: HOTEL MARION SQUARE
LOCATION: CHARLESTON, SC

QTY CARS: 3 CAR NO: 1,2 & 3

CAB AND/OR INTERIOR DESCRIPTION AND PRICING

PLATFORM: 3500# G2S

CAB HEIGHT: 93

DOORWAY: 42 X 84

DOOR TYPE: CENTER-PARTING; FRONT ONLY

SILL		CANOPY	
SHELL WALLS		VENTING	
		TRANSOM	
BASE		STRIKE POST	
WALL PANELS		RETURN PANEL(S)	
PADS & BUTTONS		COLUMN	
REVEALS		DOOR PANEL(S)	
FRIEZE		CUTOUTS	
		CERT FRAME	
HANDRAILS	1 1/2" DIA TUBE W/ WELDED END CAPS - REAR & SIDE SATIN BRONZE W/ STRAIGHT ENDS SINGLE ROW NO OXIDIZING INCLUDED	LACQUER	
		MISC	
		VERSION 127b	
CEILING		EST'D CAB WEIGHT (LBS.)	FOB DOCK, FREIGHT INCLUDED TO JOB-SITE. STD ENCLOSED TRAILER DELIVERY. FLATBED TRAILERS, LIFT GATE TRUCKS OR ANY OTHER SPECIAL SERVICES, NOT INCLUDED.
		DWG LEAD TIME	
		4-5 WEEKS	
LIGHTING		FABRICATION LEAD TIME	
		12-14 WEEKS	
		** SEE BELOW	

NET PER CAR:	\$1,755
QTY CARS:	3
NET TOTAL:	\$5,265

PRICE IS GOOD FOR SHIPMENT THRU: #VALUE!

UNLESS NOTED OTHERWISE, STEEL IS COLD ROLLED COMPLYING WITH ASTM A366; STN STN SHEET IS TYPE 302/304; BRONZE SHEET IS CDA ALLOY C28000 MUNTZ METAL, 60% COPPER & TRANSOMS, RETURNS, STRIKES, COLUMNS ARE 18 GA REINFORCED WITH 18 GA GALV STL; DOOR COVERS ARE 20 GA STN STL & BRONZE ARE GRAINED THE LONGEST DIMENSION.

THIS QUOTE IS VALID FOR A PERIOD OF (90) DAYS FROM THE DATE ISSUED FOR FABRICATION WITHIN THE TIME FRAME NOTED ABOVE. ALL QUOTES OVER (120) DAYS FROM THE ISSUE DATE SUBJECT TO ESCALATION. THIS QUOTE IS SUBJECT TO CORRECTION FOR ANY TYPOGRAPHICAL OR CLERICAL ERRORS. ALL QUOTATIONS AND AGREEMENTS ARE CONTINGENT UPON ACCIDENTS, FIRES, AVAILABILITY OF MATERIALS AND ALL OTHER CAUSES BEYOND OUR CONTROL. QUOTE COMPLIES W/ ASME A17.1/CSA B44-13 ONLY. DRAWING LEAD TIME BEGINS AFTER OF HATCH LAYOUTS; FABRICATION LEAD TIME BEGINS AFTER RECEIPT OF COMPLETE INFORMATION.

** ACTUAL MFG LEAD TIME WILL BE BASED ON FACTORY LOAD AT FINAL RELEASE

QUOTED BY: CHERYL

ELECTRONICALLY FILED - 2023 May 12 2:07 PM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

 GUNDERLIN LTD ISO 9001:2008 CERTIFIED 800-327-8490 * FAX 305-696-6078 www.gunderlin.com		QUOTE NO: CW-HOTEL DATE: 7/18/2018 REV 7/20 INFO FROM: E-MAIL - SEE BELOW FOR DETAILS QUOTE IS BASED ON OUR BEST INTERPRETATION OF THE INFO PROVIDED JOB NAME: HOTEL MARION SQUARE LOCATION: CHARLESTON, SC	
CUSTOMER: OTIS ELEVATOR OFFICE: GREENVILLE, SC ATTN: CHASE HOSKINSON		QTY CARS: 1 CAR NO 4	
CAB AND/OR INTERIOR DESCRIPTION AND PRICING			
PLATFORM: 3500# G2S CAB HEIGHT: 93 DOORWAY: 42 X 84		DOOR TYPE: CENTER-PARTING; FRONT & REAR	
SILL		CANOPY	
SHELL WALLS		VENTING	
		TRANSOM	
		STRIKE POST	
BASE		RETURN PANEL(S)	
WALL PANELS		COLUMN	
PADS & BUTTONS		DOOR PANEL(S)	
REVEALS		CUTOUTS	
FRIEZE		CERT FRAME	
HANDRAILS	1 1/2" DIA TUBE W/ WELDED END CAPS - SIDES SATIN BRONZE W/ STRAIGHT ENDS	LACQUER	
	SINGLE ROW NO OXIDIZING INCLUDED	MISC	
		VERSION 127b	
CEILING		EST'D CAB WEIGHT (LBS.) 82	FOB DOCK, FREIGHT INCLUDED TO JOB-SITE. STD ENCLOSED TRAILER DELIVERY. FLATBED TRAILERS, LIFT GATE TRUCKS OR ANY OTHER SPECIAL SERVICES, NOT INCLUDED.
		DWG LEAD TIME 4-5 WEEKS	
LIGHTING		FABRICATION LEAD TIME 12-14 WEEKS	NET PER CAR: \$1,245 QTY CARS: 1 NET TOTAL: \$1,245
		** SEE BELOW	PRICE IS GOOD FOR SHIPMENT THRU: #VALUE! UNLESS NOTED OTHERWISE: STEEL IS COLD ROLLED COMPLYING WITH ASTM A366; STN STN SHEET IS TYPE 302/304; BRONZE SHEET IS CDA ALLOY C28000 MUNTZ METAL, 60% COPPER & TRANSOMS, RETURNS, STRIKES, COLUMNS ARE 18 GA REINFORCED WITH 18 GA GALV STL; DOOR COVERS ARE 20 GA. STN STL & BRONZE ARE GRAINED THE LONGEST DIMENSION. THIS QUOTE IS VALID FOR A PERIOD OF (90) DAYS FROM THE DATE ISSUED FOR FABRICATION WITHIN THE TIME FRAME NOTED ABOVE. ALL QUOTES OVER (120) DAYS FROM THE ISSUE DATE SUBJECT TO ESCALATION. THIS QUOTE IS SUBJECT TO CORRECTION FOR ANY TYPOGRAPHICAL OR CLERICAL ERRORS. ALL QUOTATIONS AND AGREEMENTS ARE CONTINGENT UPON ACCIDENTS, FIRES, AVAILABILITY OF MATERIALS AND ALL OTHER CAUSES BEYOND OUR CONTROL. QUOTE COMPLIES W/ ASME A17.1/CSA B44-13 ONLY. DRAWING LEAD TIME BEGINS AFTER OF HATCH LAYOUTS; FABRICATION LEAD TIME BEGINS AFTER RECEIPT OF COMPLETE INFORMATION. ** ACTUAL MFG LEAD TIME WILL BE BASED ON FACTORY LOAD AT FINAL RELEASE
			QUOTED BY: CHERYL



GUNDERLIN LTD

ISO 9001:2008 CERTIFIED
800-327-8490 * FAX 305-696-6078
www.gunderlin.com

CUSTOMER: .OTIS ELEVATOR
OFFICE: .GREENVILLE, SC
ATTN: .CHASE HOSKINSON

QUOTE NO: **CW-HOTEL**

DATE: 7/18/2018
INFO FROM: E-MAIL - SEE BELOW FOR DETAILS
QUOTE IS BASED ON OUR BEST INTERPRETATION OF THE INFO PROVIDED
JOB NAME: HOTEL MARION SQUARE
LOCATION: CHARLESTON, SC

QTY CARS: 3 CAR NO: 1, 2 & 3

CAB AND/OR INTERIOR DESCRIPTION AND PRICING

PLATFORM: 3500# G2S

CAB HEIGHT: 93

DOORWAY: 42 X 84

DOOR TYPE: CENTER-PARTING; FRONT ONLY

SILL		CANOPY	
SHELL WALLS		VENTING	
BASE		TRANSOM	
WALL PANELS		STRIKE POST	
PADS & BUTTONS		RETURN PANEL(S)	
REVEALS		COLUMN	
FRIEZE		DOOR PANEL(S)	
		CUTOUTS	
		CERT FRAME	
HANDRAILS	1 1/2" DIA TUBE W/ WELDED END CAPS - REAR & SIDE SATIN BRONZE W/ STRAIGHT ENDS SINGLE ROW BRONZE TO BE OXIDIZED TO MATCH CONTROL SAMPLE FROM G/L #37256-57	LACQUER	
		MISC	
		VERSION 127b	
CEILING		EST'D CAB WEIGHT (LBS.)	FOB DOCK, FREIGHT INCLUDED TO JOB-SITE. STD ENCLOSED TRAILER DELIVERY. FLATBED TRAILERS, LIFT GATE TRUCKS OR ANY OTHER SPECIAL SERVICES, NOT INCLUDED.
		DWG LEAD TIME 4-5 WEEKS	
LIGHTING		FABRICATION LEAD TIME 12-14 WEEKS	
		** SEE BELOW	

NET PER CAR: **\$2,295**
QTY CARS: **3**
NET TOTAL: **\$6,885**

PRICE IS GOOD FOR SHIPMENT THRU: 7/18/2019

UNLESS NOTED OTHERWISE: STEEL IS COLD ROLLED COMPLYING WITH ASTM A366; STN STN SHEET IS TYPE 302/304; BRONZE SHEET IS CDA ALLOY C28000 MUNTZ METAL, 60% COPPER & TRANSOMS, RETURNS, STRIKES, COLUMNS ARE 18 GA REINFORCED WITH 18 GA GALV STL; DOOR COVERS ARE 20 GA STN STL & BRONZE ARE GRAINED THE LONGEST DIMENSION.

THIS QUOTE IS VALID FOR A PERIOD OF (90) DAYS FROM THE DATE ISSUED FOR FABRICATION WITHIN THE TIME FRAME NOTED ABOVE. ALL QUOTES OVER (120) DAYS FROM THE ISSUE DATE SUBJECT TO ESCALATION. THIS QUOTE IS SUBJECT TO CORRECTION FOR ANY TYPOGRAPHICAL OR CLERICAL ERRORS. ALL QUOTATIONS AND AGREEMENTS ARE CONTINGENT UPON ACCIDENTS, FIRES, AVAILABILITY OF MATERIALS AND ALL OTHER CAUSES BEYOND OUR CONTROL. QUOTE COMPLIES W/ ASME A17.1/CSA B44-13 ONLY. DRAWING LEAD TIME BEGINS AFTER OF HATCH LAYOUTS; FABRICATION LEAD TIME BEGINS AFTER RECEIPT OF COMPLETE INFORMATION.

** ACTUAL MFG LEAD TIME WILL BE BASED ON FACTORY LOAD AT FINAL RELEASE

QUOTED BY: CHERYL

ELECTRONICALLY FILED - 2023 May 12 2:07 PM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

 GUNDERLIN LTD ISO 9001:2008 CERTIFIED 800-327-8490 * FAX 305-696-6078 www.gunderlin.com CUSTOMER: OTIS ELEVATOR OFFICE: GREENVILLE, SC ATTN: CHASE HOSKINSON		QUOTE NO: CW-HOTEL DATE: 7/18/2018 INFO FROM: E-MAIL - SEE BELOW FOR DETAILS QUOTE IS BASED ON OUR BEST INTERPRETATION OF THE INFO PROVIDED JOB NAME: HOTEL MARION SQUARE LOCATION: CHARLESTON, SC	
QTY CARS: 1 CAR NO 4			
CAB AND/OR INTERIOR DESCRIPTION AND PRICING			
PLATFORM: 3500# G2S CAB HEIGHT: 93 DOORWAY: 42 X 84		DOOR TYPE: CENTER-PARTING; FRONT & REAR	
SILL		CANOPY	
SHELL WALLS		VENTING	
		TRANSOM	
		STRIKE POST	
BASE		RETURN PANEL(S)	
WALL PANELS			
PADS & BUTTONS		COLUMN	
REVEALS		DOOR PANEL(S)	
FRIEZE			
HANDRAILS	1 1/2" DIA TUBE W/ WELDED END CAPS - SIDES SATIN BRONZE W/ STRAIGHT ENDS SINGLE ROW BRONZE TO BE OXIDIZED TO MATCH CONTROL SAMPLE FROM G/L #37256-57	CUTOUTS	
		CERT FRAME	
		LACQUER	
		MISC	
CEILING		VERSION 127b	
		EST'D CAB WEIGHT (LBS.) 82	FOB DOCK, FREIGHT INCLUDED TO JOB-SITE. STD ENCLOSED TRAILER DELIVERY. FLATBED TRAILERS, LIFT GATE TRUCKS OR ANY OTHER SPECIAL SERVICES, NOT INCLUDED.
LIGHTING		DWG LEAD TIME 4-5 WEEKS	
		FABRICATION LEAD TIME 12-14 WEEKS	
		** SEE BELOW	PRICE IS GOOD FOR SHIPMENT THRU: 7/18/2018 NET PER CAR: \$1,620 QTY CARS: 1 NET TOTAL: \$1,620
UNLESS NOTED OTHERWISE: STEEL IS COLD ROLLED COMPLYING WITH ASTM A366; STN STN SHEET IS TYPE 302/304; BRONZE SHEET IS CDA ALLOY C28000 MUNTZ METAL, 60% COPPER & TRANSOMS, RETURNS, STRIKES, COLUMNS ARE 18 GA REINFORCED WITH 18 GA GALV STL; DOOR COVERS ARE 20 GA STN STL & BRONZE ARE GRAINED THE LONGEST DIMENSION. THIS QUOTE IS VALID FOR A PERIOD OF (90) DAYS FROM THE DATE ISSUED FOR FABRICATION WITHIN THE TIME FRAME NOTED ABOVE. ALL QUOTES OVER (120) DAYS FROM THE ISSUE DATE SUBJECT TO ESCALATION. THIS QUOTE IS SUBJECT TO CORRECTION FOR ANY TYPOGRAPHICAL OR CLERICAL ERRORS. ALL QUOTATIONS AND AGREEMENTS ARE CONTINGENT UPON ACCIDENTS, FIRES, AVAILABILITY OF MATERIALS AND ALL OTHER CAUSES BEYOND OUR CONTROL. QUOTE COMPLIES W/ ASME A17.1/CSA B44-13 ONLY. DRAWING LEAD TIME BEGINS AFTER OF HATCH LAYOUTS; FABRICATION LEAD TIME BEGINS AFTER RECEIPT OF COMPLETE INFORMATION.			
** ACTUAL MFG LEAD TIME WILL BE BASED ON FACTORY LOAD AT FINAL RELEASE		QUOTED BY: CHERYL	

Tab No. 249

Balfour Beatty Construction

August 10, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 249
SI #10 Ballroom Wall Change

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 249 in the amount of Five thousand one hundred twenty-nine (\$5,129.09) to provide additional work in accordance with the following qualifications:

SI 10 changes the L3 ballroom walls from block to structural studs. In turn, the stucco went from direct applied to a metal lath system.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Nick Starcevic
Project Manager

cc:
Jennifer Faulkinberry
Jim Clements
Marty Wall
David Simonton
Alec Dooley

RCO # 249 - File

Balfour Beatty

Construction

Hotel at Marion Square

Request for Change Order # 249- SI #10 Ballroom Wall Change

The additional work for the **SI #10 Ballroom Wall Change** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50922050.40	SI #10 Ballroom Wall Change	\$4,838.77

Total Items \$4,838.77

Total Markups \$290.32

RCO Total \$5,129.09

The total Cost to perform the work as described above is an ADD of Five thousand one hundred twenty-nine (\$5,129.09).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 249

GC: Balfour Beatty

Project: Marion Square Hotel

Sub Contractor's Summary

Status: Pending Approval

Change Order# 5:

Trade: Stucco

Sub's Name: Premier Exteriors, LLC

Project: Marion Sq

Date:

Scope of Work Description:

***Price to change to 3-coat 7/8" Stucco system w/ Lath over framed walls, in Lieu of Direct applied to CMU**

Scope of Work Description	Materials				Units UOM	Labor		Equipment			Total Cost		
	Item Description	UOM	Qty	Cost Per Unit		Total	Rate	Eq. Type	#wks	Rate		Total	
Credit for Direct Applied	Stucco over Block	1400	SF	-\$13.48	-\$18,872.00						\$0.00	-\$18,872.00	
Add for Lath, Scratch & Brown	Stucco over Frame	1400	SF	\$16.25	\$22,750.00						\$0.00	\$22,750.00	
R - 1891											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
											\$0.00	\$0.00	
	Subtotals					\$3,878.00		0.0	\$0.00	Taxable Items	0.0	\$0.00	\$3,878.00
										TAXES	8.5%		\$329.63
									(Sub-Contractors Profit \$ Overhead	15.00%		\$631.14	
Total GC No.					\$3,878.00		0.0	\$0.00			\$3,878.15	\$4,838.77	

NOTES:

1• All change orders need to be approved before work can commence via written letter or email

Color Code Green= Approved, Yellow = Pending Approval, Red= Denied or Not taken

Tab No. 250

Balfour Beatty Construction

August 13, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 250
MOD 7 Terrace Door Glass Change

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 250 in the amount of One thousand four hundred sixty-two (\$1,462.80) to provide additional work in accordance with the following qualifications:

As directed in MOD 7, the terrace doors from the Concierge Lounge to the 6th floor terrace were to be reduced in size due to ceiling height coordination. As a result, the glass for these doors needed to be reordered. Cost includes new glass for the terrace doors only. There is no charge for labor or the terrace doors themselves.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Alec Dooley
Assistant Project Manager

cc:
Jim Clements
Melissa Pense
Marty Wall
Jennifer Faulkinberry
Woody Faust
Nick Starcevic
David Simonton

RCO # 250 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 250—MOD 7 Terrace Door Change

The additional work for the **MOD 7 Terrace Door Change** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50880000.40	MOD 7 Terrace Door Change	\$1,380.00

Total Items \$1,380.00

Total Markups \$82.80

RCO Total \$1,462.80

The total Cost to perform the work as described above is an ADD of One thousand four hundred sixty-two (\$1,462.80).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: Kim Brown, Library Associates, LLC Date: _____

RCO# 250

**Change Order
Request****Change Order
Request**

3221-A Westwood Industrial Drive, Monroe, NC – Phone: 704-291-7711 – Fax: 704-291-7011

Submit To:**Change Order Request Number: 0000**

Name: Tim Spano	Date: 8/13/2018
Company: Balfour Beatty	Fax:
Address:	
City: Charleston	State: SC Zip:
Reference: MOD 7 Terrace Door Height Change	

Due to adjustments and/or at the customers' request, 1st Choice Glass, Inc. deems it necessary to adjust the agreed upon Job Proposal/Contract as noted per the Warranty & Disclaimer footnote. 1st Choice Glass reserves the right to alter contract in conjunction with customer negotiation to complete and/or vary from the described task. Note that adjustment with description and explanation shall be documented with approval below. Please note, that the requested work can not begin until Change Order Request is Signed and Approved, or Contractor Change Order is Issued.

DESCRIPTION OF WORK	LABOR	MATERIALS	OTHER
Terrace Door Height Change		\$ 1,200.00	
SUB-TOTAL:	\$ -	\$ 1,200.00	\$ -
Time Impact: Y/N			
Length of Impact: Days/Weeks			
SALES TAX:		\$ -	
5% O/H:	\$ -	\$ 60.00	\$ -
10% Profit:	\$ -	\$ 120.00	\$ -
BONDING if Required:	\$ -	\$ -	\$ -
TOTAL:	\$ -	\$ 1,380.00	\$ -
TOTAL AMOUNT OF APPROVED CHANGE ORDER:	\$1,380		

Customer Acceptance Signature X _____

1st Choice Glass Warranty & Disclaimer:

(1) Reliability of Quoted Costs. Labor costs and material costs are firm for thirty (30) days from the date of proposal stated above. If the time between the proposal date and installation exceeds thirty (30) days, 1st Choice Glass, Inc. reserves the right to amend the proposal and to add any surcharges and/or additional costs to any and all labor and/or materials.

(2) Warranty. Unless otherwise agreed in writing, 1st Choice Glass, Inc. warrants that all application and labor completed by 1st Choice Glass, Inc. shall be free from defect for one (1) year following its completion. Said warranty does not include (1) damage arising from abnormal use, negligence, misuse, or accident, which occurs as a result of no fault of 1st Choice Glass, Inc. or (2) material damaged by tear-out, retro-fit, or remodel. 1st Choice Glass, Inc. reserves the right to respond to such warranty claims by first making repairs to the defect; such repairs shall be subject to the satisfaction of the customer. 1st Choice Glass, Inc. does not warrant raw material or manufacturers' products; any warranty for such materials or products shall be limited to the manufacturer's warranty. 1ST CHOICE GLASS, INC. EXPRESSLY DISCLAIMS ANY IMPLIED WARRANTY OF MERCHANTABILITY OR IMPLIED WARRANTY OF FITNESS FOR A PARTICULAR PURPOSE.

(3) Estimate of Work Required & Changes. The work proposed herein is based on initial estimates and may require changes, alterations, and/or adjustments to complete the job as described, agreed or required by applicable codes and/or government inspections; if such changes or alterations are necessary, customer agrees to execute a written change order which shall indicate the change in the work to be completed or the materials to be used and the agreed upon price for such work and/or materials; such change order shall become an amendment to the contract and the customer shall pay all additional charges agreed upon in the change order at the time the change order is delivered by the customer to 1st Choice Glass, Inc.

(4) Specifications. Unless otherwise specified, all systems are designed to the governing codes (i.e. International Building Codes) for the location where the work is to be completed. A maximum deflection of $L/175 - 3/4$ shall apply for units less than 13'-6" in height and a maximum deflection of $L/240 + 1/4$ " shall apply for units exceeding 13'-6" in height, but less than 40'-0" in height. Individual glass lite deflection shall be limited to .75" of the glass edge.

(5) Time Frame. A minimum of two (2) weeks from the date that all shop drawings and submittals are approved is required for delivery. Installation shall be completed within a minimum of two (2) weeks after the delivery of materials if the project schedule does not delay installation.

(6) Deposit & Payment. A deposit or joint supplier payment(s) may be required at the discretion of 1st Choice Glass, Inc. and may be due to 1st Choice Glass, Inc. prior to startup. Once ordered, any and all nonrefundable special order material costs are the sole liability of the customer and shall be payable on demand. Payments of retainage are due no later than sixty (60) days from the final invoice unless otherwise agreed upon in writing. All other payments are due in net thirty (30) unless otherwise agreed in writing.

(7) Inclusions & Exclusions. All proposals include indicated labor, materials, and applicable taxes. Exclusions from this proposal include, but are not limited to, any cleaning, protection or sealing of glass or metal, any and all "Wood Blocking" required on plans or necessary for systems warranty, and additional glass, metals, labor, shop drawings, or miscellaneous materials not listed on proposed shop drawings, or addendums to such shop drawings or this proposal. All Inclusions and Exclusions contained within this Paragraph shall supersede any and all requirements related to the same identified in bid drawings, construction documents, specifications, clarifications, contracts, and any attachments, exhibits, or addendums thereto.

(8) Binding Contract. This proposal shall be considered a valid and binding contract upon 1st Choice Glass, Inc. and the customer upon the signing of all parties. Once signed by the parties, this contract and any addendums and exhibits attached hereto comprise the entire agreement between the parties hereto and supersede all prior negotiations. This contract may only be amended by a written instrument signed by both parties hereto.

(9) Headings. The headings of the paragraphs herein are for convenience only and shall not affect the meaning or interpretation of the contents thereof.

(10) Authority. Each party signing this proposal represents to the other that the terms of this proposal are accepted, and that the resulting contract, the rights and obligations contemplated herein, and the execution and delivery hereof are authorized or have been duly authorized by all necessary limited liability company or corporate proceedings and actions, as applicable, pursuant to applicable law.

ACCEPTED:

1st Choice Glass, Inc.

Customer Name:

By: _____

By: _____

Mike Tsiukes

Title: President

Title: _____

Date: _____

Date: _____

Dooley, Alec

From: Brian Rinehart <brinehart@designcontinuuminc.com>
Sent: Thursday, September 1, 2016 10:07 AM
To: Christine Spence; 'James Clements'; Starcevic, Nicholas; Dooley, Alec
Cc: Jennifer Faulkinberry; Karen Jenkins
Subject: RE: 630 / Marion Square / MSH - Sixth Floor Terrace Doors
Attachments: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

Christine,

Please see the attached and let us know if you have any questions. This clash condition also affects room 635.

Thanks.
 Brian

Brian Rinehart
 Project Director
Design Continuum, Inc.
 44 Broad Street NW
 Suite 310
 Atlanta, GA 30303
 P (404) 266-0095
 F (404-266-8252)
brinehart@designcontinuuminc.com
<http://www.designcontinuuminc.com>

From: Christine Spence [mailto:CSpence@lpbatlanta.com]
Sent: Wednesday, August 31, 2016 8:51 PM
To: 'James Clements' <jclements@matrixse.com>; Starcevic, Nicholas <NStarcevic@Balfourbeattyus.com>; 'adooley@Balfourbeattyus.com' <adooley@Balfourbeattyus.com>
Cc: Jennifer Faulkinberry <JFaulkinberry@lpbatlanta.com>; Brian Rinehart <brinehart@designcontinuuminc.com>; Karen Jenkins <kjenkins@designcontinuuminc.com>
Subject: RE: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

Please see attached response to RFI 0667. - Christine

From: James Clements [mailto:jclements@matrixse.com]
Sent: Wednesday, August 31, 2016 8:11 PM
To: Christine Spence; Starcevic, Nicholas
Cc: Jennifer Faulkinberry; Brian Rinehart; Karen Jenkins
Subject: RE: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

Just sent it to you

Jim Clements
[Matrix Program Management Services, LLC](#)

O. 704.676.9996
 C. 704 905.1165
jcllements@matrixse.com
www.matrixse.com

From: Christine Spence [<mailto:CSpence@lpbatlanta.com>]
Sent: Wednesday, August 31, 2016 7:35 PM
To: Starcevic, Nicholas <NStarcevic@Balfourbeattyus.com>
Cc: James Clements <jcllements@matrixse.com>; Jennifer Faulkinberry <JFaulkinberry@lpbatlanta.com>; Brian Rinehart <brinehart@designcontinuuminc.com>; Karen Jenkins <kjenkins@designcontinuuminc.com>
Subject: RE: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

I'm back at the office now, but I can't find RFI 667. Could you please forward it to me so I can response to it?

From: Christine Spence
Sent: Wednesday, August 31, 2016 6:37 PM
To: Starcevic, Nicholas
Cc: James Clements; Jennifer Faulkinberry; Brian Rinehart; Karen Jenkins
Subject: RE: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

yes

From: Starcevic, Nicholas [NStarcevic@Balfourbeattyus.com]
Sent: Wednesday, August 31, 2016 6:35 PM
To: Christine Spence
Cc: James Clements; Jennifer Faulkinberry; Brian Rinehart; Karen Jenkins
Subject: Re: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

Please issue response to RFI and then include in MOD 7. Is that still being issued tomorrow?

Nick Starcevic | Balfour Beatty Construction
 Cell: 704.361.3265

On Aug 31, 2016, at 6:34 PM, Christine Spence <CSpence@lpbatlanta.com> wrote:

Can this/should this be a part of Mod 7?

From: James Clements [jcllements@matrixse.com]
Sent: Wednesday, August 31, 2016 5:54 PM
To: Starcevic, Nicholas; Jennifer Faulkinberry; Christine Spence
Cc: Brian Rinehart; Karen Jenkins
Subject: RE: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

Thanks, Nick

Christine

I saw Brian's instruction. Please issue it

Jim Clements
[Matrix Program Management Services, LLC](mailto:jclements@matrixse.com)
 O. 704.676.9996
 C. 704.905.1165
jclements@matrixse.com
www.matrixse.com

From: Starcevic, Nicholas [<mailto:NStarcevic@Balfourbeattyus.com>]
Sent: Wednesday, August 31, 2016 5:53 PM
To: Jennifer Faulkinberry <JFaulkinberry@lpbatlanta.com>; James Clements <jclements@matrixse.com>; Christine Spence <CSpence@lpbatlanta.com>
Cc: Brian Rinehart <brinehart@designcontinuuminc.com>; Karen Jenkins <kjenkins@designcontinuuminc.com>
Subject: RE: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

Just spoke with 1st choice and we need direction by end of week. There will be a small impact fee to make the adjustments from Graham's, but should be at or below 1k.

Delivery will not be affected.

Nick Starcevic | Project Manager
 mobile: 704-361-3265 | email: NStarcevic@Balfourbeattyus.com
 Balfour Beatty Construction | 306 Meeting St. Suite 300, Charleston, SC 29401

www.balfourbeattyus.com | [Facebook](#) | [Twitter](#) | [YouTube](#) | [LinkedIn](#)

<image007.jpg><image008.jpg><image009.jpg>

From: Jennifer Faulkinberry [<mailto:JFaulkinberry@lpbatlanta.com>]
Sent: Wednesday, August 31, 2016 5:51 PM
To: James Clements <jclements@matrixse.com>; Christine Spence <CSpence@lpbatlanta.com>
Cc: Brian Rinehart <brinehart@designcontinuuminc.com>; Karen Jenkins <kjenkins@designcontinuuminc.com>, Starcevic, Nicholas <NStarcevic@Balfourbeattyus.com>
Subject: RE: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

There's an rfi out there about this. It can be a response. ..

Jennifer Faulkinberry
 Sent via the Samsung Galaxy Note® 4

----- Original message -----

From: James Clements <jclements@matrixse.com>
 Date: 8/31/2016 5:44 PM (GMT-05:00)
 To: Christine Spence <CSpence@lpbatlanta.com>

Cc: Brian Rinehart <brinehart@designcontinuuminc.com>, Jennifer Faulkinberry <JFaulkinberry@lpbatlanta.com>, Karen Jenkins <kjenkins@designcontinuuminc.com>, NStarcevic@Balfourbeattyus.com
Subject: RE: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

Christine

In Jennifer's absence, can you get this rolling? BBC needs direction right away – they wanted it tonight.

Jim Clements
[Matrix Program Management Services, LLC](mailto:jclements@matrixse.com)
O. 704 676.9996
C. 704 905.1165
jclements@matrixse.com
www.matrixse.com

From: Brian Rinehart [<mailto:brinehart@designcontinuuminc.com>]
Sent: Wednesday, August 31, 2016 4:49 PM
To: Jennifer Faulkinberry <JFaulkinberry@lpbatlanta.com>; Karen Jenkins <kjenkins@designcontinuuminc.com>; James Clements <jclements@matrixse.com>
Subject: 630 / Marion Square / MSH - Sixth Floor Terrace Doors

Jennifer,

We don't have an official ASI form so, by copy of this e-mail we clarify that all 6th floor exterior aluminum Terrace doors type "J" are to reduce to 7'-0" in overall height from the currently scheduled 8'-1 ½". This is being done to coordinate door head heights with available clear ceiling/bulkhead heights in the perimeter Terrace rooms on 6th floor.

Please review the above and let us know if you have any questions.

Thanks.
Brian

Brian Rinehart
Project Director
Design Continuum, Inc.
44 Broad Street NW
Suite 310
Atlanta, GA 30303
P (404) 266-0095
F (404-266-8252)
brinehart@designcontinuuminc.com

<http://www.designcontinuuminc.com>

From: James Clements [<mailto:jclements@matrixse.com>]
Sent: Wednesday, August 31, 2016 4:23 PM
To: Brian Rinehart <brinehart@designcontinuuminc.com>, Kim Brown <kbrown@bennetthospitality.com>; NStarcevic@Balfourbeattyus.com
Cc: jfaulkinberry@lpbatlanta.com, Karen Jenkins <kjenkins@designcontinuuminc.com>; Christine Spence <CSpence@lpbatlanta.com>
Subject: RE: MSH - Sixth Floor Terrace Doors

Just to clarify, this is 6th floor only

Jim Clements
[Matrix Program Management Services, LLC](http://www.matrixse.com)
 O. 704 676.9996
 C. 704 905.1165
jclements@matrixse.com
www.matrixse.com

From: James Clements
Sent: Wednesday, August 31, 2016 4:22 PM
To: 'Brian Rinehart' <brinehart@designcontinuuminc.com>; Kim Brown <kbrown@bennetthospitality.com>; NStarcevic@Balfourbeattyus.com
Cc: jfaulkinberry@lpbatlanta.com, Karen Jenkins <kjenkins@designcontinuuminc.com>; Christine Spence <CSpence@lpbatlanta.com>
Subject: RE: MSH - Sixth Floor Terrace Doors

Nick

Due to structure and plumbing coordination constraints, we have no choice but to reduce the exterior terrace door height to 7'0", which will realize a minimum bulkhead height of 7'10". DCI (Brian) will issue an ASI to WLA.

First Choice Glass has been straight with us and my hope is they can make this work little or no impact to the schedule. Pls let me know otherwise.

Jim Clements
[Matrix Program Management Services, LLC](http://www.matrixse.com)
 O. 704 676.9996
 C. 704 905.1165
jclements@matrixse.com
www.matrixse.com

From: Brian Rinehart [<mailto:brinehart@designcontinuuminc.com>]
Sent: Wednesday, August 31, 2016 2:53 PM
To: James Clements <jclements@matrixse.com>
Cc: jfaulkinberry@lpbatlanta.com, Karen Jenkins <kjenkins@designcontinuuminc.com>; Christine Spence <CSpence@lpbatlanta.com>
Subject: FW: MSH - Sixth Floor Terrace Doors

Jim,

Please read through the e-trail below and let us know your thoughts.

Thanks.
Brian

Brian Rinehart
Project Director
Design Continuum, Inc.
44 Broad Street NW
Suite 310
Atlanta, GA 30303
P (404) 266-0095
F (404-266-8252)
brinehart@designcontinuuminc.com
<http://www.designcontinuuminc.com>

From: Jennifer Faulkinberry [<mailto:JFaulkinberry@lpbatlanta.com>]
Sent: Wednesday, August 31, 2016 2:51 PM
To: Brian Rinehart <brinehart@designcontinuuminc.com>; Christine Spence <CSpence@lpbatlanta.com>
Subject: Fwd: MSH - Sixth Floor Terrace Doors

Sounds like changes to these door height will cost time and/or money. I agree they should all shorten to clear ceilings but owner needs to approve any cost or time.

Jennifer Faulkinberry
Sent via the Samsung Galaxy Note® 4

----- Original message -----

From: "Dooley, Alec" <adooley@Balfourbeattyus.com>
Date: 8/31/2016 12:29 PM (GMT-05:00)

To: "Starcevic, Nicholas" <NStarcevic@Balfourbeattyus.com>, Jennifer Faulkinberry <JFaulkinberry@lpbatlanta.com>, James Clements <jclements@matrixse.com>, Brian Rinehart <brinehart@designcontinuuminc.com>
Cc: "Spano, Tim" <tmspano@Balfourbeattyus.com>
Subject: RE: MSH - Sixth Floor Terrace Doors

Direction for this door size is being tracked as RFI 0667

Thank you,

Alec Dooley | Senior Project Engineer

mobile: 704.614.4907 | email: adooley@balfourbeattyus.com

Balfour Beatty Construction | 306 Meeting Street, Suite 300, Charleston, SC 29401 | www.balfourbeattyus.com

<image011.jpg>

From: Starcevic, Nicholas

Sent: Wednesday, August 31, 2016 12:28 PM

To: Jennifer Faulkinberry <JFaulkinberry@lpbatlanta.com>, James Clements <jclements@matrixse.com>, Brian Rinehart <brinehart@designcontinuuminc.com>

Cc: Dooley, Alec <adooley@Balfourbeattyus.com>, Spano, Tim <tmspano@Balfourbeattyus.com>

Subject: FW: MSH - Sixth Floor Terrace Doors

Team,

Wanted to clarify my comment on the BIM call earlier... While the doors are not currently in manufacturing, the glass has been released so changing sizes could delay the entire order. We are not stopping the order unless directed to. Once we get direction on the door sizes, we'll call the subcontractor to see what can be done.

Let me know if you have questions.

Nick Starcevic | Project Manager

mobile: 704-361-3265 | email: NStarcevic@Balfourbeattyus.com

Balfour Beatty Construction | 306 Meeting St. Suite 300, Charleston, SC 29401

www.balfourbeattyus.com | [Facebook](#) | [Twitter](#) | [YouTube](#) | [LinkedIn](#)

<image007.jpg><image014.jpg><image009.jpg>

From: Paul Dustin [<mailto:pauldustin@glass1st.net>]

Sent: Wednesday, August 31, 2016 11:27 AM

To: Dooley, Alec <adooley@Balfourbeattyus.com>

Subject: RE: MSH - Sixth Floor Terrace Doors

Ok, changing the glass sizes could delay the entire order. We need to get this answered as soon as possible to avoid any delays.

Paul Dustin

Project Manager

704-507-8264

From: Dooley, Alec [<mailto:adooley@Balfourbeattyus.com>]
Sent: Wednesday, August 31, 2016 11:25 AM
To: Paul Dustin <pauldustin@glass1st.net>
Subject: RE: MSH - Sixth Floor Terrace Doors

We still do not have a final height for these doors I am hoping for resolution on Tuesday

Alec Dooley | Senior Project Engineer
 mobile: 704.614.4907 | email: adooley@balfourbeattyus.com
 Balfour Beatty Construction | 306 Meeting Street, Suite 300, Charleston, SC 29401 | www.balfourbeattyus.com
 <image017.jpg>

From: Paul Dustin [<mailto:pauldustin@glass1st.net>]
Sent: Wednesday, August 31, 2016 11:22 AM
To: Dooley, Alec <adooley@Balfourbeattyus.com>
Cc: Denney, Brandon <BDenney@Balfourbeattyus.com>, Starcevic, Nicholas <NStarcevic@Balfourbeattyus.com>, Ricci, Daniel <DRicci@Balfourbeattyus.com>, Denney, Brandon <BDenney@Balfourbeattyus.com>
Subject: RE: MSH - Sixth Floor Terrace Doors

How are we looking on this? I need to get them some info asap. I'm not sure if it will cause delays at this point. But it is a possibility.

Paul Dustin

Project Manager
 704-507-8264

From: Dooley, Alec [<mailto:adooley@Balfourbeattyus.com>]
Sent: Monday, August 29, 2016 8:47 AM
To: Paul Dustin <pauldustin@glass1st.net>
Cc: Denney, Brandon <BDenney@Balfourbeattyus.com>, Starcevic, Nicholas <NStarcevic@Balfourbeattyus.com>; Ricci, Daniel <DRicci@Balfourbeattyus.com>, Denney, Brandon <BDenney@Balfourbeattyus.com>
Subject: MSH - Sixth Floor Terrace Doors

Paul,

Following up on our conversation, the BIM team has discovered some issues with the ceiling heights in the managers apartment and concierge suite. Lowering the ceiling is going to impact the final height of your doors in these areas. As of today, we do not know the full impact or final height of these doors but hope to have resolution when the team reconvenes on Wednesday for the regularly scheduled BIM coordination meeting. BBC is generating an RFI to the Architect for documentation (0661).

I will follow up with you soon.

Thanks,

Alec Dooley | Senior Project Engineer
 mobile: 704.614.4907 | email: adooley@balfourbeattyus.com

Balfour Beatty Construction | 306 Meeting Street, Suite 300, Charleston, SC 29401 | www.balfourbeattyus.com
<image019.jpg>

ELECTRONICALLY FILED - 2023 May 12 2:07 PM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

Tab No. 251

Balfour Beatty Construction

August 31, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 251
Dining Room MOD 1-8 Millwork Change Order

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 251 in the amount of Twenty-two thousand three hundred five (\$22,305.58) to provide additional work in accordance with the following qualifications:

Provide added millwork trim at the Dining Room from the GMP drawings thru the approved shop drawings. This cost specifically includes:

- Add wall paneling at curved banquet knee wall and window wall. (Clouded in blue in the attached back up)
- Remove wall paneling for decorative metal screen behind knee wall. (Clouded in red in the attached back up)
- Add blocking for HVAC crown drop for discreet HVAC. (Highlighted in Orange in the attached back up).
- Add raised paneling at window ceiling beams and ceiling beams at soffit west of Stairs. (Clouded in yellow in the attached back up)
- Add paint grade T&G to accent ceiling north of Stair 04. (Clouded in Green in the attached back up).
- Remove stiles and panel mold where paneling was modified.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,

Alec Dooley
Assistant Project Manager

cc:
Melissa Pense
Marty Wall
Jim Clements
Jennifer Faulkinberry
Wood Faust
Nick Starcevic
David Simonton

MSH RCO #251

Page 1 of 2

R - 1907

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 251– Dining Room MOD 1-8 Millwork Change Order

The additional work for the **Dining Room MOD 1-8 Millwork Change Order** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50925200.40	Dining Room MOD 1-8 Millwork Change Order	\$21,043.00

Total Items \$21,043.00

Total Markups \$1,262.58

RCO Total \$22,305.58

The total Cost to perform the work as described above is an ADD of Twenty-two thousand three hundred five (\$22,305.58).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 251



LOW COUNTRY CASE & MILLWORK
3270 Benchmark Drive
Ladson, SC 29456
(843) 797-0881



Page No. 1 of 2

CHANGE ORDER

PROPOSAL SUBMITTED TO Balfour Beatty		TODAY'S DATE 8/14/2018	DATE OF PLANS/PAGE #'S MOD # 1-8 SI #39
PHONE NUMBER	FAX NUMBER	SPECIFICATIONS AND ADDENDUMS (include dates) None Provided - See Note 1	
JOB NAME Hotel at Marion Square CO - Dining Mod Millwork		JOB LOCATION Charleston, SC	

We propose to furnish material, labor, tools, and equipment to complete the following work in accordance with the plans and specifications:

NOTES

1. If project specifications are not provided, LCCM reserves the right to alter the amount of this proposal.
2. LCCM standard work hours are 8:00 a.m. - 5:00 p.m., Monday - Thursday. Up-charges will apply to any work that is required for any reason to be performed before or after the hours listed.
3. **LCCM standard lead time is 4-6 weeks from receipt of approved submittals and field verified site conditions (field verified site conditions include metal stud walls/soffits framed, plumbing and electrical rough-ins complete). An up-charge of 10% will be added to any jobs that require a lead time of 4 weeks or less.**
4. All millwork is priced per AWI specifications for custom grade.

EXCLUSIONS

- Anything not listed on this proposal
- In Wall Blocking
- SF-01 Finish
- Mirrors

CHANGE ORDER

Dining 147 - Mod 1

- Add wall paneling (A/911.2, A/911.3, & B/911.3)
 - Remove wall paneling (A/911.1, B/911.2)
 - Add blocking for HVAC crown drop
 - Add raised paneling at window ceiling beams and ceiling beam right of stairs
 - Add paint grade T&G to accent ceiling
- \$19,283

Dining 147 - Mod 8

- Remove stiles and panel mold where paneling was modified
- (\$463)

Dining 147 - SI #39

- Remove stiles and panel mold where paneling was modified
- (\$1,058)

RAW MATERIAL & MANUFACTURING = \$12,434.00

INSTALL LABOR = \$5,329.00

15% MARK-UP = \$2,664.00

SUBTOTAL = \$20,427.00

AWI FEE (0.5%) = \$102.00BONDING (2.5%) = \$513.00**TOTAL ADDITIONAL COST = \$21,043.00**

We propose hereby to furnish material and labor – complete in accordance with above specifications for the sum of:
 TWENTY ONE THOUSAND FORTY THREE AND NO/100***** dollars (\$21,043.00)

Payment as follows: Progress payments for stored materials to be billed monthly.
 Balance due upon completion of LCCM's scope.

All material is guaranteed to be as specified. All work to be completed in a substantial workmanlike manner according to specifications submitted, per standard practices. Any alteration or deviation from above specifications involving extra costs will be executed only upon written orders, and will become an extra charge over and above the estimate. All agreements contingent upon strikes, accidents or delays beyond our control. Owner to carry fire, tornado and other necessary insurance. Our workers are fully covered by Workmen's Compensation Insurance. If either party commences legal action to enforce its rights pursuant to this agreement, the prevailing party in said legal action shall be entitled to recover its reasonable attorney's fees and costs of litigation relating to said legal action, as determined by a court of competent jurisdiction.

Authorized
 Signature Christian Datz


Note: this proposal may be withdrawn by us
 if not accepted within 30 days.

ACCEPTANCE OF PROPOSAL The above prices, specifications and
 conditions are satisfactory and are hereby accepted. You are authorized
 to do the work as specified. Payment will be made as outlined above.

Signature _____

Signature _____

Date of Acceptance _____

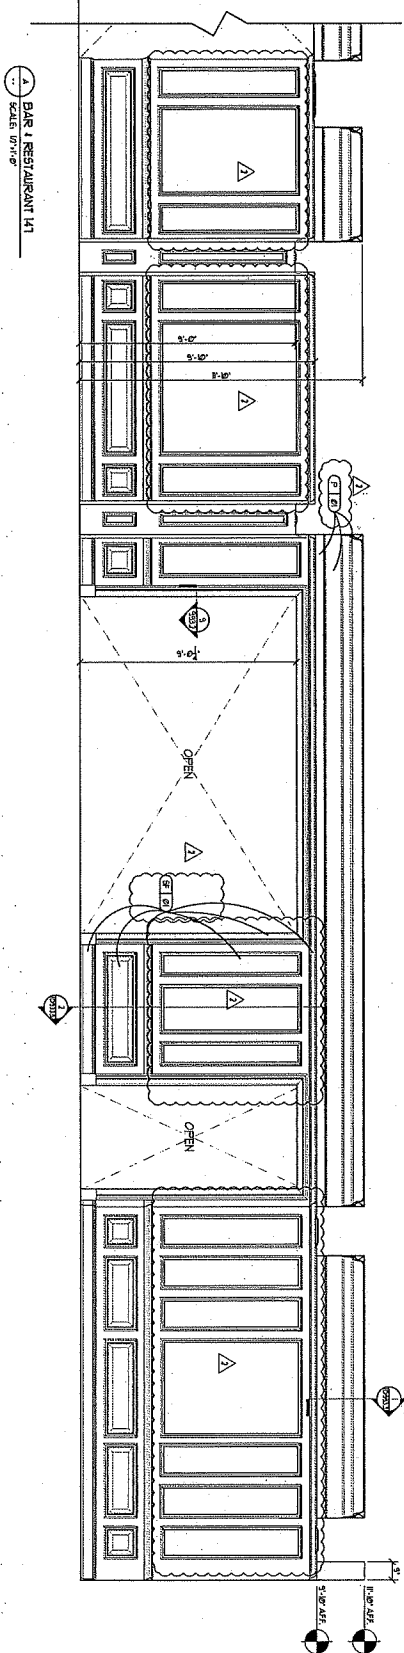


CUSTOM BIFOLDING DOOR
TO BE CUT TO RECEIVE
CROWN, CHAIRRAIL & BASE

[illegible]

404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403





DESIGN
CONTINUUM
INCORPORATED
44 BROAD STREET NW, ATLANTA, GEORGIA 30303
(404) 525-1000

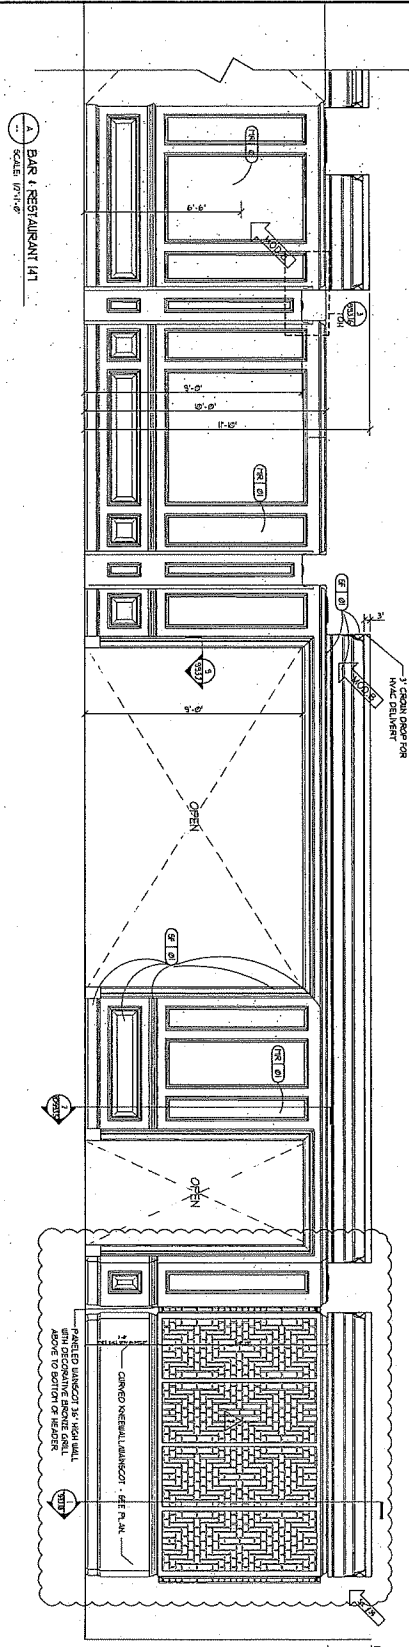

DESIGN
CONTINUUM
INCORPORATED
44 BROAD STREET NW, ATLANTA, GEORGIA 30300
TEL: 404/524-7400 FAX: 404/524-7401

BR3042.dwg 01/12/00 16:50

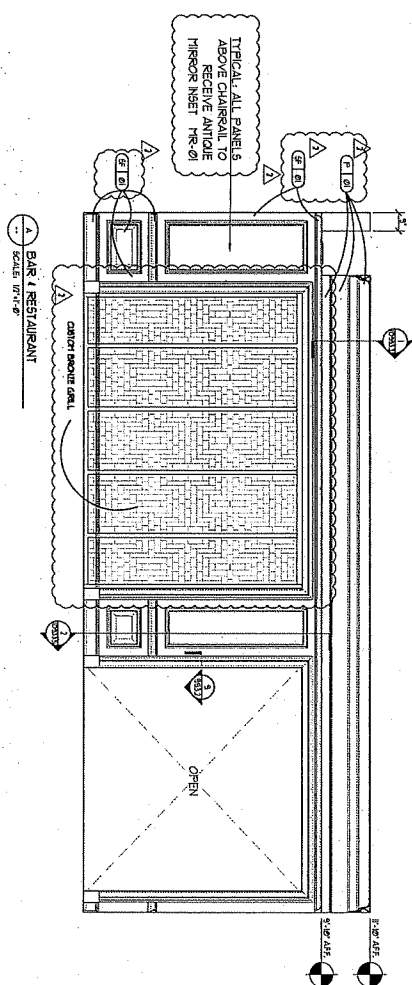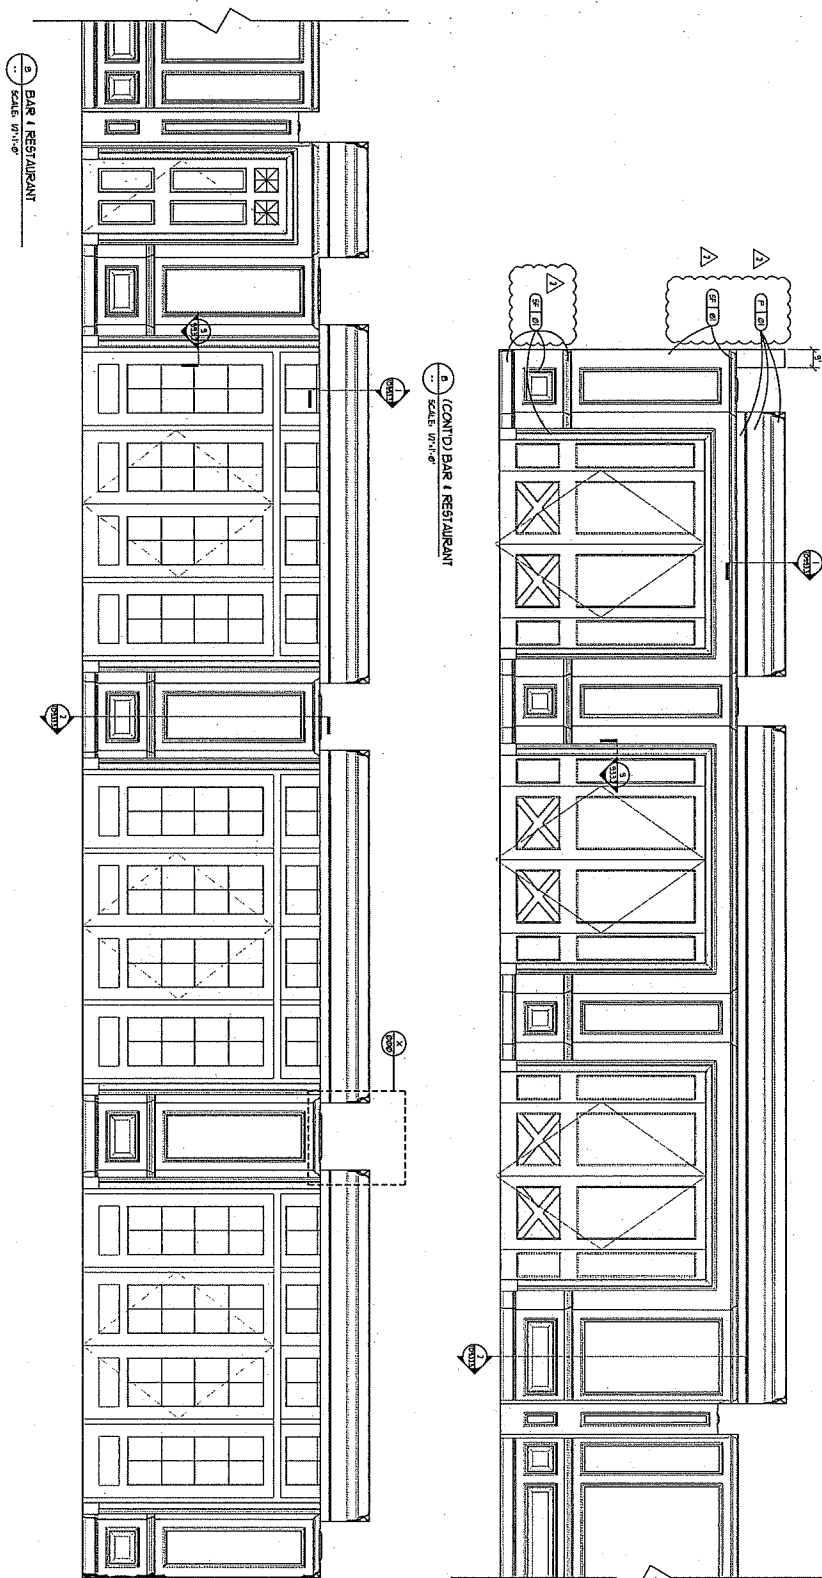

THE HOTEL AT MARION SQUARE

404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403




DESIGN
CONTINUUM
INCORPORATED
44 BROAD STREET NW, ATLANTA, GEORGIA 30307
TELEPHONE (404) 259-0095

R - 1913


REVISIONS		DATE	BY	DESCRIPTION
1	DESIGN	01/12/00	BR	INITIAL DESIGN
2	DESIGN	01/12/00	BR	REVISIONS
3	DESIGN	01/12/00	BR	REVISIONS
4	DESIGN	01/12/00	BR	REVISIONS
5	DESIGN	01/12/00	BR	REVISIONS
6	DESIGN	01/12/00	BR	REVISIONS
7	DESIGN	01/12/00	BR	REVISIONS
8	DESIGN	01/12/00	BR	REVISIONS
9	DESIGN	01/12/00	BR	REVISIONS
10	DESIGN	01/12/00	BR	REVISIONS
11	DESIGN	01/12/00	BR	REVISIONS
12	DESIGN	01/12/00	BR	REVISIONS
13	DESIGN	01/12/00	BR	REVISIONS
14	DESIGN	01/12/00	BR	REVISIONS
15	DESIGN	01/12/00	BR	REVISIONS
16	DESIGN	01/12/00	BR	REVISIONS
17	DESIGN	01/12/00	BR	REVISIONS
18	DESIGN	01/12/00	BR	REVISIONS
19	DESIGN	01/12/00	BR	REVISIONS
20	DESIGN	01/12/00	BR	REVISIONS
21	DESIGN	01/12/00	BR	REVISIONS
22	DESIGN	01/12/00	BR	REVISIONS
23	DESIGN	01/12/00	BR	REVISIONS
24	DESIGN	01/12/00	BR	REVISIONS
25	DESIGN	01/12/00	BR	REVISIONS
26	DESIGN	01/12/00	BR	REVISIONS
27	DESIGN	01/12/00	BR	REVISIONS
28	DESIGN	01/12/00	BR	REVISIONS
29	DESIGN	01/12/00	BR	REVISIONS
30	DESIGN	01/12/00	BR	REVISIONS
31	DESIGN	01/12/00	BR	REVISIONS
32	DESIGN	01/12/00	BR	REVISIONS
33	DESIGN	01/12/00	BR	REVISIONS
34	DESIGN	01/12/00	BR	REVISIONS
35	DESIGN	01/12/00	BR	REVISIONS
36	DESIGN	01/12/00	BR	REVISIONS
37	DESIGN	01/12/00	BR	REVISIONS
38	DESIGN	01/12/00	BR	REVISIONS
39	DESIGN	01/12/00	BR	REVISIONS
40	DESIGN	01/12/00	BR	REVISIONS
41	DESIGN	01/12/00	BR	REVISIONS
42	DESIGN	01/12/00	BR	REVISIONS
43	DESIGN	01/12/00	BR	REVISIONS
44	DESIGN	01/12/00	BR	REVISIONS
45	DESIGN	01/12/00	BR	REVISIONS
46	DESIGN	01/12/00	BR	REVISIONS
47	DESIGN	01/12/00	BR	REVISIONS
48	DESIGN	01/12/00	BR	REVISIONS
49	DESIGN	01/12/00	BR	REVISIONS
50	DESIGN	01/12/00	BR	REVISIONS
51	DESIGN	01/12/00	BR	REVISIONS
52	DESIGN	01/12/00	BR	REVISIONS
53	DESIGN	01/12/00	BR	REVISIONS
54	DESIGN	01/12/00	BR	REVISIONS
55	DESIGN	01/12/00	BR	REVISIONS
56	DESIGN	01/12/00	BR	REVISIONS
57	DESIGN	01/12/00	BR	REVISIONS
58	DESIGN	01/12/00	BR	REVISIONS
59	DESIGN	01/12/00	BR	REVISIONS
60	DESIGN	01/12/00	BR	REVISIONS
61	DESIGN	01/12/00	BR	REVISIONS
62	DESIGN	01/12/00	BR	REVISIONS
63	DESIGN	01/12/00	BR	REVISIONS
64	DESIGN	01/12/00	BR	REVISIONS
65	DESIGN	01/12/00	BR	REVISIONS
66	DESIGN	01/12/00	BR	REVISIONS
67	DESIGN	01/12/00	BR	REVISIONS
68	DESIGN	01/12/00	BR	REVISIONS
69	DESIGN	01/12/00	BR	REVISIONS
70	DESIGN	01/12/00	BR	REVISIONS
71	DESIGN	01/12/00	BR	REVISIONS
72	DESIGN	01/12/00	BR	REVISIONS
73	DESIGN	01/12/00	BR	REVISIONS
74	DESIGN	01/12/00	BR	REVISIONS
75	DESIGN	01/12/00	BR	REVISIONS
76	DESIGN	01/12/00	BR	REVISIONS
77	DESIGN	01/12/00	BR	REVISIONS
78	DESIGN	01/12/00	BR	REVISIONS
79	DESIGN	01/12/00	BR	REVISIONS
80	DESIGN	01/12/00	BR	REVISIONS
81	DESIGN	01/12/00	BR	REVISIONS
82	DESIGN	01/12/00	BR	REVISIONS
83	DESIGN	01/12/00	BR	REVISIONS
84	DESIGN	01/12/00	BR	REVISIONS
85	DESIGN	01/12/00	BR	REVISIONS
86	DESIGN	01/12/00	BR	REVISIONS
87	DESIGN	01/12/00	BR	REVISIONS
88	DESIGN	01/12/00	BR	REVISIONS
89	DESIGN	01/12/00	BR	REVISIONS
90	DESIGN	01/12/00	BR	REVISIONS
91	DESIGN	01/12/00	BR	REVISIONS
92	DESIGN	01/12/00	BR	REVISIONS
93	DESIGN	01/12/00	BR	REVISIONS
94	DESIGN	01/12/00	BR	REVISIONS
95	DESIGN	01/12/00	BR	REVISIONS
96	DESIGN	01/12/00	BR	REVISIONS
97	DESIGN	01/12/00	BR	REVISIONS
98	DESIGN	01/12/00	BR	REVISIONS
99	DESIGN	01/12/00	BR	REVISIONS
100	DESIGN	01/12/00	BR	REVISIONS

ID-9112


BDR3042.dwg 01/12/00 16:50

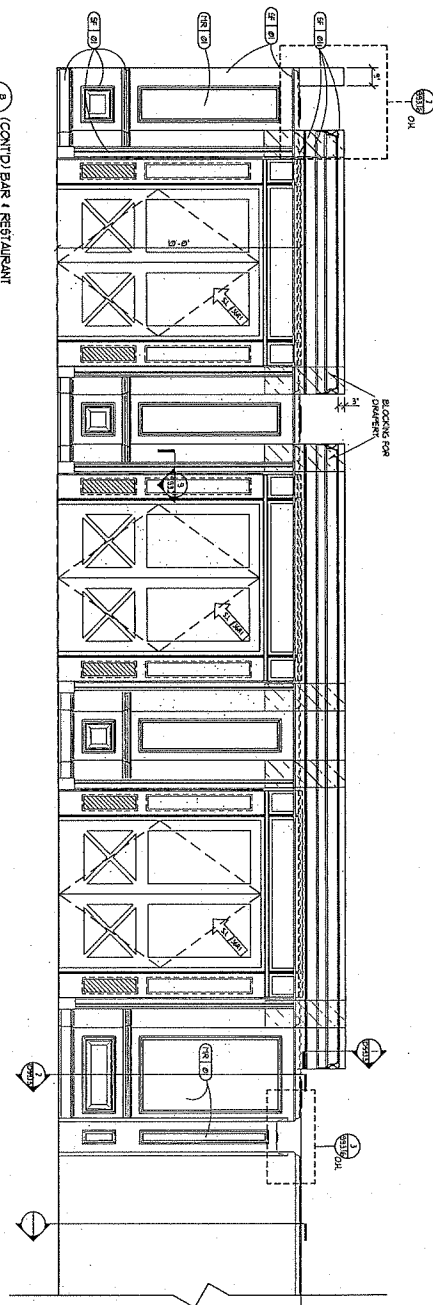


8 (CONT'D) BAR & RESTAURANT
SCALE 1/8"=1'-0"

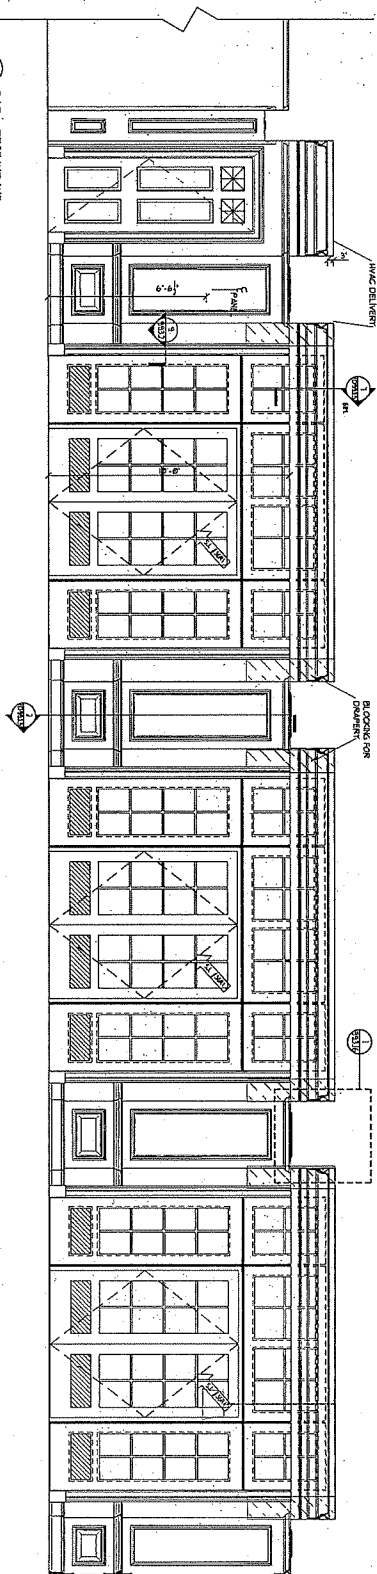

9 BAR & RESTAURANT
SCALE 1/8"=1'-0"



10 SERVICE ALCOVE HS - REAR
SCALE 1/8"=1'-0"

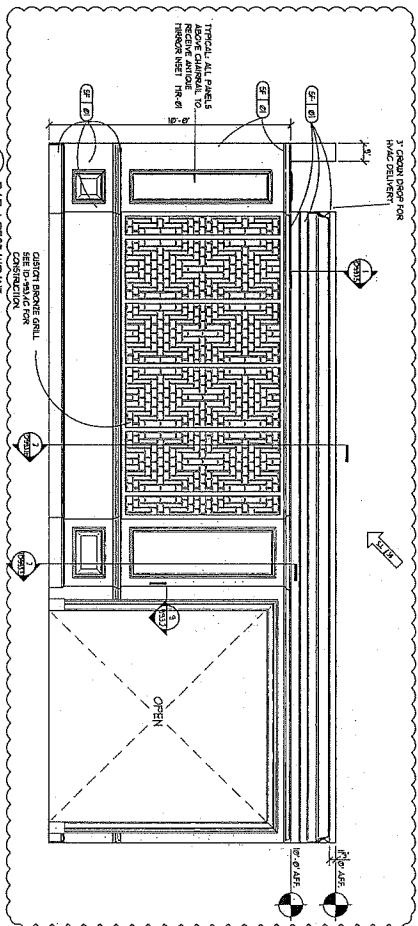

11 BAR & RESTAURANT
SCALE 1/8"=1'-0"

THE HOTEL AT MARION SQUARE

404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403

R - 1914





DESIGN
CONTINUUM
INCORPORATED
44 BROAD STREET N.W. ATLANTA, GEORGIA 30309
TELEPHONE (404) 526-9025

THIS DRAWING IS THE PROPERTY OF
AND SHALL REMAIN THE PROPERTY OF
UNLESS RETURNED TO THE ARCHITECT
WITHIN 30 DAYS OF THE DATE OF
COMPLETION OF THE PROJECT.

REVISION	DATE	BY	DESCRIPTION
1	01/12/00	WFA/BSH	ISSUED FOR PERMITTING
2	05/05/00	WFA/BSH	ISSUED FOR CONSTRUCTION

SCALE: ELEVATIONS
1/8"=1'-0"

INTERIOR ELEVATIONS
RESTAURANT
D-9112

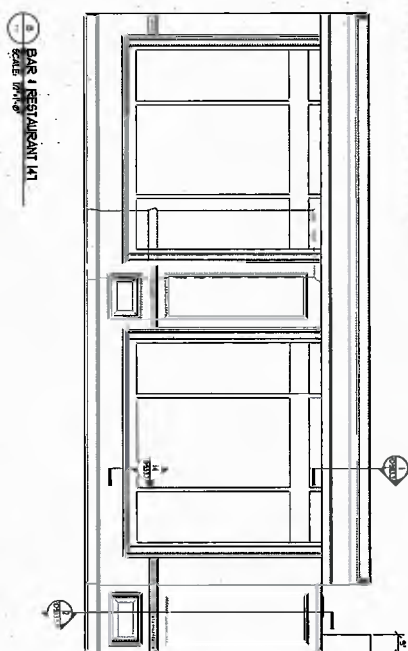[illegible]


404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403

R - 1915




DESIGN
CONTINUUM
INCORPORATED
44 BRIND STREET NW, ATLANTA, GEORGIA 30309

BDR2042.dwg 01/12/00 16:50

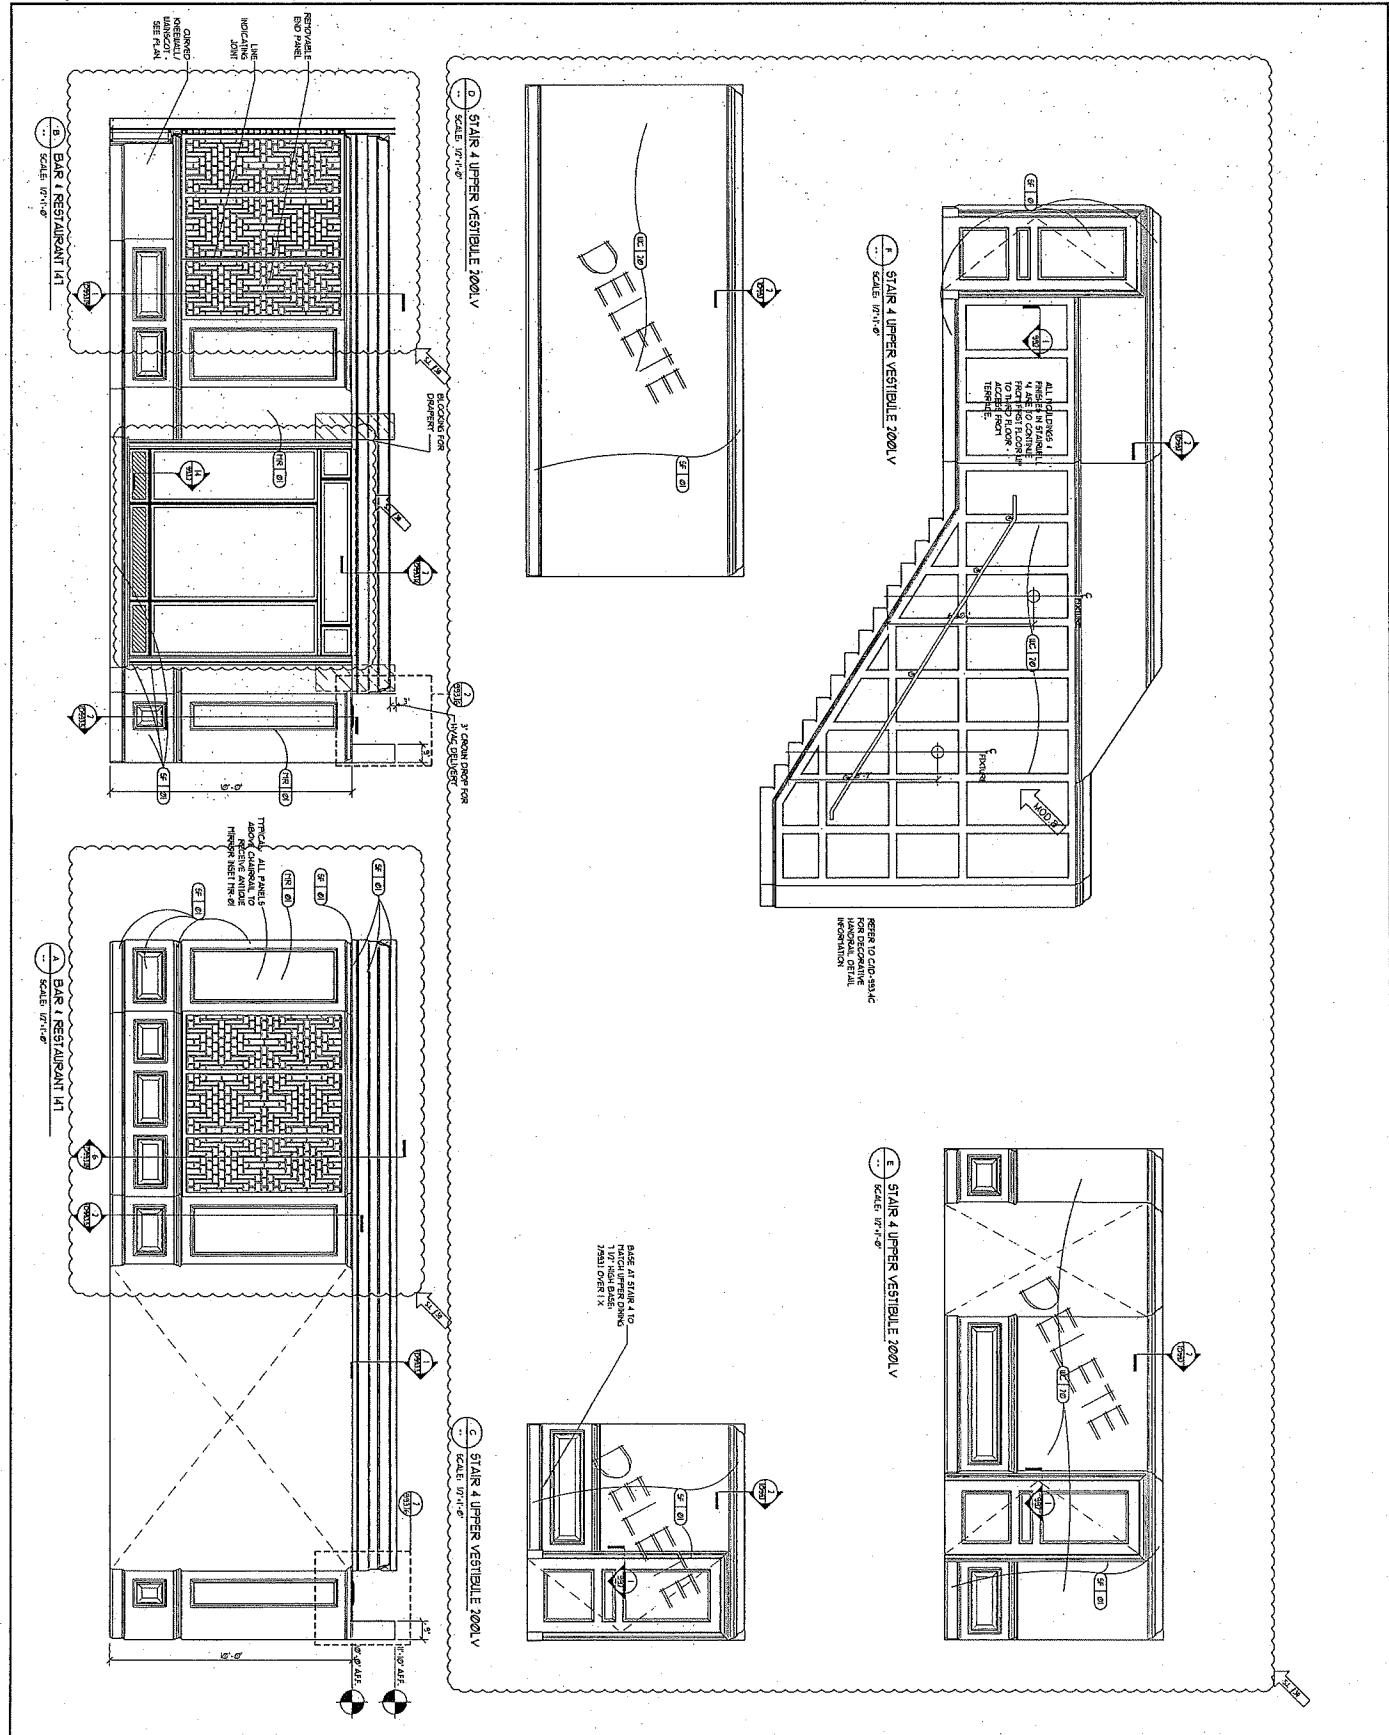

THE HOTEL AT MARION SQUARE 404 KING STREET CHARLESTON, SOUTH CAROLINA 29403 R - 1916		DESIGN CONTINUUM INCORPORATED 44 BROAD STREET AVE. ATLANTA, GEORGIA 30301 TELEPHONE (404) 255-0055					
THIS DRAWING IS THE PROPERTY OF DESIGN CONTINUUM INCORPORATED AND NOT BE REPRODUCED OR USED IN ANY MANNER WITHOUT THE WRITTEN PERMISSION OF DESIGN CONTINUUM INCORPORATED REVISIONS: <table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th>DATE</th> <th>NO.</th> <th>DESCRIPTION</th> </tr> </thead> <tbody> <tr> <td>01/12/00</td> <td>1</td> <td>ISSUED FOR PERMIT</td> </tr> </tbody> </table> PROJECT NO. 2042 PROJECT NAME: HOTEL AT MARION SQUARE PROJECT LOCATION: 404 KING STREET, CHARLESTON, SC PROJECT ARCHITECT: BDR2042.DWG PROJECT DATE: 01/12/00 PROJECT SCALE: 1/8\"/>	DATE	NO.	DESCRIPTION	01/12/00	1	ISSUED FOR PERMIT	PROJECT NO. 2042 PROJECT NAME: HOTEL AT MARION SQUARE PROJECT LOCATION: 404 KING STREET, CHARLESTON, SC PROJECT ARCHITECT: BDR2042.DWG PROJECT DATE: 01/12/00 PROJECT SCALE: 1/8\"/>
DATE	NO.	DESCRIPTION					
01/12/00	1	ISSUED FOR PERMIT					

10R3042.dwg 01/12/00 16:50

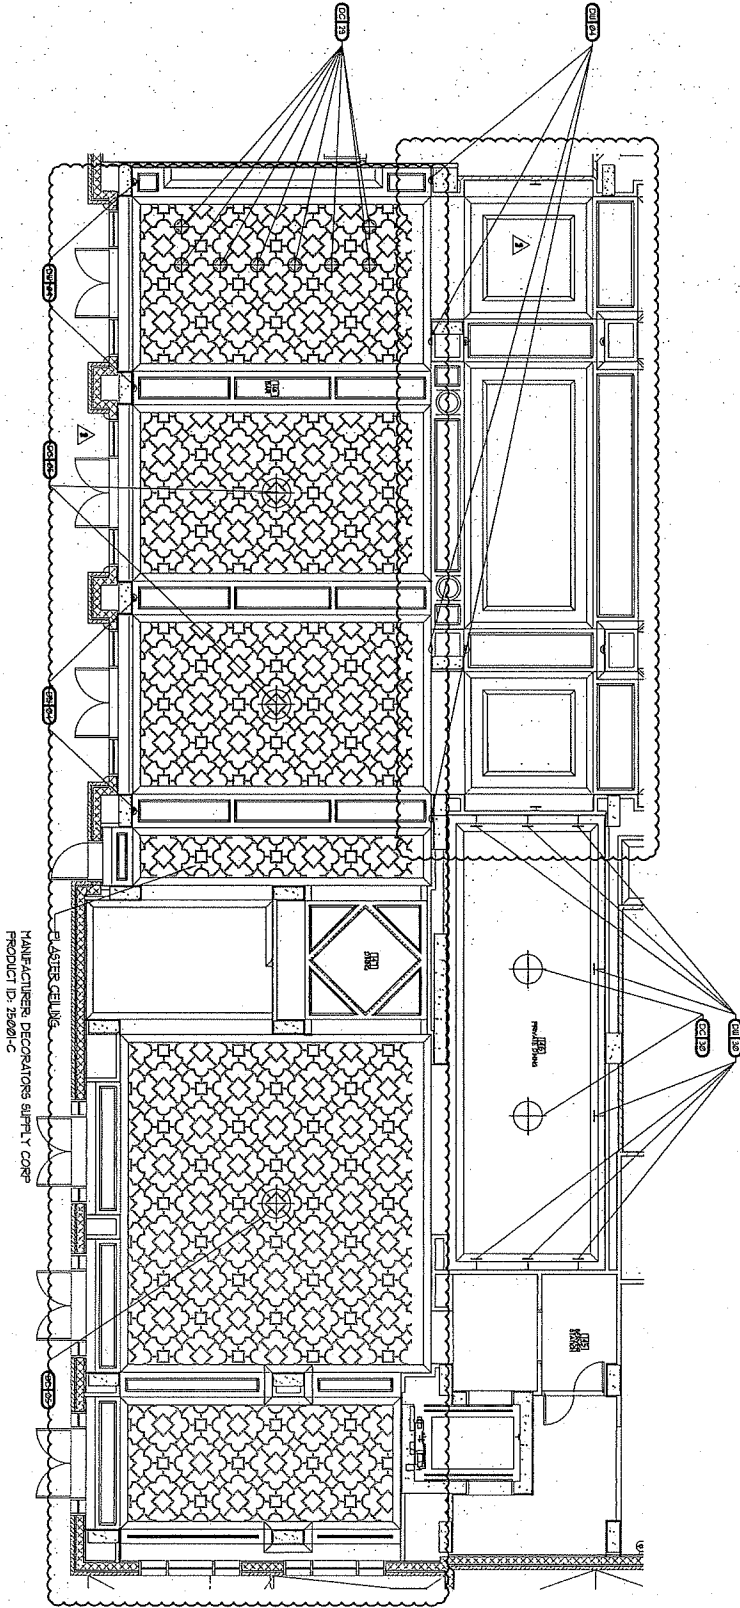

EXPANDED 1st FLOOR RCP
SCALE 1/8" = 1'-0"

THE HOTEL AT MARION SQUARE


404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403



DESIGN
CONTINUUM
INCORPORATED
44 BROAD STREET, 11TH FLOOR, ATLANTA, GEORGIA 30303
TELEPHONE (404) 525-0300

R - 1917

BDR3042.dwg 01/12/00 16:50

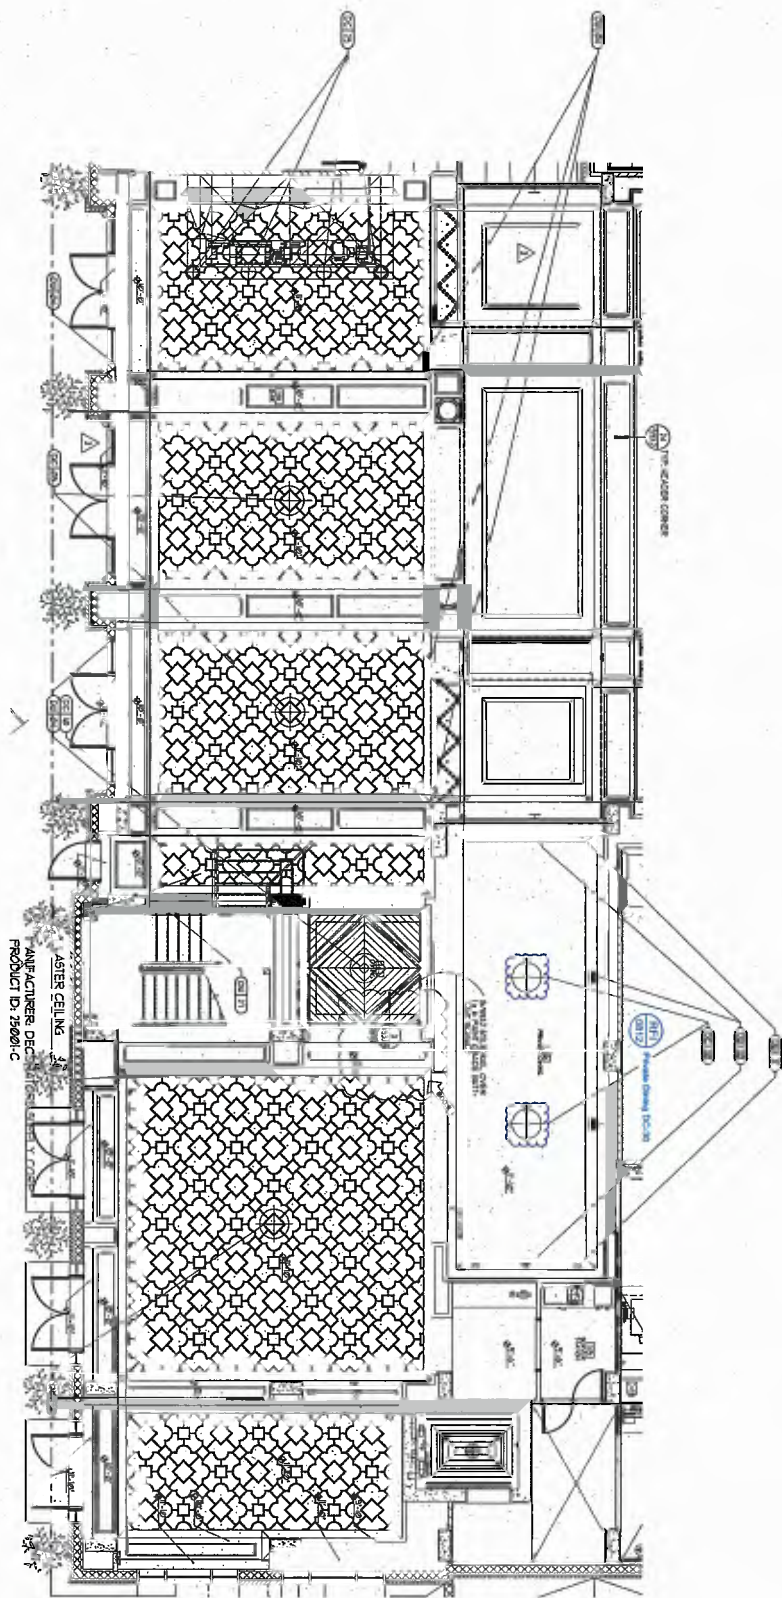

THE HOTEL AT MARION SQUARE

404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403

R - 1918



DESIGN
CONTINUUM
INCORPORATED
44 BROAD STREET NW, ATLANTA, GEORGIA 30303
TELEPHONE (404) 255-0055

REVISIONS		DATE	BY	DESCRIPTION
1	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
2	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
3	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
4	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
5	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
6	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
7	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
8	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
9	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
10	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
11	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
12	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
13	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
14	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
15	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
16	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
17	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
18	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
19	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
20	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
21	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
22	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
23	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
24	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
25	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
26	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
27	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
28	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
29	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
30	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
31	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
32	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
33	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
34	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
35	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
36	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
37	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
38	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
39	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
40	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
41	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
42	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
43	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
44	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
45	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
46	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
47	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
48	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
49	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
50	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
51	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
52	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
53	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
54	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
55	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
56	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
57	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
58	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
59	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
60	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
61	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
62	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
63	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
64	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
65	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
66	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
67	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
68	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
69	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
70	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
71	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
72	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
73	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
74	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
75	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
76	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
77	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
78	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
79	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
80	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
81	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
82	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
83	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
84	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
85	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
86	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
87	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
88	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
89	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
90	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
91	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
92	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
93	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
94	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
95	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
96	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
97	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
98	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
99	EXPANDED 1st FLOOR RCP	01/12/00	16:50	
100	EXPANDED 1st FLOOR RCP	01/12/00	16:50	

Tab No. 253

Balfour Beatty Construction

August 14, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 253
Add Crown at Dome Rotunda's

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 253 in the amount of Ten thousand fifty-five (\$10,055.16) to provide additional work in accordance with the following qualifications:

Furnish and install crown (detail 6/993.2) around the interior edge of the first and second floor Dome Rotunda as shown on sheet ID901 detail A.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Alec Dooley
Assistant Project Manager

cc:
Marty Wall
Melissa Pense
Jim Clements
Woody Faust
David Simonton
Nick Starcevic

RCO # 253 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 253— Add Crown at Dome Rotunda's

The additional work for the **Add Crown at Dome Rotunda's** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50640000.40	Add Crown at Dome Rotunda Layer	\$9,486.00

Total Items \$9,486.00

Total Markups \$569.16


RCO Total \$10,055.16

The total Cost to perform the work as described above is an ADD of Ten thousand fifty-five (\$10,055.16).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 253

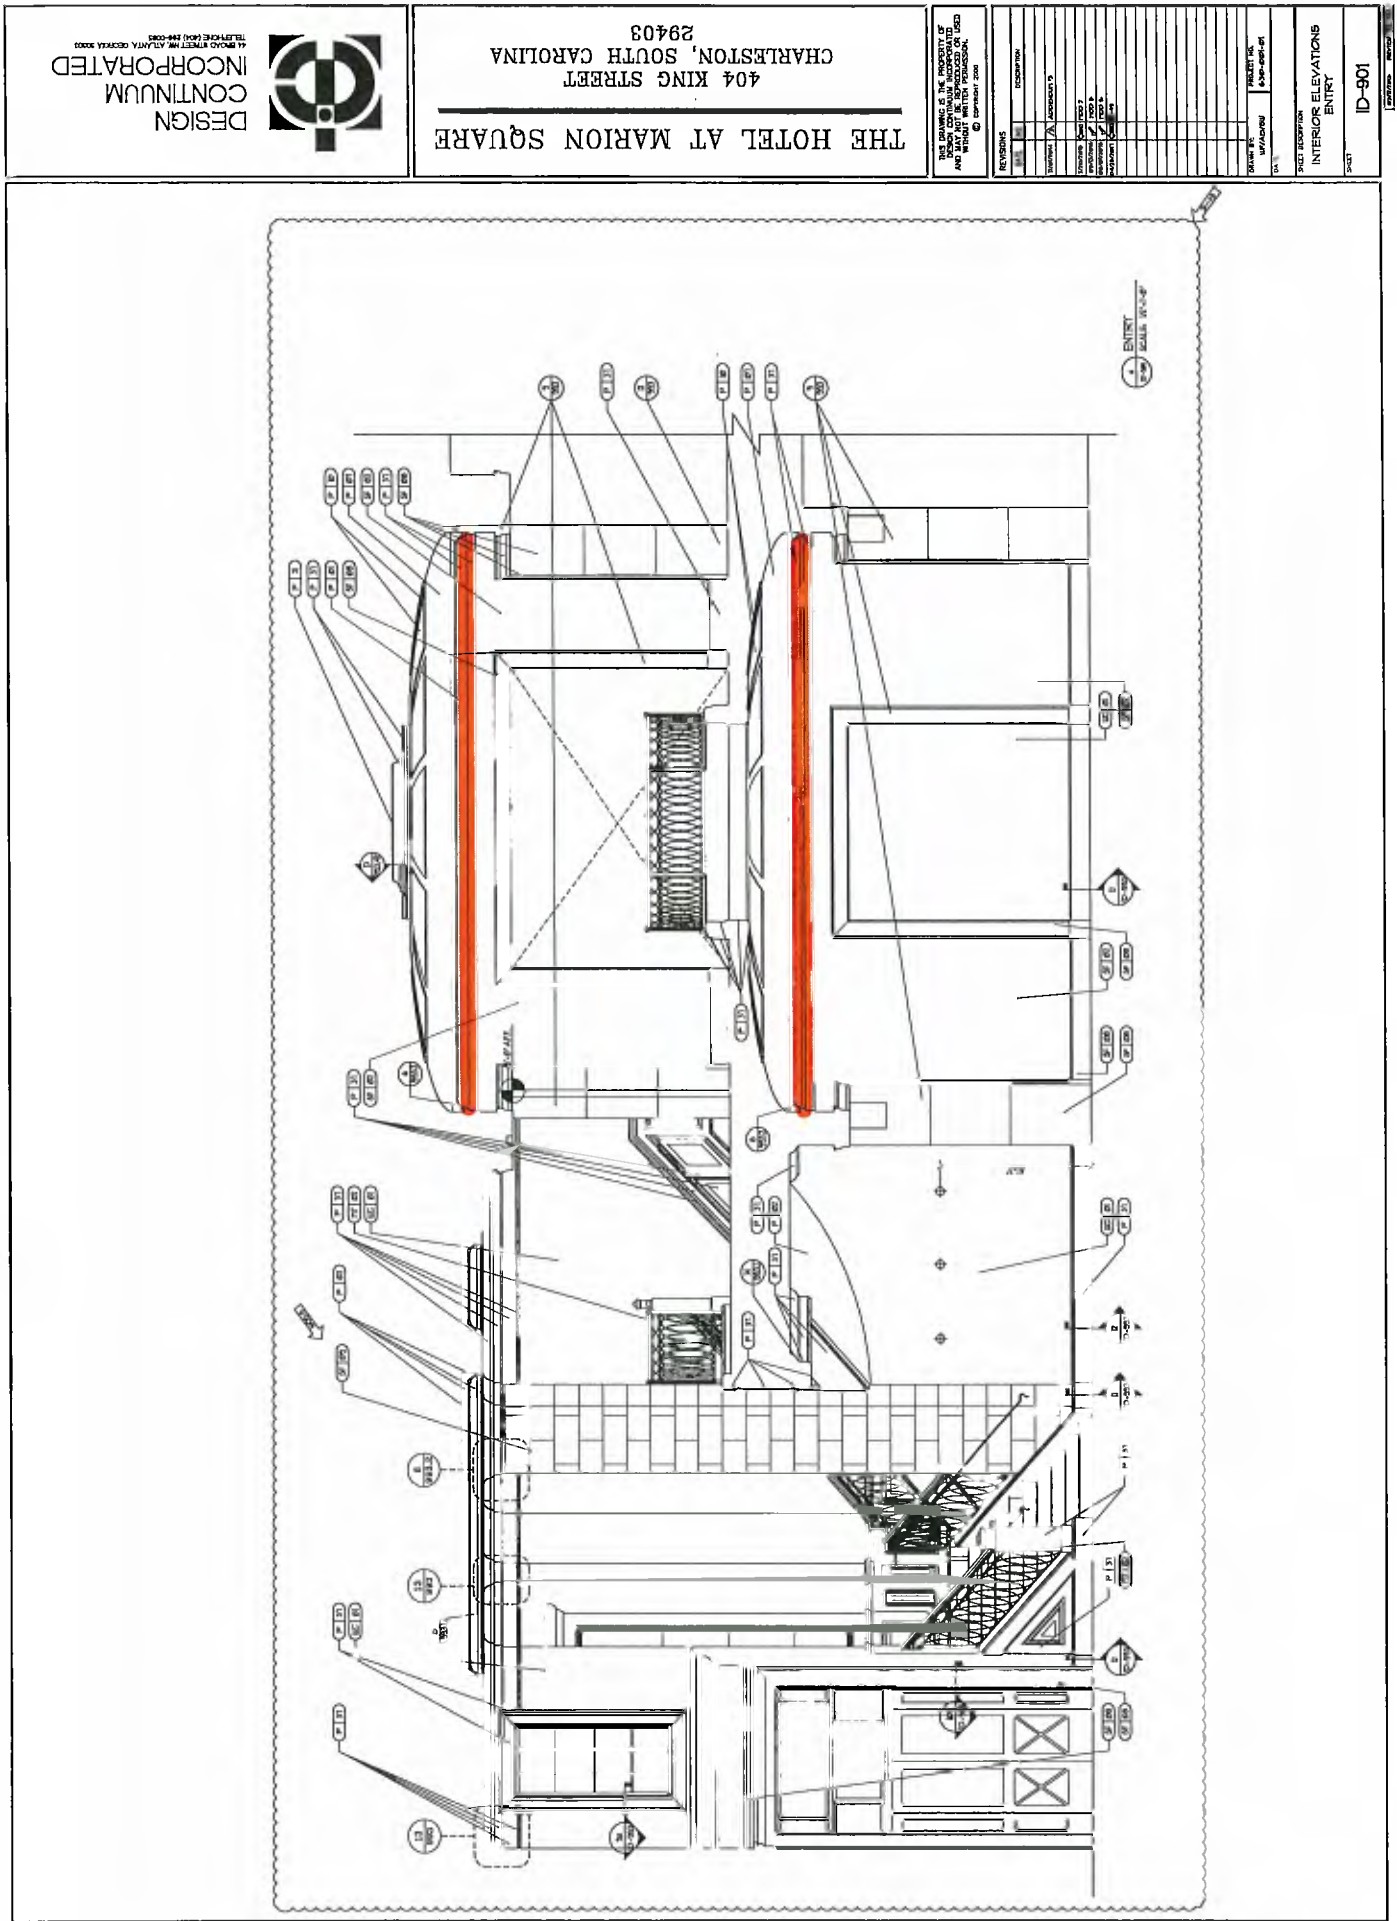

Tab No. 255

Balfour Beatty Construction

August 31, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 255
Add Trim to Conceal Pocket Door Header

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 255 in the amount of Eleven thousand seven hundred eighty-nine (\$11,789.32) to provide additional work in accordance with the following qualifications:

At the request of the owner, Low Country Case and Millwork to add wood side pieces above the door casing to conceal air space above the pocket door headers. Cost includes added trim work only.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Alec Dooley
Assistant Project Manager

cc:
Marty Wall
Melissa Pense
Jim Clements
Jennifer Faulkinberry
Nick Starcevic
David Simonton

RCO # 255 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 255— Add Trim to Conceal Pocket Door Header

The additional work for the **Add Trim to Conceal Pocket Door Header** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50640000.40	Add Trim to Conceal Pocket Door Header	\$11,122.00

Total Items \$11,122.00

Total Markups \$667.32

RCO Total \$11,789.32

The total Cost to perform the work as described above is an ADD of Eleven thousand seven hundred eighty-nine (\$11,789.32).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 255



LOW COUNTRY CASE & MILLWORK
3270 Benchmark Drive
Ladson, SC 29456
(843) 797-0881



Page No. 1 of 2

CHANGE ORDER

PROPOSAL SUBMITTED TO Balfour Beatty		TODAY'S DATE 12/8/17	DATE OF PLANS/PAGE #'S Per Site Direction
PHONE NUMBER	FAX NUMBER	SPECIFICATIONS AND ADDENDUMS (Include dates) None Provided - See Note 1	
JOB NAME Hotel at Marion Square		JOB LOCATION Charleston, SC	

We propose to furnish material, labor, tools, and equipment to complete the following work in accordance with the plans and specifications:

NOTES

1. If project specifications are not provided, LCCM reserves the right to alter the amount of this proposal.
2. LCCM standard work hours are 8:00 a.m. - 5:00 p.m., Monday - Thursday. Up-charges will apply to any work that is required for any reason to be performed before or after the hours listed.
3. **LCCM standard lead time is 4-6 weeks from receipt of approved submittals and field verified site conditions (field verified site conditions include metal stud walls/soffits framed, plumbing and electrical rough-ins complete). An up-charge of 10% will be added to any jobs that require a lead time of 4 weeks or less.**
4. All millwork is priced per AWI specifications for custom grade:

EXCLUSIONS


- Anything not listed on this proposal
- Blocking

ADDED POCKET DOOR TRIM

A total of (179) bathroom pocket doors will receive an added piece of trim above the upper jamb extension in order to hide the pocket door hardware (see sketch below).

- The piece will be primed, paint grade.
- The added piece will NOT be removable.

The original detail can be found on Sheet ID-992.1 (SI #36 R1).

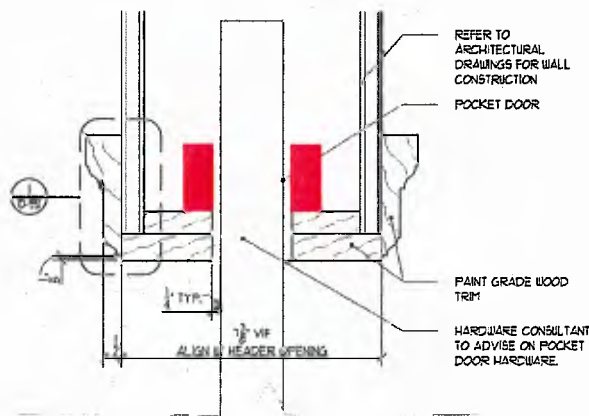

4
12-992
DETAIL SECTION - GUESTBATH DOOR JAMB DETAIL
SCALE: 6"=1'-0"

RAW MATERIALS AND MANUFACTURING = \$4,020.00

INSTALL LABOR = \$5,603.00

SUBTOTAL = \$9,623.00

MARK-UP

A 15% mark-up has been added to all of the above work.

TOTAL MARK-UP = \$1,444.00

ADDITIONAL CHARGES

AWI Certification

All of the above work will be AWI Certified (0.5% fee).

Total = \$55.00

TOTAL PRICE FOR ADDED POCKET DOOR TRIM = \$11,122.00

We propose hereby to furnish material and labor – complete in accordance with above specifications for the sum of:

ELEVEN THOUSAND ONE HUNDRED TWENTY TWO AND NO/100*** dollars (\$ 11,122.00)**

Payment as follows: Progress payments for stored materials to be billed monthly.
Balance due upon completion of LCCM's scope.

All material is guaranteed to be as specified. All work to be completed in a substantial workmanlike manner according to specifications submitted, per standard practices. Any alteration or deviation from above specifications involving extra costs will be executed only upon written orders, and will become an extra charge over and above the estimate. All agreements contingent upon strikes, accidents or delays beyond our control. Owner to carry fire, tornado and other necessary insurance. Our workers are fully covered by Workmen's Compensation Insurance. If either party commences legal action to enforce its rights pursuant to this agreement, the prevailing party in said legal action shall be entitled to recover its reasonable attorney's fees and costs of litigation relating to said legal action, as determined by a court of competent jurisdiction.

Authorized Signature David Stasiukaitis

Note: this proposal may be withdrawn by us
if not accepted within 30 days.

ACCEPTANCE OF PROPOSAL The above prices, specifications and conditions are satisfactory and are hereby accepted. You are authorized to do the work as specified. Payment will be made as outlined above.

Signature _____

Signature _____

Date of Acceptance _____



Tab No.258

Balfour Beatty Construction

March 28, 2019

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 258
Additional Mock Up Revisions

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 258 in the amount of Sixty-five thousand seven hundred eighty-two (\$65,782.09) to provide additional work in accordance with the following qualifications:

1. Paint Tie Back Rods
2. Additional Demo of New and Revised Mock Up.
3. Added Prep and Paint of Pergola (mock up and in L3 Pergola)
4. Reskim Mock Up after shutter revisions
5. Remove Hope's Doors from Mock Up and Install in Building
6. Additional Labor to Install (5) Shutters (6 hours ea)
7. Support / Clean Up for Demo (78 hours)
8. Hope's reinstallation (BBC Support) (10 hours)

*This change order does not include any considerations for time for the construction of the mock up or the impact, direct and indirect, of the revised mock u, materials, or inspections.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Nick Starcevic
Project Manager

cc:
Jim Clements
Jennifer Faulkinberry

Balfour Beatty Construction

David Simonton
Tim Spano
Shanti Pieniak

RCO # 258 - File

Balfour Beatty

Construction

Hotel at Marion Square

Request for Change Order # 258-- Additional Mock Up Revisions

The additional work for the **Additional Mock Up Revisions** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50991000.40	Paint Rods on Mock Up	\$383.00
2	400.50200000.40	Demo of Additional Mock Up	\$21,336.35
3	400.50991000.40	Added Prep and Paint of Pergola	\$14,994.58
4	400.50922050.40	Reskim Mock Up	\$3,391.00
5	400.50840000.40	Remove and Reinstall Hope's Door	\$9,564.65
6	400.51000000.40	(5) Revised Shutters	\$7,283.00
7	400.50306510.40	BBC Labor and OHP	\$5,106.00

Total Items \$62,058.58

Total Markups \$3,723.51

RCO Total \$65,782.09

The total Cost to perform the work as described above is an ADD of Sixty-five thousand seven hundred eighty-two (\$65,782.09).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 258



Change Order Request

Date: 24-Jul-17

Request # 16

Attention: Alec Dooley, Nick Starcevic
Balfour Beatty

Project Name: Hotel at Marion Square

From: Scott McCormack

RE: Exterior Mock Up

Item # Description
1 Paint Iron Pipe in Patina Copper Finish; Exterior Mock Up Touch Ups

LABOR	Units	Unit Cost	Total
Foreman	5	\$45.00	\$225.00
			\$0.00
			\$0.00
			\$0.00
			\$0.00
			\$0.00
Subtotal	5		\$225.00

MATERIAL	Units	Unit Cost	Total
1 Quart Copper Paint	1	\$61.92	\$61.92
1 Gallon Eider White DTM	1	\$27.52	\$27.52
			\$0.00
			\$0.00
			\$0.00
			\$0.00
			\$0.00
Subtotal			\$89.44

Sales Tax	8.5%	\$	7.60
Subtotal			\$322.04
Overhead	10%	\$	32.20
Profit	5%	\$	17.71
P&P Bond	3.5%	\$	13.02

Total Amount Requesting.	\$384.98
--------------------------	----------



3820 FABER PLACE • SUITE 200 • NORTH CHARLESTON, SC 29405
(843) 572-4363 • FAX (843) 572-9609
www.gulfstreamconstruction.com

To:	Balfour Beatty - Charlotte Division	Contact:	Nick Starcevic
Address:	100 N Tyron Charlotte, NC 28202	Phone:	
Project Name:	Hotel At Marion Square - COR30 Demo Mockups	Bid Number:	
Project Location:	404 King Street, Charleston, SC	Bid Date:	8/17/2018

Item Description	Estimated Quantity	Unit	Total Price
Demo Original Mockup	1.00	LS	\$15,852.11
Demo Mockup Addns:	1.00	LS	\$21,336.35

Total Bid Price: \$37,188.46

ACCEPTED:

The above prices, specifications and conditions are satisfactory and are hereby accepted.

Buyer: _____

Signature: _____

Date of Acceptance: _____

CONFIRMED:

Gulf Stream Construction Company

Authorized Signature: _____

Estimator: Mark Hylton, V.P., PE, LEED AP
(843) 572-4363 mhylton@gulfstreamconstruction.com

DECO (Demolition Environmental Company, LLC)

PO Box 61900

North Charleston, SC 29419

843-554-8408 Phone

843-554-8409 Fax

Celebrating 15 years of Service!

March 28, 2019

Mark Hylton, PE, LEED®AP
Executive Vice President

Tel: 843.572.4363

Mobile: 843.296.8236

Fax: 843.572.9609

Email: mhylton@gulfstreamconstruction.comWeb: www.gulfstreamconstruction.com1983 TECHNOLOGY DR
CHARLESTON, SC 29492**RE: Hotel at Marion Square Mock Up Demo**

DECO proposes to furnish all labor, material, equipment, and supervision necessary to perform the scope of work associated with the complete demolition site visit see break down below:

Demolition of mock up panels	\$11,112.00
------------------------------	-------------

SCOPE OF WORK: From site visit**INCLUDES:**

- 1) Demolition of vertical walls of mock ups

EXCLUDES:

- 1) Hauling and disposal of the structures.
- 2) Foundation demolition.
- 3) City or County Permitting

ASSUMPTIONS:

- 1) All work will be performed under one mobilization
- 2) **DECO will retain all rights to salvaged materials.**
- 3) All work to be performed during normal working hours Monday – Friday
- 4) All Utility Disconnects will be handled by others. IE (Electric, Water, Sewer, Gas, fiber optics etc.).
- 5) DECO Will not be held liable for utility disconnects that were not completed prior to demolition

INSURANCE:

DECO maintains a standard 2 million dollar aggregate insurance coverage. With a five million dollar umbrella coverage for both comprehensive general liability and workman's comp. DECO also carries a 1 million dollar Pollution policy that is demolition and asbestos specific.

COMPANY BACKGROUND:

DECO has become a unique provider of a full range of demolition, abatement, site development, and environmental site remediation service. Our skilled staff and specialized equipment deliver safe and efficient solutions for all demolition and environmental needs. Our management has over 20 years' experience in the demolition, construction, and equipment industries.

DECO has become a market leader in the demolition industry by successfully providing our services to a wide range of projects including large scale commercial developments, industrial facilities, and government/municipal facilities. We pride ourselves providing our customers professional, safe, and efficient execution of the designated work to meet their needs. The goal of DECO is to exceed the scheduling and cost performance goals of the customer while following all applicable safety and health regulations.

We sincerely appreciate the opportunity to quote this project. Should you have any questions or require additional information, please do not hesitate to contact me.

Sincerely,

DECO

Brian Hillen
Vice President

Professional, Reliable



Change Order Request

Date: 7/2/2018

Request # 79

Attention: Balfour Beatty- Alec Dooley/ Nick Starcevic

Project Name: Marion Hotel

From: Scott McCormack

RE: Paint Redwood Pergola Per BAR

Date	Description	Foreman		Journeyman		Material		Line Item Total
		Units	Unit Costs	Units	Unit Costs	Units	Unit Costs	
7/2/2018	In lieu of stain, prep cedar pergola to accept exterior paint finish and apply one prime coat and one coat of exterior wood paint per BAR comments and mock-up approval	90	\$45.00	180	\$40.00	1	\$1,236.55	\$12,486.55
								\$0.00
								\$0.00
								\$0.00
								\$0.00
	Subtotals	90	\$4,050.00	180	\$7,200.00		\$1,236.55	\$12,486.55

Sales Tax	9.0%	\$111.29
Subtotal		\$12,597.84
O&P	15%	\$ 1,889.68
P&P Bond	3.5%	\$ 507.06

TOTAL LABOR and MATERIAL	\$14,994.58
--------------------------	-------------

Change Order Request Summary

Strong Tower Construction, LLC, dba Koch Corporation
1131 Logan Street
Louisville, KY 40204

Date (mm/dd/yy) August 6, 2018

Change Order Request Koch # 006

Project Name Hotel at Marion Square
Project Number 2759 Charleston, SC
Subcontract No./Package

Change Order Type

Work Order # 6

Pricing Type

Type of Contract

Lump Sum
6 Work Days

Description of Work: Furnish labor and material to remove mockup door from mockup area and install into the building

Engineering/Drafting not required.

A. Labor Summary (including fringe benefits)

Standard Hours and Rate				Premium Hours and Rate				Classification	
Fab		hours x	\$ 54.71 /hour +		hours x	\$ 82.07 /hour =	\$ -	Shop Labor, Curtain	13-10
Fab Super		hours x	\$ 64.68			\$ 97.02 /hour =	\$ -	Shop Labor - Supen	13-52
Fab Delivery		hours x	\$ 54.71 /hour +		hours x	\$ 82.07 /hour =	\$ -	Shop Labor, Load, E	13-15
Field Install	80	hours x	\$ 54.71 /hour +		hours x	\$ 82.07 /hour =	\$ 4,376.80	Curtain Wall, Ladder	1-50
Field Caulking	12	hours x	\$ 54.71 /hour +		hours x	\$ 82.07 /hour =	\$ 656.52	Caulking, Exterior w	1-30
Field		hours x	/hour +		hours x	\$ - /hour =	\$ -	#N/A	
Field		hours x	/hour +		hours x	\$ - /hour =	\$ -	#N/A	
Field Foreman	8	hours x	\$ 71.58 /hour +		hours x	\$ 107.37 /hour =	\$ 572.64	Field, Superintendent	1-100
Field Superinter		hours x	\$ 86.93 /hour +		hours x	\$ 130.40 /hour =	\$ -	Field, General Super	1-95
Project Mgr	2	hours x	\$ 135.00 /hour				\$ 270.00	Project Management	15
Engineering		hours x	\$ 125.00 /hour				\$ -	Drafting and Engine	13
Drafting		hours x	\$ 85.00 /hour				\$ -	Drafting and Engine	13

Labor Summary (including Fringe and Burden)

- B. Equipment Rental
C. Owned Equipment
D. Trucking (\$3.25 / mile for Flatbed Truck, to Site and back to Shop)
E. Other (type Description of item)
F. Travel and Per Diem

Miles One Way =

Total (A)	\$ 5,875.96
Total (B)	\$ 416.67
Total (C)	
Total (D)	\$ -
Total (E)	
Total (F)	\$ 1,487.50

Fasteners

Caulking

Material Subtotal 1	\$ 40.69
Material Subtotal 2	\$ 87.75
Material Subtotal 3	\$ -
Material Subtotal 4	\$ -
Material Subtotal 5	\$ -
Material Subtotal 6	\$ -
Material Subtotal 7	\$ -
Material Subtotal 8	\$ -
Material Subtotal 9	\$ -
Material Subtotal 10	\$ -
Material Subtotal 11	\$ -
Material Subtotal 12	\$ 69.03

Miscellaneous Material

- G. Material (Tax is included if a non-exempt job)
H. General Conditions
I. Worker's Comp, General Liability Insurance
J. Koch Overhead
K. Koch Profit
L.

x 1.53% (0% if enrolled in CCIP)
x 10.0%
x 5.0%

Material Total (G)	\$ 197.47
Total (H)	
Total (I)	\$ 122.06
Total (J)	\$ 809.97
Total (K)	\$ 445.48
Total (L)	\$ 9,355.10

- M. Subcontractor Tier Cost
N. Subcontractor Tier Markup

x

Total (M)	
Total (N)	\$ -

O.

P. Bond

Q.

Sub Total (A - N)	\$ 9,355.10
Total (P)	\$ 209.55
GRAND TOTAL (Sub Total + P)	\$ 9,564.65

Print Name: PM - Larry Vihlidal


Prepared By Signature:

Print Name: Operations Manager - Darren Beagle

Reviewed By Signature:

Print Name: President - Benjamin Feinn

Approved By Signature:



Date: February 7, 2018

Job: Hotel at Marion Square

Attn: Nick Starcevic – Balfour Beatty Construction

RE: COR#21 – Shutter Mock Up

Scope of Work

Shutters – associated cost with providing and installing five shutters complete with black powder coated hinges and holdbacks for complete provision

Quote: \$7,283.00

Thank you for allowing Warco Construction the opportunity to contribute to this project. If you have any questions or concerns, feel free to contact me at (704) 521 5200.

Thank you,

A handwritten signature in black ink, appearing to read 'Nick Peak', written in a cursive style.

Nick Peak
Warco Construction Inc.

3910 Stuart Andrew Blvd
Charlotte, North Carolina 28217

(704) 521 5200
Fax (704) 521 5199

Tab No. 259

Balfour Beatty Construction

August 30, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 259
Hudson Street Storm Repair

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 259 in the amount of Thirty-three thousand three hundred ninety-eight (\$33,398.68) to provide additional work in accordance with the following qualifications:

Hydro Vac and construct new storm box. Detail cost breakdown from Gulf Stream below.

1. Labor and Equipment [\$12,000] - Our crews are worth \$5,000/day on any jobsite they are able to work productively on. We plan on this work taking 4 days of their time and have only charged you \$3,000/day as hopefully we will be able to keep a few guys from the crew busy at another project or elsewhere on your project.

2. Hydro-Ex Sub [\$2875] - Sub cost \$275/hour, 4 hour minimum, and \$425/load to dispose. I estimate 6 hours and 2 loads to be disposed, +15% GSCC Markup. If we don't excavate in the correct location the first time, there could be more cost here that we will end up eating.

3. Materials [\$3,700] -

a. 5CY mix for bottom slab, \$750.

b. 57 Stone for foundation, \$200.

c. 5CY Flow Fill, \$750.

d. Precast top slab, ring and cover, \$1,200.

e. Misc. Masonry Supplies (Sand, mortar, block, mixer rental), \$800

f. Small tools, chop saw blades, trowels, ect

Total rough cost above of \$18,575.00 should cover GS if everything goes as planned. This is what is carried in our proposal (\$18,808).

Per Ted Barker, the city requires the road to be milled and overlaid, with the milled area to extend from curb-line to curb-line, 2' beyond the cut.

*No cost for asphalt patching is included. GS will not be charging for this.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set forth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Balfour Beatty Construction

Sincerely,



Nick Starcevic
Project Manager

cc:

Jennifer Faulkinberry

Jim Clements

Jenny Palmer

David Simonton

Tim Spano

RCO # 259 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 259- Hudson Street Storm Repair

The additional work for the **Hudson Street Storm Repair** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50200000.40	Hudson Street Storm Repair	\$29,408.19
2		Protection, Clean Up, and Gate Guards	\$2,100.00

Total Items \$31,508.19

Total Markups \$1,890.49


RCO Total \$33,398.68


The total Cost to perform the work as described above is an ADD of Thirty-three thousand three hundred ninety-eight (\$33,398.68).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: Kim Brown, Library Associates, LLC Date: _____

RCO# 259

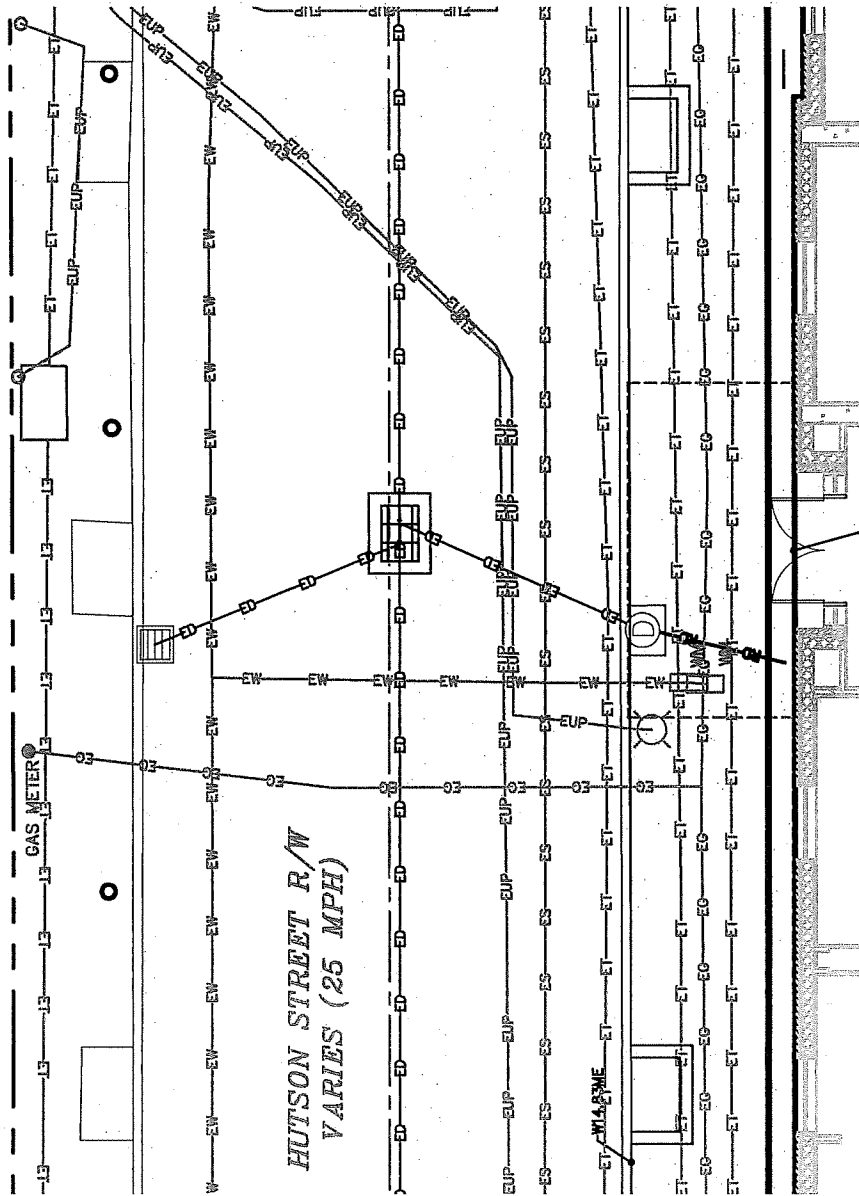

REFERENCES NATIONAL DOCUMENTS SCDOT DOCUMENTS RELATED DRAWINGS & NETWORKS		GENERAL NOTES 1.01 WORK ALL APPROPRIATE SHEETS TOGETHER 1.02 WHEN LOCATING DRAINAGE STRUCTURES THAT ARE IN CONFLICT WITH UTILITIES, FOUNDATIONS, RETAINING WALL COMPONENTS, GUARDRAIL POSTS, OR OTHER SUBSURFACE STRUCTURES, NOTIFY THE ENGINEER BEFORE RELOCATING EITHER CONFLICTING PART. 1.03 THIS GENERAL NOTES SECTION WILL BE IMPLEMENTED BEFORE SECTION 719 IS UPDATED. SO NOTES HERE MAY BE DUPLICATED OR IN CONFLICT WITH NOTES ON THE INDIVIDUAL DRAWING PAGES. WHEN THIS GENERAL NOTE SECTION CONFLICTS WITH EITHER THE STANDARD SPECIFICATION OR THE NOTES ON A STANDARD DRAWING WITHIN THE 719 SECTION, NOTES IN THIS SECTION SHOULD BE USED. ENGINEER MAY OVERRULE THIS METHOD IF SUFFICIENT JUSTIFICATION IS PROVIDED THAT THE OTHER NOTE IS APPROPRIATE FOR THE SITE. 1.04 FOLLOW ALL OSHA REGULATIONS INCLUDING LIFTING AND TRENCH REQUIREMENTS.		15.00 REFERENCES 15.01 QPL 14 PRECAST DRAINAGE STRUCTURES 15.02 QPL 28 READY MIX CONCRETE PLANTS 15.03 QPL 30, 68, 69 PIPE CULVERTS 15.04 QPL 45 STEEL FRAMES, GRATES, AND RISERS FOR DRAINAGE STRUCTURES 15.05 QPL 45 CAST IRON FRAMES, GRATES, AND RISERS FOR DRAINAGE STRUCTURES (WHEN AVAILABLE) 15.06 QPL 48 SURFACE ADJUSTMENT RISERS FOR DRAINAGE STRUCTURES (UNLESS MERGED INTO QPL 45) 15.07 QPL 60 REINFORCING STEEL	
5.00 MATERIALS 5.01 USE CLASS 4000P OR HIGHER PRECAST CONCRETE COMPONENTS AS INDICATED ON THE STANDARD DRAWING FROM A SINGLE SOURCE FOR EACH DRAINAGE STRUCTURE LOCATION. 5.02 USE CLASS 4000 OR HIGHER CAST IN PLACE CONCRETE AS INDICATED ON THE STANDARD DRAWING. 5.03 USE ASTM A706 GRADE 60 DEFORMED BARS OR AASHTO M 55 OR M 221 WIRE MESH FOR REINFORCEMENT STEEL 5.04 USE 2500 PSI OR HIGHER MASONRY UNITS CONFORMING TO ASTM C 55 GRADE S-II FOR CONCRETE BRICK, ASTM C 139 FOR SOLID CONCRETE BLOCK (NO LARGER THAN 4X8X16), OR AASHTO M 114 GRADE SW FOR CLAY BRICK. 5.05 USE TYPE S OR M MORTAR FOR MASONRY CONSTRUCTION 5.06 USE ONLY NON-SHRINK GROUT. 5.07 USE EITHER GRAY IRON (AASHTO M 105 CLASS 35B) OR DUCTILE IRON (ASTM A 536) CASTINGS TESTED IN ACCORDANCE WITH AASHTO M 306 FOR 40 KIP PROOF LOAD (HEAVY DUTY) OR 25 KIP PROOF LOAD (LIGHT DUTY MANHOLE COVER ONLY). 5.08 CORROSION PROTECTED STEEL RISERS, FRAMES, AND GRATES MAY BE USED WHERE REQUIRED AS LONG AS THEY MEET AASHTO M 306 PROOF LOAD OF 40 KIP (HEAVY DUTY), AND ARE PROTECTED FROM CORROSION WITH GALVANIZING, SUPER DURABLE POWDER COATING, OR AT LEAST 3 COATS OF EPOXY PAINT OR COLD GALVANIZING COMPOUND ON ALL SURFACES. STEEL GRATES MUST BE BOLT-DOWN FOR ALL LOCATIONS SUBJECT TO TRAFFIC. 5.09 USE A NONWOVEN GEOTEXTILE FOR DRAINAGE FILTRATION TO WRAP RISER JOINTS. 5.10 USE AT LEAST 6" THICK PRECAST WALLS, OR 8" THICK BRICK MASONRY WALLS. USE THICKER WALLS WHEN REQUIRED BY THE STANDARD DRAWING, INDUSTRY STANDARDS, OR CUSTOM DESIGN REQUIREMENTS. 5.11 PROVIDE FOUNDATION MATERIALS, BEDDING MATERIALS, GEOTEXTILE WRAP, AND GEOGRID IMPROVED FOUNDATION MATERIAL IN CONFORMANCE WITH SC-M-714 OR SECTION 714 OF THE STANDARD DRAWINGS.		15.00 LIMITATIONS 15.01 DO NOT CONSTRUCT PRECAST KNOCKOUT BOXES DEEPER THAN THE BOX HEIGHT PLUS 30". DO NOT USE RISERS OR TRANSITION SLABS WITH KNOCKOUT BOXES. INLET ADAPTER SLABS MAY ONLY BE USED IF INLET STRUCTURE AND INLET ADAPTER SLAB FIT WITHIN THE 30" LIMITATION. 15.02 DO NOT USE BRICK MASONRY WALLS WHEN THE FLOW LINE OF ANY INLET PIPE IS HIGHER THAN 4 FEET ABOVE THE BOTTOM SLAB OR TRANSITION SLAB AT THE BASE OF THE MASONRY WITHOUT WRITTEN APPROVAL FROM THE DEPARTMENT [SCOUR ON MORTAR]. 15.03 DO NOT CONSTRUCT BRICK MASONRY DRAINAGE STRUCTURES DEEPER THAN 12'. BRICK MASONRY EXTENSIONS MAY BE BUILT ON TOP OF INLET ADAPTER SLABS WHEN THE EXTENDED PORTION IS NO DEEPER THAN 12' AND THE STRUCTURE BELOW IS PRECAST. GROUT FILLER WITH BRICK SHIMS MAY BE USED DEEPER THAN 12' TO PATCH PREFORMED HOLES IN PRECAST STRUCTURES ONLY AROUND PIPE CONNECTIONS. OVERALL THICKNESS OF GROUT FILLER AT THESE LOCATIONS SHOULD BE AT LEAST 1 1/2 THE BURY DEPTH OF THE FILLER (IE. AT LEAST 20" THICK FOR 20' OF COVER). DO NOT USE GROUT OR BRICK MASONRY FILLER AS A REPLACEMENT FOR PRECAST REQUIREMENTS AT THESE DEPTHS. 15.04 DO NOT CONSTRUCT STANDARD SOLID WALL PRECAST DRAINAGE STRUCTURES (CIRCULAR OR RECTANGULAR) DEEPER THAN 35' (ASSUMES 30" MAX PIPE COVER + 48" PIPE + BOTTOM SLAB & PIPE WALL). 15.05 FOR DRAINAGE STRUCTURES (AS WITH PIPE CULVERTS), WHEN THE OVERALL DEPTH EXCEEDS 30', USE A CUSTOM DESIGNED STRUCTURE AS SHOWN IN THE PROJECT PLANS OR PROVIDE A CUSTOM DESIGNED STRUCTURE WHEN NOT PROVIDED IN THE PROJECT PLANS. 15.06 SEE DRAINAGE STRUCTURE PARTS SHEETS FOR MISCELLANEOUS PARTS TO CREATE MORE SITE-SPECIFIC ASSEMBLIES. 15.07 SEE PROJECT PLANS FOR NON-STANDARD CATCH BASIN DETAILS. 15.08 CONSTRUCT BRICK MASONRY STRUCTURES ONLY AS SQUARE, CIRCULAR, OR RECTANGULAR WITH VERTICAL WALLS. DO NOT TAPER, CORBEL, OR VARY THE RUNNING BOND BRICK LAY PATTERN. MINIMUM DIAMETER OF CIRCULAR BRICK STRUCTURES IS 4 FEET. FOR ALL BRICK STRUCTURE TYPES, USE EITHER PRECAST TOP SLAB, TRANSITION SLAB, OR A CAST IRON FRAME DESIGNED TO SIT DIRECTLY ON BRICK WALLS. 15.09 USE NO MORE THAN ONE TRANSITION SLAB AND ONE INLET ADAPTER SLAB IN A SINGLE STRUCTURE. WHEN A LARGER BOX IS REQUIRED TO ACCOMMODATE LARGE OR MULTIPLE PIPE, ONE TRANSITION SLAB MAY BE USED TO ADJUST THE LARGER LOWER BOX TO THE STANDARD UPPER BOX CONSTRUCTED FOR THE DRAINAGE STRUCTURE. AN ADDITIONAL INLET ADAPTER SLAB MAY BE USED WHEN THE CASTING OR THROAT REQUIRES THE USE OF THIS PIECE. LOCATE TRANSITION AND INLET ADAPTER SLABS AT LEAST 8 INCHES AWAY FROM HOLES FOR PIPE.			
THIS DRAWING IS ONLY VALID FOR CONSTRUCTION WHEN SEALED AND SIGNED BY A PROFESSIONAL ENGINEER REGISTERED IN THE STATE OF SOUTH CAROLINA. CHECK WWW.SCDOT.ORG FOR LATEST UPDATE.  7/20/2015 12/17/2015		SCDOT DESIGN STANDARDS OFFICE 1000 SOUTH STREET COLUMBIA, SC 29201 STANDARD DRAWING DRAINAGE STRUCTURE GENERAL NOTES			
719-000-01 EFFECTIVE LIFTING DATE		719-000-01 JAN. 719			

20.00	PEDESTRIAN, BICYCLE, CONTROLLED ACCESS, AND TRAFFIC	30.06	INCLUDE FABRICATION MARKINGS ON EACH PIECE THAT IDENTIFY MANUFACTURER NAME AND DATE, APPLICABLE SCOT OR ASTM SPECIFICATION, SIZE, AND MAXIMUM BURY DEPTH. LOCATE MARKINGS ON EXTERIOR WALLS OR ON TOP OF SLABS FOR ALL PARTS EXCEPT SURFACE SLABS USED IN SIDEWALK.	REFERENCES
20.01	WITHIN THE PEDESTRIAN ACCESS ROUTE (SIDEWALKS, CROSSWALKS, ACCESSIBLE PARKING, ETC.) USE ONLY DRAINAGE SYSTEMS DESIGNATED AS ADA COMPLIANT.	30.07	FABRICATE KNOCKOUT BOXES WITH FLAT JOINTS AT THE TOP OR WITH A FULLY GROUTED KEY JOINT. RISERS (719-310-00 DETAIL 1) ARE NOT ALLOWED ABOVE KNOCKOUT BOXES. IF A GROUTED KEY JOINT IS PROVIDED, MANUFACTURER MUST DETAIL THE FULL HEIGHT OF THE KEY TO EXTEND ABOVE THE 6" MINIMUM TOP BEAM HEIGHT ON THE BOX AND FULLY GROUT THE KEY EITHER IN THE PLANT OR IN THE FIELD PRIOR TO INSTALLATION OF THE UPPER STRUCTURE. DO NOT LEAVE AIR POCKETS IN GROUTED PORTIONS OF TOP KEY TO ENSURE FULL CONTACT BETWEEN THE KNOCKOUT BOX TOP BEAM AND THE UPPER STRUCTURE.	SCOT DOCUMENTS
20.02	LOCATE BICYCLE RATED GRATES OUTSIDE OF THE PEDESTRIAN ACCESS ROUTE. SET BICYCLE RATED GRATES FLUSH TO WITHIN +0" TO - 1/4" OF ADJACENT PAVEMENT GRADE OR FLUSH TO WITHIN +0" TO - 1" OF ADJACENT SOIL FOR NON-PAVED LOCATIONS.	30.08	DO NOT EXTEND REINFORCING STEEL THROUGH KNOCKOUT PORTION OF THE BOX WALLS.	RELATED DRAWINGS & KEYWORDS
20.04	INSTALL CONTROLLED ACCESS STRUCTURES ONLY IN LOCATIONS WHERE PEDESTRIANS AND BICYCLES ARE PROHIBITED (TYPICALLY INTERSTATE). DO NOT INSTALL THESE STRUCTURES WITHIN 200 FEET OF RAMP CONNECTIONS TO NON-INTERSTATE ROUTES.	30.09	MAXIMUM KNOCKOUT PANEL HEIGHT IS 5 FEET. MAXIMUM KNOCKOUT BOX BURY DEPTH (D) FROM TOP OF SIDEWALK EQUALS H + 2.5 FEET COVER FROM FINISHED GRADE TO TOP OF BOTTOM SLAB, NO EXCEPTIONS. H2 => D4.5', H2.5 => D5', H3 => D5.5', H4 => D6.5', H5 => D7.5', & H6 => D8.5' (MAX).	THIS DRAWING IS ONLY VALID FOR CONSTRUCTION WHEN SEALS AND SIGNED BY A PROFESSIONAL ENGINEER REGISTERED IN THE STATE OF SOUTH CAROLINA. CHECK WWW.SCOT.ORG FOR LATEST UPDATE.
20.05	WHERE PRACTICAL, LIMIT THE PLACEMENT OF DRAINAGE STRUCTURES WITHIN TRAVEL LANES. WHEN DRAINAGE STRUCTURE IS REQUIRED, USE ONLY A HEAVY DUTY RATED SYSTEM WITHIN PAVEMENT, GUTTER OR DRIVEWAYS.	30.10	WHEN EXTENDING KNOCKOUT BOX HEIGHT (719-310-00 NOTE 14) FOR INLET WALLS, USE ONLY THE FULL 6" WALL THICKNESS AND REINFORCE THE EXTENDED PORTION CONSISTENT WITH A SOLID WALL RISER SECTION (719-315-00) OF EQUAL SIZE.	REGISTERED PROFESSIONAL ENGINEER SOUTH CAROLINA NO. 21242 JAMES W. KENDRICK SIGNATURE
25.00	ACCESS	30.11	REQUESTS FOR ALTERATIONS TO DESIGN LIMITS SHOW IN THE STANDARD DRAWING MUST INCLUDE SHOP DRAWINGS AND STRUCTURAL DESIGN CALCULATIONS SEALED BY A PROFESSIONAL ENGINEER REGISTERED IN SOUTH CAROLINA FOR REVIEW PRIOR TO FABRICATION FOR EACH VARIATION.	DATE 10/22/2015
25.01	PROVIDE STEPS (719-5XX-XX) IN ALL DRAINAGE STRUCTURES DEEPER THAN 54". LOCATE STEPS WITHIN REASONABLE PROXIMITY TO ACCESS POINT (MANHOLE OR GRATE OPENING) WITHOUT INTERFERING WITH PIPE ORIENTATIONS.	35.00	CAST IRON & STEEL FABRICATION	6
25.02	WHERE PRACTICAL, ALIGN BOX WALL WITH STEPS WITHIN 6" OF HOLES IN INLET ADAPTER AND TRANSITION SLAB. WHERE PRACTICAL, ALIGN ALL ACCESS HOLES VERTICALLY AND OF THE SAME SIZE AND SHAPE AS THE UPPER ACCESS POINT. IF STANDARD INLET ADAPTER OR TRANSITION SLAB RESTRICTS OPENING GEOMETRY, ALIGN THE STANDARD OPENING TO MAXIMIZE WORKER ACCESS.	35.01	FABRICATE ALL STEEL AND IRON COMPONENTS IN ACCORDANCE WITH SECTION 106.11 OF THE STANDARD SPECIFICATIONS.	5
25.03	WHEN OPENINGS ARE NOT ALIGNED, PROVIDE ENOUGH VERTICAL SEPARATION BETWEEN SLABS TO FACILITATE MANEUVERING TO OTHER ACCESS HOLE AND FEEDING CLEANOUT EQUIPMENT THROUGH LOWER HOLE (TYPICALLY 7" VERTICAL). IN THIS CASE, PROVIDE A SECOND LADDER RUN THAT EXTENDS FROM THE BOTTOM SLAB TO AT LEAST 3 FEET ABOVE THE TRANSITION SLAB AND IS LOCATED ON THE CLOSEST WALL TO THE TRANSITION SLAB OPENING.	35.02	ENSURE FULL CONTACT BETWEEN GRATE, RISER, AND FRAME SEATS. MACHINE SURFACES WHEN NECESSARY TO ACHIEVE EVEN CONTACT.	4
		35.03	IN ADDITION TO STANDARD FOUNDRY MARKINGS, MARK ALL PIECES WITH "DUMP NO WASTE" AND "DRAINS TO WATERWAY". WHERE SPACE PERMITS, ALSO INCLUDE SCOT LOGO AND ANY OTHER PATTERN INDICATED ON THE INDIVIDUAL CASTING SHEET.	3
		35.04	WHERE SHOWN, PROVIDE A CAGED NUT BOLT DOWN DETAIL USING A STANDARD HEX-HEAD BOLT.	2
30.00	PRECAST FABRICATION	40.00	FOUNDATION, BASE & BOTTOM SLABS	1
30.01	PROVIDE STEPS INDICATED IN THE ACCESS SECTION.	40.01	WHEN THE PROJECT PLANS SPECIFY IMPROVED FOUNDATION FOR PIPE, EXTEND THIS UNDERCUT AND IMPROVED PROCEDURE THROUGH AND UNDER THE FOOTPRINT OF THE BASE SLAB OF THE DRAINAGE STRUCTURE.	0
30.02	WHERE LIFTING DEVICES ARE REQUIRED, PROVIDE LIFT HOLES NO LARGER THAN 3.05" DIAMETER OR STEEL LUGS OR HOOKS THAT ARE FULLY RECESSED BELOW THE SURFACE, OR CAN BE CUT OFF BELOW THE SURFACE BEFORE GROUTING CLOSED.	40.02	USE THE SAME FOUNDATION AND BEDDING DETAIL ESTABLISHED FOR THE PIPE CULVERTS (SEE STANDARD DRAWING SECTION 714).	172016
30.03	FABRICATE SLAB WITH A BROOMED TOP SURFACE FINISH AND FABRICATE FLAT UNLESS KEYS OR LAP JOINTED DETAIL IS ORDERED BY THE CONTRACTOR.	40.03	WHEN CONSTRUCTING THE ENTIRE WALL SYSTEM OF THE DRAINAGE STRUCTURE FROM BRICK MASONRY, CONSTRUCT A REINFORCED CONCRETE BASE SLAB MEETING THE THICKNESS AND REINFORCEMENT SHOWN FOR THE SAME SIZE PRECAST RECTANGULAR BOX (719-3XX-XX). A PRECAST BASE SLAB MAY ALSO BE USED AS REQUIRED TO FACILITATE THE MASONRY CONSTRUCTION. LEVEL THE BASE SLAB BEFORE CONSTRUCTING BOX WALLS.	NEW
30.04	FABRICATE PRECAST SLABS WITH SYMMETRICAL REINFORCEMENT OR PROVIDE LIFTING LUGS AND MARKINGS INDICATING TOP SIDE OF SLAB.	40.04	FOR SITES WHERE A CUSTOM PIPE FOUNDATION IS REQUIRED, CONSTRUCT A CUSTOM DRAINAGE STRUCTURE FOUNDATION AS SPECIFIED IN THE PLANS OR SPECIAL PROVISION.	DESCRIPTION
30.05	WHERE STANDARD REQUIRES EMBEDMENT OF A CAST IRON OR STEEL FRAME, USE ONLY FRAMES FROM A QUALIFIED SOURCE, AND EMBED INTO PRECAST PART IN ACCORDANCE WITH INDUSTRY STANDARDS. WHEN FRAME IS EMBEDDED, SUPPLY CORRESPONDING CAST IRON OR STEEL RISERS, GRATES, OR COVERS FROM THE SAME FOUNDRY AS THE FRAME EMBEDDED IN THE PRECAST PIECE. CONFIRM FULL CONTACT BETWEEN THE GRATE, RISERS, AND FRAME BEFORE POURING THE PIECE. AFTER FABRICATION, THOROUGHLY CLEAN THE SEAT AND EDGE TO REMOVE ANY CONCRETE FROM THE PRECAST OPERATION. CONFIRM PROPER SEATING OF CAST IRON PARTS BEFORE SHIPPING ASSEMBLY.	40.05	SET AND LEVEL BASE SECTION OR BOTTOM SLAB SO THAT WALLS ARE CONSTRUCTED WITHIN 1 DEGREE OF PLUMB PRIOR TO BACKFILLING (NO MORE THAN 6" HORIZONTAL OVER 30" VERTICAL). ALL ADJUSTMENTS REQUIRED TO MEET SURFACE SLOPES SHOULD OCCUR WITHIN 2 FEET OF THE FINISHED GRADE.	DESIGN STANDARDS OFFICE 955 PARK STREET ROOM 405 COLUMBIA, SC 29201

REFERENCES		45.00 PIPE CONNECTIONS AND GROUTING		50.04 FOR BOXES DEEPER THAN 12' WRAP THE EXTERIOR OF THE BOX (FULL HEIGHT OF STRUCTURE) WITH NONWOVEN GEOTEXTILE FOR DRAINAGE FILTRATION TO PREVENT THE MOVEMENT OF SOIL THROUGH THE JOINTS. TAPE THE GEOTEXTILE TO THE BOX WALL/ITSELF USING WEATHERPROOF TAPE AND A 1 FOOT OVERLAP PRIOR TO BACKFILLING AROUND THE BOX. ALTERNATELY, TAPE 1 FOOT WIDE STRIPS OF NONWOVEN GEOTEXTILE AROUND THE ENTIRE PERIMETER OF THE BOX AT EACH RISER JOINT (FULL HEIGHT OF STRUCTURE). IF THE PLANS INDICATE THAT GROUNDWATER WILL NOT BE PRESENT AT THE 12' OR DEEPER DRAINAGE STRUCTURE, SEAL THE EXTERIOR JOINTS WITH COLD APPLIED WATERPROOFING OR JOINT TAPE PRIOR TO BACKFILLING. IF FILTERED WEEPING THROUGH THE RISER JOINTS IS PREFERRED WHEN THE STRUCTURE IS DEEP AND GROUNDWATER IS PRESENT TO MINIMIZE BUOYANCY EFFECTS.]	
RELATED DOCUMENTS		45.01 PROJECT PIPE THROUGH THE INSIDE FACE OF THE BOX (AND FIELD CUT IF NECESSARY) 1" (+/- 1/4") BEYOND THE INSIDE FACE WHEN MEASURED AT THE SPRINGLINE OF THE PIPE. THIS FINISHED PROJECTION IS REFERRED TO AS "FLUSH" IN THIS AND OTHER SPECIFICATIONS. AND IS PREFERRED TO GET A PROPER SEAL AROUND THE PIPE. NOTE THAT PIPE ENTERING THROUGH THE CORNER OF A BOX OR THROUGH CIRCULAR DRAINAGE BASES WILL PROJECT FURTHER IF MEASURED AT THE TOP AND BOTTOM OF THE PIPE, AND THAT THIS ADDITIONAL PROJECTION SHOULD BE FULLY GROUTED TO MINIMIZE DEBRIS SNAG POINTS.		50.05 FOR CAST OR STEEL FRAMES PLACED DIRECTLY ON BRICK OR CONCRETE, USE EITHER A NON-SHRINK GROUT LIFT OR A PREFABRICATED RISER/GASKET SPECIFICALLY MADE FOR THIS INTERFACE. FOLLOW THE MANUFACTURER'S INSTALLATION INSTRUCTIONS WHEN USING PREFABRICATED RISER/GASKET SECTIONS BELOW THE FRAME. ALIGN FRAME PARALLEL TO THE PAVEMENT SURFACE (IF APPLICABLE) SO THAT FINISHED GRADE ELEVATION SITS FLUSH WITH (UP TO 1/2" BELOW) SURFACE COURSE.	
STANDARD DRAWING		45.02 SKEWED PIPE MAY BE REQUIRED TO EXTEND FURTHER INTO PIPE TO FACILITATE THE FLUSH CUT. FLUSH CUT EACH SKEWED PIPE TO FACILITATE THE PROJECTION AND FLUSH CUTTING OF ANY OTHER SKEWED PIPE INSIDE THE BOX.		50.06 COMPLETELY REMOVE LIFTING DEVICES FROM TOP SLABS, AND ALL SLABS WHERE A WORKER WILL STAND. CLOSE ANY RECESSES OR LIFT HOLES IN SLABS THAT FORM THE SIDEWALK SURFACE WITH GROUT. FOR BELOW GRADE HOLES LESS THAN 3.05" DIAMETER, GROUT, PLUG, OR COVER WITH TAPED GEOTEXTILE PRIOR TO BACKFILLING.	
DRAINAGE STRUCTURE		45.03 FULLY GROUT THE PERIMETER OF THE PIPE TO FILL THE BOX WALL OPENING. PERFORM THIS GROUTING AS SOON AS ALL PIPE ARE INSTALLED WITHIN THE BOX OR WHEN DIRECTED BY THE ENGINEER (TYPICALLY PRIOR TO A PREDICTED RAIN EVENT TO PREVENT TRENCH MATERIAL FROM CLOGGING THE BOX WALL OPENING.) IN THE EVENT THAT DEBRIS HAS ENTERED THE BOX WALL OPENING, PRESSURE WASH THIS AREA FROM THE INSIDE OF THE BOX TO REMOVE FOREIGN MATTER PRIOR TO GROUTING.		55.00 BACKFILLING	
GENERAL NOTES		45.04 ON THE INSIDE FACE OF THE BOX, BEVEL THE GROUT THE FULL AMOUNT OF EACH PIPE PROJECTION AND TO FULLY COVER THE BOX WALL OPENING WITH 1" OVERLAP. ON THE OUTSIDE FACE OF THE BOX, PACK GROUT UNDER THE PIPE TO FILL ANY GAPS IN THE PIPE BEDDING/FOUNDATION DIRECTLY AT THE BOX AND BEVEL GROUT AROUND THE PERIMETER OF THE PIPE TO FULLY COVER THE BOX WALL OPENING WITH 1" OVERLAP.		55.01 USE PIPE SELECT BACKFILL AND COMPACTION METHODS DESCRIBED IN SC-M-714 FOR SOIL AROUND THE ENTIRE PERIMETER OF THE BOX WITHIN EACH PIPE EMBEDMENT ZONE AND THE TRENCH EXCAVATION CREATED TO INSTALL THE BOX AND PIPE(S). WHEN WRAPPING THE PIPE STRUCTURAL BACKFILL, CONTINUE THE WRAPPING DETAIL UNDER AND AROUND THE DRAINAGE STRUCTURE.	
		45.05 WHEN TWO PIPES INSIDE THE BOX ARE WITHIN 3" OF EACH OTHER, GROUT THE FULL AREA BETWEEN THE PIPES TO CREATE A NEW INSIDE BOX WALL OR CORNER TO MINIMIZE DEBRIS SNAG POINTS.		55.02 BETWEEN PIPE EMBEDMENT ZONES, USE SOIL MEETING THE EMBANKMENT SPECIFICATION AROUND THE BOX. IF THE ENTIRE DRAINAGE SYSTEM (BOXES, PIPE, ETC.) IS INSTALLED IN A TRENCH, USE PIPE SELECT BACKFILL AROUND THE DRAINAGE STRUCTURE TO FACILITATE PROPER COMPACTION WITHIN THE TRENCH.	
		45.06 GROUT OR MORTAR THE ENTIRE FLOOR OF THE BOX UP TO THE INVERT ELEVATION OF THE LOWEST OUTLET PIPE. SLOPE THE FLOOR GROUT IN ALL DIRECTIONS TOWARDS THE OUTLET PIPE BETWEEN 2% AND 8%, BUT DO NOT COVER THE INVERT OF ANY OTHER PIPE WITHIN THE BOX. IN A BOX WHERE INLET AND OUTLET FLOW LINES ARE EQUAL, CONSTRUCT A SLIGHT TROUGH IN THE FLOOR GROUT WITH THE LOW POINT IN THE GROUT MATCHING THE FLOW LINE. PLACE FLOOR GROUTING PRIOR TO SETTING TRANSITION SLABS, INLET ADAPTERS, OR INLET STRUCTURES.		55.03 USE COMPACTION EQUIPMENT LESS THAN 3 TONS FOR COMPACTING PIPE SELECT BACKFILL AND EMBANKMENT SOILS WITHIN 3 FEET OF DRAINAGE STRUCTURE WALLS. USE SYMMETRICAL LIFTS AND COMPACTION METHODS THAT DO NOT PUSH THE DRAINAGE STRUCTURE OUT OF PLUMB TOLERANCE.	
		50.00 BOX, RISER, TRANSITIONS, INLET ADAPTERS AND INLET JOINTS		55.04 USE ONLY FLOWABLE FILL BACKFILL AROUND PIPE CULVERT AND DRAINAGE BOXES WHEN THE PIPE TRENCH IS WITHIN 2 PIPE DIAMETERS OF THE LOWER SIDE OF A RETAINING WALL STEM OR WHEN DIRECTED BY THE ENGINEER.	
		50.01 CONSTRUCT KEYED OR LAPPED JOINTS FOR ALL PRECAST SOLID WALL BOX AND RISER SECTIONS EXCEPT WHEN JOINT ATTACHES TO A FLAT ADAPTER SLAB OR BRICK CONSTRUCTION.		55.05 USE ONLY COARSE AGGREGATE BACKFILL AROUND PIPE CULVERT AND DRAINAGE BOXES WHEN THE PIPE TRENCH IS WITHIN 2 PIPE DIAMETERS OF THE HIGHER SIDE OF A RETAINING WALL STEM. TIE THE PIPE STRUCTURAL BACKFILL INTO THE WEEP SYSTEM FOR THE WALL WHERE APPLICABLE.	
		50.02 CONSTRUCT TRANSITION OR INLET ADAPTER SLABS WITH JOINT DETAIL TO MATCH RISER OR BOX ABOVE AND BELOW, OR CONSTRUCT THE SLAB FLAT AND GROUT THE INTERFACE BETWEEN THE BOX/RISERS AND THE SLAB WITH A 1/2" LIFT OF NON-SHRINK GROUT.		55.06 DO NOT EXCEED A 4' LIFT OF FLOWABLE FILL IN A SINGLE POUR AROUND A DRAINAGE STRUCTURE.	
		50.03 DO NOT USE JOINT SEALANT IN KEYED OR LAPPED BOX/RISER JOINTS UNLESS SPECIFIED BY THE PRECAST MANUFACTURER.			
DATE		7/29/2015			
BY		JAMES W. KENDALL			
SIGNATURE		[Signature]			
REGISTERED PROFESSIONAL ENGINEER		NO. 21242			
STATE OF SOUTH CAROLINA					
CHECK W/INCHES FOR LATEST UPDATE					
THIS DRAWING IS ONLY VALID FOR CONSTRUCTION WHEN SEALED AND SIGNED BY A PROFESSIONAL ENGINEER REGISTERED IN THE STATE OF SOUTH CAROLINA. CHECK W/INCHES FOR LATEST UPDATE.					
SCDOT					
DESIGN STANDARDS OFFICE					
355 PARK STREET					
COLUMBIA, SC 29201					
STANDARD DRAWING					
DRAINAGE STRUCTURE					
GENERAL NOTES					
719-000-03					
EFFECTIVE DTD DATE					


R - 1948


60.00	THROATS, APRONS, SURFACE TREATMENTS, AND FINISH WORK
60.01	WHERE REQUIRED, HAND FORM THROATED INLETS AND CONCRETE APRONS.
60.02	USE COMPACTION EQUIPMENT LESS THAN 3 TONS FOR COMPACTING ASPHALT WITHIN 3 FEET OF DRAINAGE STRUCTURE WALLS OR PROVIDE A WRITTEN PROCEDURE TO THE ENGINEER OF ALTERNATE COMPACTION METHODS THAT WILL NOT DAMAGE THE DRAINAGE STRUCTURE WALLS.
60.03	BEFORE INSTALLING CAST IRON FRAME, CONFIRM FULL AND EVEN SEATING OF RISERS, GRATE AND/OR COVER INTO FRAME. IF NECESSARY, MATCH MARK PIECES FOR LATER IDENTIFICATION.
60.04	BEFORE FINAL PLACEMENT OF METAL RISER, GRATE OR OTHER COVER, THOROUGHLY CLEAN/SCRAPE THE SEAT AND EDGE OF THE FRAME TO REMOVE EXCESS ASPHALT OR DEBRIS. CONFIRM FULL SEATING OF TOP PIECE AND TIGHTEN BOLTS IF APPLICABLE.
60.05	WHERE PRECAST COMPONENTS SERVE AS SIDEWALK SURFACE, SET ELEVATION TO MATCH SIDEWALK CROSS SLOPE AND PROFILE WITH NO MORE THAN 1/8" GRADE DIFFERENCE.
60.06	WHERE PRECAST COMPONENTS INTERFACE ROADWAY PAVEMENTS, SET ELEVATION OF SLAB TO WITHIN 1/4" OF FINISHED GRADE ELEVATION.
95.00	PAYMENT
95.01	REPAIR ANY DAMAGE TO THE DRAINAGE STRUCTURE PRIOR TO SUBMITTING PAYMENT REQUEST.
95.02	PAYMENT FOR EACH ITEM INCLUDES ALL MATERIALS AND LABOR TO COMPLETE THE FINISHED INSTALLATION SHOWN.
95.03	SEE DRAINAGE STRUCTURE PARTS SHEETS FOR MISCELLANEOUS PARTS TO CREATE MORE SITE-SPECIFIC ASSEMBLIES.

REFERENCES																																	
NATIONAL DOCUMENTS																																	

SCOTT DOCUMENTS																																	

RELATED DRAWINGS & KEYWORDS																																	

THIS DRAWING IS ONLY VALID FOR CONSTRUCTION WHEN SEALED AND SIGNED BY A PROFESSIONAL ENGINEER REGISTERED IN THE STATE OF SOUTH CAROLINA. CHECK FOR ANY CHANGES FOR LATEST UPDATE.																																	
																																	
																																	
7/29/2015																																	
DATE																																	
<table border="1"> <tr> <th>#</th> <th>DATE</th> <th>CHK</th> <th>DESCRIPTION</th> </tr> <tr> <td>6</td> <td></td> <td></td> <td></td> </tr> <tr> <td>5</td> <td></td> <td></td> <td></td> </tr> <tr> <td>4</td> <td></td> <td></td> <td></td> </tr> <tr> <td>3</td> <td></td> <td></td> <td></td> </tr> <tr> <td>2</td> <td></td> <td></td> <td></td> </tr> <tr> <td>1</td> <td></td> <td></td> <td></td> </tr> <tr> <td>0</td> <td>1/2016</td> <td>DSO</td> <td>NEW</td> </tr> </table>		#	DATE	CHK	DESCRIPTION	6				5				4				3				2				1				0	1/2016	DSO	NEW
#	DATE	CHK	DESCRIPTION																														
6																																	
5																																	
4																																	
3																																	
2																																	
1																																	
0	1/2016	DSO	NEW																														
																																	
SOUTH CAROLINA DEPARTMENT OF TRANSPORTATION DESIGN STANDARDS OFFICE 355 PARK STREET ROOM 405 COLUMBIA, SC 29201																																	
STANDARD DRAWING																																	
DRAINAGE STRUCTURE																																	
GENERAL NOTES																																	
719-000-04																																	
EFFECTIVE SETTING DATE																																	

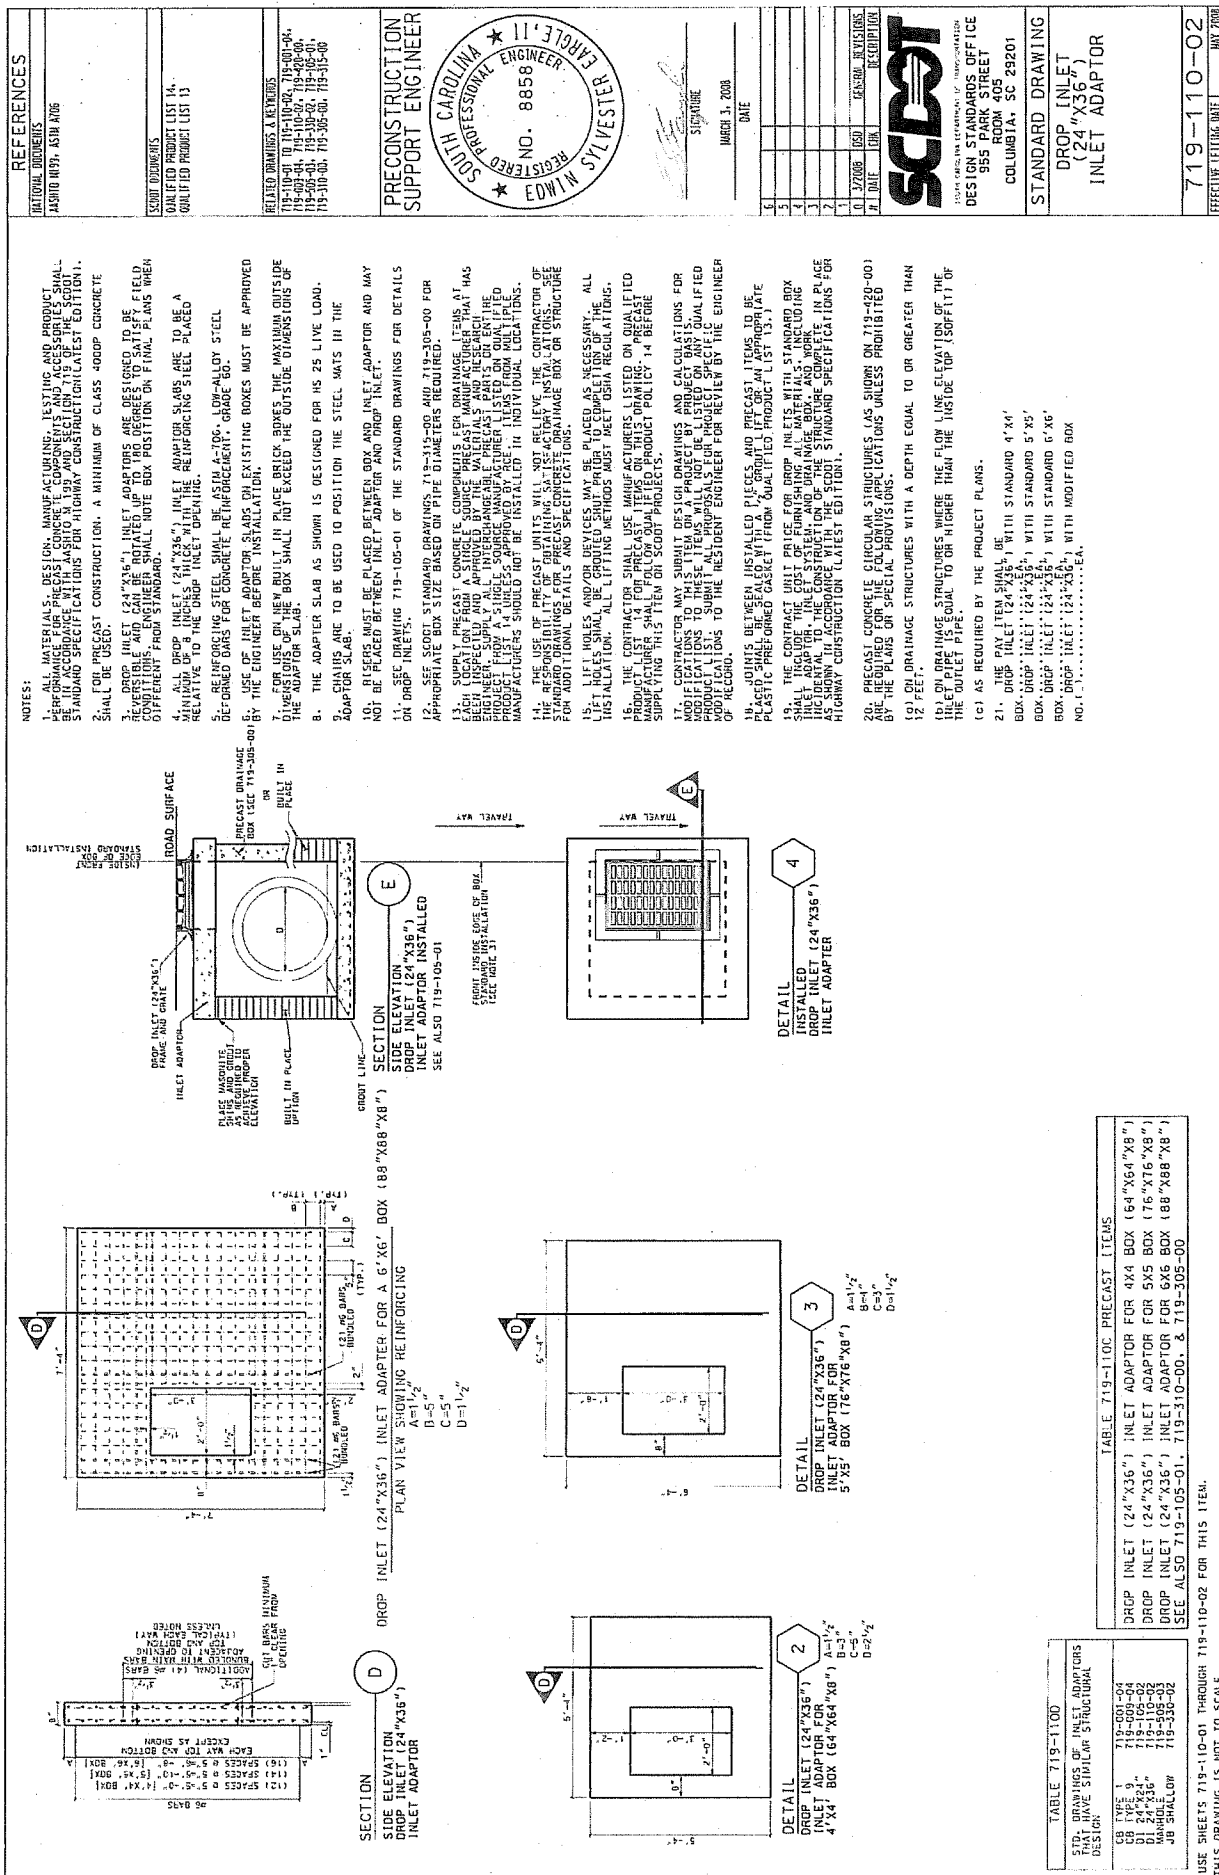



Together We Build Success

1980 Harley Street, North Charleston, SC 29406
P.O. Box 60959, North Charleston, SC 29419
Office: (843) 744-4261, Toll Free: (800) 922-4261
Fax: (843) 534-2095

To:	Gulf Stream Construction Company, Inc.	Contact:	Justin Ballard
Address:	3820 Faber Place Drive, Suite 200 North Charleston, SC 29405	Phone:	843-572-4363
		Fax:	843-572-3780
Project Name:	Marion Square Patch	Bid Number:	
Project Location:	Marion Square, Charleston	Bid Date:	8/28/2018

Item #	Item Description	Estimated Quantity	Unit	Unit Price	Total Price
1	Mill Existing Asphalt 2" (12'x26')	1.00	LS	\$5,000.00	\$5,000.00
2	Install 2" Surface Type C Asphalt (12'x26')	35.00	SY	\$160.00	\$5,600.00

Total Bid Price: \$10,600.00

Notes:

- As used herein, the terms SBCC shall refer to Sanders Brothers Construction Company, Inc. and the terms GC shall refer to the general contractor or Owner of the site or the primary contractor or the other party with whom this agreement is being made.
- It is understood that no overtime is included in this proposal.
- Unless specifically stated herein, the price quoted does not include: engineering, testing and staking or layout, mucking, or fill due to mucking or other subsurface preparation. Unless specifically stated herein, SBCC shall dispose of all excess material on site.
- SBCC will not be liable for delays resulting from weather, strikes, or any conditions beyond the control of SBCC.
- SBCC agrees to comply with all labor law requirements in effect at the time this agreement is entered into, and the proposal herein is based on compliance with such provisions.
- SBCC agrees to carry Workmen's Compensation and General Liability Insurance coverage in an amount not to exceed \$1,000,000.00. Additional liability or other insurance required by GC shall be an expense to GC.
- The proposal does not include the cost of any bond required and the cost of same shall be charged as an extra. Bond cost is to be billed at cost, directly to GC and not added to contract amount. Should bond cost be included in contract, the bond plus 10% is to be added.
- It is the responsibility of the GC to notify SBCC of any special billing requirements such as statements, certifications, and dates invoices are to be received by the GC. The GC's failure to properly notify SBCC shall not be grounds for withholding payment.
- Invoices representing monthly estimates are to be honored as submitted within ten (10) days and are not subject to alteration by GC or owner without notice to and consent of SBCC. Should any payment request be altered without the opportunity of SBCC to produce evidence justifying the amount invoiced, such reductions will be handled as provided in paragraph 9 and be a basis for stopping further work.
- Notwithstanding any other provision in this contract or law pertaining to the same, title to the materials furnished under the provisions of this quotation shall not pass to the owner and shall not become fixtures upon the land until same shall have been paid for in full. SBCC shall have the right to enter the project and to take up and remove the installed materials in the event that payment therefor is not made in accordance with the contract provisions.
- This quotation is good for 45 days from the date submitted and is specifically based upon the conditions set forth here and on the face hereof which will become an exhibit to the contract. Any subsequent agreement shall be on AIA Document A401 Subcontract or AIA Document A101 Owner/Contractor form (2017 Edition) as appropriate.
- Unless specifically stated herein, the price quoted is based on one mobilization. Any additional mobilizations required will be at an additional cost.
- ***** SPECIAL PROJECT CONDITIONS *****
- If the Monthly Asphalt Binder Adjustment Index increases or decreases more than five percent (5%) over or under the listed price at the time of the work, Sanders Brothers Construction Company, Inc. shall provide appropriate documentation so that adjusted compensation can be made. The bid items in this proposal shall remain the same, but the contract unit bid prices for all items containing liquid asphalt cement will be adjusted to compensate for increases or decreases in the Liquid Asphalt Cement Index. This will be in accordance with the South Carolina Department of Transportation Supplemental Specification dated March 3, 2009. The monthly index can be found on the SCDOT website at www.dot.state.sc.us/doing/monthlyindexes.asp. The index date applicable to this project is August 1, 2018. The index price is \$560.42 per ton. The percent of liquid asphalt in the surface mix is 5.5%, the percent of liquid asphalt in the AABC or Binder mix is 5.0%.
- All required permits, inspection, tap, and impact fees to be furnished and/or paid by the Owner or Engineer.
- SWPPP inspections and reports are not included in this proposal.
- Proposal based on measurements of 12'x26'. Should measurements change, we reserve the right to change our price.

- This proposal assumes that the onsite excavated material and in-situ subgrade soils are suitable for use as structural fill on the site and of sufficient stability to support the proposed loading. No remedial subgrade work is included. If unsuitables are encountered, in-place stabilization or removal and replacement will be performed on a unit price basis under the direction of the Engineer.

Payment Terms:

Final payment, including all retention withheld, becomes due 30 days following the date of the final invoice for all completed work of SBCC.

Failure to comply with the terms of payment set forth below shall be grounds for SBCC to stop work. SBCC does not agree under any circumstances that the right of SBCC to receive payment from GC is contingent upon GC receiving payment from Owner.

Payment Terms:

A. That the seller shall invoice the buyer for the value of the work performed and the materials furnished. A billing cycle shall run from the 26th of each month to the 25th of the month following. All amounts invoiced in a billing cycle shall be due and payable in full on the 30th of the month following the end of a billing cycle.

B. That the seller reserves the right to apply all payments received on account first to the payment of unpaid service charges and then to the payment of unpaid principal charges, the oldest such charges to be paid first in any event. That the buyer agrees that any amounts remaining unpaid from and after the 30th day of the month following the end of a billing cycle shall bear interest at the rate of one and one-half percent (1.5%) per month, eighteen percent (18%) per annum and buyer also agrees to pay all costs of collection including, but not limited to reasonable attorney's fees in the event that seller refers the within account to an attorney for collection.

C. Account will be closed if any balance becomes 60 days past due.

ACCEPTED: The above prices, specifications and conditions are satisfactory and are hereby accepted. Buyer: _____ Signature: _____ Date of Acceptance: _____	CONFIRMED: Sanders Bros. Construction Co., Inc. Authorized Signature: _____ Estimator: _____
--	---



3820 FABER PLACE • SUITE 200 • NORTH CHARLESTON, SC 29405
 (843) 572-4363 • FAX (843) 572-9610
www.gulfstreamconstruction.com

ELECTRONICALLY FILED - 2023 May 12 2:07 PM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

To:	Balfour Beatty - Charlotte Division	Contact:	Tim Spano
Address:	100 N Tyron Charlotte, NC 28202	Phone:	
Project Name:	Hotel At Marion Square - COR #31 Hutson St Storm Box	Fax:	
Project Location:	404 King Street, Charleston, SC	Bid Number:	
		Bid Date:	8/28/2018

Item Description	Estimated Quantity	Unit	Unit Price	Total Price
Locate And Hydro-Excavate To Expose Existing Utilities	1.00	LS	\$5,119.08	\$5,119.08
Dewatering	1.00	LS	\$1,488.16	\$1,488.16
Construct Foundation And Bottom Slab Beneath Utilities	1.00	LS	\$3,497.46	\$3,497.46
Construct Custom Box In Hutson And Set Basin Top With Ring And Cover	1.00	LS	\$7,438.28	\$7,438.28
Flow-fill Excavation Area	1.00	LS	\$1,265.21	\$1,265.21
Mill Roadway	1.00	DY	\$5,000.00	\$5,000.00
Asphalt Patching	35.00	SY	\$160.00	\$5,600.00
Total Price for above Items:				\$29,408.19

Total Bid Price: \$29,408.19

Notes:

- This proposal is for the Hutson St storm drain repair as designed by SWA on 8/24/18.

ACCEPTED: The above prices, specifications and conditions are satisfactory and are hereby accepted. Buyer: _____ Signature: _____ Date of Acceptance: _____	CONFIRMED: Gulf Stream Construction Company Authorized Signature: _____ Estimator: Justin Ballard (843) 572-4363 jballard@gulfstreamconstruction.com
---	--

Tab No. 260

Balfour Beatty Construction

March 1, 2019

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 260R1
ASI 52 Added Wallcovering

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 260R1 in the amount of Five thousand five hundred eighty-six (\$5,586.12) to provide additional work in accordance with the following qualifications:

Per the revisions to the finish schedule in Supplemental Instructions 052, contractor to install Owner furnished wallcovering in the following areas.

- ADA Guestroom Bathroom Bath Tub Alcoves (WC-40) – See ID 951.1
- Dome Rotunda Alcoves (WC-41) – No elevation given. See finish schedule.
- Rooftop Bar (WC-42) - See ID 913

** The 9th floor bar was an owner requested redesign. The ADA bathrooms were changed from paint to wallcovering when the tub wallcovering was added in typical rooms. Paint credit provided for the ADA bathrooms. Rotunda wallcovering line items removed due to GMP documents showing wallcovering in the rotunda alcoves in elevation.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set forth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,

Nick Starcevic
Project Manager

cc:

RCO # 260R1 - File

Balfour Beatty

Construction

Hotel at Marion Square

Request for Change Order # 260R1– ASI 52 Added Wallcovering

The additional work for the **ASI 52 Added Wallcovering** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50991000.40	ASI 52 Added Wallcovering UPDATED	\$5,269.93

Total Items \$5,269.93

Total Markups \$316.19

RCO Total \$5,586.12

The total Cost to perform the work as described above is an ADD of Five thousand five hundred eighty-six (\$5,586.12).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 260R1



Change Order Request

Date: 11/27/2018 Request # 17 REVISED TO INCLUDED WC INSTALL
 Attention: Nick Starcevic / Alec Dooley- Balfour Beatty Project Name: Marion Hotel
 From: Scott McCormack RE: ASI #52- REVISED FOR OPEN ITEMS ONLY

	Description	Foreman		Journeyman		Material		Line Item Total
		Units	Unit Costs	Units	Unit Costs	Units	Unit Costs	
	Paint SF05 At Camellia's- ISSUED IN CO #17	16	\$45.00			0	\$36.48	\$0.00
	Paint Crown & Base in lieu of SF-08 at Elev Lobbies - ISSUED IN CO #23	16	\$45.00	32	\$40.00	0	\$36.48	\$0.00
	Paint Base in lieu of SF-08 at Camellia's - ISSUED IN CO #23			12	\$40.00	0	\$36.48	\$0.00
	Paint newly identified at paneling at 6th Fl Concierge	99	\$50.00	6	\$40.00	1	\$36.48	\$276.48
	Install added WC 40 & 41 at ADA Guest Baths, Rooftop Bar					4	\$34.10	\$5,086.40
	Deduct paint at ADA Guest Baths			-20.00	\$40.00	-1	\$138.24	-\$938.24
	Install Added WC-43 at Ballrooms- PREFINISHED by PWI							\$0.00
	Install WC-37, WC-38, WC-42 & WC-33- Using Artist's installer							\$0.00
	*Rotunda Lower Level	1	\$0.00					\$0.00
	*Rotunda Upper Level	1	\$0.00					\$0.00
	*Roof Top	1	\$0.00					\$0.00
	Change Request EXCLUDES any responsibility and/or liability for owner directed subcontractor selection on material damage, installation warranty, quality, schedule or other claims due per subcontract agreement							\$0.00
	Subtotals			30.00	\$1,200.00		\$34.64	\$4,424.64

Overtime Required \$0.00

Sales Tax	8.5%	\$2.94
Subtotal		\$4,427.58
O&P	15%	\$ 664.14
P&P Bond	3.5%	\$ 178.21

TOTAL LABOR and MATERIAL \$ 5,269.93

BR3042.dwg 01/12/90 16:50

NO.	DESCRIPTION	FINISH	FINISH DESCRIPTION	REMARKS	NOTES	STATUS
WC-1	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-2	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-3	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-4	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-5	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-6	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-7	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-8	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-9	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-10	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-11	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-12	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-13	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-14	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-15	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-16	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-17	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-18	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-19	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-20	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-21	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-22	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-23	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-24	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-25	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-26	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-27	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-28	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-29	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-30	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-31	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-32	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-33	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-34	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-35	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-36	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-37	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-38	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-39	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-40	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-41	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-42	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-43	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-44	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-45	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-46	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-47	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-48	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-49	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-50	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-51	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-52	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-53	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-54	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-55	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-56	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-57	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-58	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-59	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-60	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-61	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-62	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-63	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-64	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-65	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-66	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-67	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-68	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-69	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-70	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-71	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-72	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-73	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-74	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-75	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-76	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-77	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-78	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-79	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-80	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-81	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-82	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-83	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-84	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-85	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-86	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-87	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-88	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-89	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-90	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-91	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-92	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-93	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-94	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-95	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-96	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-97	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-98	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-99	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD
WC-100	WALL COVERING	WOOD	WOOD	WOOD	WOOD	WOOD

THE HOTEL AT MARION SQUARE

404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403

R - 1959

DESIGN
CONTINUUM
INCORPORATED

44 BROAD STREET NW, ATLANTA, GEORGIA 30303
TELEPHONE (404) 266-0085

THIS DRAWING IS THE PROPERTY OF
DESIGN CONTINUUM INCORPORATED
AND IS NOT TO BE REPRODUCED OR
TRANSMITTED IN ANY FORM OR BY
ANY MEANS, ELECTRONIC OR MECHANICAL,
INCLUDING PHOTOCOPYING, RECORDING,
OR BY ANY INFORMATION STORAGE
RETRIEVAL SYSTEM, WITHOUT THE
WRITTEN PERMISSION OF DESIGN
CONTINUUM INCORPORATED.


DATE: 01/12/90
BY: J. L. BROWN
CHECKED: J. L. BROWN
APPROVED: J. L. BROWN

FINISH DESCRIPTION
ID-007

SECTION		DATE	NO.	DESCRIPTION
1	1	1/25/79	1	1.00000000
2	2	2/1/79	2	2.00000000
3	3	3/1/79	3	3.00000000
4	4	4/1/79	4	4.00000000
5	5	5/1/79	5	5.00000000
6	6	6/1/79	6	6.00000000
7	7	7/1/79	7	7.00000000
8	8	8/1/79	8	8.00000000
9	9	9/1/79	9	9.00000000
10	10	10/1/79	10	10.00000000
11	11	11/1/79	11	11.00000000
12	12	12/1/79	12	12.00000000
13	13	1/1/80	13	13.00000000
14	14	2/1/80	14	14.00000000
15	15	3/1/80	15	15.00000000
16	16	4/1/80	16	16.00000000
17	17	5/1/80	17	17.00000000
18	18	6/1/80	18	18.00000000
19	19	7/1/80	19	19.00000000
20	20	8/1/80	20	20.00000000
21	21	9/1/80	21	21.00000000
22	22	10/1/80	22	22.00000000
23	23	11/1/80	23	23.00000000
24	24	12/1/80	24	24.00000000
25	25	1/1/81	25	25.00000000
26	26	2/1/81	26	26.00000000
27	27	3/1/81	27	27.00000000
28	28	4/1/81	28	28.00000000
29	29	5/1/81	29	29.00000000
30	30	6/1/81	30	30.00000000
31	31	7/1/81	31	31.00000000
32	32	8/1/81	32	32.00000000
33	33	9/1/81	33	33.00000000
34	34	10/1/81	34	34.00000000
35	35	11/1/81	35	35.00000000
36	36	12/1/81	36	36.00000000
37	37	1/1/82	37	37.00000000
38	38	2/1/82	38	38.00000000
39	39	3/1/82	39	39.00000000
40	40	4/1/82	40	40.00000000
41	41	5/1/82	41	41.00000000
42	42	6/1/82	42	42.00000000
43	43	7/1/82	43	43.00000000
44	44	8/1/82	44	44.00000000
45	45	9/1/82	45	45.00000000
46	46	10/1/82	46	46.00000000
47	47	11/1/82	47	47.00000000
48	48	12/1/82	48	48.00000000
49	49	1/1/83	49	49.00000000
50	50	2/1/83	50	50.00000000
51	51	3/1/83	51	51.00000000
52	52	4/1/83	52	52.00000000
53	53	5/1/83	53	53.00000000
54	54	6/1/83	54	54.00000000
55	55	7/1/83	55	55.00000000
56	56	8/1/83	56	56.00000000
57	57	9/1/83	57	57.00000000
58	58	10/1/83	58	58.00000000
59	59	11/1/83	59	59.00000000
60	60	12/1/83	60	60.00000000
61	61	1/1/84	61	61.00000000
62	62	2/1/84	62	62.00000000
63	63	3/1/84	63	63.00000000
64	64	4/1/84	64	64.00000000
65	65	5/1/84	65	65.00000000
66	66	6/1/84	66	66.00000000
67	67	7/1/84	67	67.00000000
68	68	8/1/84	68	6

404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403

DESIGN
CONTINUUM
INCORPORATED
44 BROAD STREET NW, ATLANTA, GEORGIA 30309
770.522.0000

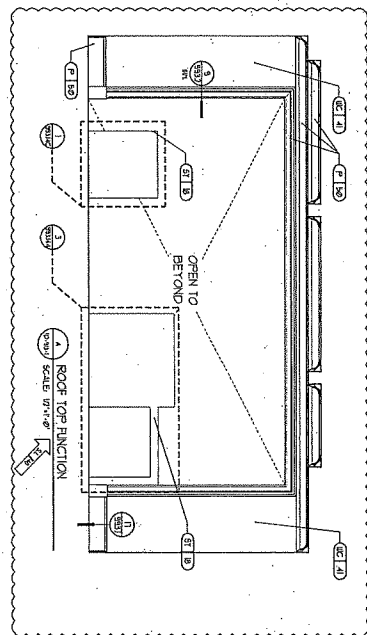

THE HOTEL AT MARION SQUARE

404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403

R - 1961




DESIGN
CONTINUUM
INCORPORATED
44 BROAD STREET NW, ATLANTA, GEORGIA 30303
TELEPHONE (404) 265-0093

THIS DRAWING IS THE PROPERTY OF
DESIGN CONTINUUM INCORPORATED
AND IS NOT TO BE REPRODUCED OR
TRANSMITTED IN ANY FORM OR BY
ANY MEANS, WITHOUT THE WRITTEN
PERMISSION OF DESIGN CONTINUUM
INCORPORATED.

REVISIONS

DATE	NO.	DESCRIPTION
01/12/00	1	DESIGN
01/12/00	2	DESIGN
01/12/00	3	DESIGN
01/12/00	4	DESIGN
01/12/00	5	DESIGN
01/12/00	6	DESIGN
01/12/00	7	DESIGN
01/12/00	8	DESIGN
01/12/00	9	DESIGN
01/12/00	10	DESIGN
01/12/00	11	DESIGN
01/12/00	12	DESIGN
01/12/00	13	DESIGN
01/12/00	14	DESIGN
01/12/00	15	DESIGN
01/12/00	16	DESIGN
01/12/00	17	DESIGN
01/12/00	18	DESIGN
01/12/00	19	DESIGN
01/12/00	20	DESIGN
01/12/00	21	DESIGN
01/12/00	22	DESIGN
01/12/00	23	DESIGN
01/12/00	24	DESIGN
01/12/00	25	DESIGN
01/12/00	26	DESIGN
01/12/00	27	DESIGN
01/12/00	28	DESIGN
01/12/00	29	DESIGN
01/12/00	30	DESIGN
01/12/00	31	DESIGN
01/12/00	32	DESIGN
01/12/00	33	DESIGN
01/12/00	34	DESIGN
01/12/00	35	DESIGN
01/12/00	36	DESIGN
01/12/00	37	DESIGN
01/12/00	38	DESIGN
01/12/00	39	DESIGN
01/12/00	40	DESIGN
01/12/00	41	DESIGN
01/12/00	42	DESIGN
01/12/00	43	DESIGN
01/12/00	44	DESIGN
01/12/00	45	DESIGN
01/12/00	46	DESIGN
01/12/00	47	DESIGN
01/12/00	48	DESIGN
01/12/00	49	DESIGN
01/12/00	50	DESIGN
01/12/00	51	DESIGN
01/12/00	52	DESIGN
01/12/00	53	DESIGN
01/12/00	54	DESIGN
01/12/00	55	DESIGN
01/12/00	56	DESIGN
01/12/00	57	DESIGN
01/12/00	58	DESIGN
01/12/00	59	DESIGN
01/12/00	60	DESIGN
01/12/00	61	DESIGN
01/12/00	62	DESIGN
01/12/00	63	DESIGN
01/12/00	64	DESIGN
01/12/00	65	DESIGN
01/12/00	66	DESIGN
01/12/00	67	DESIGN
01/12/00	68	DESIGN
01/12/00	69	DESIGN
01/12/00	70	DESIGN
01/12/00	71	DESIGN
01/12/00	72	DESIGN
01/12/00	73	DESIGN
01/12/00	74	DESIGN
01/12/00	75	DESIGN
01/12/00	76	DESIGN
01/12/00	77	DESIGN
01/12/00	78	DESIGN
01/12/00	79	DESIGN
01/12/00	80	DESIGN
01/12/00	81	DESIGN
01/12/00	82	DESIGN
01/12/00	83	DESIGN
01/12/00	84	DESIGN
01/12/00	85	DESIGN
01/12/00	86	DESIGN
01/12/00	87	DESIGN
01/12/00	88	DESIGN
01/12/00	89	DESIGN
01/12/00	90	DESIGN
01/12/00	91	DESIGN
01/12/00	92	DESIGN
01/12/00	93	DESIGN
01/12/00	94	DESIGN
01/12/00	95	DESIGN
01/12/00	96	DESIGN
01/12/00	97	DESIGN
01/12/00	98	DESIGN
01/12/00	99	DESIGN
01/12/00	100	DESIGN

DESIGN CONTINUUM INCORPORATED
44 BROAD STREET NW, ATLANTA, GEORGIA 30303
TELEPHONE (404) 265-0093
FAX (404) 265-0094
WWW.DESIGNCONTINUUM.COM
ID-9131



404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403



DESIGN
CONTINUUM
INCORPORATED
44 BROAD STREET NW, ATLANTA, GEORGIA 30303


ADA Bathrooms Thru SI 39 no wall covering.

TYPICAL GUESTROOM DETAIL KEY REFERENCES - SEE SHEET ID-992	
①	CROWN - STALL AT LOWER CEILING
②	CASING - AT DOORS AND OPENINGS
③	CLOSET SHELF AND ROD

① GUEST BATHROOM - TYPE 32
SCALE: 1/4" = 1'-0"

② GUEST BATHROOM - TYPE 32
SCALE: 1/4" = 1'-0"

③ GUEST BATHROOM - TYPE 32
SCALE: 1/4" = 1'-0"

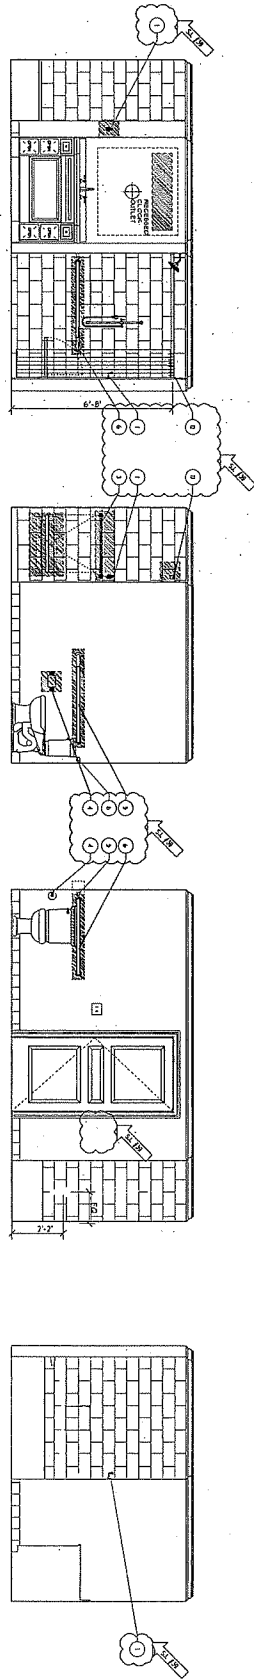


④ GUEST BATHROOM - TYPE 32
SCALE: 1/4" = 1'-0"
ROOM TYPE 32:
307

⑤ GUEST BATHROOM - TYPE 32
SCALE: 1/4" = 1'-0"

⑥ GUEST BATHROOM - TYPE 32
SCALE: 1/4" = 1'-0"

⑦ GUEST BATHROOM - TYPE 32
SCALE: 1/4" = 1'-0"




⑧ GUEST BATHROOM - TYPE 31
SCALE: 1/4" = 1'-0"
ROOM TYPE 31:
371 471 571 671 771 871

⑨ GUEST BATHROOM - TYPE 31
SCALE: 1/4" = 1'-0"

⑩ GUEST BATHROOM - TYPE 31
SCALE: 1/4" = 1'-0"

⑪ GUEST BATHROOM - TYPE 31
SCALE: 1/4" = 1'-0"

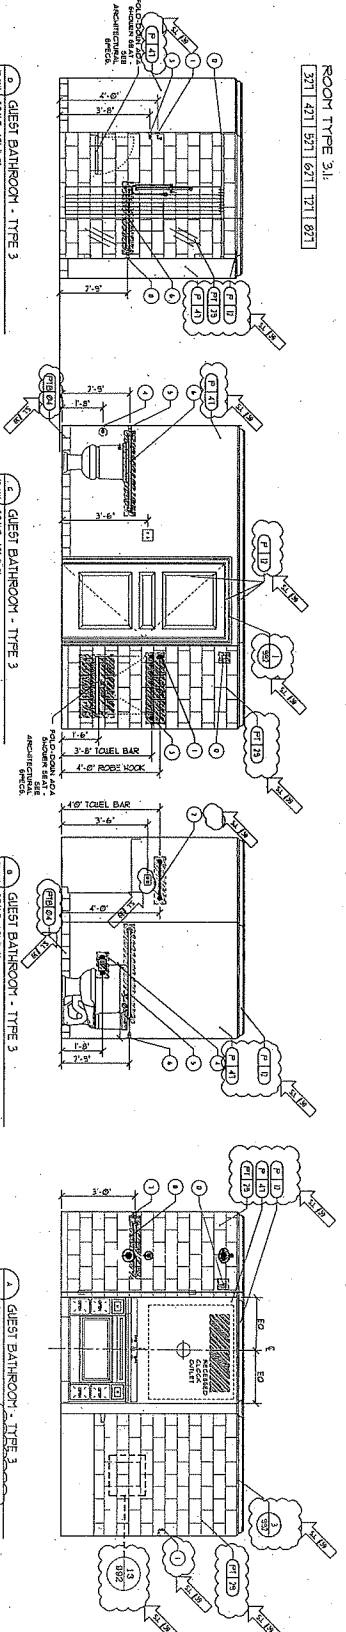

⑫ GUEST BATHROOM - TYPE 3
SCALE: 1/4" = 1'-0"
ROOM TYPE 3:
377

⑬ GUEST BATHROOM - TYPE 3
SCALE: 1/4" = 1'-0"

⑭ GUEST BATHROOM - TYPE 3
SCALE: 1/4" = 1'-0"

⑮ GUEST BATHROOM - TYPE 3
SCALE: 1/4" = 1'-0"

NOTES:
1. SEE D-98 FOR TYPICAL GUEST BATHROOM FINISHES AND ACCESSORY SCHEDULE.
2. ACCESSORY SCHEDULES APPLY TO ALL TYPICAL ACCESSORIES AND DIMENSIONS OF TO CORRELATE AND COORDINATE APPROPRIATE ROOMS FOR THE SPECIFIC ACCESSORIES - SEE D-99 FOR TYPICAL.

THE HOTEL AT MARION SQUARE

404 KING STREET
CHARLESTON, SOUTH CAROLINA
29403

R - 1963



DESIGN
CONTINUUM
INCORPORATED
44 BRIDGES STREET, SUITE 200, ATLANTA, GEORGIA 30303
TELEPHONE (404) 246-0055

THE DRAWING IS THE PROPERTY OF
DESIGN CONTINUUM INCORPORATED
AND SHALL BE RETURNED TO THE
FIRM WITHOUT PERMISSION. ©2020
© DESIGN CONTINUUM

DATE	BY	REVISION
10/12/2019	10/12/2019	10/12/2019
10/12/2019	10/12/2019	10/12/2019
10/12/2019	10/12/2019	10/12/2019

PROJECT: GUESTROOM BATH
INTERIOR ELEVATIONS
ID-9611

DESIGN CONTINUUM

Tab No. 262

Balfour Beatty Construction

August 31, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 262
RFI 1004 TV Wall Revisions

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 262 in the amount of Fifteen thousand six hundred thirty-five (\$15,635.00) to provide additional work in accordance with the following qualifications:

Per the response to RFI 1004, the east wall between the lounge room and the bathroom in rooms 315, 415, and 515 to be selectively demolished and reframed. Cost includes the relocation of data, fire alarm, and electrical devices to avoid the TV headboard as well as to adjacent wall to the south end of the lounge (between X15 and X13).

This price does not include any cost for revisions to sprinkler piping or HVAC grills.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Alec Dooley
Assistant Project Manager

cc:
Marty Wall
Melissa Pense
Jim Clements
Jennifer Faulkinberry
Woody Faust
Nick Starcevic
David Simonton

RCO # 262 - File

Balfour Beatty

Construction

Hotel at Marion Square

Request for Change Order # 262— RFI 1004 TV Wall Revisions

The additional work for the **RFI 1004 TV Wall Revisions** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50640000.40	RFI 1004 - Framing and Drywall	\$6,483.00
2	400.51600000.40	RFI 1004 - CCN 163 Electrical Rework Third Floor	\$4,549.00
3	400.51600000.40	RFI 1004 - CCN 162 Electrical Revisions Fifth Floor	\$3,718.00

Total Items \$14,750.00

Total Markups \$885.00

RCO Total \$15,635.00

The total Cost to perform the work as described above is an ADD of Fifteen thousand six hundred thirty-five (\$15,635.00).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 262



REQUEST FOR CHANGE ORDER

Page 1 of 2

Ref.# CO-18608
GC #
Date Aug 31, 2017
Job # 14-1278

To: Balfour Beatty Construction
406 S McDowell Street, Suite 200
Raleigh, NC 27601
Phone: (919)233-5001

Project: Hotel @ Marion Square
404 King Street
Charleston, SC 29403

Description: RFI 1004 - Changes in rooms 315, 415, and 515

Labor	Total Hrs	Rate	Total
Demolition	16.00	42.00	\$672.00
Metal Framing	16.00	42.00	\$672.00
Hang Drywall	24.00	42.00	\$1,008.00
Finishing (Walls Only)	30.00	42.00	\$1,260.00
Insulation Thermal Labor	6.00	42.00	\$252.00
Fire Stopping-Caulk	6.00	42.00	\$252.00
Clean-up/Material Handling	10.00	30.00	\$300.00
Working Foreman	5.00	55.00	\$275.00
Total Labor			\$4,691.00

Material	Size	Quantity	UOM	Unit Price	Total
METAL FRAMING	-	1.00	EA	121.80 EA	\$121.80
DRYWALL & ACCESSORIES	-	1.00	EA	638.40 EA	\$638.40
INSULATION & ACCESSORIES	-	1.00	EA	420.00 EA	\$420.00
FINISHING & ACCESSORIES	-	1.00	EA	84.00 EA	\$84.00
CAULK & ADHESIVE	-	0.00	EA	42.00 EA	\$0.00
FASTENERS	-	1.00	EA	35.00 EA	\$35.00
Total Material					\$1,299.20

Equipment	Total Equipment
	\$0.00

Subtotal for Detail \$5,990.20

Miscellaneous	Total
Freight and Delivery Expense	\$0.00
Tool & Equipment Expense 10%	\$129.92
Total Miscellaneous Charges	\$129.92

Adjustments	Total
ROUNDING	\$0.60
Total Adjustments	\$0.60

Notes: Per FRI 1004 and onsite review with BBC and the other trades the following work will take place in each corner room 315,415, and 515.

- 8 pieces of drywall and associated insulation will be removed by Precision Walls.
- The pocket door openings will need to be shifted which will result in added framing.
- Once other trades complete their work the areas where the drywall was taken down will need to be re-insulated, re-hung, refinished, and re-caulked.

All material handling to get metal studs and drywall from ground floor through freight elevator to floors 3-5.

- Prices firm for 7 days and based on current job conditions
- Contract time extension of: 15 days
- Material delivery time of: 5 days

7317 Peppermill Pkwy, N. Charleston, South Carolina, 29418

T:843-793-6020

Fax:

Run on: August 31, 2017 3:21 PM

R - 1967

ELECTRONICALLY FILED - 2023 May 12 2:07 PM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

**REQUEST FOR CHANGE ORDER
CONTINUED**

14-1278
Hotel @ Marion Square

Aug 31, 2017

Page 2 of 2
CO-18608

d. We will not proceed with this work without a written Change Order

Michael Thomas Zinna
Project Manager

Adjustments Total:	\$0.60	
Sub Total:	\$6,120.72	
Sales Tax on Materials:	\$128.62	9.00%
OH&P (Material & Equipment):	\$233.66	15.00%
Sub Total:	\$6,483.00	
Total:	\$6,483.00	

ELECTRONICALLY FILED - 2023 May 12 2:07 PM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108

PROPOSED CHANGE ORDER

Watson Electrical

3215 Fortune Drive, Suite 109
North Charleston, South Carolina 29418

CCN #

163

Date:

1/30/2018

Project Name:

Marion Square Hotel

Project Number:

21046

Page Number:

1

Client Address:

Balfour Beatty Construction

306 Meeting Street
Charleston, South Carolina

Work Description

We reserve the right to correct this quote for errors and omissions.

This FWO includes the labor and delivery for the changes made to rooms 315 per RFI 1004. Scope as follows:

Reloacted switch, horn / strobe and smoke detector due to TV furniture covering entire wall.

Removed devices and re installed on fire wall between 313 and 315.

Ran new pathway for fire alarm devices.

Moved switch to hall.

Removed and re installed boxes and MC cable for C circuit for lighting, added boxes and extension rings.

This quote covers direct costs only and we reserve the right to claim for impact and consequential costs.

This price is good for acceptance within 30 days from the date of receipt.

We request a time extension of 0 days.

We will supply and install all materials, labor, and equipment as per your instructions on <CCN_163_RFI 1004 (2)> <ccn_163>.

Itemized Breakdown

Description	Qty	Net Price U	Total Mat.	Labor U	Total Hrs.
3/4" CONDUIT - EMT - RED FIRE ALARM	20	59.76 C	11.95	7.50 C	0.00
3/4" CONN COMP DC INSUL - EMT	6	54.60 C	3.28	21.00 C	0.00
3/4" EMT TO 3/4" FLEX COUPLING	2	439.69 C	8.79	25.00 C	0.00
3/4" 1-H STRAP - EMT - STEEL	18	9.76 C	1.76	6.00 C	0.00
3/4" FLEX - ALUMINUM	30	104.42 C	31.33	6.70 C	0.00
3/4" CONN FLEX DC SQUEEZE STRAIGHT	2	100.94 C	2.02	18.90 C	0.00
#12/2C CABLE MC - ALUM ARMOR	250	439.73 M	109.93	45.00 M	0.00
3/4" CONN SADDLEGRIP DC FOR FLEX / AC-90 / MC	8	243.71 C	19.50	28.00 C	0.00
4" SQ BOX EXT RING 3/4" KO	2	248.10 C	4.96	40.00 C	0.00
SQ BOX MNTG BRKT FOR 16" OC STUD	3	144.00 C	4.32	15.00 C	0.00
Totals	341		197.83		0.00

Summary

General Materials		197.83
Material Tax	(@ 8.500 %)	16.82
Material Total		214.65
JOURNEYMAN	(61.00 Hrs @ \$52.00)	3,172.00
FOREMAN @ 15%	(10.00 Hrs @ \$55.00)	550.00
MILEAGE	(71.00 @ 0.00 @ \$2.50 + 0.000 % + 0.000 % + 0.000 %)	177.50
CONSUMABLES	(71.00 @ 0.00 @ \$0.30 + 0.000 % + 0.000 % + 0.000 %)	21.30

ORIGINAL

R - 1969

PROPOSED CHANGE ORDER

Client Address:

Watson Electrical3215 Fortune Drive, Suite 109
North Charleston, South Carolina 29418**Balfour Beatty Construction**306 Meeting Street
Charleston, South Carolina

CCN #

163

Date:

1/30/2018

Project Name:

Marion Square Hotel

Project Number:

21046

Page Number:

2

Summary (Cont'd)

Subtotal

(@ 10.000 %)

4,135.45

413.55

Subtotal

4,549.00

Final Amount

\$4,549.00**CONTRACTOR CERTIFICATION**

Name: _____

Date: _____

Signature: _____

I hereby certify that this quotation is complete and accurate based on the information provided.

CLIENT ACCEPTANCE

CCN #: 163

Final Amount: \$4,549.00

Name: _____

Date: _____

Signature: _____

Change Order #: _____

I hereby accept this quotation and authorize the contractor to complete the above described work.

ORIGINAL

R - 1970



1163

DAILY TIME & MATERIAL WORK REPORT

--	--	--	--

Date

Job No.

Work Order No.

1/8 & 1/1-2016

21016

M

T

W

T

F

S

S

Job Name

marion sq

Description of Work:

RFT-1004 Rm 315 Relocate switch, Horn/Smoke & Smoke

Detector because TV Function covers all of wall. Remove device & install on fire wall between 313 & 315. Run new cabling for fire alarm devices. Move switch to wall. Run and install horn & smoke detector for lighting. Moved & added boxes & extension

MATERIAL LIST

Quantity	Description	Rate	Amount
30'	3/4" Green Field Flex		
2	3/4" Flex Connectors (straight)		
2	3/4" Change size EMT to Flex		
2	4 Square Box Extension		
250'	MC Cable 12/2 w/gnd		
8	MC Connector w/out short		
20'	3/4" Red EMT		
4	3/4" EMT couplings		
3	Box mounting slide bracket/screws		
18	strips		
Total			\$

LABOR LIST

Name	Title	Reg Hrs	Rate	OT Hrs	Rate	Amount
Kevin Sloan		10				
Bill Taylor		17				
Fred Rayner II		17				
Ernest Brown		17				
James		2				
Fred		2				
Total						\$

EQUIPMENT LIST

Description	Hours	Rate	Amount	Mileage	Rate	Amount
Total						\$

Completed By:

Approved By:

Watson Electrical Construction Co. LLC

☐

Job Complete

☐

Not Complete

Form No. 447 (3/03)

R-1971

**Plaintiff Balfour Beatty's
Trial Exhibit # 12**
(part 5 of 11)

PROPOSED CHANGE ORDER

Watson Electrical

3215 Fortune Drive, Suite 109
North Charleston, South Carolina 29418

CCN # 162
Date: 1/29/2018
Project Name: Marion Square Hotel
Project Number: 21046
Page Number: 1

Client Address:

Balfour Beatty Construction

306 Meeting Street
Charleston, South Carolina

Work Description

We reserve the right to correct this quote for errors and omissions.

This FWO includes the labor and materials to re work room 515 according to RFI 1004. Scope includes the following:

Relocated switch to hallway.

Relocated horn / strobe and smoke detector to fire wall between room 513 and 515.

Removed and reinstalled pathway for horn / strobe and lighting.

Moved / added boxes and extension rings.

This quote covers direct costs only and we reserve the right to claim for impact and consequential costs.

This price is good for acceptance within 30 days from the date of receipt.

We request a time extension of 0 days.

We will supply and install all materials, labor, and equipment as per your instructions on <CCN_162_RFI 1004> <ccn_162>.

Itemized Breakdown

Description	Qty	Net Price U	Total Mat.	Labor U	Total Hrs.
3/4" CONDUIT - EMT - RED FIRE ALARM	20	59.76 C	11.95	7.50 C	0.00
3/4" CONN COMP DC INSUL - EMT	6	54.60 C	3.28	21.00 C	0.00
3/4" EMT TO 3/4" FLEX COUPLING	2	439.69 C	8.79	25.00 C	0.00
3/4" 1-H STRAP - EMT - STEEL	20	9.76 C	1.95	6.00 C	0.00
3/4" FLEX - ALUMINUM	25	104.42 C	26.11	6.70 C	0.00
3/4" CONN FLEX DC SQUEEZE STRAIGHT	2	100.94 C	2.02	18.90 C	0.00
#12/2C CABLE MC - ALUM ARMOR	250	439.73 M	109.93	45.00 M	0.00
3/4" CONN SADDLEGRIP DC FOR FLEX / AC-90 / MC	8	243.71 C	19.50	28.00 C	0.00
4" SQ BOX EXT RING 3/4" KO	2	248.10 C	4.96	40.00 C	0.00
SQ BOX MNTG BRKT FOR 16" OC STUD	3	144.00 C	4.32	15.00 C	0.00
Totals	338		192.81		0.00

Summary

General Materials		192.81
Material Tax (@ 8.500 %)		16.39
Material Total		209.20
JOURNEYMAN (45.00 Hrs @ \$52.00)		2,340.00
FOREMAN @ .15% (8.00 Hrs @ \$55.00)		440.00
OVERTIME ADJUSTMENT (3.00 Hrs @ \$78.00)		234.00
MILEAGE (56.00 @ 0.00 @ \$2.50 + 0.000 % + 0.000 % + 0.000 %)		140.00
CONSUMABLES (56.00 @ 0.00 @ \$0.30 + 0.000 % + 0.000 % + 0.000 %)		16.80

ORIGINAL

R - 1973

PROPOSED CHANGE ORDER

Client Address:

Watson Electrical3215 Fortune Drive, Suite 109
North Charleston, South Carolina 29418**Balfour Beatty Construction**306 Meeting Street
Charleston, South Carolina

CCN #

162

Date:

1/29/2018

Project Name:

Marion Square Hotel

Project Number:

21046

Page Number:

2

Summary (Cont'd)

Subtotal		3,380.00
	(@ 10.000 %)	338.00
Subtotal		3,718.00
Final Amount		\$3,718.00

CONTRACTOR CERTIFICATION

Name: _____

Date: _____

Signature: _____

I hereby certify that this quotation is complete and accurate based on the information provided.

CLIENT ACCEPTANCE

CCN #: 162

Final Amount: \$3,718.00

Name: _____

Date: _____

Signature: _____

Change Order #: _____

I hereby accept this quotation and authorize the contractor to complete the above described work.

ORIGINAL

R - 1974



DAILY TIME & MATERIAL WORK REPORT

Date					Job No.					Work Order No.				
1/9, 1/10, 1/11/12-2018					21046									
M	T	W	T	F	S	S	Job Name							
	X	X	X	X			Mason							

Description of Work: RFE-1004 Run 515 Relocate Switch to hall. Relocate Horn/Stroke
 & Smoke Detector to RFE with location 513 & 515. Remove & Reinstall ~~sm~~ Pullstation from the 1st floor
 & Smoke Detector. Reconnect the cable for Smoke Detector. Run new cable cable for Smoke Detector
 & Lighting Alarm & Add 1 more & Relocate rings

MATERIAL LIST

MATERIAL LIST		Rate	Amount
Quantity	Description		
25'	3/4" Greenfield Flex		
2	3/4" Flex Connector (Straight)		
2	3/4" Change over ENT to flex		
230'	11C cable 13/2 w/ground		
8	11C connector w/anti shock		
2	4 square box extension		
20'	Red ENT 3/4"		
6	3/4" ENT Connector		
3	Red Mounting Slide Brackets w/screws		
20	Straps		
Total			\$

LABOR LIST

Name	Title	Reg Hrs	Rate	OT Hrs	Rate	Amount
Kevin Sloan		8				
Pill Taylor		15		1.5		
Fred Rayonell		15		1.5		
Emanet Brown		15				
Total						\$

EQUIPMENT LIST

Description	Hours	Rate	Amount	Mileage	Rate	Amount
Total						\$

Completed By:	Approved By:
Watson Electrical Construction Co. LLC	<i>Ben Farnsworth</i>
☐ Job Complete	<i>BBOW</i>
☐ Not Complete	<i>1/11/10</i>

Tab No. 264

Balfour Beatty Construction

September 4, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 264
RFI 1180 Sprinkler Heads in TV Walls

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 264 in the amount of Fourteen thousand three hundred ninety (\$14,390.21) to provide additional work in accordance with the following qualifications:

Per RFI 1180 and the subsequent field report issued by DCI on 2/8/18, Contractor to relocate sprinkler heads to the side columns of the TV headboards. Cost also includes the installation of a second symmetrical head to the other side column. See the below summary of costs.

- Sprinkler - \$7,951.67 to cut out and relocate 6 heads as well as add 6 heads in rooms 610, 710, 810, 644, 744, and 844.
- FF&E Modification - \$2,600 to make two field cuts the TV wallboard furniture.
- Sheetrock - \$3,024 to patch and repair sheetrock at both the TV wall as well as the bathroom ceilings behind the TV wall cut open for sprinkler access.

This change order does not include any costs for painting, tile repair, wall paper repair.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set forth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Balfour Beatty Construction

Please contact me with any questions regarding this request for Change Order.

Sincerely,

Alec Dooley
Assistant Project Manager

cc:
Melissa Pense
Marty Wall
Jim Clements
Jennifer Faulkinberry
Woody Faust
Nick Starcevic
David Simonton

RCO # 264 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 264- RFI 1180 Sprinkler Heads in TV Walls

The additional work for the **RFI 1180 Sprinkler Heads in TV Walls** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.51550000.40	RFI 1180 Sprinkler Heads in TV Walls	\$7,951.67
2	200.11900000.10	Bathroom Ceiling Framing, Hanging, and Finishing	\$3,024.00
3	400.51200001.40	RFI 1180 Sprinkler Heads in TV Walls	\$2,600.00

Total Items \$13,575.67

Total Markups \$814.54

RCO Total \$14,390.21

The total Cost to perform the work as described above is an ADD of Fourteen thousand three hundred ninety (\$14,390.21).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 264



Charleston • Columbia • Atlanta

DATE:

01/08/18

C.O.#

CHANGE ORDER PROPOSAL

RFI 1180

JOB NAME:	Marion Square
CONTRACTOR	Balfour Beatty
ADDRESS	
DATE OF EXISTING CONTRACT:	
CONTRACT #:	
ATT:	Nick Starcevic
PH:	
Reference	

We hereby agree to make the following change's) specified below:

Pasco to add six heads and relocate six heads as per RFI#1180. all work will be done on OVERTIME. Design to reveiw and add to red line drawings on OVERTIME rate ONLY.

NOTE: This Change Order reflects pricing for additional and/or revised work outside of the contacted scope of work.

WE AGREE hereby to make the change specified above at this price >>>>>>>>		\$7,951.67
PREVIOUS CONTRACT AMOUNT		
REVISED CONTRACT AMOUNT		
Signature (SUB-CONTRACTOR):		
ACCEPTED - The above prices and specifications of this work to be performed under the same terms and conditions as specified in the original contract unless otherwise specified. Price is valid for 30 days from receipt.	Accepted By: (Signature)	
	Date of Acceptance:	

Summary

DATE:

01/08/18

We hereby agree to make the following change's) specified below:

Pasco to add six heads and relocate six heads as per RFI#1180. all work will be done on OVERTIME. Design to reveiw and add to red line drawings on OVERTIME rate ONLY.

Fire Sprinkler

Contract Work

1.	Products (itemized breakdown attached):		\$488.40	
2.	Rent of Equipment (listed separately):*		\$0.00	
	Total of 1 + 2		\$488.40	(A)
3.	Labor (itemized breakdown attached):		\$6,390.00	
4.	security, or as otherwise required or specified):	0%	\$0.00	
	Total of (A) + 3 + 4		\$6,878.40	(B)
5.	Overhead and Profit (% of total (B)):**	15%	\$1,031.76	
	Total of (B) + 5		\$7,910.16	(C)
6.	Sales Taxes on total (A):	8.5%	\$41.51	
	Total of (C) + 6		\$7,951.67	(D)
7.	Subcontract work (if applicable in a similar breakdown through total (D):			
8.	Prime Contractor's overhead and profit on sub-bids (7):	10%	\$0.00	
	Total of 7 + 8		\$0.00	(E)
	Total of (D) + (E)		\$7,951.67	(F)
9.	Performance - Payment Bond on Total (F):	0.0%	\$0.00	(G)
	TOTAL QUOTATION (F) + (G)		\$7,951.67	

Extension of time requested: _____ calendar day(s)

Date: 01/08/18

PRODUCTS - ITEMIZED BREAKDOWN

PRODUCTS TOTAL:	\$488.40
------------------------	-----------------

01/08/18

LABOR - ITEMIZED BREAKDOWN

LABOR TOTAL:		\$6,390.00
---------------------	--	------------

EQUIPMENT

Date:

01/08/18

Pasco to add six heads and relocate six heads as per RFI#1180. all work will be done on OVERTIME. Design to reveiw and add to red line drawings on OVERTIME rate ONLY.

RENT OF EQUIPMENT - ITEMIZED BREAKDOWN

Qty	Description	Unit	Total
	N/A		0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00
			0.00

RENT OF EQUIPMENT TOTAL:	\$0.00
--------------------------	--------

Dooley, Alec

From: Starcevic, Nicholas
Sent: Friday, August 31, 2018 4:51 PM
To: Dooley, Alec
Subject: FW: Holes in TV panels

Here you go. This is what I have!

Nick Starcevic
Project Mgr | Balfour Beatty
O: (843) 974-4590 | C: (704) 361-3265
E: nstarcevic@balfourbeattyus.com | www.balfourbeattyus.com
306 Meeting Street, Suite 300, Charleston, SC 29401

-----Original Message-----

From: Rob Jacoby [mailto:rob@westleycontract.com]
Sent: Friday, February 16, 2018 8:01 AM
To: Ledford, Ryan <RLedford@Balfourbeattyus.com>; Dale, Marty <mdale@balfourbeattyus.com>; Starcevic, Nicholas <NStarcevic@Balfourbeattyus.com>
Cc: Curt Westley <curt@westleycontract.com>; Robin Money <robin@westleycontract.com>
Subject: Holes in TV panels

Ryan

The price for us to cut holes in tv columns for sprinkler heads will be \$200 per hole. Please authorize us to proceed at your first opportunity.

Thanks.

Robert Jacoby
Westley Contract Services
678-640-4099



Tab No. 266

Balfour Beatty Construction

September 7, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square
Re: Request for Change Order # 266
Additional Framing and Sheetrock Requests

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 266 in the amount of Two thousand two hundred three (\$2,203.74) to provide additional work in accordance with the following qualifications:

The enclosed cost items are being submitted as added scope of work to the project done on Time and Material Tickets.

- PWI COR 18309 - Add Wall Furring for Electrical Panel 225V
 - Electrical Panel Schedule sheet E617 calls for the Spa Panel in vestibule 225V to be a surface mounted electrical panel. Precision Walls was directed on Time and Material to furr out the wall to flush out the panel for aesthetic reasons.
- PWI COR 18240 - Add Sheetrock to Foyer Side of Radius Soffit 2nd Floor
 - Partition plans call for the wing wall and soffit above the Won-Door entering the second floor dome rotunda to be a 1-Hr rated wall. The Won-Doors are a two hour rated product. After discussions with the Architect, Precision Walls was directed on Time and Material to add sheetrock to the foyer side of the rotunda soffit to achieve a longer fire rating.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set forth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Balfour Beatty Construction

Please contact me with any questions regarding this request for Change Order.

Sincerely,



Alec Dooley
Assistant Project Manager

cc:

Melissa Pense
Marty Wall
Jennifer Faulkinberry
Jim Clements
Nick Starcevic
David Simonton

RCO # 266 - File

Balfour Beatty Construction

Hotel at Marion Square

Request for Change Order # 266— Additional Framing and Sheetrock Requests

The additional work for the **Additional Framing and Sheetrock Requests** by Balfour Beatty Construction is hereby approved:

#	Budget Code	Description	Total
1	400.50925200.40	PWI COR 18309 - Add Wall Furring for Electrical Panel 225V	\$396.00
2	400.50925200.40	PWI COR 18240 - Add Sheetrock to Foyer Side of Radius Soffit 2nd Floor	\$1,683.00

Total Items \$2,079.00

Total Markups \$124.74

RCO Total \$2,203.74

The total Cost to perform the work as described above is an ADD of Two thousand two hundred three (\$2,203.74).

Please indicate your acceptance and approval of this additional work in the space provided below.

Authorization Granted by: _____ Date: _____
Kim Brown, Library Associates, LLC

RCO# 266

ELECTRONICALLY FILED - 2023 May 12 2:07 PM - CHARLESTON - COMMON PLEAS - CASE#2019CP1001108



REQUEST FOR CHANGE ORDER

Page 1 of 1

Ref.# CO-18309
GC #
Date Apr 12, 2017
Job # 14-1278

To: Balfour Beatty Construction
406 S McDowell Street, Suite 200
Raleigh, NC 27601
Phone: (919)233-5001

Project: Hotel @ Marion Square
404 King Street
Charleston, SC 29403

Description: Plan Grid Issue #297 Install metal stud wall fur out at electrical box in vestibule 225V

Labor				Total Hrs	Rate	Total	
Metal Framing				8.00	42.00	\$336.00	
				Total Labor		\$336.00	
Material	Size	Quantity	UOM	Unit Price		Total	
METAL FRAMING		1.00	EA	43.40 EA		\$43.40	
				Total Material		\$43.40	
				Subtotal for Detail		\$379.40	
Miscellaneous						Total	
Freight and Delivery Expense						\$0.00	
Tool & Equipment Expense 10%						\$4.34	
Total Miscellaneous Charges						\$4.34	
Adjustments						Total	
ROUNDING						\$0.43	
						Total Adjustments	\$0.43


Notes: Add fur out wall around electrical box in vestibule 225V per pull planning walk.

- Prices firm for 7 days and based on current job conditions
- Contract time extension of: 0 days
- Material delivery time of: 0 days
- We will not proceed with this work without a written Change Order

Michael Thomas Zinna
Project Manager

Adjustments Total:	\$0.43	
Sub Total:	\$384.17	
Sales Tax on Materials:	\$4.06	8.50%
OH&P (Material & Equipment):	\$7.77	15.00%
Sub Total:	\$396.00	
Total:	\$396.00	

#297 Wall Repair

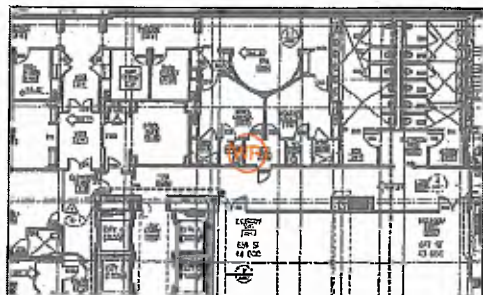

Sheet
A102

Status
Open

Created
Mar 28, 2017 at 11:02am
mzinna@precisionwalls.com

Description

Add fur out for electrical per Marty

Photos



Mar 28, 2017 at 11:02am



REQUEST FOR CHANGE ORDER

Page 1 of 1

Ref.# CO-18240
GC #
Date Mar 28, 2017
Job # 14-1278

To: Balfour Beatty Construction
406 S McDowell Street, Suite 200
Raleigh, NC 27601
Phone: (919)233-5001

Project: Hotel @ Marion Square
404 King Street
Charleston, SC 29403

Description: REVISED Added Radius Soffit Work at 2nd Floor Rotunda Extra Work Order 3/22/17 & 3/24/17

Labor		Total Hrs	Rate	Total
Hang DW Ceilings		18.00	42.00	\$756.00
Frame-Soffits/Bulkheads		10.00	42.00	\$420.00
Total Labor				\$1,176.00
Material	Size	Quantity UOM	Unit Price	Total
DRYWALL & ACCESSORIES		1.00 EA	368.90 EA	\$368.90
Total Material				\$368.90
Subtotal for Detail				\$1,544.90
Miscellaneous				Total
Freight and Delivery Expense				\$0.00
Tool & Equipment Expense 10%				\$36.89
Total Miscellaneous Charges				\$36.89
Adjustments				Total
ROUNDING				\$0.68
Total Adjustments				\$0.68

Notes: Provide labor and material to radd a 2nd layer of drywall over the radius soffit on 2nd floor at rotunda area to increase the fire rating per BBC. See attached verified extra work order executed by Marty Dale.

- Prices firm for 7 days and based on current job conditions
- Contract time extension of: 0 days
- Material delivery time of: 0 days
- We will not proceed with this work without a written Change Order

Michael Thomas China
Project Manager

Adjustments Total:	\$0.68	
Sub Total:	\$1,582.47	
Sales Tax on Materials:	\$34.49	8.50%
OH&P (Material & Equipment):	\$66.04	15.00%
Sub Total:	\$1,683.00	
Total:	\$1,683.00	

EXTRA WORK ORDER

DATE 03-14-17

G.C. JOB # _____

PWI JOB # 12-16-78

PROJECT NAME: ADON HOTEL / PAPER

PROJECT MANAGER: WILLIAM J. BROWN

TO: PRECISION WALLS, INC.

FROM: BBC

AUTHORIZATION FOR PAYMENT AND COMMENCEMENT OF WORK:

TITLE:

SIGNATURE

DATE: _____

BRIEF DESCRIPTION AND LOCATION OF WORK: REFERENCE BY BBC TO 1, AN 6

DOUBLE LAYER FOR SOFFIT AT 2 FLOOR (AROUND RADIUS SOFFIT)
where Fire Rated door is to be installed (Ratumbra Precu)

QUANTITY	UNIT	DESCRIPTION OF MATERIAL OR EQUIPMENT	UNIT PRICE	EXTENSION
5		DEYWALL		
DESIGN CEMENT Jarl. half material shen 4/11/17				

TOTAL MAT'L.	\$
--------------	----

[illegible]

HOURS TO DATE: 6

WORK APPROVED

AS COMPLETED

SIGNATURE:

TITLE:

DATE: _____

SIGNATURE:

DATE: _____

INCOMPLETE

COMPLETE

SUPERVISION

SAFETY

TOTAL LABOR

OTHER DIRECT COSTS

TOTAL


This extra work order will/may increase the duration allotted for the performance of our work.
Please adjust the schedule accordingly.

WORK ORDER

Customer - White Project Manager - Canary GC Superintendent - Pink Foreman - Goldenrod

1 of 2

R - 1995

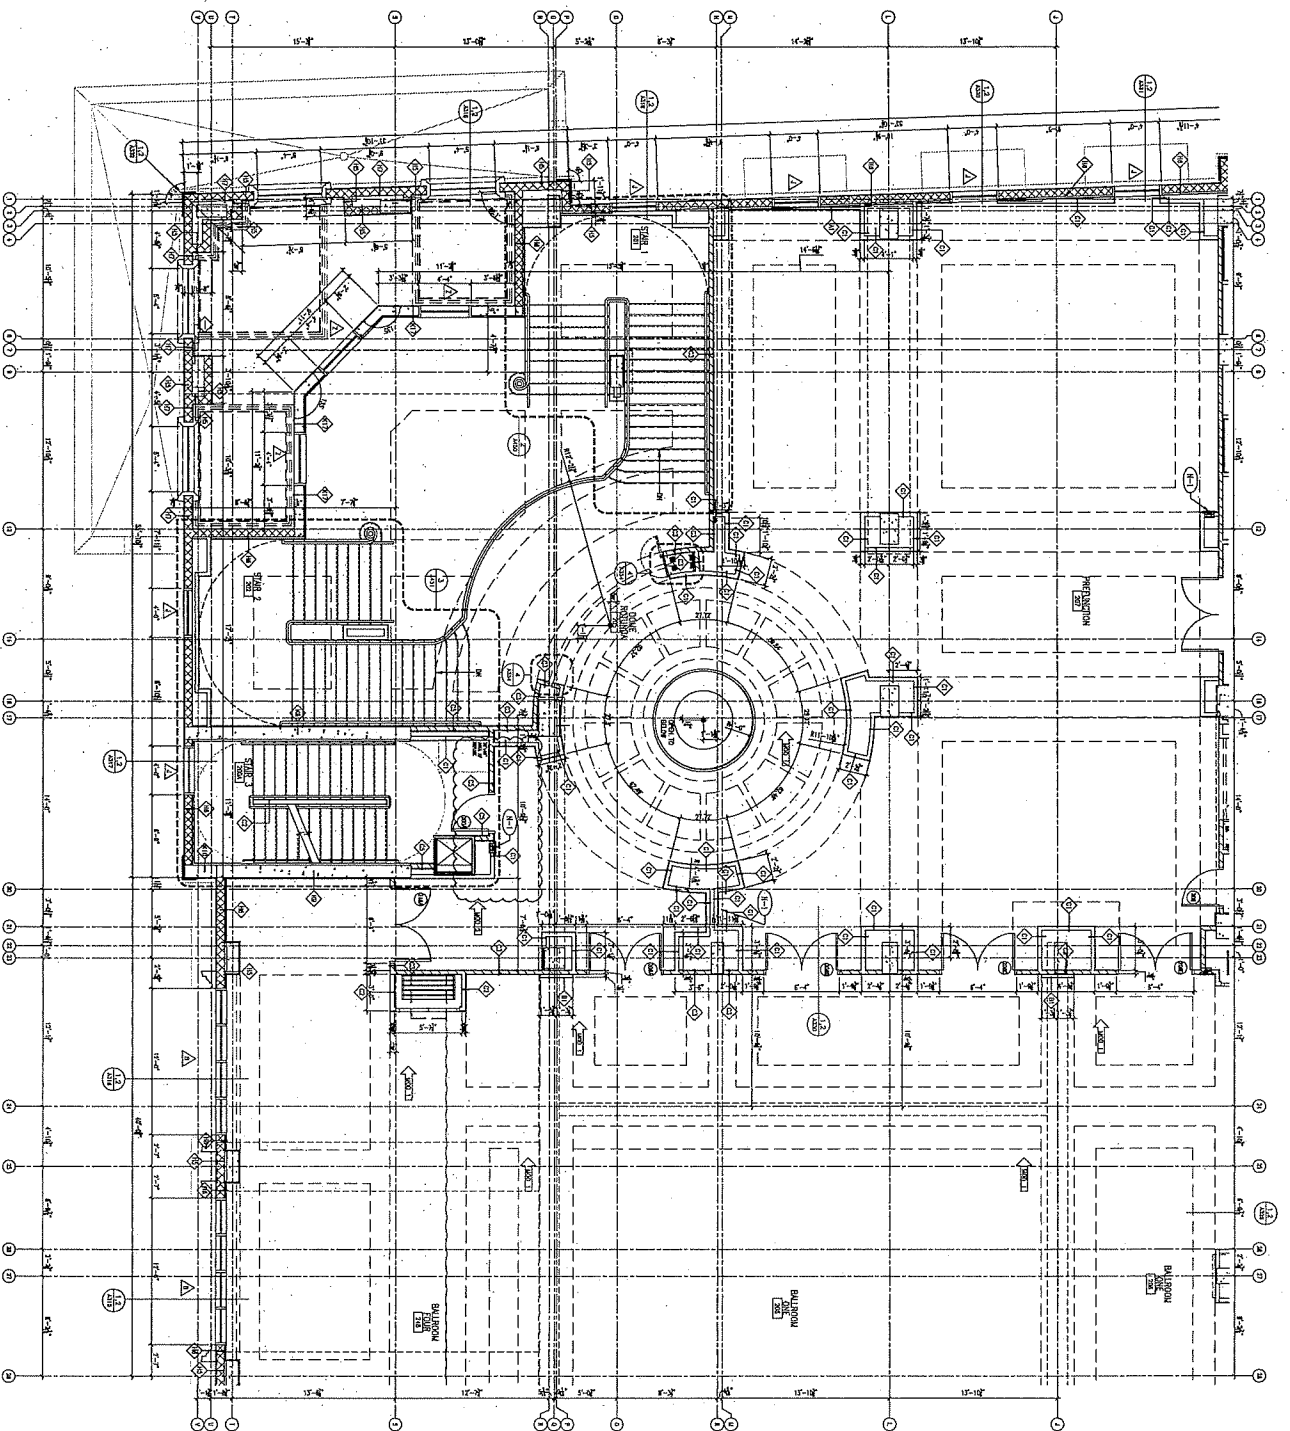[illegible]

① EXPANDED 2ND FLOOR PLAN

A407	A408
A409	

LIBRARY
ASSOCIATES,
LLC.
RICE MILL
BUILDING
17 LOCKWOOD
DRIVE
CHARLESTON,
SC 29401

344 WEST PINE STREET
LAWRENCEVILLE, GA 30046
770 963 8888
770 962 8182 FAX.

**WINFORD
LINDSAY
ARCHITECT**

THE HOTEL
AT
MARION
SQUARE

1997

404 KING STREET
CHARLESTON, SC
29403

PROJECT NO.: 2005-09
DRAWN BY:
CHECKED BY:
APPROVED BY:
PLOT DATE:
© 2011 M.A. MOORE RECREATION
BUREAU (EAST) DISTRICT

A406

Tab No. 267

Balfour Beatty

Construction

September 7, 2018

Ms. Kim Brown
Library Associates, LLC
17 Lockwood Drive
Charleston, SC 29401

Project: Hotel at Marion Square

Re: Request for Change Order # 267
Rooftop Bar MOD 1-8 Millwork

Dear Ms. Brown:

We are submitting, herewith, our Request for Change Order # 267 in the amount of Seven thousand nine hundred twenty-two (\$7,922.44) to provide additional work in accordance with the following qualifications:

Rooftop Bar MOD 1-8 Millwork to revise millwork at the rooftop bar from paint grade tongue and groove to WD-02. This was later credited in SI 40. Millwork revisions submitted in RCO 149 (SI 40) assumed the execution of the MOD 1-8 millwork revisions at the rooftop bar submitted in RCO 142. This change order was struck from RCO 142 until the rooftop bar design could be finalized. The credits associated with RCO 149 for the change in ceiling assumed that the adds were taken within MOD 1-8 Millwork. See attached summary from LCCM.

This Change Order Request addresses those requests for costs and/or time associated with the Construction Change Directive and Change Order Request(s) referenced above which are undisputed; however, this Change Order does not resolve related requests for costs and/or time which remain in dispute, and those requests are expressly reserved. This proposal covers only the changes to the specific work as set fourth in the attached proposal breakout. Changes in the work and associated price adjustments other than those noted in our proposal are not included. Pricing included in this proposal is valid for thirty (30) days.

Please contact me with any questions regarding this request for Change Order.

Sincerely,

Alec Dooley
Assistant Project Manager

cc:
Melissa Pense
Marty Wall
Jim Clements
Jennifer Faulkinberry
Woody Faust
Nick Starcevic
David Simonton
RCO # 267 - File
